

dandara new homes

Construction Environmental Management Plan

Land at Stakers Farm North End Road, Yapton

Rev: D

Date: 8th January 2021

Document Control

Site Name: Yapton
Document Title: Construction Environmental Management Plan
Document Reference: YAP-ENG-04-4.9.1
Date of First Completion: 27th March 2020

	Name	Position	Date
Prepared by:	Murray Armstrong	Civil Engineering Technician	27.03.20
Reviewed by:	Christian O'Brien	Engineering Manager	27.03.20
Approved by:	Paul Ebbs	Production Director	27.03.20

Revision	Date	Description	Prepared	Reviewed	Approved
A	27.03.20	Initial issue for planning	MA	COB	PE
B	17.09.20	Section 3.1 updated to clarify access arrangements and Appendix B updated to include location of wheel washing facilities as per West Sussex County Council comments.	MA	COB	PE
C	02.11.20	Section 5.10 updated to suit comments from West Sussex County Council	MA	COB	PE
D	08.01.21	Section 4.4 revised to add "All loose loads should be sheeted" as per Highways England comments. Appendix A updated restriction hours as per Section 3.3.	COB	COB	PE

Internal Distribution

Revision	Date	Name	Position	Department

Contents

1	Introduction	1
1.1	Background	1
1.2	Objectives	1
1.3	Scope	1
2	Proposed Works	2
2.1	Site Background	2
2.2	Construction Programme	2
2.3	Enabling Works	2
2.4	Construction of Substructures and Superstructures	3
3	Vehicle Access and Restrictions	4
3.1	Site Access	4
3.2	Proposed Estate Roads	4
3.3	Site Restrictions	4
4	Construction Traffic Management	5
4.1	Site Location	5
4.2	Heavy Goods Vehicles	5
4.3	Construction Access Route	6
4.4	Loading, Unloading and Storage of Plant Materials	8
4.5	Turning Facilities	8
4.6	Onsite Holding Areas	8
4.7	Wheel Washing Facilities	9
4.8	Air Quality and Dust Suppression	9
5	Construction Organisation	10
5.1	Site Compound	10
5.2	Welfare Facilities	10
5.3	Parking for Site Operatives and Visitors	10
5.4	Hours of Working	11
5.5	Noise	11
5.6	Site Contacts	11
5.7	Communication Strategy	12
5.8	Responsibilities of the Principal Contractor	12
5.9	Security Hoarding	12
5.10	Public Right of Way	12
5.11	Lighting	12
5.12	Recycling and Waste Disposal	13

Appendices

- Appendix A Construction Access Map
- Appendix B Construction Environmental Method Plan
- Appendix C Large Tipper Tracking

1 Introduction

1.1 Background

This Construction Environmental Management Plan (CEMP) was written and targeted specifically for Dandara's proposed 38 residential unit scheme (Y/88/18/OUT) as part of a 108-unit development, Yapton, located on North End Road, Yapton.

The nature of construction and its associated activities, has the potential to cause an impact on the local area and its existing residents if improperly managed, coordinated and mitigated. Therefore, the purpose of this CEMP is to ensure that the impact of the development's construction work on local residents and the nearby highway network is kept to an absolute minimum.

1.2 Objectives

The primary objective of this CEMP is to comprehensively demonstrate how impacts of the construction traffic upon North End Road and the local highway network will be successfully managed, coordinated and mitigated to provide safe, suitable and convenient access for all users, while also protecting nearby residents' living conditions.

The secondary objective of this CEMP is to submit to the Local Planning Authority, Arun District Council, to satisfy and discharge planning Condition 6 of Outline Application Ref: Y/88/18/OUT.

1.3 Scope

It is intended that the agreed CEMP will cover the following:

- The anticipated number, frequency and types of vehicles used during construction (Section 4.6)
- The method of access, number, routing and types of vehicles during construction (Section 3.1, 3.2 & 4.3)
- The parking of vehicles by site operatives and visitors (Section 5.3)
- The loading and unloading of plant, materials and waste (Section 4.4)
- The storage of plant and materials used in construction (Section 4.4)
- The erection and maintenance of security hoarding (Section 5.9)
- The provision of wheel washing facilities and other works required to mitigate the impact of construction upon the public highway (Section 4.7)
- Details of public engagement (Section 5.7)
- Indicative programme of works (Section 2.2)
- Measures to minimise the noise and vibration generated by construction (Section 5.5)
- Details of any floodlighting (Section 5.11)
- Measures to control the emission of dust during construction (Section 4.8)
- Scheme for recycling/disposing of waste from demolition and construction (Section 5.12)

2 Proposed Works

2.1 Site Background

Yapton is a greenfield site that is used primarily for animal grazing use by the adjacent Stakers Farm. It has no known previous use other than for agricultural land.

The Yapton C of E primary school is located on the southern boundary, with hedges separating the land.

The east of the site runs adjacent to North End Road and is where the site is accessed. An existing residential development is also located east of the site, on the other side of North End Road.

Proposed works include site clearance and the subsequent construction of 108 total dwellings across the land; comprising of low-rise traditional masonry 2-storey houses.

2.2 Construction Programme

The total construction duration is anticipated to be in the region of 6 months, with groundworks proposed for August 2020.

The construction programme is influenced by several constraints, including the available working space and resources. As such, the development will be completed in approximately 4 stages to permit the most efficient means of working.

All works will be completed within our site boundary.

The Plots currently scheduled within each Stage are as follows:

- Stage 1: Plots 1-3
- Stage 2: Plots 6-16
- Stage 3: Plots 4-5 & 17-28
- Stage 4: Plots 29-38

2.3 Enabling Works

Enabling works will consist of earthworks and associated topsoil strip, without the requirement for major vegetation clearance or removal of excavated materials.

The proposed site levels have been designed using a “cut and fill” approach, to optimise the re-use of excavated materials locally at the site and significantly reducing construction traffic movements in/out of the site during this stage.

Trees and areas of vegetation to be retained will be protected from adverse effects during construction through the installation of temporary fencing, as appropriate and in accordance with the approved tree protection measures prior to the works.

All of the main estate roads, including unallocated vehicular spaces, and adjacent footways will be first constructed prior to Plot construction up to base level, with a temporary wearing course used for construction traffic.

2.4 Construction of Substructures and Superstructures

The construction period minus the preliminary works is anticipated to be 6 months. A typical construction programme for each unit is shown in Table 1, illustrating the activities undertaken and the corresponding durations.

Table 1 – Construction programme for a typical unit

Activity	Duration (Weeks)
Foundation, Drainage and Oversite	4
Brickwork and Joist	7
Roof Carcass	2
Glazing and First Fix	2
Plastering / Drylining	2
Second Fix	2
Tiling and Decorating	2
Finishes and Externals	2
Quality Control Final Inspection, CML and Handover	4
Total Duration:	27

3 Vehicle Access and Restrictions

3.1 Site Access

Access to the site will be made via the proposed site entrance as per the Construction Management Plan (CMP) approved under condition 2 of the separate access planning application (Ref: Y/17/20PL).

3.2 Proposed Estate Roads

Any temporary onsite haul roads will form the geometry of the proposed estate roads that have been designed to accommodate the tracking of a fire tender and refuse vehicle.

A swept path analysis for a large tipper has been undertaken, confirming that the proposed access is suitable for construction vehicles and is shown in Appendix C.

Table 2 – Comparison between Fire Tender, Refuse Vehicle and Large Tipper

Specification (units)	Fire Tender	Refuse Vehicle	Large Tipper
Overall Length (m)	8.680	9.860	10.201
Overall Width (m)	2.180	2.450	2.495
Overall Body Height (m)	3.452	3.814	2.890
Min. Body Ground Clearance (m)	0.337	0.366	0.341
Track Width (m)	2.121	2.450	2.471
Lock to Lock Time (seconds)	6.00	4.00	6.00
Kerb to Kerb Turning Radius (m)	7.910	9.500	11.550

3.3 Site Restrictions

Due to the limited site compound area, deliveries should be made 'just in time', with strictly no construction traffic queuing on North End Road and its vicinity.

There is the Yapton C of E primary school located on the boundary of the site, with students and families using North End Road as a means of commute by walking, cycling or by car. As such, there will be a restriction on deliveries to reduce the impacts of construction traffic and material deliveries during peak hours.

Suppliers will be advised that there will be no deliveries made to the site during the hours of:

- 8:00am – 9:00am
- 2:45pm – 3:45pm

Construction traffic must not use Ford Road in Arundel as their route when accessing or leaving the site. Caution should be given to the railway crossing located on North End Road 0.40 miles north of the site.

4 Construction Traffic Management

4.1 Site Location

Figure 2 shows the location of the development within Yapton and the wider highway network.

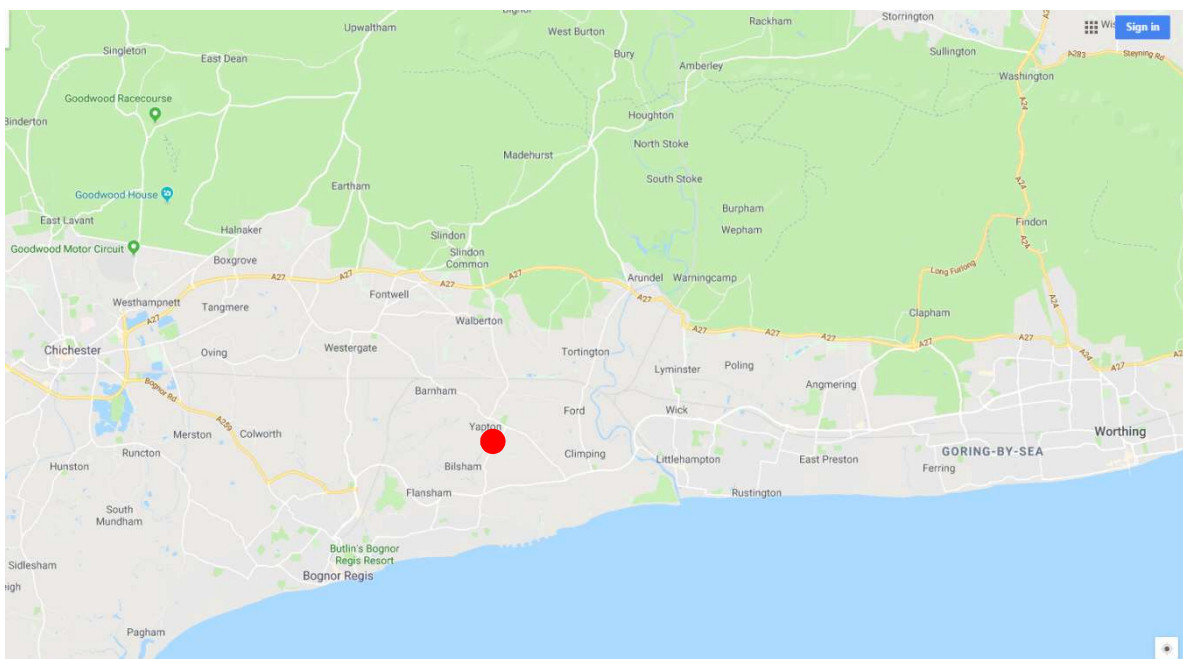


Figure 2 - Indicative Site Location within the wider Highway Network

4.2 Heavy Goods Vehicles

Heavy Goods Vehicles (HGV's), including that typically used for construction related traffic, are permitted to use any classification of road for access and deliveries, hence it is difficult to restrict their movements. The situation is made increasingly more difficult due to HGV's being operated by other companies, suppliers and organisations out of our direct control; who may not fully understand or appreciate the potential consequences and impacts of their HGV movements. However, this CMS and supporting appendices will be issued to appropriate third parties who will be directly involved in the development, on how best to manage their HGV movements, to ensure minimal impact on the surrounding highway network.

As a main through route, HGV's are directed to use the most appropriate route via motorways, dual carriageways and main roads.

4.3 Construction Access Route

The main routes into Yapton are via the A27, B2132 and B2233. Research has been undertaken to assess the most suitable routes for construction traffic utilising these road networks towards Yapton.

Figures 3, 4 and 5 show routes from various strategic locations that were checked by inputting vehicle dimensions from Table 1 into an online freight journey planner, which contains information on the locations of any height, weight and width restrictions along the proposed route.

Therefore, a strategy for the means of access for construction traffic has been determined by assessing the local road conditions, in addition with the site vehicular access and associated restrictions. As a result, Appendix A shows the recommended route for construction traffic local to the site, to minimise the impacts associated with the construction of the Yapton development on the local highway network.

A copy of the pre-determined recommended routes in the form of the 'Construction Access Map' (Appendix A) will be distributed to our suppliers and sub-contractors who will be involved with the site.

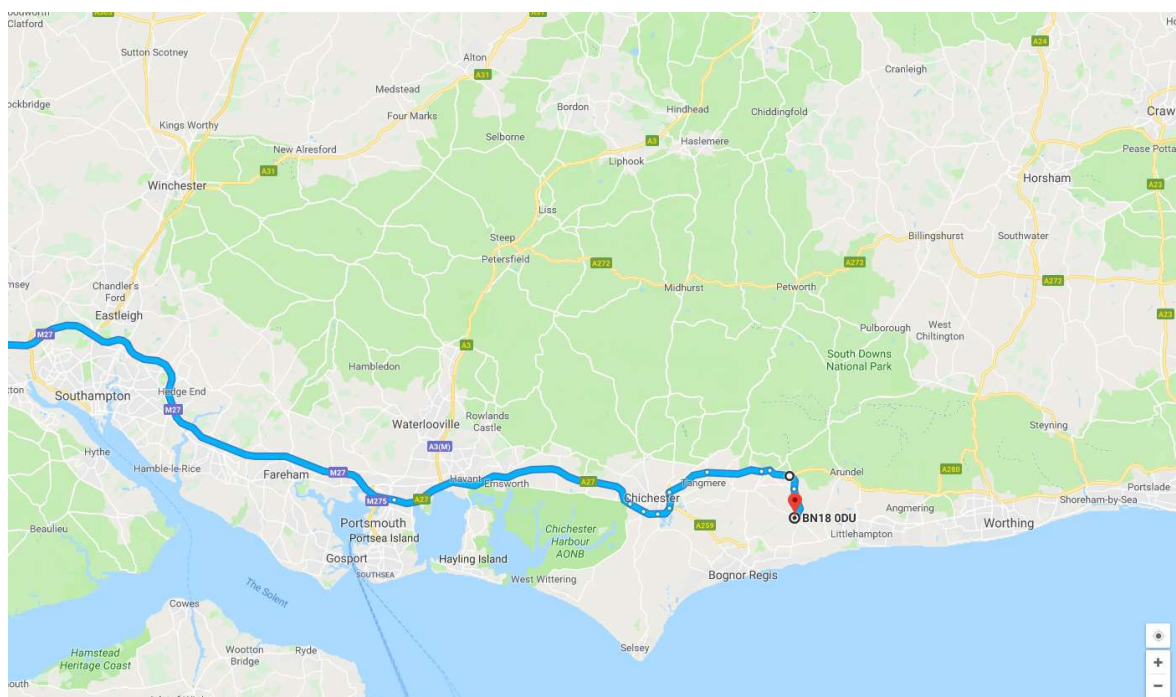


Figure 3 – Construction Access to North End Road from Chichester, Portsmouth and Southampton

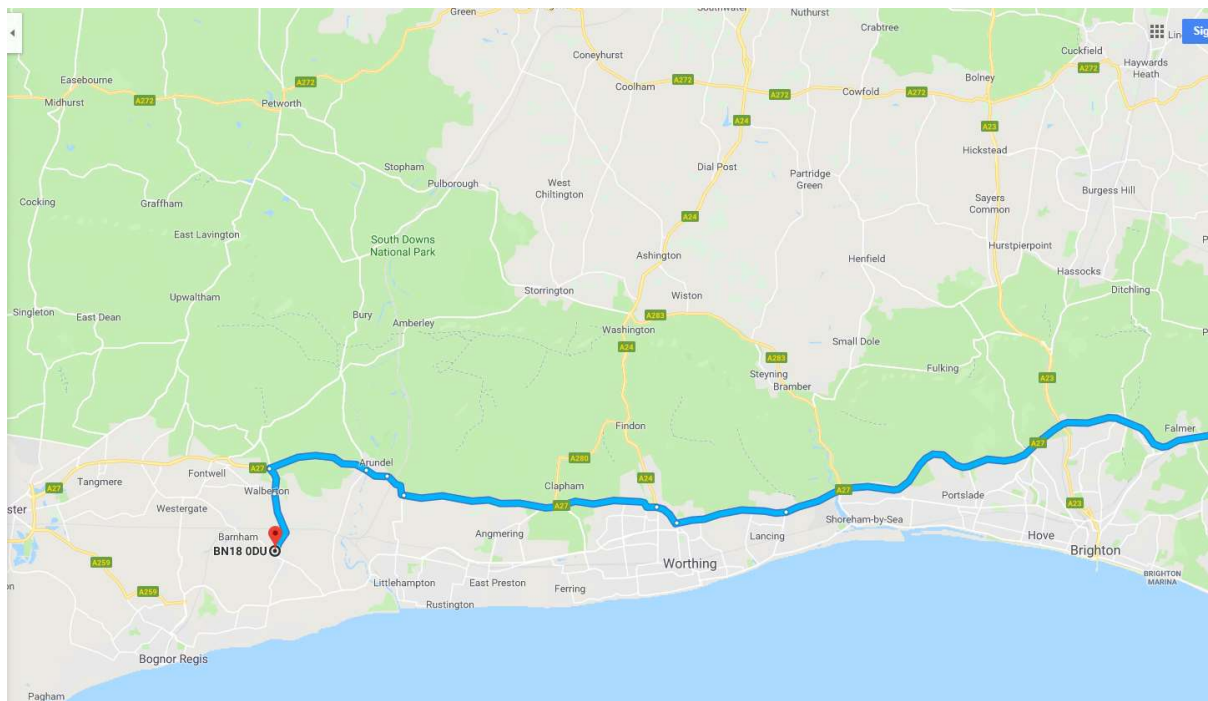


Figure 4 – Construction Access to North End Road from Worthing, Brighton and Eastbourne

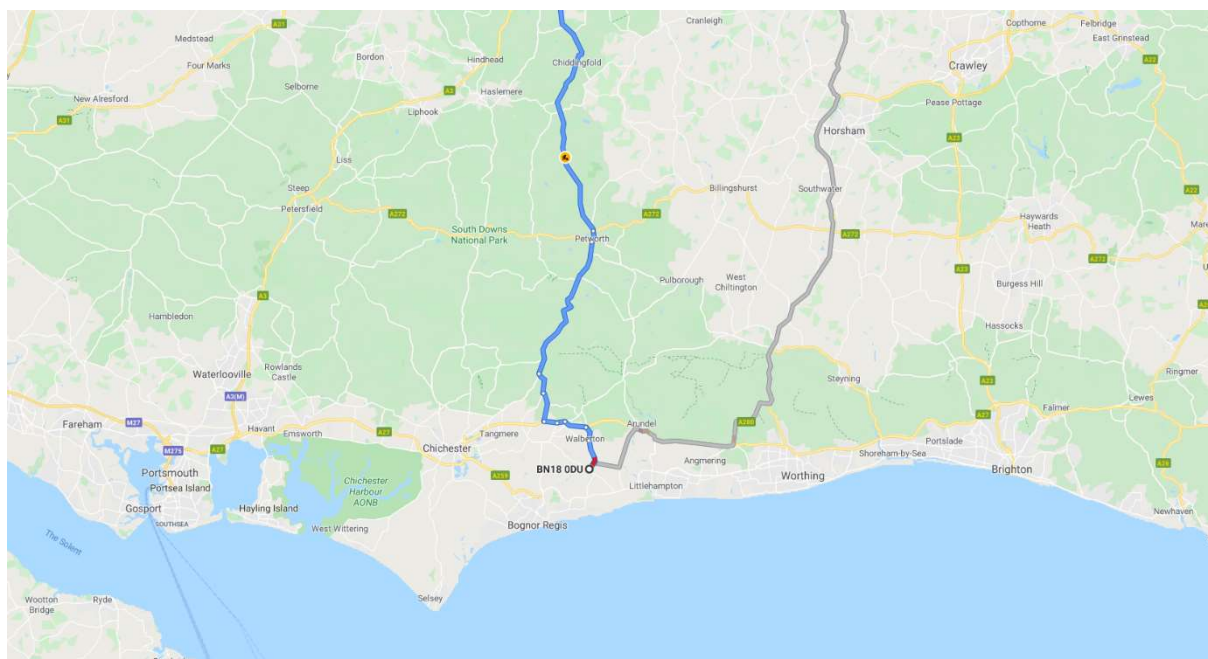


Figure 5 – Construction Access to North End Road from Guildford and London

4.4 Loading, Unloading and Storage of Plant Materials

To facilitate the efficient and safe loading and unloading of plant and materials, in addition to 4 No. 20'x8' secure stores within the main compound, a loading and secure storage area will be temporarily provided as indicated on the 'Construction Environmental Method Plan' in Appendix B.

Materials for use in the works will be stockpiled in the site compound, temporary storage area or adjacent to the immediate work area. Material storage areas shall be suitably demarcated, and segregation shall be maintained at all stages to ensure minimal contamination and/or waste.

All loose loads should be sheeted.

4.5 Turning Facilities

There is to be no reversing into the site or onto North End Road.

All vehicular turning is to be restricted on site, with the Principal Contractor providing such facility as part of their proposed Traffic Management Plan. It is recommended that a turning head is constructed near the compound to enable construction traffic to safely turn on site and enable access/egress to the site in a forward gear. This has been demonstrated on the 'Construction Method Plan' in Appendix B.

4.6 Onsite Holding Areas

It is anticipated that through organised project planning by the Site Manager, deliveries can be scheduled to stagger throughout the day, particularly avoiding peak hours, as well as avoiding multiple deliveries on site at the same time.

An estimation of the primary delivery frequencies, when required, is shown in Table 3. The frequencies in Table 3 are only indicative and are not to be looked at as an absolute total or minimum and are subject to change according to the stage of build.

Where it is unavoidable and multiple deliveries occur and/or are attempting to leave the site simultaneously, construction vehicles will be conducted to a lay-by within the site as a temporary holding area if deemed necessary by the Site Manager or Gateman.

Table 3 – Schedule of Estimated Primary Deliveries

Materials	Stages Required	Estimated Frequency
Large Plant and Equipment	E and Completion	2 per day
Aggregates	E, SS	6 per day
General Contractors Materials	E, SS, L	6 per day
Fuel Deliveries	SS	1 per week
General Deliveries	E, SS, L	4 per day

E = Enabling Works; SS = Substructures and Superstructures; L = Landscaping

4.7 Wheel Washing Facilities

Due to the nature of the cohesive materials on site, it is likely that tyres will gather material from the site before surfaced roads have been constructed. The presence of mud can constitute a public nuisance and loss, or injury, can result in a claim for negligence. Due to the occurrence of materials collecting on tyres being unavoidable at certain stages of the works, active measures will be taken to prevent dirt, mud and debris from being deposited on the road.

As a first defence, vehicles shall first be limited to trafficking on hard surfaces on the site, where possible, to minimise initial collation of materials on tyres. Vehicles will also abide by the site speeds of no more than 10mph, or that stated otherwise on site, primarily for safety purposes, but also to help retain any dirt and debris on the vehicle.

For all vehicles leaving the site at North End Road, wheel wash facilities will be used in the form and specification of a manned hand-held jet wash, with road sweepers on full time where necessary whilst importing any fill material. No vehicles leaving the site will have mud on its tyres. All vehicles leaving the site will be inspected and confirmed to be sufficiently clean to prevent the migration of dirt and debris onto North End Road and the nearby public highway. This will be monitored daily by the Principal Contractor's Site Manager to ensure public highways and site roads are kept clean.

4.8 Air Quality and Dust Suppression

Dust is particularly problematic for unpaved granular roads; however temporary haul roads are to be capped with a tarmac surfacing to prevent fines from the sub-base material from being airborne from vehicle movements and tyre 'plucking'.

The likelihood of dust is ultimately determined by the local geological strata, which is more likely in loose particulate strata like sandstones and chalks. The predominant soil type is clay, which is a cohesive material and should not give rise to fugitive dust in the interim, prior to the tarmac surfacing.

If unforeseen fugitive dust occurs, then the generated dust will be mitigated in general accordance with BRE Report 456 – 'Control of dust from construction and demolition activities. This includes damping down of fill material embankments and/or haul roads using towed spray bowsers.

5 Construction Organisation

5.1 Site Compound

The ground workers will be Principal Contractor during the enabling works and prior to Dandara having an onsite presence. The ground workers will have a satellite compound, which will allow its location to be moved in accordance with the necessary phasing of construction. The satellite compound will still comprise of the necessary temporary cabins, welfare, and material storage.

Once Dandara become Principal Contractor at the start of the house building phase, a construction site compound will be set up as indicated on the 'Construction Environmental Method Plan' in Appendix B. The site compound will have segregated areas for pedestrians and vehicles, allocated parking spaces, offices for staff, canteen, drying area, toilets and material storage.

5.2 Welfare Facilities

In accordance with the Construction Design and Management Regulations 2015, welfare facilities on site will include:

- Suitable and sufficient sanitary convenience
- Suitable and sufficient washing facilities, including showers
- Adequate supply of wholesome drinking water
- Suitable and sufficient changing rooms and lockers
- Suitable and sufficient rest rooms

5.3 Parking for Site Operatives and Visitors

Specific parking areas as indicated on the 'Construction Method Plan' in Appendix B, will be located adjacent to the compound with overflow available at strategic locations around the site to suit the current area of works or to avoid conflict with occupations.

Additional temporary parking at peak periods of construction will be provided when necessary, utilising some of the constructed unallocated vehicular spaces spread across the site that will be formed up to base level. Parking areas will be clearly signed and monitored by the Site Manager.

A total of 26 parking spaces are available at the main compound (Site Manager, Forklift Driver, Building Control or Dandara Office Staff Visitor, and Site Operatives), with a further 4 parking spaces available in visitor bays prior to occupation. The total of 30 potential spaces is deemed suitable and sufficient parking to accommodate the anticipated staff of approximately 50 (assuming the typical car share for the trades contractors).

All personnel transportation vehicles will be required to park within the designated areas and strictly no parking will be permitted on North End Road. Only construction plant will be permitted overnight parking onsite.

5.4 Hours of Working

In general, site working hours are envisaged as being within the following:

- Monday to Friday: 8:00am to 6:00pm
- Saturday: 8:00am to 1:00pm
- Sundays or Bank Holidays: No construction activity will take place

5.5 Noise

All works will be undertaken in accordance with the Control of Noise at Work Regulations 2005, including the associated Lower Exposure Action Value of 80dB, Upper Exposure Action Value of 85dB and Exposure Limit Value of 87dB.

As approved for guidance by The Control of Noise (Code of Practice for Construction and Open Sites) (England) Order 2015 statutory instrument, the British Standard BS5228 Code of practice for noise and vibration control on construction and open sites – Part 1: Noise, will be used to guide basic methods of noise control relating to construction.

Where the operative and/or Site Manager believes a significant disturbance may be caused, the Site Manager will contact the nearby property owner/resident to inform them of the intended works and their duration, and if required what measures are being employed to mitigate.

5.6 Site Contacts

The ground worker who has been appointed to undertake the groundworks element of the scheme and who is initially the Principal Contractor for the main works is:

TBC – Contractor not yet appointed but information will be provided to the Local Authority as soon as this information becomes available.

- Foreman TBC (Mobile: TBC)
- Contract Manager TBC (Mobile: TBC)

Once the development has reached the oversite stage (approximately 16 weeks), the groundworker will step down as Principal Contractor and will then be the responsibility and duty of Dandara.

Dandara Limited (Southern), Roman House, South Hampshire Industrial Park, Eddystone Road, Totton, Hampshire, SO40 3SA

- Site Manager TBC (Mobile: TBC)
- Construction Manager TBC (Mobile: TBC)

Dandara's Site Manager will be located on site and responsible for the day-to-day operations of the development. If Dandara's Site Manager is unavailable, then the Construction Manager should be contacted as the secondary point of contact for any enquiries regarding the construction of the development.

5.7 Communication Strategy

Communication to the local residents and commerce about the works will be through a letter drop before commencing the works. The site will be continually monitored to ensure compliance with the CEMP requirements and company procedures. Any non-conformances will be highlighted at monthly team meetings and a remedial strategy implemented as soon as is reasonably practicable.

5.8 Responsibilities of the Principal Contractor

It will be the responsibility of the Principal Contractor's Site Manager for ensuring that the construction activities relating to the proposed development are undertaken in strict accordance with this CEMP.

A contractor (including a Principal Contractor) appointed to work on a project will have the skills, knowledge and experience necessary to fulfil the role that they are appointed to undertake, in a manner that secures the health and safety of any person affected by the project, in accordance with the Construction (Design and Management) Regulations 2015.

All site personnel, visitors, sub-contractors and suppliers will be expected to abide by this CEMP. Where delivery drivers will be regularly coming to the site, they will be issued with copies of this plan either as paper copies or in electronic form. The plan will also be posted on the site office notice board and will be discussed during the site induction as part of the site traffic management plan.

5.9 Security Hoarding

Security hoarding or fencing is to be erected along all necessary boundaries. Refer to the Construction Environmental Method Plan in Appendix B for full details on their location. Safe access for vehicles and a separate pedestrian's access is to be provided, where possible, at the site entrance.

Weekly maintenance checks will be undertaken to establish any damage and general condition of the hoarding/fencing.

5.10 Public Right of Way

There are two existing public right of ways on site. The first right of way on the southern part of the site follows the boundary along Yapton CE Primary School. This shall have Heras fencing erected along its entirety to restrict access to site whilst maintaining a 3.0m clear and usable public right of way. The northern right of way which cuts directly through the site from the south-east, shall be informally redirected in the interest of public health and safety. The new route shall follow the southern right of way to the far western boundary before turning northbound to intersect its original route. Separate applications for diversions or temporary closures, as appropriate, shall be made prior to any works starting on the public right of ways.

5.11 Lighting


As per Section 5.4, the proposed working hours fall during daylight hours and as such there will be no immediate requirement for floodlighting. Lighting may be deemed necessary during winter months when daylight hours are limited. This will be at the discretion of the Principal Contractor and installed as such so it does not affect neighbouring properties. Details of locations, heights, type and direction of light sources and intensity of illumination will be provided if such circumstances occur. Minor security lighting will be provided to the temporary welfare/office and sales compound where necessary.

5.12 Recycling and Waste Disposal

There are no demolition works associated with the site. However, skips with appropriate signage shall be provided to separate general waste from potential recyclable or reusable materials. Any waste or recycling to be disposed of off-site shall be dealt with by the appropriate Contractor and taken to an approved and licensed waste or recycling facility. Waste transfer note/certificate records shall be kept as evidence of such procedures being undertaken in accordance with company policy. Any movements of vehicles from site into the local highway network shall be in accordance with Section 4.7.

This page is intentionally blank

Appendix A Construction Access Map

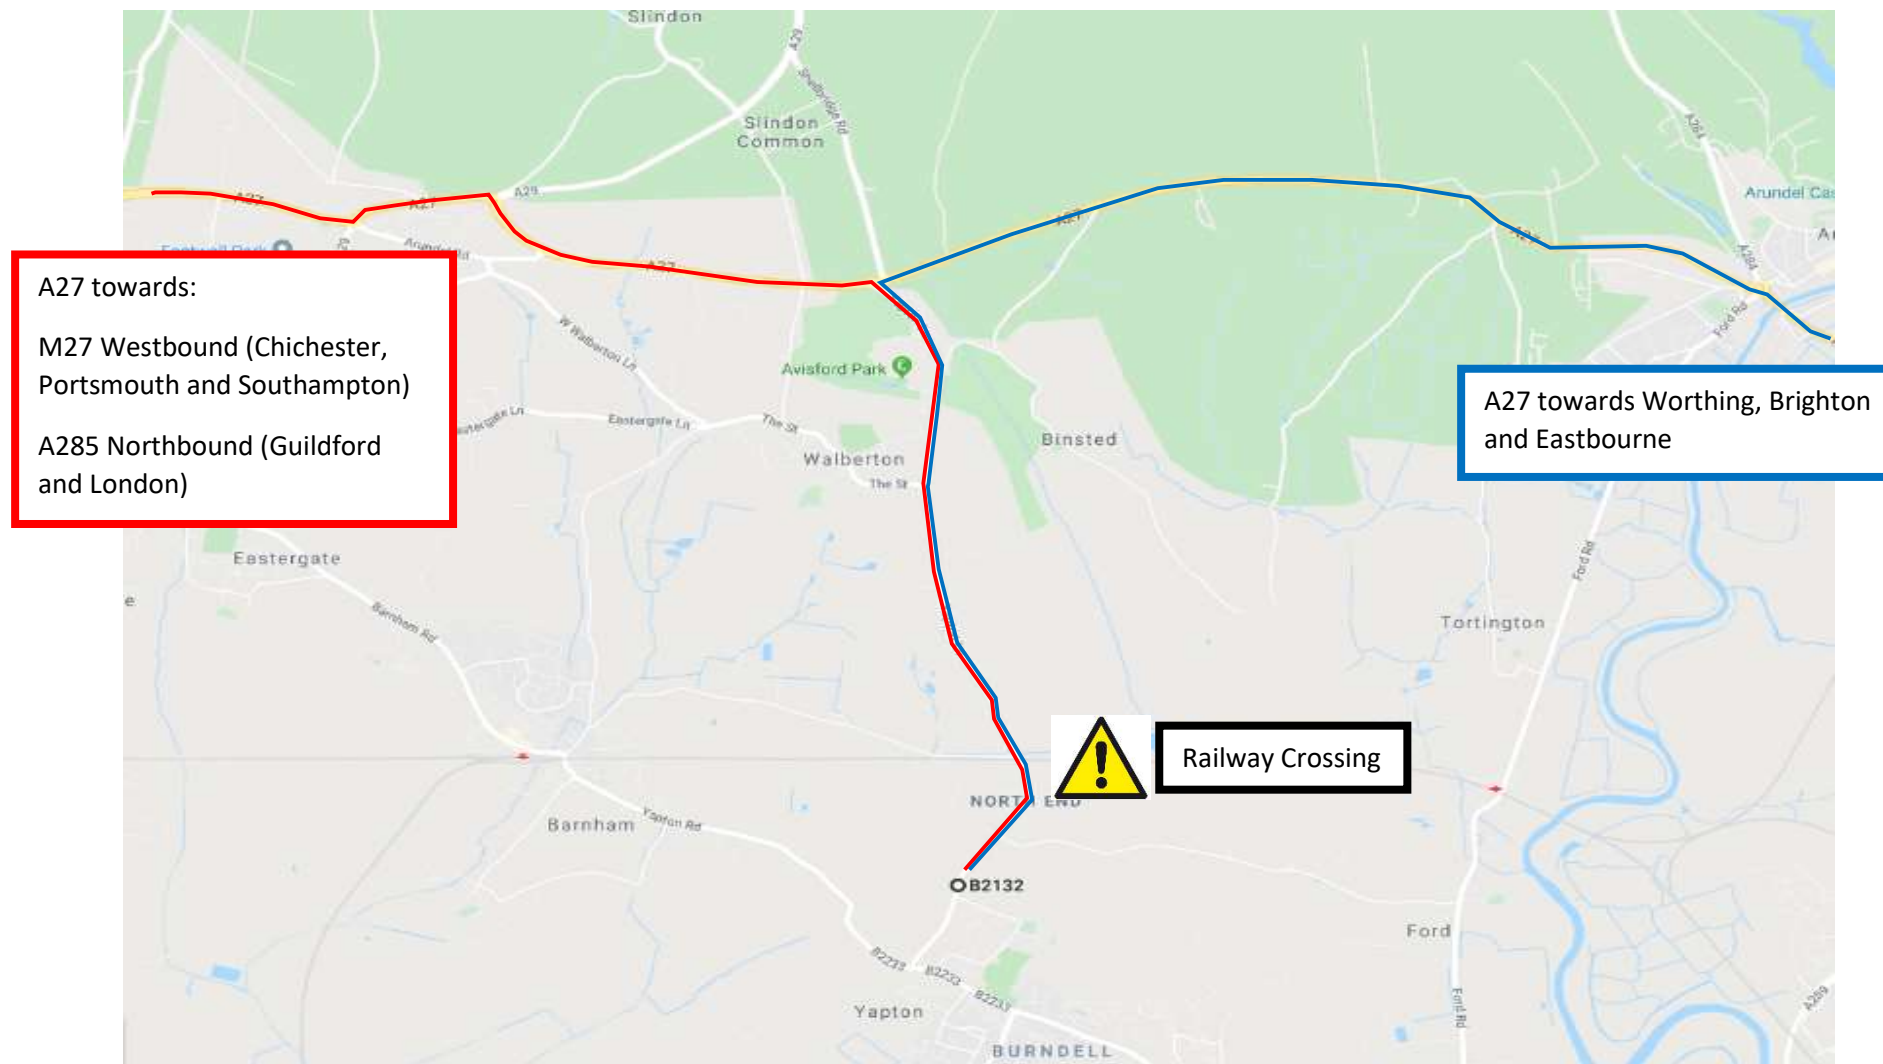


Construction Access Map

Land at Stakers Farm, North End Road, Yapton, BN18 ODU

No deliveries shall take place between 08:00-09:00 and 14:45-15:45 to avoid spike in traffic around School Areas

Appendix B Construction Environmental Method Plan

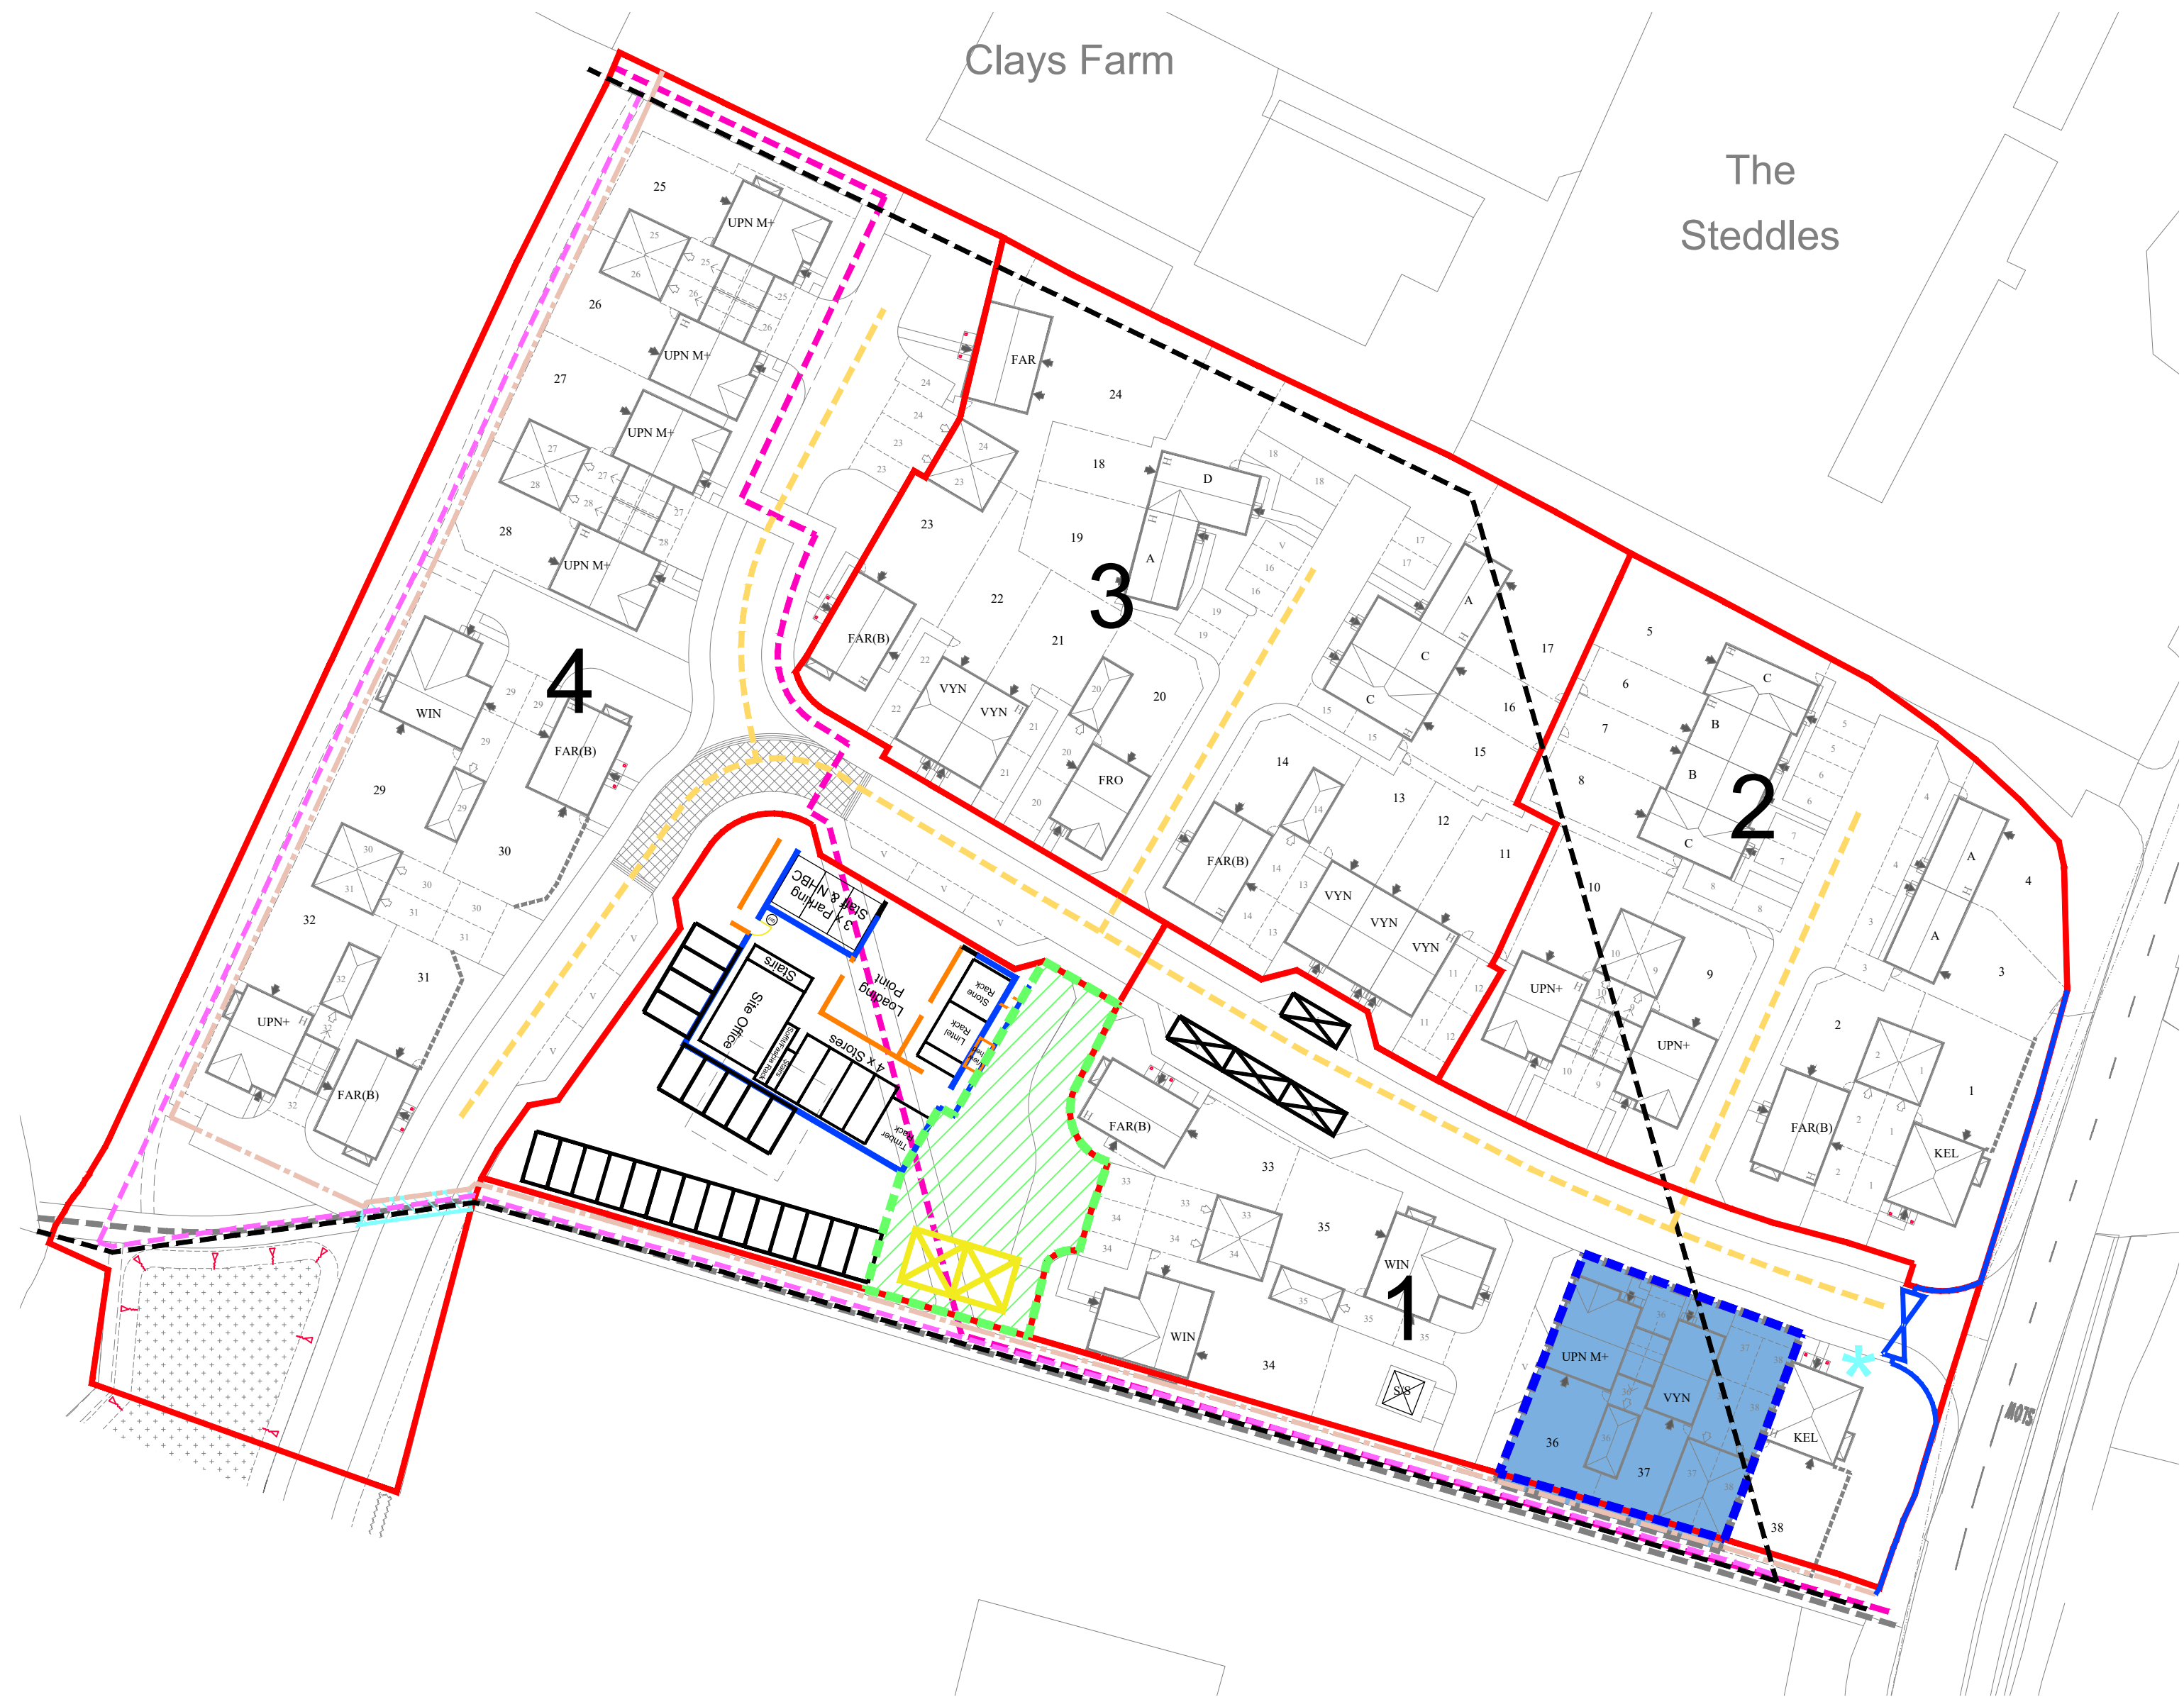

- Legend:
- Material Storage
 - Sales Area
 - Public Crossing
 - Silos
 - Lay-By / On-Site Holding Area
 - Public Right of Way
 - Informal redirection of Public Right of Way
 - Vehicle Routing
 - Timber Fencing
 - Timber Hoarding
 - Heras Fencing
 - Site Entrance Gate and Security Hoarding
 - Staff / Visitor Parking
 - Location of wheel washing facilities

Note: Layout indicative only. Please refer to Architect's proposed site plan for full detailed layout.

E	17/09/20	Location of wheel washing facilities added	MA
D	23/07/20	Site layout updated	MA
C	16/03/20	Site layout updated	MA
B	09/01/20	Site layout updated	MA
A	30/10/19	Initial issue	MA
Rev.	Date	Description	Initial

Development
North End Road, Yapton

Drawing Title
Engineering Details - Construction
Environmental Method Plan


Status
FOR INFORMATION

dandara
new homes
Roman House, South Hampshire Industrial Park,
Eddystone Road, Totton, SO40 3SA
Tel: 02382 124061


Scale	Paper Size	Date	Drawn	Checked
NTS	A2	30/10/19	MA	COB

Drwg. No.	Rev.
YAP-CMP-01	E


Appendix C Large Tipper Tracking

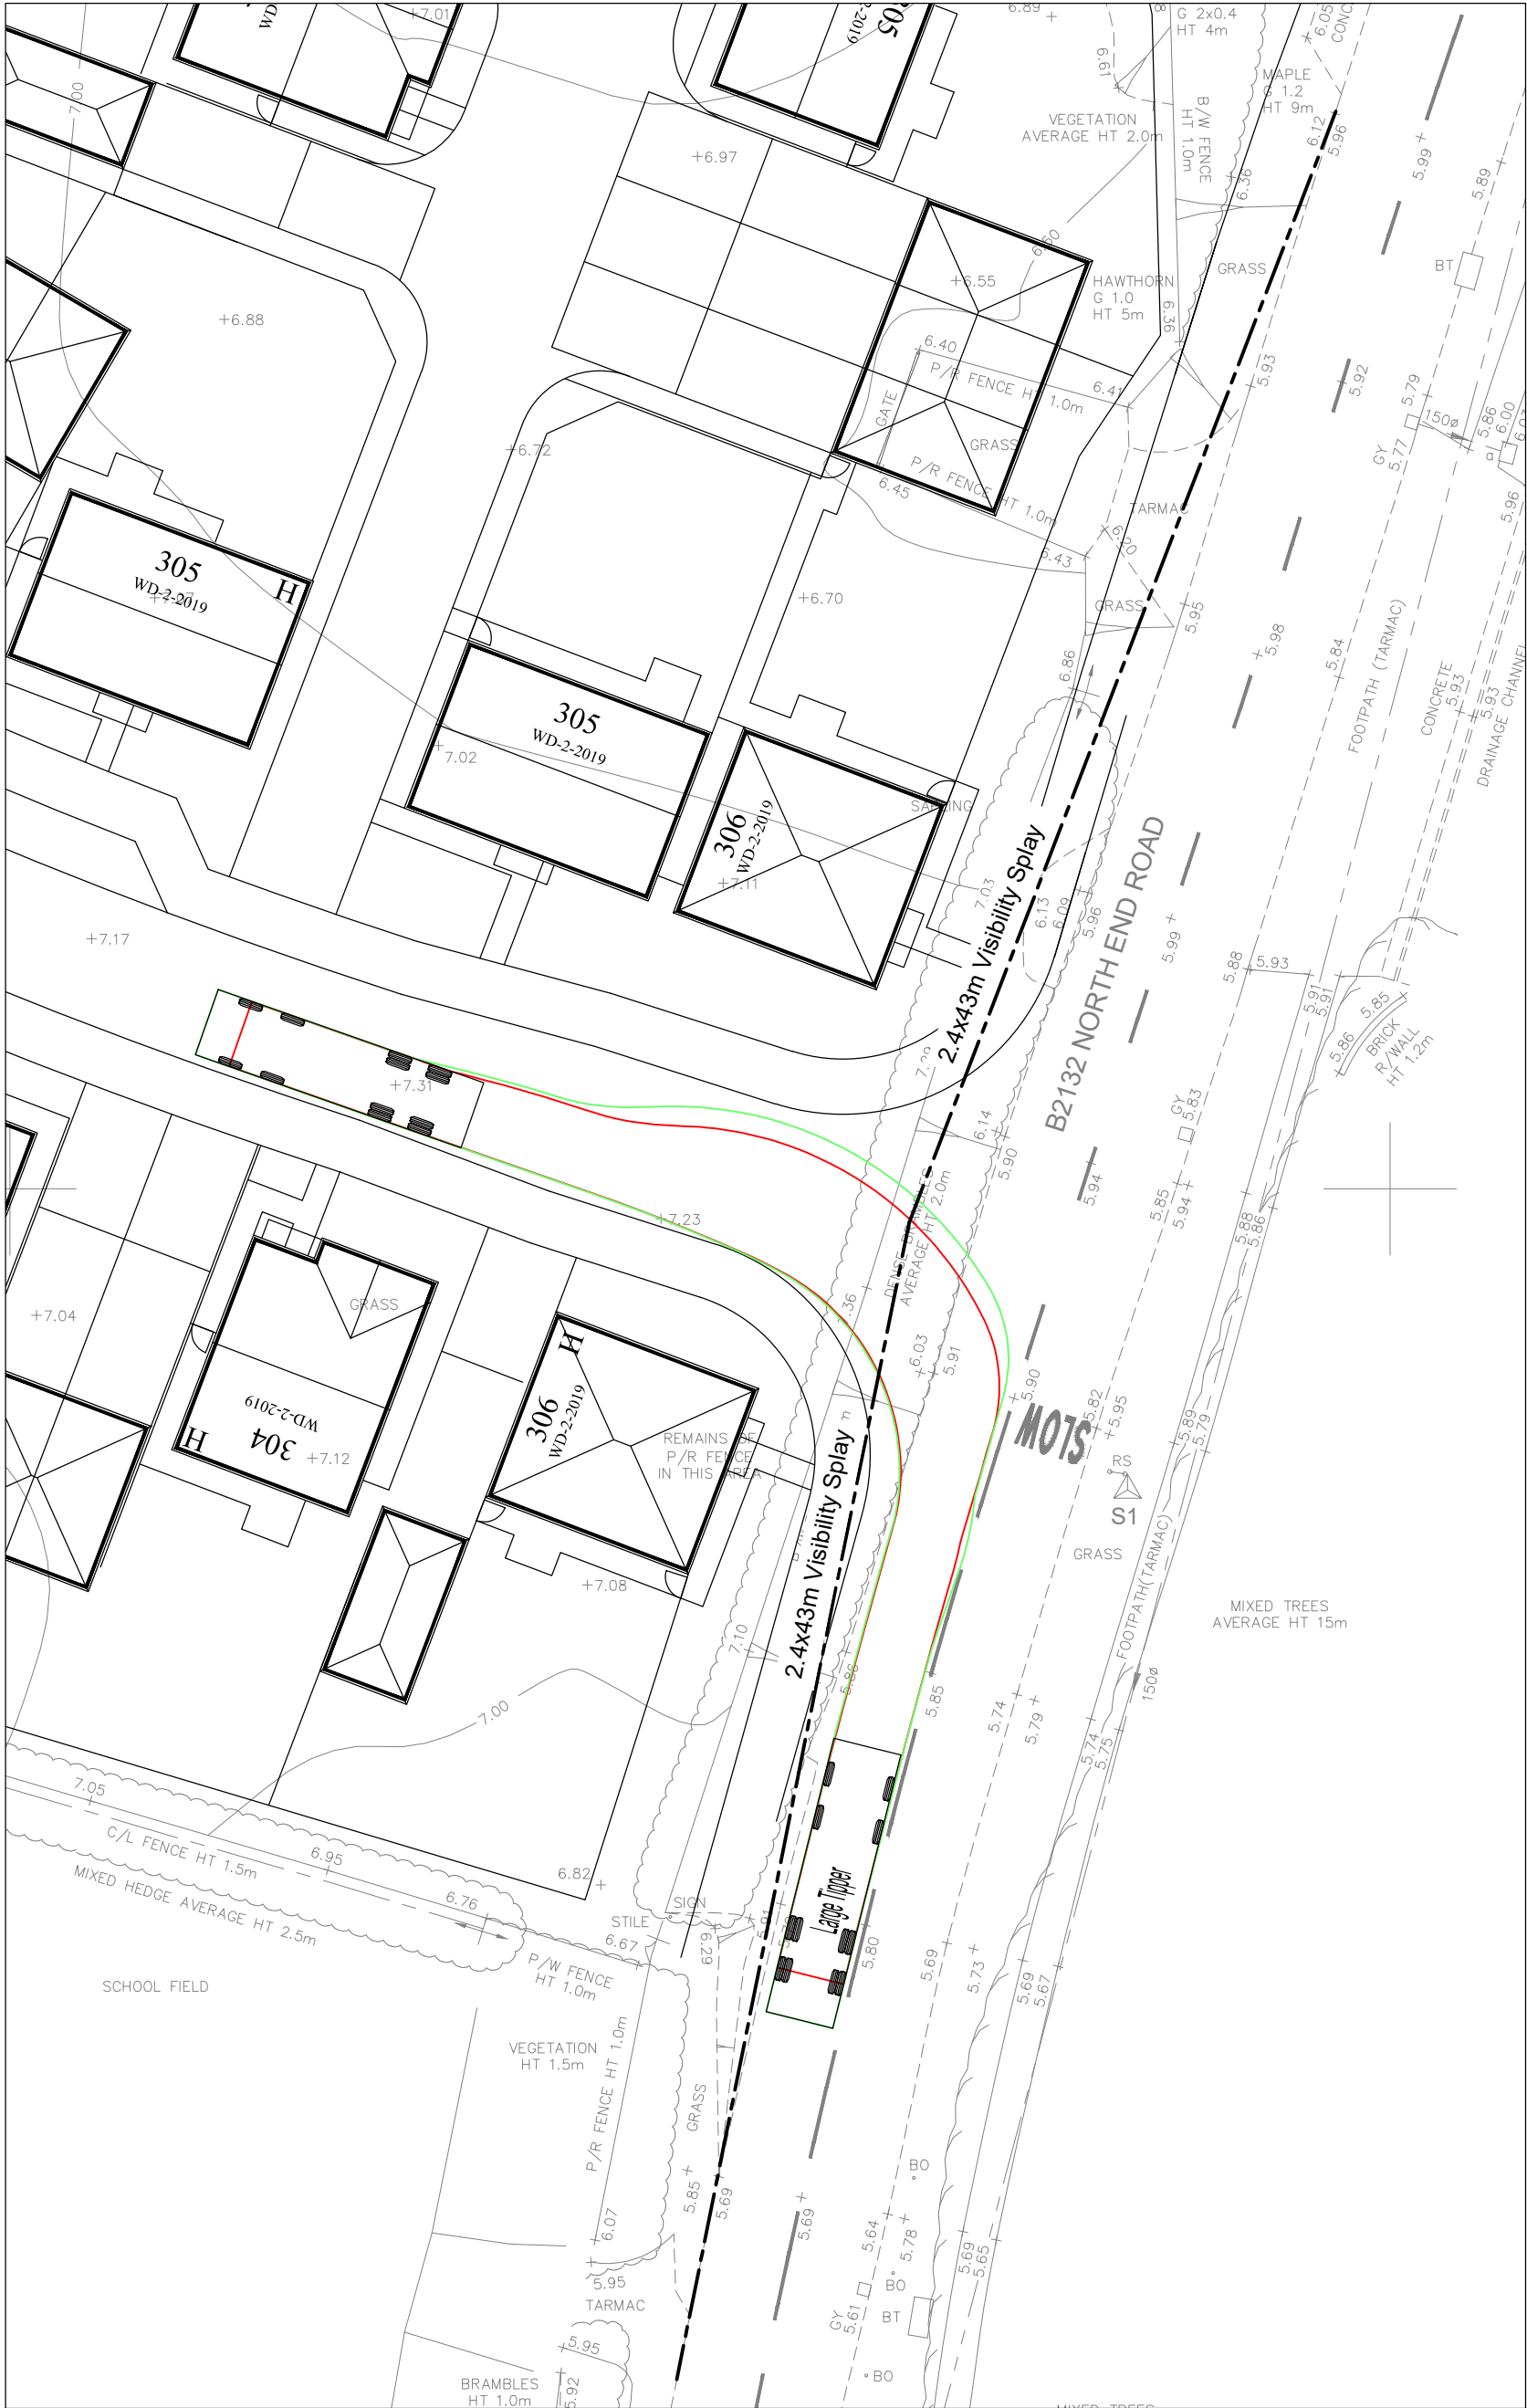

Proposed Access - Entry (North Bound)

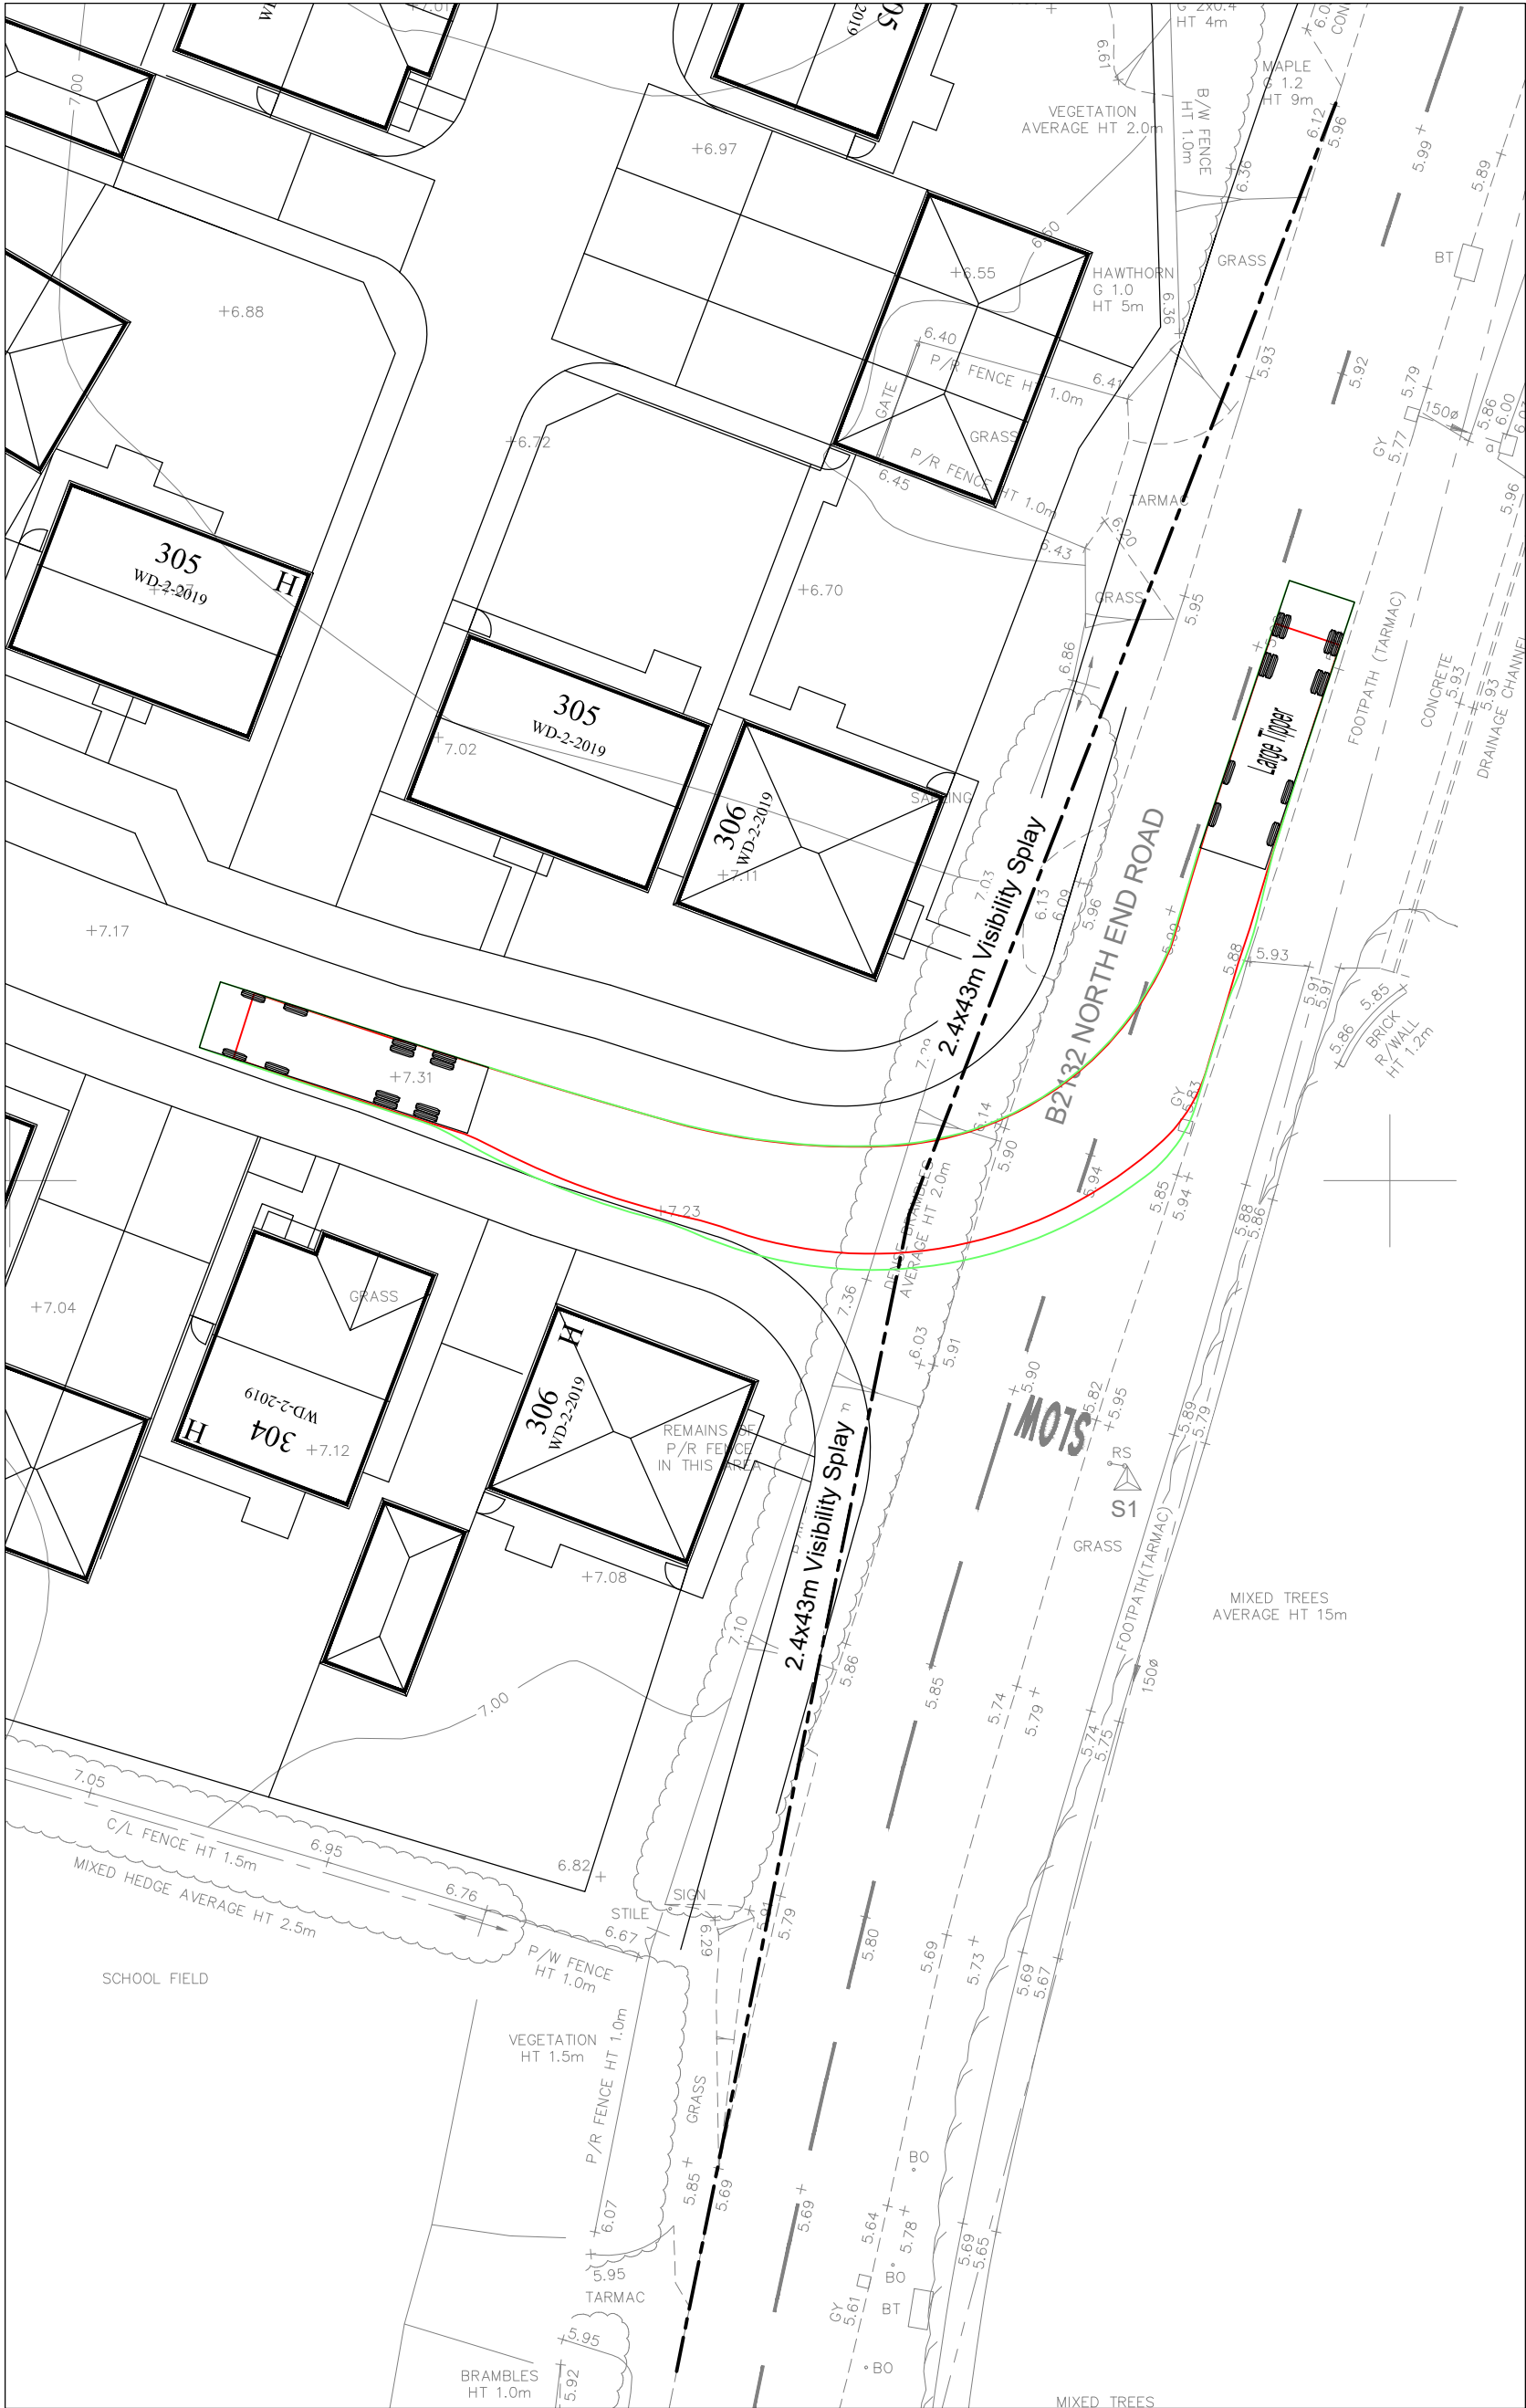


Proposed Access - Entry (South Bound)




Large Tipper
Overall Length 10.201m
Overall Width 2.495m
Overall Body Height 2.890m
Min Body Ground Clearance 0.341m
Track Width 2.471m
Lock to lock time 6.00s
Kerb to Kerb Turning Radius 11.550m

Note: Layout indicative only. Please refer to Architect's proposed site plan for full detailed layout.

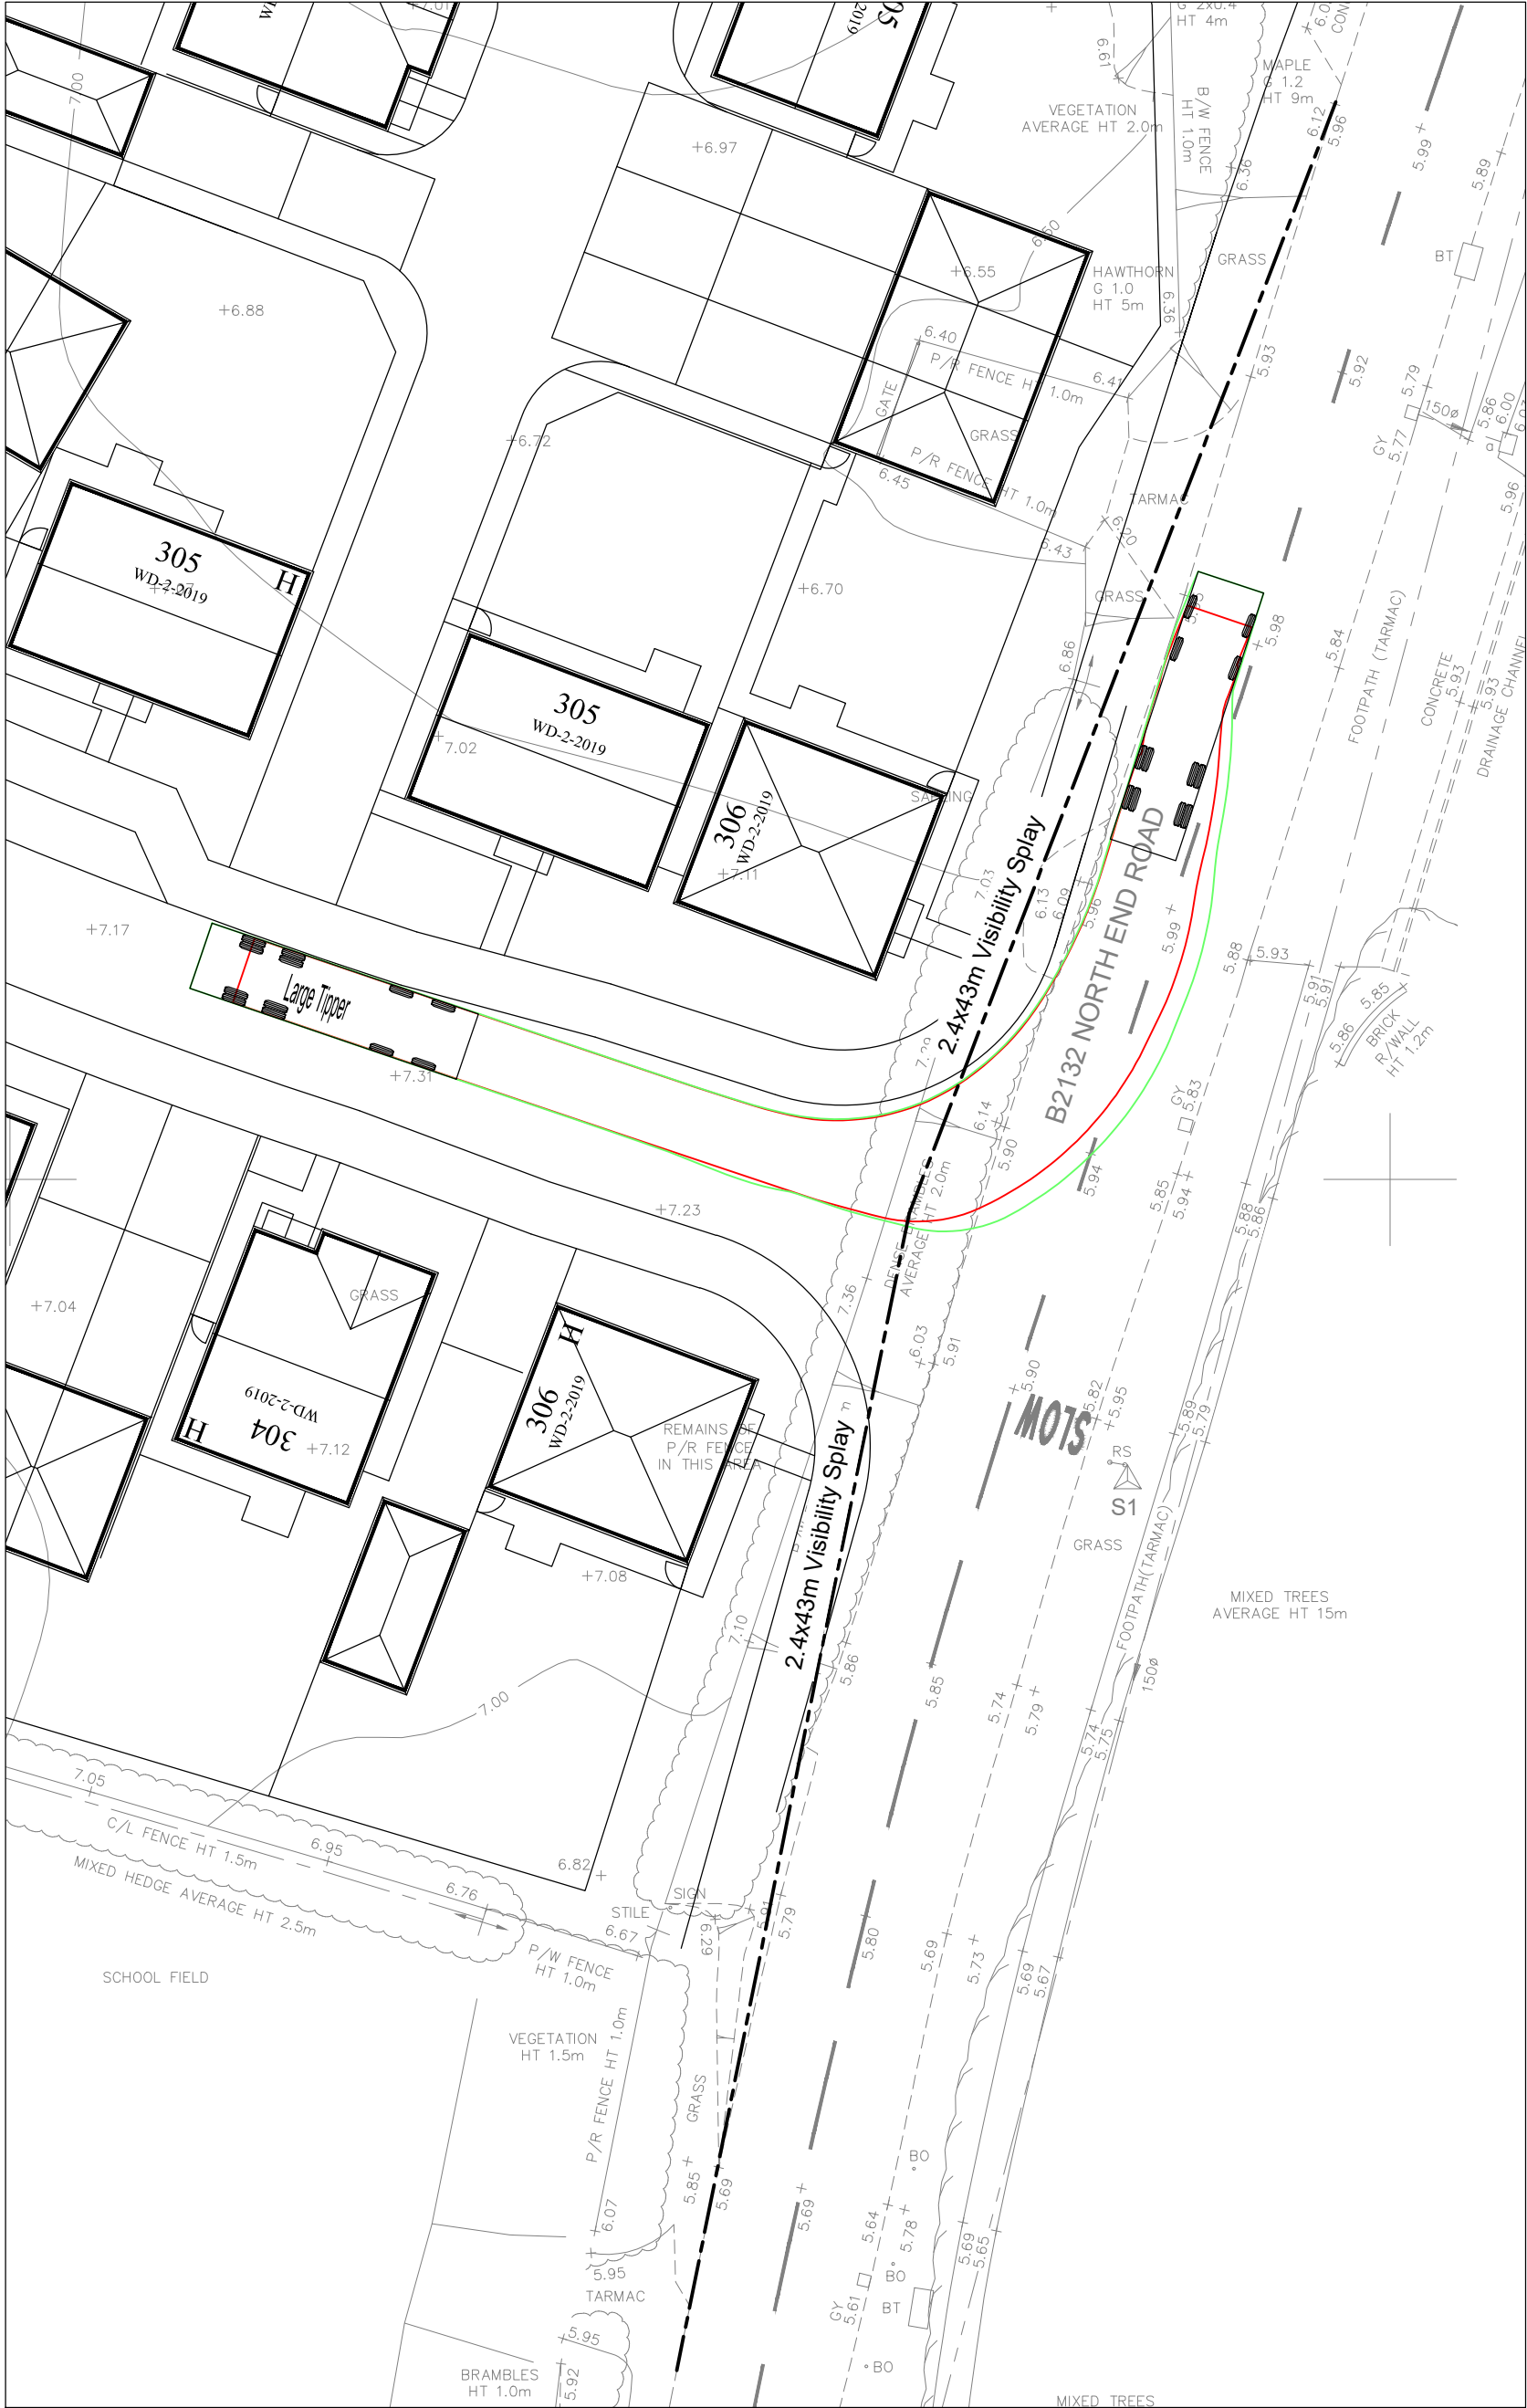

Proposed Access - Egress (North Bound)

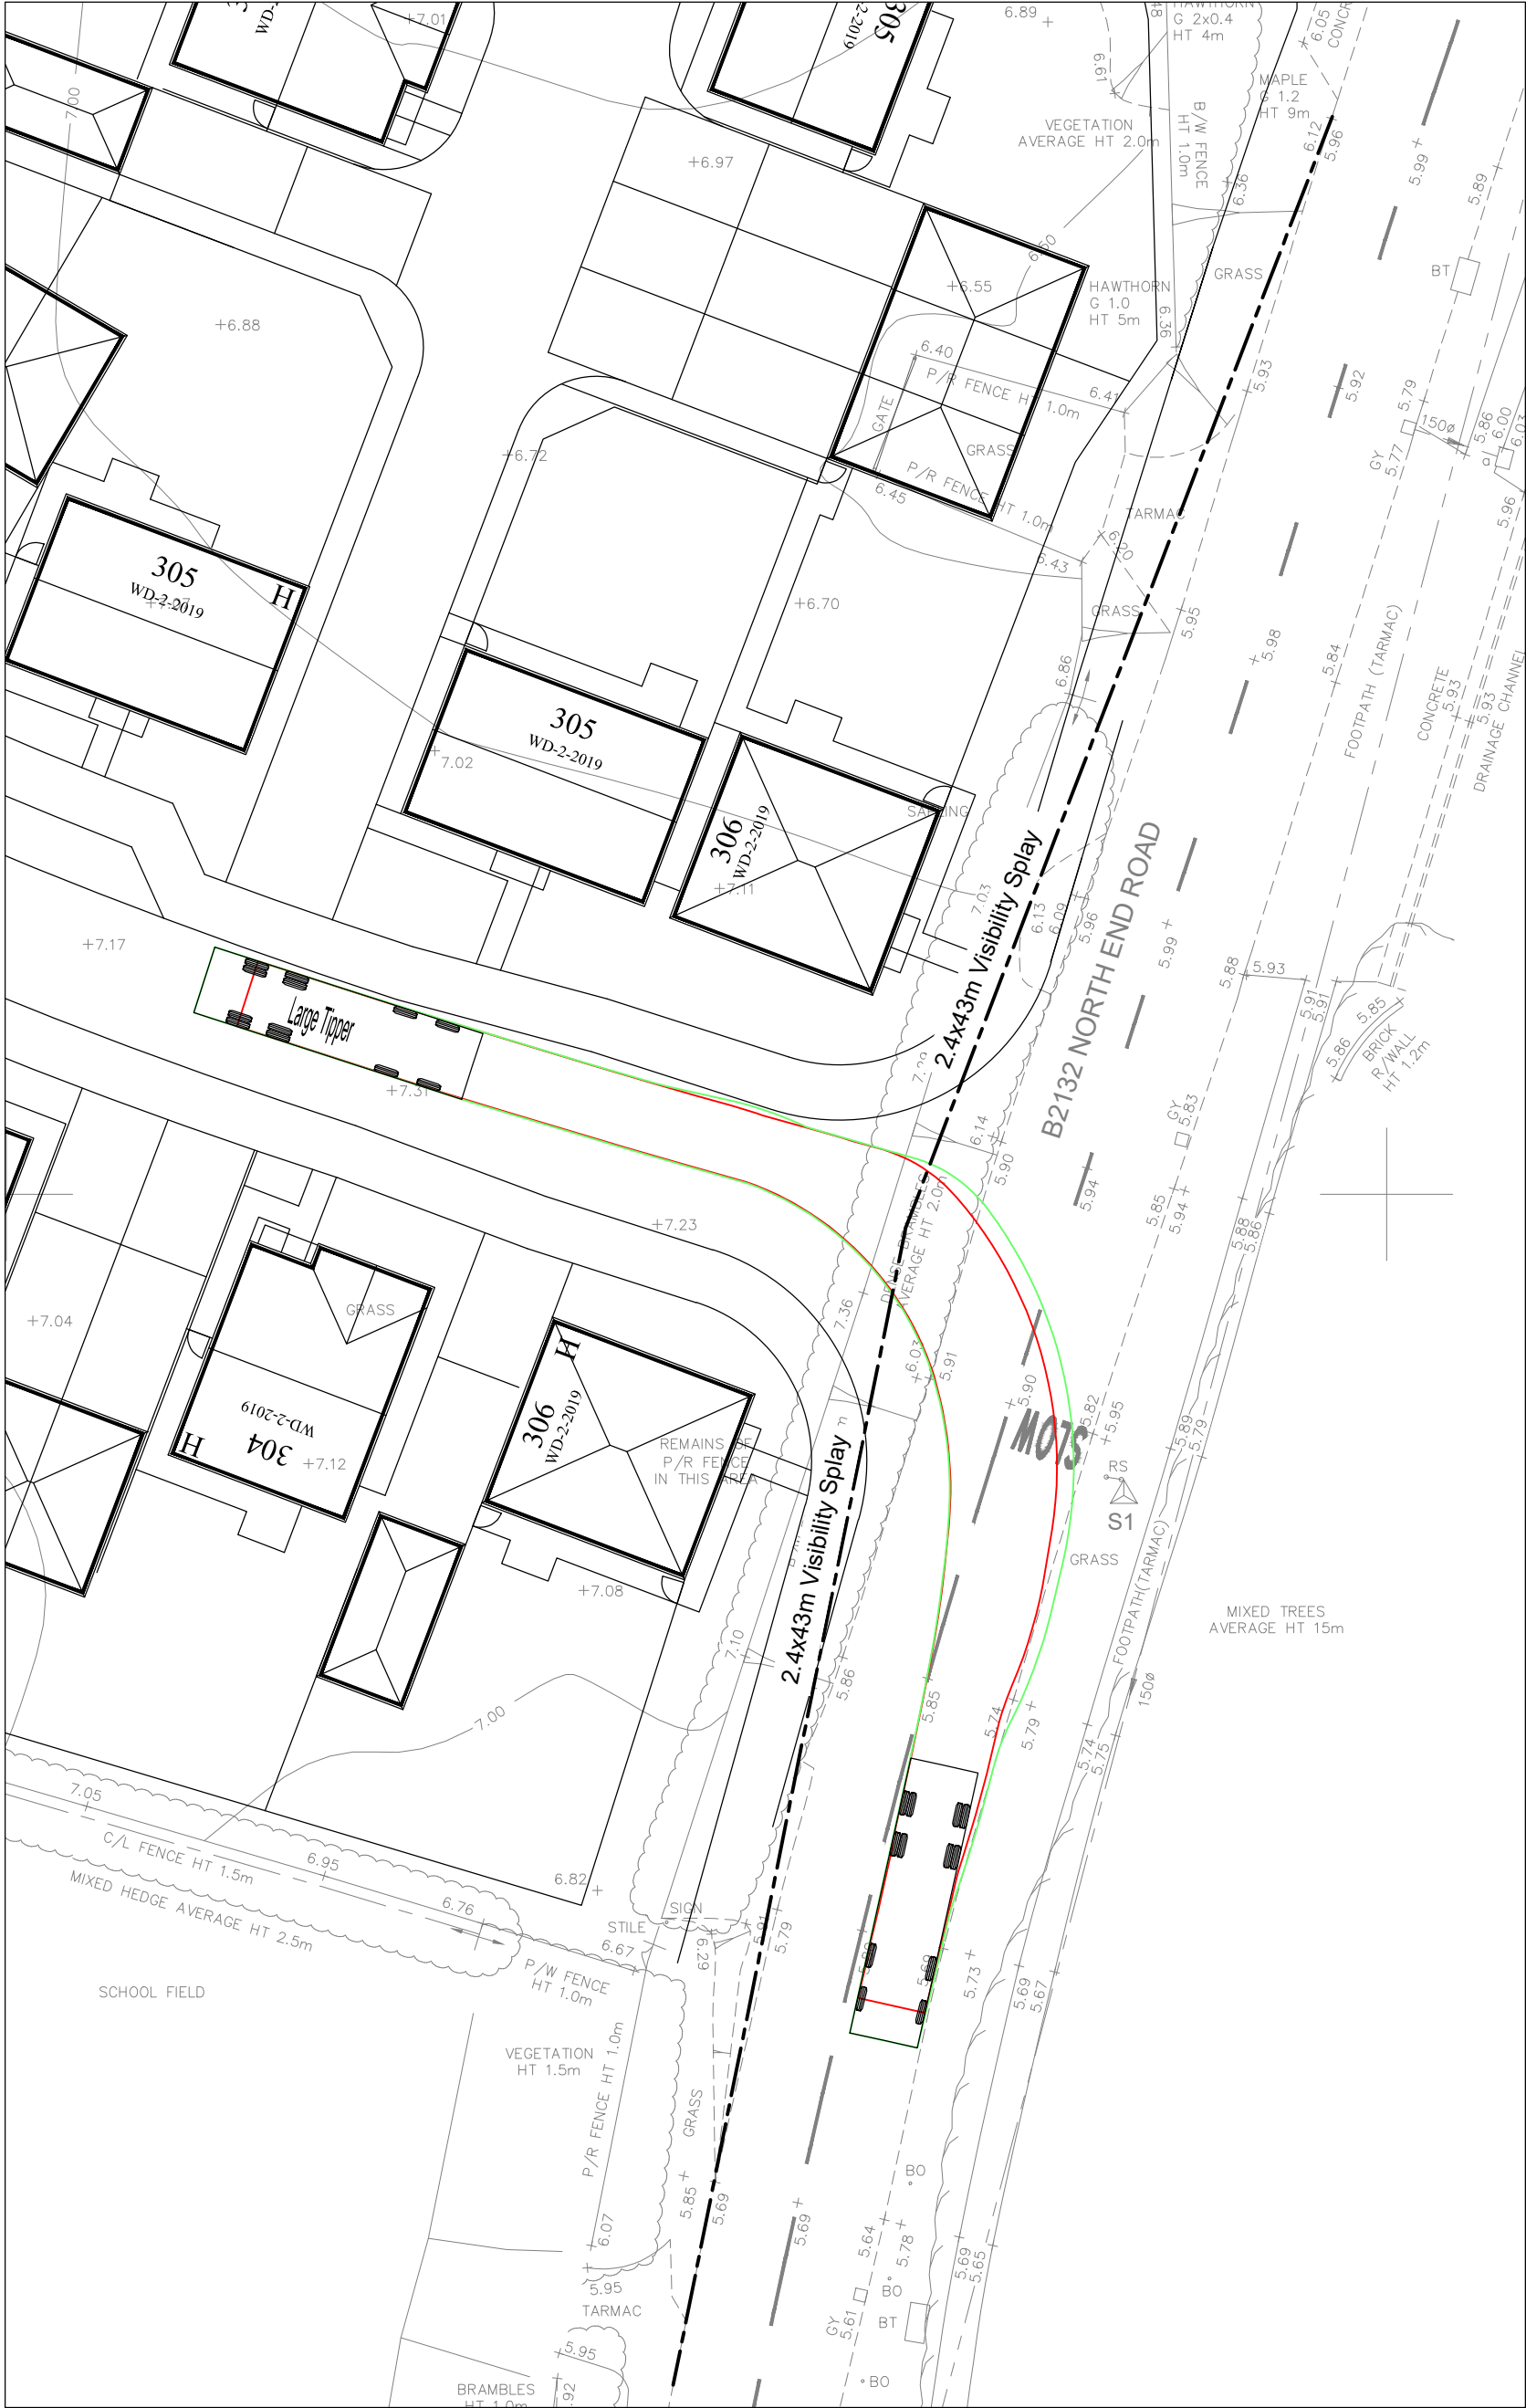

Proposed Access - Egress (South Bound)

B	16.03.20	Note added	MA
A	22.11.19	Initial Issue	MA
Rev.	Date	Description	Initial

Development
North End Road, Yapton

Drawing Title
Large Tipper Vehicle Tracking
Proposed Site Access

Status
FOR INFORMATION

dandara
new homes
Roman House, South Hampshire Industrial Park,
Eddystone Road, Totton, SO40 3SA
Tel: 02382 124061

Scale	Paper Size	Date	Drawn	Checked
1:200	A1	22.11.19	MA	COB

Drwg. No. YAP-TRA-02	Rev. B
-------------------------	-----------
