


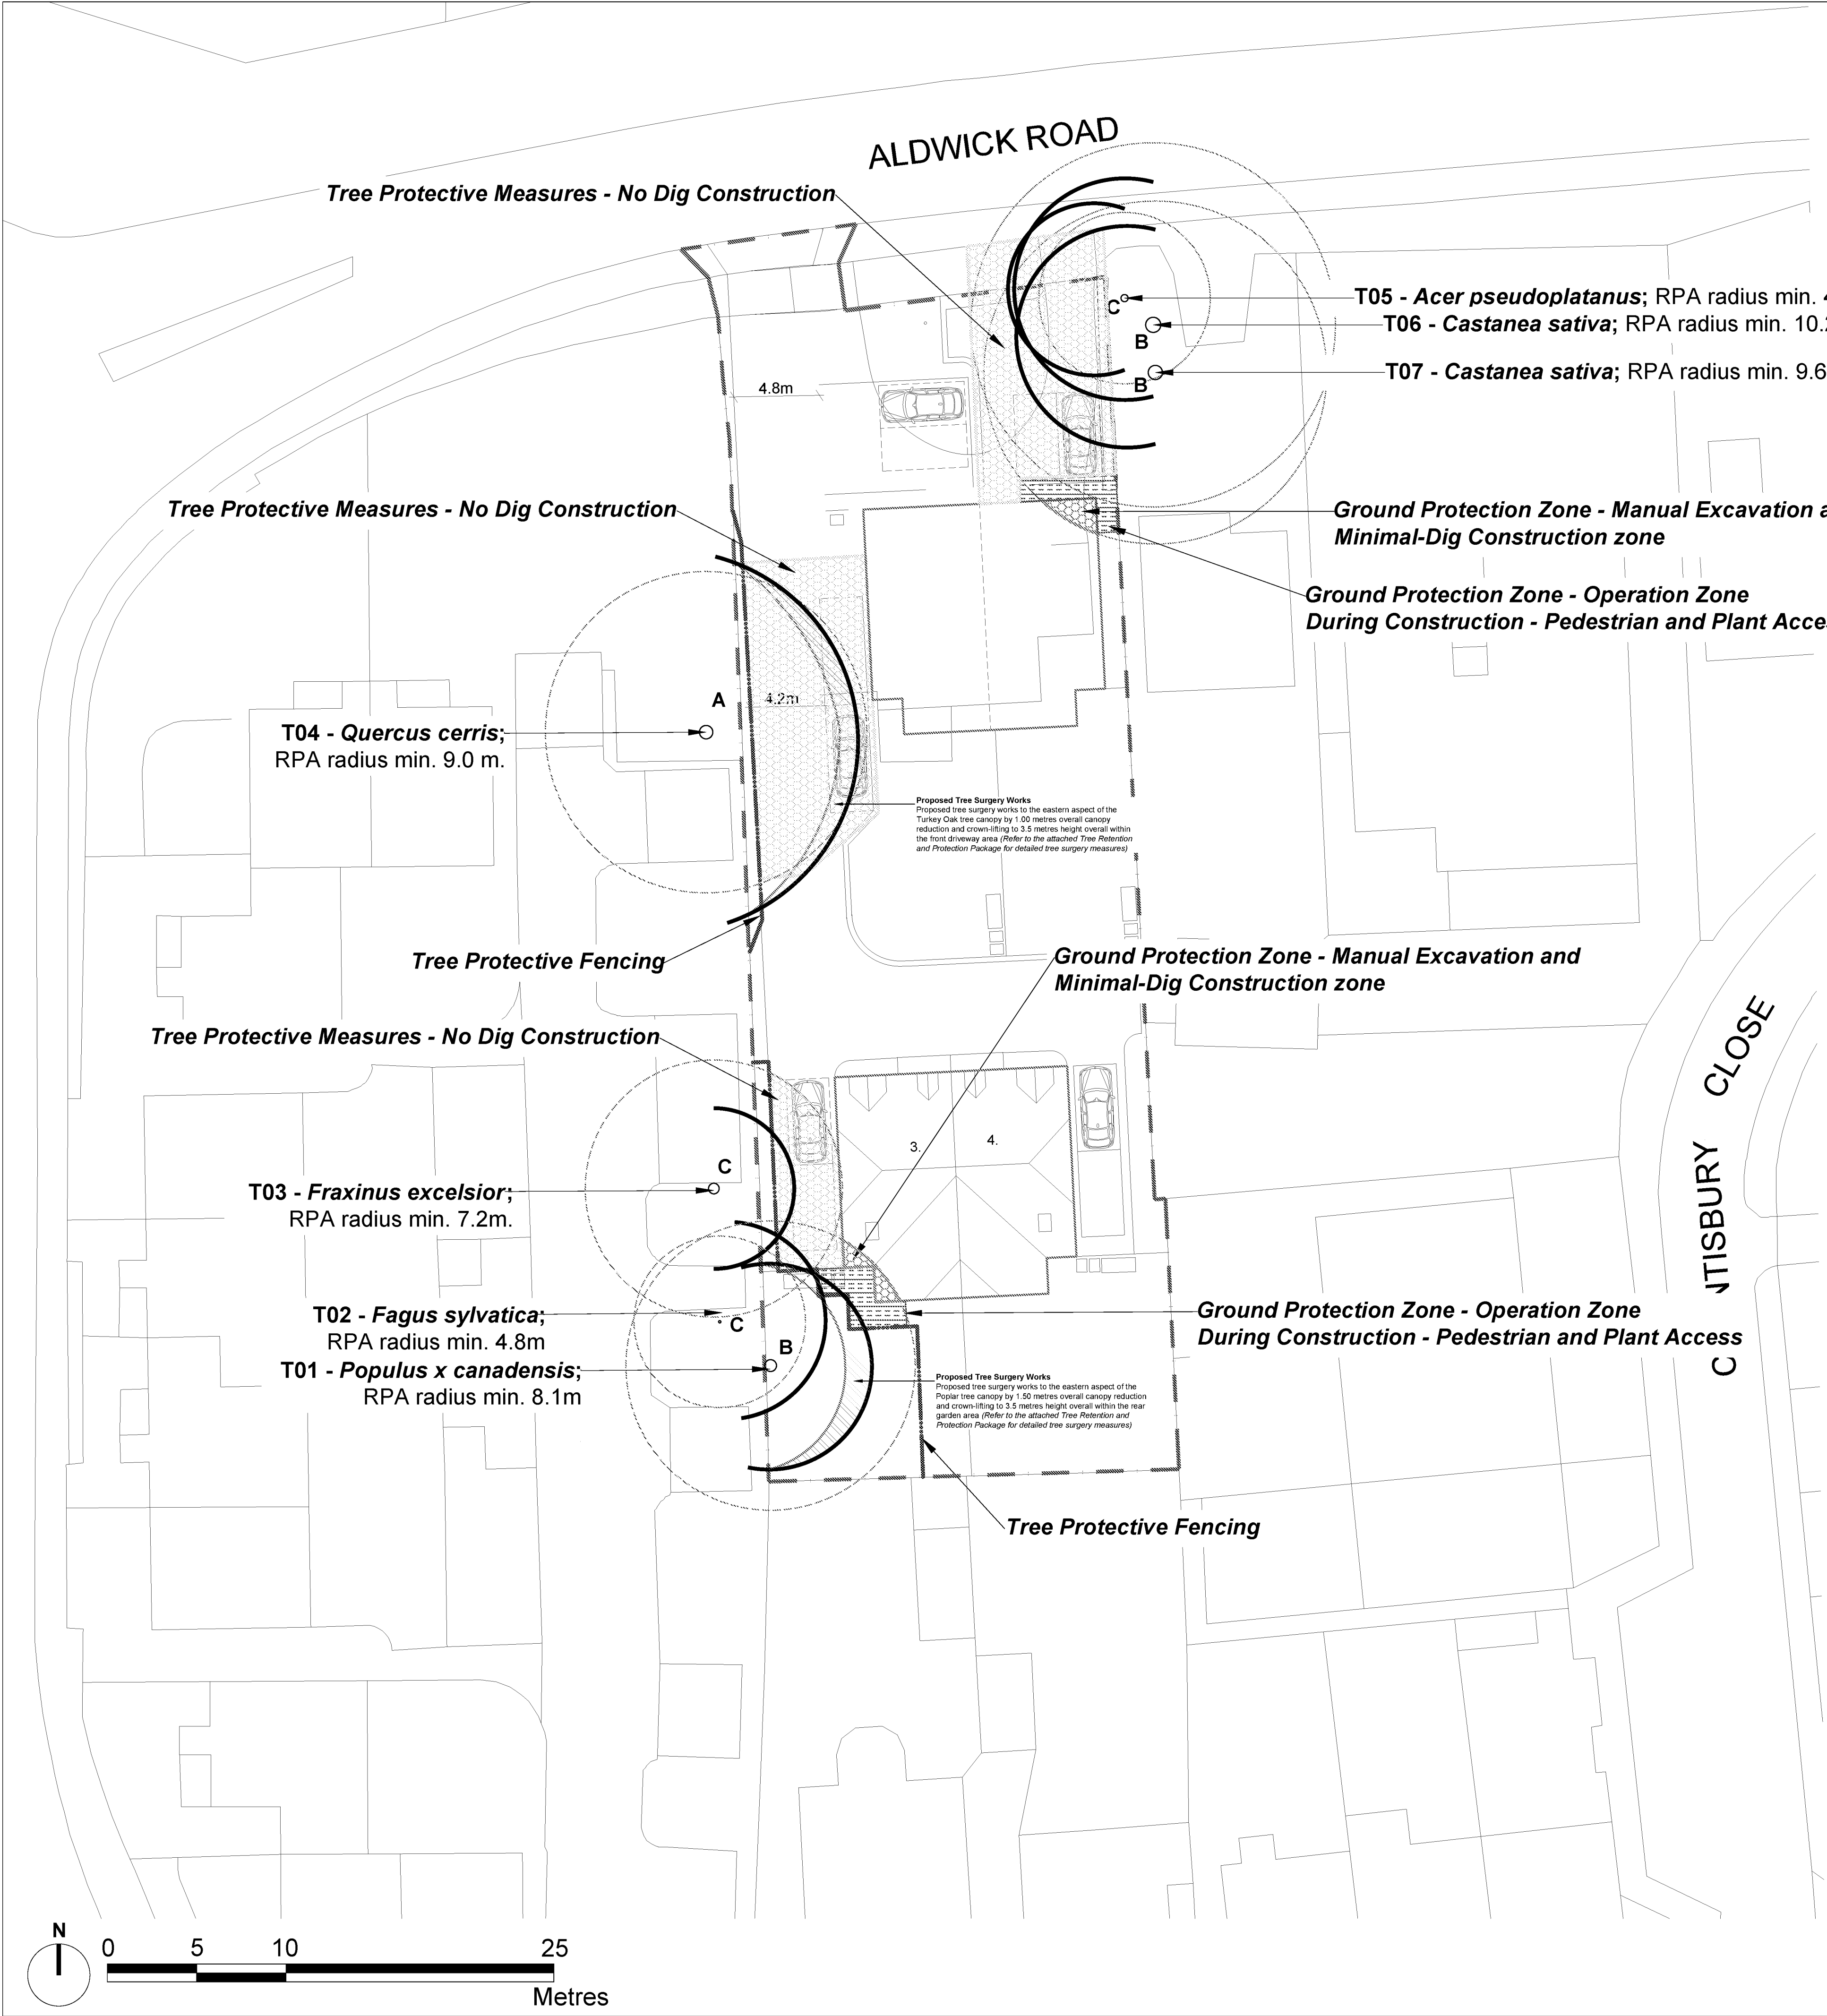

Ground Protection Zone - Manual Excavation and Minimal-Dig Construction Zone

Where the proposed dwelling foundations increases the depth of construction within the tree RPA, a manual excavation and 'minimal-dig' construction method shall be employed in order to avoid damage to existing tree roots and localised compaction of subsoil within the tree root protection areas of existing trees.

Tree Protective Fencing

All Tree Protection and Tree Protective Fencing to be in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'. Tree Protective Fencing - to be 2.0 metres height 'Heras' Welded Wire Mesh Fencing secured to a scaffolding framework, set into the existing ground, and positioned to the outside edge of the existing Tree Root Protection Area, or as specified.

Tree Protective Measures - No-Dig Construction

A 'no-dig' Construction method shall be employed during the construction of driveway access area in order to avoid damage to existing tree roots and localised compaction of subsoil within the tree root protection areas of trees proposed for retention.

Existing surfacing materials shall be left undisturbed and retained during the construction period for as long as possible in order to protect the tree root protection area of the existing trees to be retained; existing soft ground layers shall be removed carefully by hand within the existing tree root protection areas. A ground stabilising geo-mesh ('TDP SN20 GeoGrid' or equal and approved), shall be rolled out over the existing ground level and evenly covered with a No Fines - Open Graded Aggregate (in accordance with Highways Agency Specification; Clause 805 (Type 3) or equal and approved.)

The granular fill shall be incorporated within a 3 dimensional GeoCell (Terram Geocell 25/10 or equal and approved) and shall ensure a minimum supportive construction depth of 150 mm. A geo-textile filter membrane is to be laid over the granular fill construction (Geotextile filter membrane to be TDP 115 Non woven Geotextile Fabric or equal and approved.) A permeable system and construction method shall be installed over the prepared sub-base layers. A bedding layer of crushed aggregate (to BS EN13242; range size; 4 - 14 mm) is to be laid level and compacted above the Geotextile filter membrane to a depth of 25 mm. A permeable top layer, which could consist of (for example) resin-bound gravel, tarmac or permeable block-paving shall then be installed above the bedding layer to create the terrace areas.

Ground Protection Zone - Operation Zone During Construction

While construction work is commencing on the proposed dwellings, parking areas and access roads, the existing ground levels within the RPAs of trees to be retained are to be protected. For pedestrian access only, protection should consist of a single thickness of scaffold boards placed either on top of a driven scaffold frame, so as to form a suspended walkway, or on top of a compression-resistant layer (such as 100 mm depth of woodchip), laid onto a geotextile membrane; for pedestrian-operated plant up to a gross weight of 2 tonnes, proprietary, inter-linked ground protection boards placed on top of a compression-resistant layer (such as 150 mm depth of woodchip), laid onto a geotextile membrane should be used. The ground protection should be in place for the duration of the construction period in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'. When construction work is completed the ground protection can be removed.

Legend

Site Survey Boundary.

Proposed Dwellings.

Tree Root Protection Areas
Tree root protection areas calculated in accordance with BS5837; 2012 - 'Trees in Relation to Design, Demolition and Construction Recommendations'.

Category A Trees
Trees of High Quality and Value.

Category B Trees
Trees of Moderate Quality and Value.

Category C Trees
Trees of Low Quality and Value.

Tree Protective Fencing

Tree Protective Measures - 'No-Dig' Construction.

Ground Protection Zone - Operation Zone During Construction

Ground Protection Zone - Manual Excavation and Minimal-Dig Construction Zone

Proposed Tree Surgery Works
Proposed tree surgery works to the eastern aspect of the Turkey Oak and Poplar tree canopy overall within the scheme proposals (Refer to the attached Arboricultural Impact Assessment for detailed tree surgery measures).

Notes:
The original of this drawing was produced in colour - a monochrome copy should not be relied upon.
Drawing to be viewed in conjunction with:
LLD1425-ARB-TCP - Tree Constraints Plan;
LLD1425-ARB-ETS - Existing Tree Schedule and Schedule of Tree Works;
LLD1425-ARB-AIA - Arboricultural Impact Assessment and Method Statement.

Planning Issue

Rev	Description	Date	Initials
01	Planning Issue	21.06.18	LB

LIZARD

Landscape Design and Ecology

The Old Bank, 34 South Street, Tarring, Worthing, West Sussex, BN14 7LH
T: 01903 216033 E: lizardlandscape@btconnect.com W: lizardlandscapeology.com

Project Title and Location

261 Aldwick Road, Bognor Regis

Client

Domusea Developments Limited

Drawing Title

Tree Retention and Protection Plan

Scale

1:200@A1

Drawn

LB

Approved

JJ

Date

21.06.18

Drawing No

LLD-ARB-DWG-002

CAD Filename

Revision

00

Tree Retention and Protection Plan
261 Aldwick Road, Bognor Regis
