


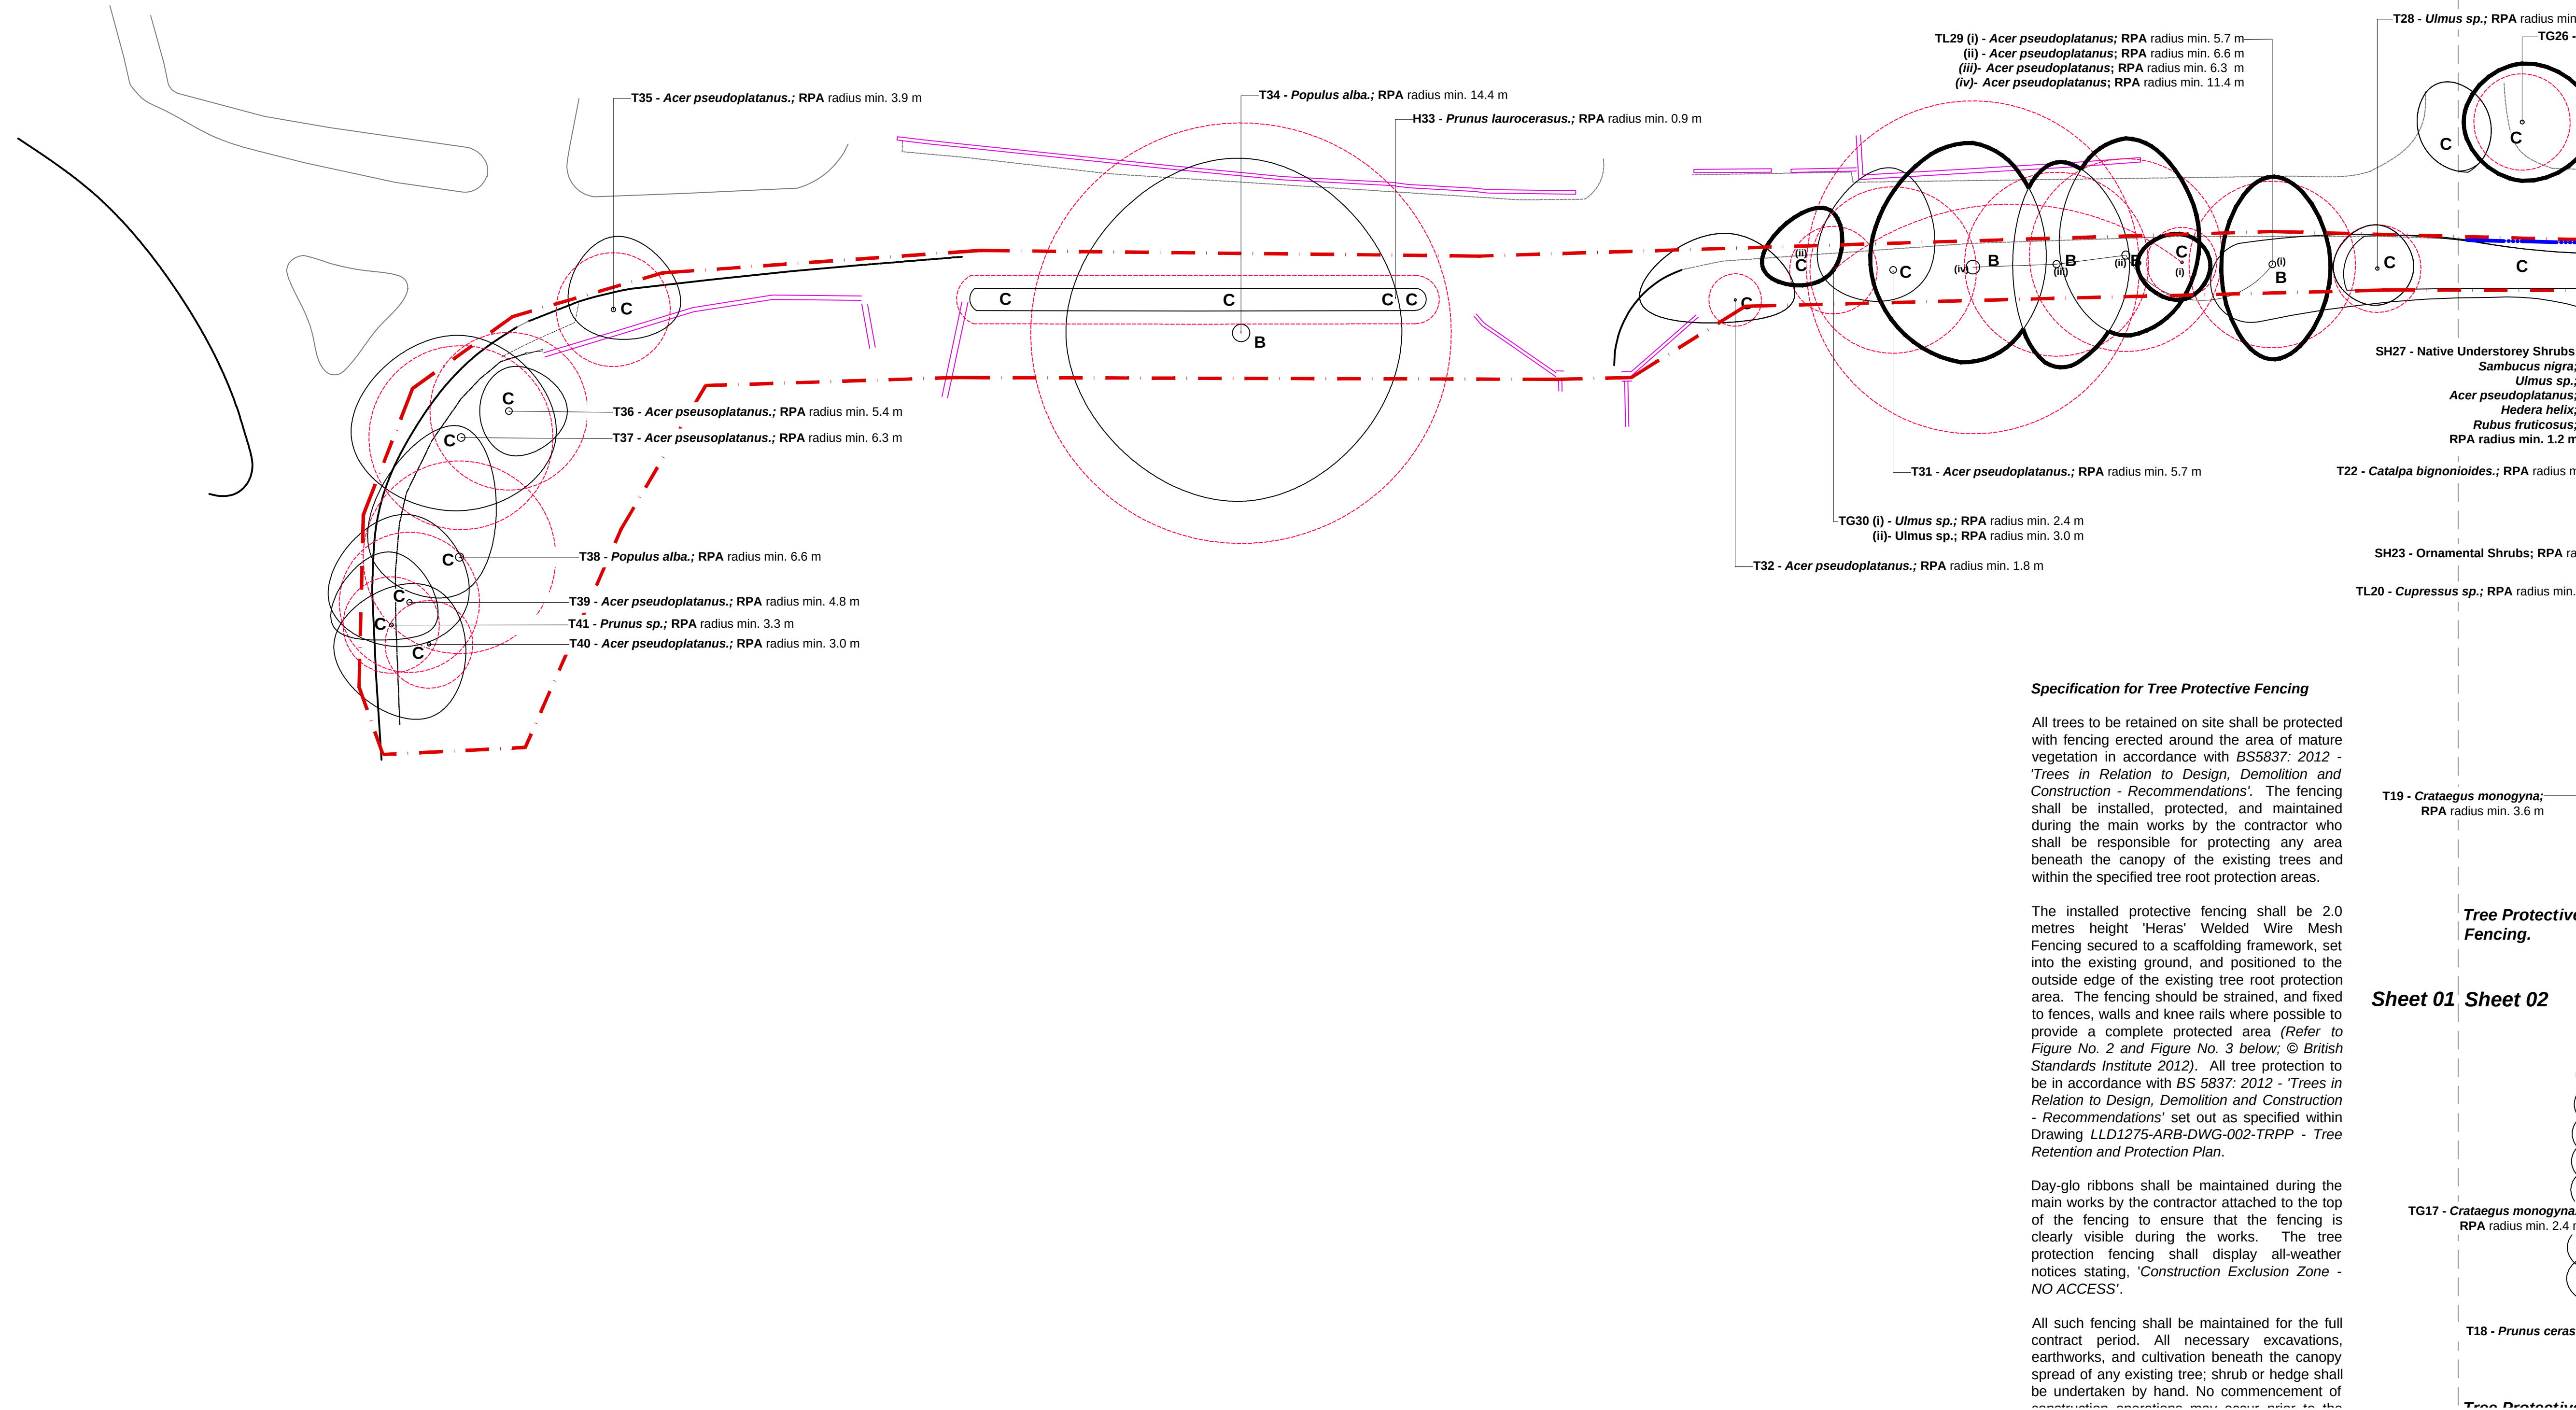

Specification for Tree Protective Fencing

All trees to be retained on site shall be protected with fencing erected around the area of mature vegetation in accordance with BS5837: 2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations'. The fencing shall be installed, protected, and maintained during the main works by the contractor who shall be responsible for protecting any area beneath the canopy of the existing trees and within the specified tree root protection areas.

The installed protective fencing shall be 2.0 metres height 'Heras' Welded Wire Mesh Fencing secured to a scaffolding framework, set into the existing ground, and positioned to the outside edge of the existing tree root protection area. The fencing should be strained, and fixed to fences, walls and knee rails where possible to provide a complete protected area (Refer to Figure No. 2 and Figure No. 3 below; © British Standards Institute 2012). All tree protection to be in accordance with BS 5837: 2012 - 'Trees in Relation to Design, Demolition and Construction - Recommendations' set out as specified within Drawing LLD1275-ARB-DWG-002-TRPP - Tree Retention and Protection Plan.

Day-glo ribbons shall be maintained during the main works by the contractor attached to the top of the fencing to ensure that the fencing is clearly visible during the works. The tree protection fencing shall display all-weather notices stating, 'Construction Exclusion Zone - NO ACCESS'.

All such fencing shall be maintained for the full contract period. All necessary excavations, earthworks, and cultivation beneath the canopy spread of any existing tree; shrub or hedge shall be undertaken by hand. No commencement of construction operations may occur until the


Legend

- Site Survey Boundary.
- Existing Walls/Fences.
- T03 - Pinus sp.;
- Tree/ Tree Group/ Tree Line/ Hedge Identification Label
- Tree Root Protection Areas
Tree Root Protection Areas calculated and specified in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition and Construction'.
- Road.
- Category B Trees
Trees of Moderate Quality and Value.
- Category C Trees
Trees of Low Quality and Value.
- Category C Shrubs and Hedges
Ornamental and Understorey Shrubs and Hedges of Low Quality and Value.
- Proposed Tree Surgery Works
- Tree Protective Fencing
- Existing Trees to be Removed
Trees and Shrubs Recommended for Removal from Site Prior to Tree Protection Works / Measures.
- Tree Protection Zone - Manual Excavation Area.

Notes:
1. Drawing to be viewed in colour (Refer to LLD1275-ARB-SCH-001-ETS - Existing Tree Schedule and LLD1275-ARB-REP-001-AIA - Arboricultural Impact Assessment and Method Statement).

PLANNING ISSUE

Rev	Description	Date	Initials
04	Planning Issue	20.07.18	GS
03	Planning Issue	14.03.18	GS
02	Planning Issue	13.03.18	GS
01	Draft Planning Issue	09.03.18	GS
00	Draft Issue	06.03.18	GS



LIZARD
Landscape Design and Ecology

The Old Bank, 34 South Street, Tarring, Worthing, West Sussex, BN14 7LH
T: 01903 216633 E: lizardlandscape@btconnect.com W: lizardlandscape.co.uk

Project Title and Location

Manor Nursery, Angmering, West Sussex

Client

Roffey Homes Ltd

Drawing Title

**Tree Retention and Protection Plan
Sheet 01**

Scale: **1:250@A1** Drawn: **GS** Date: **06.03.18**
Approved: **JJ**

Drawing No: **LLD1275-ARB-DWG-002** Revision: **04**
CAD Filename: **LLD1275/CAD/ARB**

Tree Retention and Protection Plan - Sheet 01
Manor Nursery, Angmering, West Sussex

