


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
1			Planning Condition Tasks	30 days	Mon 22/07/19	Fri 30/08/19	
2			Asbestos assesment	30 days	Mon 22/07/19	Fri 30/08/19	
3			SUDS design	30 days	Mon 22/07/19	Fri 30/08/19	
4			Vehicular access and footway	30 days	Mon 22/07/19	Fri 30/08/19	
5			Demolition and construction method statement	30 days	Mon 22/07/19	Fri 30/08/19	
6			Stage 1 road safety audit	30 days	Mon 22/07/19	Fri 30/08/19	
7			Impact statement and tree protection plan	30 days	Mon 22/07/19	Fri 30/08/19	
8			Renewable energy design	30 days	Mon 22/07/19	Fri 30/08/19	
9			Pre Construction	45 days	Mon 07/10/19	Fri 06/12/19	
10			Tree clearance including watching brief	10 days	Mon 25/11/19	Fri 06/12/19	
11			Hoarding installation including heras fencing	5 days	Mon 07/10/19	Fri 11/10/19	
12			Cabin installation and tempoary power supply	5 days	Wed 13/11/19	Tue 19/11/19	11
13			Demolition of existing barn and garages	5 days	Wed 20/11/19	Tue 26/11/19	12
14			Construction	361 days	Mon 02/12/19	Mon 19/04/21	
15			Road Formation	20 days	Mon 02/12/19	Fri 27/12/19	13
16			Groundworks/excavations	20 days	Mon 30/12/19	Fri 24/01/20	15
17			Foundations to plots 2, 3 & 4	15 days	Mon 27/01/20	Fri 14/02/20	16
18			Foundations to plots 5 & 6	15 days	Mon 17/02/20	Fri 06/03/20	17
19			Foundations to plots 8 & 9	15 days	Mon 09/03/20	Fri 27/03/20	18
20			Foundations to plots 10 & 11	15 days	Mon 30/03/20	Fri 17/04/20	19
21			Foundations to plots 12 & 13	15 days	Mon 20/04/20	Fri 08/05/20	20
22			Foundations to plots 14 & 15	15 days	Mon 11/05/20	Fri 29/05/20	21

Project: Dappers Lane - Angme
Date: Tue 05/05/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
23			Foundations to plots 16 & 7	15 days	Mon 01/06/20	Fri 19/06/20	22
24			Foundations to plots 17 & 18	15 days	Mon 22/06/20	Fri 10/07/20	23
25			Timber frame installation to plots 2, 3 & 4	15 days	Thu 07/05/20	Wed 27/05/20	27
26			Timber frame installation to plots 5 & 6	15 days	Thu 28/05/20	Wed 17/06/20	25
27			Covid-19 Shutdown	30 days	Thu 26/03/20	Wed 06/05/20	
28			Timber frame installation to plots 8 & 9	15 days	Thu 07/05/20	Wed 27/05/20	27
29			Timber frame installation to plots 10 & 11	15 days	Thu 28/05/20	Wed 17/06/20	28
30			Timber frame installation to plots 12 & 13	15 days	Thu 18/06/20	Wed 08/07/20	29
31			Timber frame installation to plots 14 & 15	15 days	Thu 09/07/20	Wed 29/07/20	30
32			Timber frame installation to plots 16 & 7	15 days	Thu 30/07/20	Wed 19/08/20	31
33			Timber frame installation to plots 17 & 18	15 days	Thu 20/08/20	Wed 09/09/20	32
34			Façade works to plots 2, 3 & 4	10 days	Thu 11/06/20	Wed 24/06/20	42
35			Façade works to plots 5 & 6	10 days	Thu 09/07/20	Wed 22/07/20	43
36			Façade works to plots 8 & 9	10 days	Thu 06/08/20	Wed 19/08/20	44
37			Façade works to plots 10 & 11	10 days	Thu 03/09/20	Wed 16/09/20	45
38			Façade works to plots 12 & 13	10 days	Thu 01/10/20	Wed 14/10/20	46
39			Façade works to plots 14 & 15	10 days	Thu 29/10/20	Wed 11/11/20	47
40			Façade works to plots 16 & 7	10 days	Thu 26/11/20	Wed 09/12/20	48
41			Façade works to plots 17 & 18	10 days	Thu 10/12/20	Wed 23/12/20	49
42			Roofing to plots 2, 3 & 4	10 days	Thu 28/05/20	Wed 10/06/20	28
43			Roofing to plots 5 & 6	20 days	Thu 11/06/20	Wed 08/07/20	42
44			Roofing to plots 8 & 9	20 days	Thu 09/07/20	Wed 05/08/20	43

Project: Dappers Lane - Angme
Date: Tue 05/05/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
45			Roofing to plots 10 & 11	20 days	Thu 06/08/20	Wed 02/09/20	44
46			Roofing to plots 12 & 13	20 days	Thu 03/09/20	Wed 30/09/20	45
47			Roofing to plots 14 & 15	20 days	Thu 01/10/20	Wed 28/10/20	46
48			Roofing to plots 16 & 7	20 days	Thu 29/10/20	Wed 25/11/20	47
49			Roofing to plots 17 & 18	10 days	Thu 26/11/20	Wed 09/12/20	48
50			Window and door installation to plots 2, 3 & 4	5 days	Thu 11/06/20	Wed 17/06/20	42
51			Window and door installation to plots 5 & 6	5 days	Thu 09/07/20	Wed 15/07/20	43
52			Window and door installation to plots 8 & 9	5 days	Thu 06/08/20	Wed 12/08/20	44
53			Window and door installation to plots 10 & 11	5 days	Thu 03/09/20	Wed 09/09/20	45
54			Window and door installation to plots 12 & 13	5 days	Thu 01/10/20	Wed 07/10/20	46
55			Window and door installation to plots 14 & 15	5 days	Thu 29/10/20	Wed 04/11/20	47
56			Window and door installation to plots 16 & 7	5 days	Thu 26/11/20	Wed 02/12/20	48
57			Window and door installation to plots 17 & 18	5 days	Thu 10/12/20	Wed 16/12/20	49
58			Fencing Installation	40 days	Thu 24/12/20	Wed 17/02/21	49
59			Soft Landscaping	40 days	Thu 24/12/20	Wed 17/02/21	49
60			Internal partitions to plots 2, 3 & 4	5 days	Thu 09/07/20	Wed 15/07/20	68
61			Internal partitions to plots 5 & 6	5 days	Thu 06/08/20	Wed 12/08/20	69
62			Internal partitions to plots 8 & 9	5 days	Thu 03/09/20	Wed 09/09/20	70
63			Internal partitions to plots 10 & 11	5 days	Thu 01/10/20	Wed 07/10/20	71
64			Internal partitions to plots 12 & 13	5 days	Thu 29/10/20	Wed 04/11/20	72
65			Internal partitions to plots 14 & 15	5 days	Thu 26/11/20	Wed 02/12/20	73
66			Internal partitions to plots 16 & 7	5 days	Thu 24/12/20	Wed 30/12/20	74

Project: Dappers Lane - Angme
Date: Tue 05/05/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
67			Internal partitions to plots 17 & 18	5 days	Thu 24/12/20	Wed 30/12/20	74
68			1st fix mechanical and electrical to plots 2, 3, & 4	20 days	Thu 11/06/20	Wed 08/07/20	42
69			1st fix mechanical and electrical to plots 5 & 6	20 days	Thu 09/07/20	Wed 05/08/20	43
70			1st fix mechanical and electrical to plots 8 & 9	20 days	Thu 06/08/20	Wed 02/09/20	44
71			1st fix mechanical and electrical to plots 10 & 11	20 days	Thu 03/09/20	Wed 30/09/20	45
72			1st fix mechanical and electrical to plots 12 & 13	20 days	Thu 01/10/20	Wed 28/10/20	46
73			1st fix mechanical and electrical to plots 14 & 15	20 days	Thu 29/10/20	Wed 25/11/20	47
74			1st fix mechanical and electrical to plots 16 & 7	20 days	Thu 26/11/20	Wed 23/12/20	48
75			1st fix mechanical and electrical to plots 17 & 18	20 days	Thu 10/12/20	Wed 06/01/21	49
76			Carpentry work to plots 2, 3 & 4	10 days	Thu 03/09/20	Wed 16/09/20	70
77			Carpentry work to plots 5 & 6	10 days	Thu 17/09/20	Wed 30/09/20	76
78			Carpentry work to plots 8 & 9	10 days	Thu 01/10/20	Wed 14/10/20	77
79			Carpentry work to plots 10 & 11	10 days	Thu 15/10/20	Wed 28/10/20	78
80			Carpentry work to plots 12 & 13	10 days	Thu 29/10/20	Wed 11/11/20	79
81			Carpentry work to plots 14 & 15	10 days	Thu 12/11/20	Wed 25/11/20	80
82			Carpentry work to plots 16 & 7	10 days	Thu 26/11/20	Wed 09/12/20	81
83			Carpentry work to plots 17 & 18	10 days	Thu 10/12/20	Wed 23/12/20	82
84			Tiling work to plots 2, 3 & 4	16 days	Thu 22/10/20	Thu 12/11/20	76
85			Tiling work to plots 5 & 6	16 days	Fri 13/11/20	Fri 04/12/20	84
86			Tiling work to plots 8 & 9	16 days	Mon 07/12/20	Mon 28/12/20	85
87			Tiling work to plots 10 & 11	16 days	Tue 29/12/20	Tue 19/01/21	86
88			Tiling work to plots 12 & 13	16 days	Wed 20/01/21	Wed 10/02/21	87

Project: Dappers Lane - Angme
Date: Tue 05/05/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
89			Tiling work to plots 14 & 15	16 days	Thu 11/02/21	Thu 04/03/21	88
90			Tiling work to plots 16 & 7	16 days	Fri 05/03/21	Fri 26/03/21	89
91			Tiling work to plots 17 & 18	16 days	Mon 29/03/21	Mon 19/04/21	90
92			Kitchen & bathroom installation to plots 2, 3 & 4	5 days	Fri 13/11/20	Thu 19/11/20	84
93			Kitchen & bathroom installation to plots 5 & 6	5 days	Fri 20/11/20	Thu 26/11/20	92
94			Kitchen & bathroom installation to plots 8 & 9	5 days	Fri 27/11/20	Thu 03/12/20	93
95			Kitchen & bathroom installation to plots 10 & 11	5 days	Fri 04/12/20	Thu 10/12/20	94
96			Kitchen & bathroom installation to plots 12 & 13	5 days	Fri 11/12/20	Thu 17/12/20	95
97			Kitchen & bathroom installation to plots 14 & 15	5 days	Fri 18/12/20	Thu 24/12/20	96
98			Kitchen & bathroom installation to plots 16 & 7	5 days	Fri 25/12/20	Thu 31/12/20	97
99			Kitchen & bathroom installation to plots 17 & 18	5 days	Fri 01/01/21	Thu 07/01/21	98
100			Decoration to plots 2, 3 & 4	10 days	Fri 20/11/20	Thu 03/12/20	92
101			Decoration to plots 5 & 6	10 days	Fri 04/12/20	Thu 17/12/20	100
102			Decoration to plots 8 & 9	10 days	Fri 18/12/20	Thu 31/12/20	101
103			Decoration to plots 10 & 11	10 days	Fri 01/01/21	Thu 14/01/21	102
104			Decoration to plots 12 & 13	10 days	Fri 15/01/21	Thu 28/01/21	103
105			Decoration to plots 14 & 15	10 days	Fri 29/01/21	Thu 11/02/21	104
106			Decoration to plots 16 & 7	10 days	Fri 12/02/21	Thu 25/02/21	105
107			Decoration to plots 17 & 18	10 days	Fri 26/02/21	Thu 11/03/21	106
108			2nd fix mechanical and electrical to plots 2,3 & 4	10 days	Fri 04/12/20	Thu 17/12/20	100
109			2nd fix mechanical and electrical to plots 5 & 6	10 days	Fri 18/12/20	Thu 31/12/20	108
110			2nd fix mechanical and electrical to plots 8 & 9	10 days	Fri 01/01/21	Thu 14/01/21	109


Project: Dappers Lane - Angme
Date: Tue 05/05/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
111			2nd fix mechanical and electrical to plots 10 & 11	10 days	Fri 15/01/21	Thu 28/01/21	110
112			2nd fix mechanical and electrical to plots 12 & 13	10 days	Fri 29/01/21	Thu 11/02/21	111
113			2nd fix mechanical and electrical to plots 14 & 15	10 days	Fri 12/02/21	Thu 25/02/21	112
114			2nd fix mechanical and electrical to plots 16 & 7	10 days	Fri 26/02/21	Thu 11/03/21	113
115			2nd fix mechanical and electrical to plots 17 & 18	10 days	Fri 12/03/21	Thu 25/03/21	114
116			Demobilise site	5 days	Fri 12/03/21	Thu 18/03/21	107
117			Handover	1 day	Fri 19/03/21	Fri 19/03/21	116

Project: Dappers Lane - Angme
Date: Tue 05/05/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

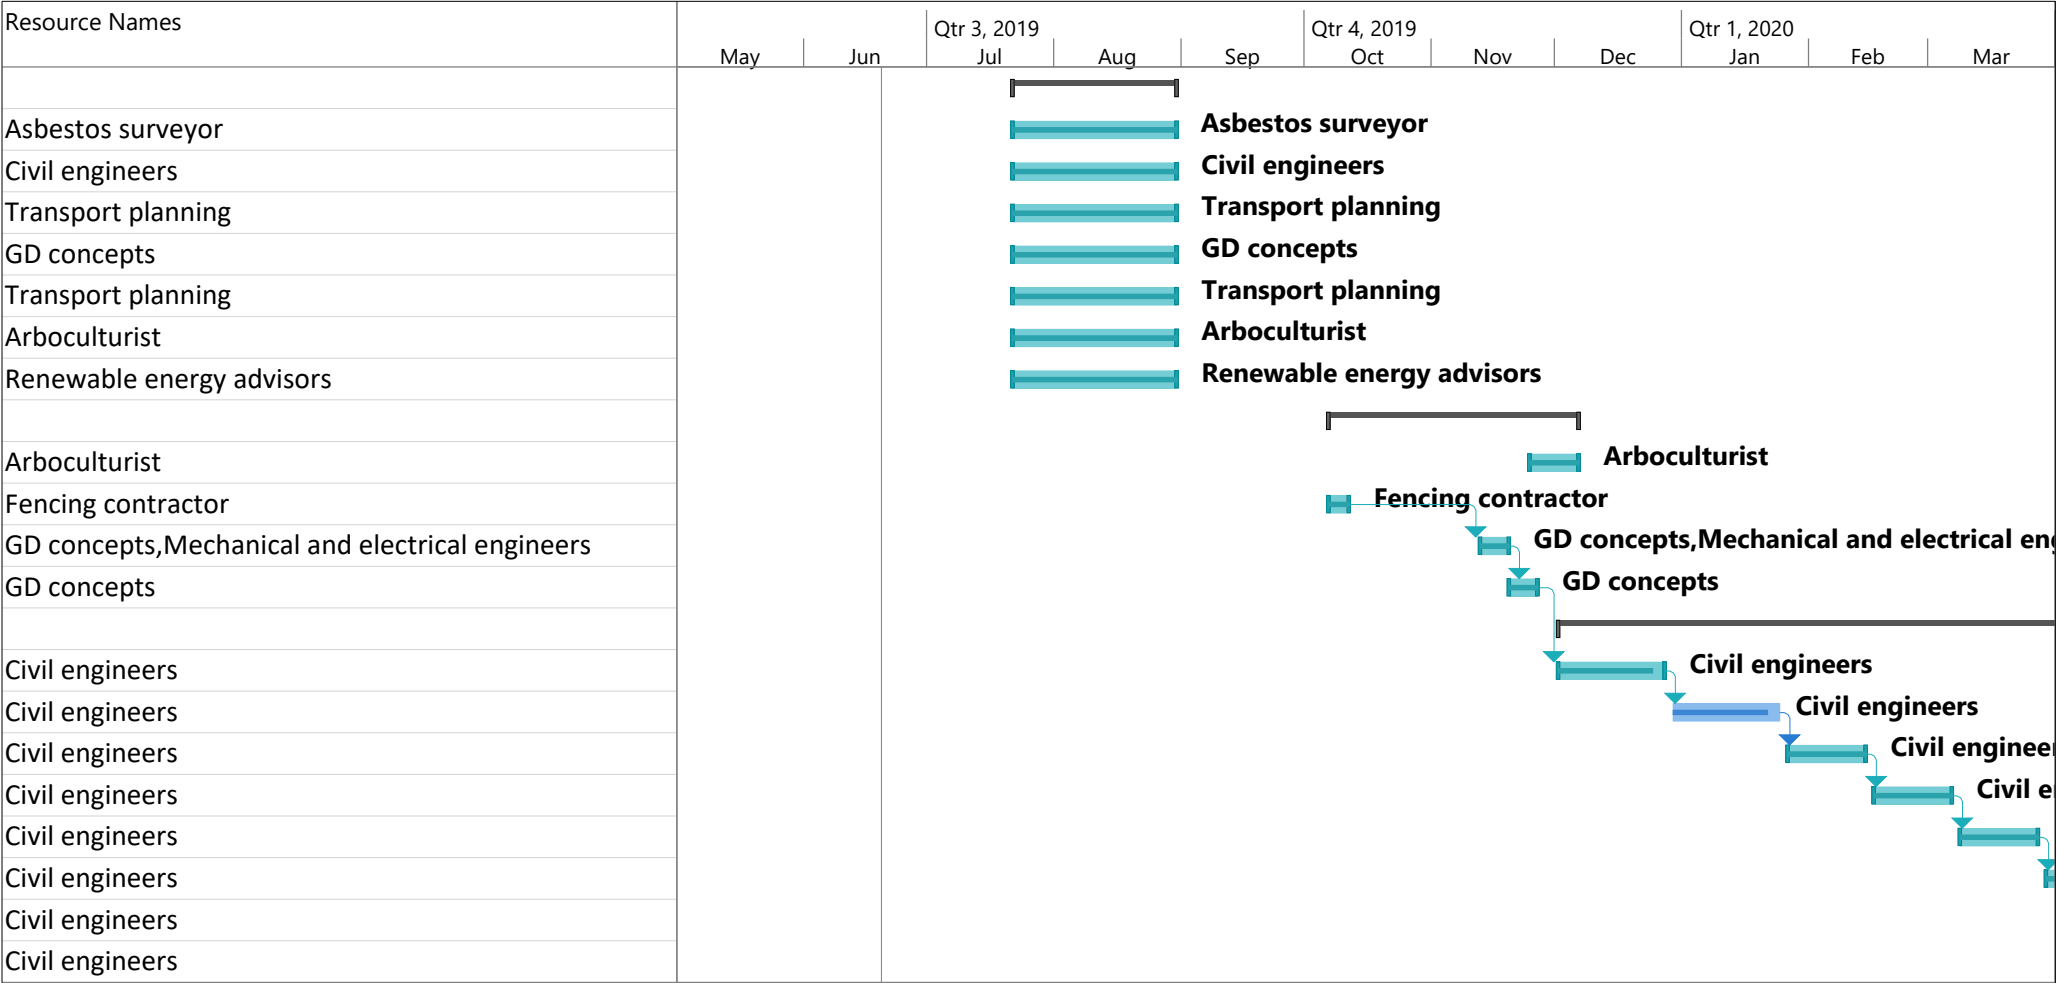

Project: Dappers Lane - Angme
Date: Tue 05/05/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Resource Names	May	Jun	Qtr 3, 2019 Jul	Aug	Sep	Qtr 4, 2019 Oct	Nov	Dec	Qtr 1, 2020 Jan	Feb	Mar
Civil engineers											
Civil engineers											
Timber Frame Contractors											
Timber Frame Contractors											
Timber Frame Contractors											
Timber Frame Contractors											
Timber Frame Contractors											
Timber Frame Contractors											
Timber Frame Contractors											
Timber Frame Contractors											
Bricklayers											
Bricklayers											
Bricklayers											
Bricklayers											
Bricklayers											
Bricklayers											
Bricklayers											
Bricklayers											
Roofers											
Roofers											
Roofers											

Project: Dappers Lane - Angme Date: Tue 05/05/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Resource Names	May	Jun	Qtr 3, 2019 Jul	Aug	Sep	Qtr 4, 2019 Oct	Nov	Dec	Qtr 1, 2020 Jan	Feb	Mar
Roofers											
Roofers											
Roofers											
Roofers											
Roofers											
Window and door installers											
Window and door installers											
Window and door installers											
Window and door installers											
Window and door installers											
Window and door installers											
Window and door installers											
Window and door installers											
Fencing contractor											
Landscapers											
Internal fit-out team											
Internal fit-out team											
Internal fit-out team											
Internal fit-out team											
Internal fit-out team											
Internal fit-out team											
Internal fit-out team											

Project: Dappers Lane - Angme Date: Tue 05/05/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Resource Names	May	Jun	Qtr 3, 2019 Jul	Aug	Sep	Qtr 4, 2019 Oct	Nov	Dec	Qtr 1, 2020 Jan	Feb	Mar
Internal fit-out team											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Carpenters											
Carpenters											
Carpenters											
Carpenters											
Carpenters											
Carpenters											
Carpenters											
Carpenters											
Tilers											
Tilers											
Tilers											
Tilers											
Tilers											

Project: Dappers Lane - Angme Date: Tue 05/05/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


Resource Names	May	Jun	Qtr 3, 2019 Jul	Aug	Sep	Qtr 4, 2019 Oct	Nov	Dec	Qtr 1, 2020 Jan	Feb	Mar
Tilers											
Tilers											
Tilers											
Kitchen & bathroom fitters											
Kitchen & bathroom fitters											
Kitchen & bathroom fitters											
Kitchen & bathroom fitters											
Kitchen & bathroom fitters											
Kitchen & bathroom fitters											
Kitchen & bathroom fitters											
Kitchen & bathroom fitters											
Decorators											
Decorators											
Decorators											
Decorators											
Decorators											
Decorators											
Decorators											
Decorators											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Mechanical and electrical engineers											


Project: Dappers Lane - Angme Date: Tue 05/05/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Resource Names	May	Jun	Qtr 3, 2019 Jul	Aug	Sep	Qtr 4, 2019 Oct	Nov	Dec	Qtr 1, 2020 Jan	Feb	Mar
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
Mechanical and electrical engineers											
GD concepts											
GD concepts											




Project: Dappers Lane - Angme Date: Tue 05/05/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

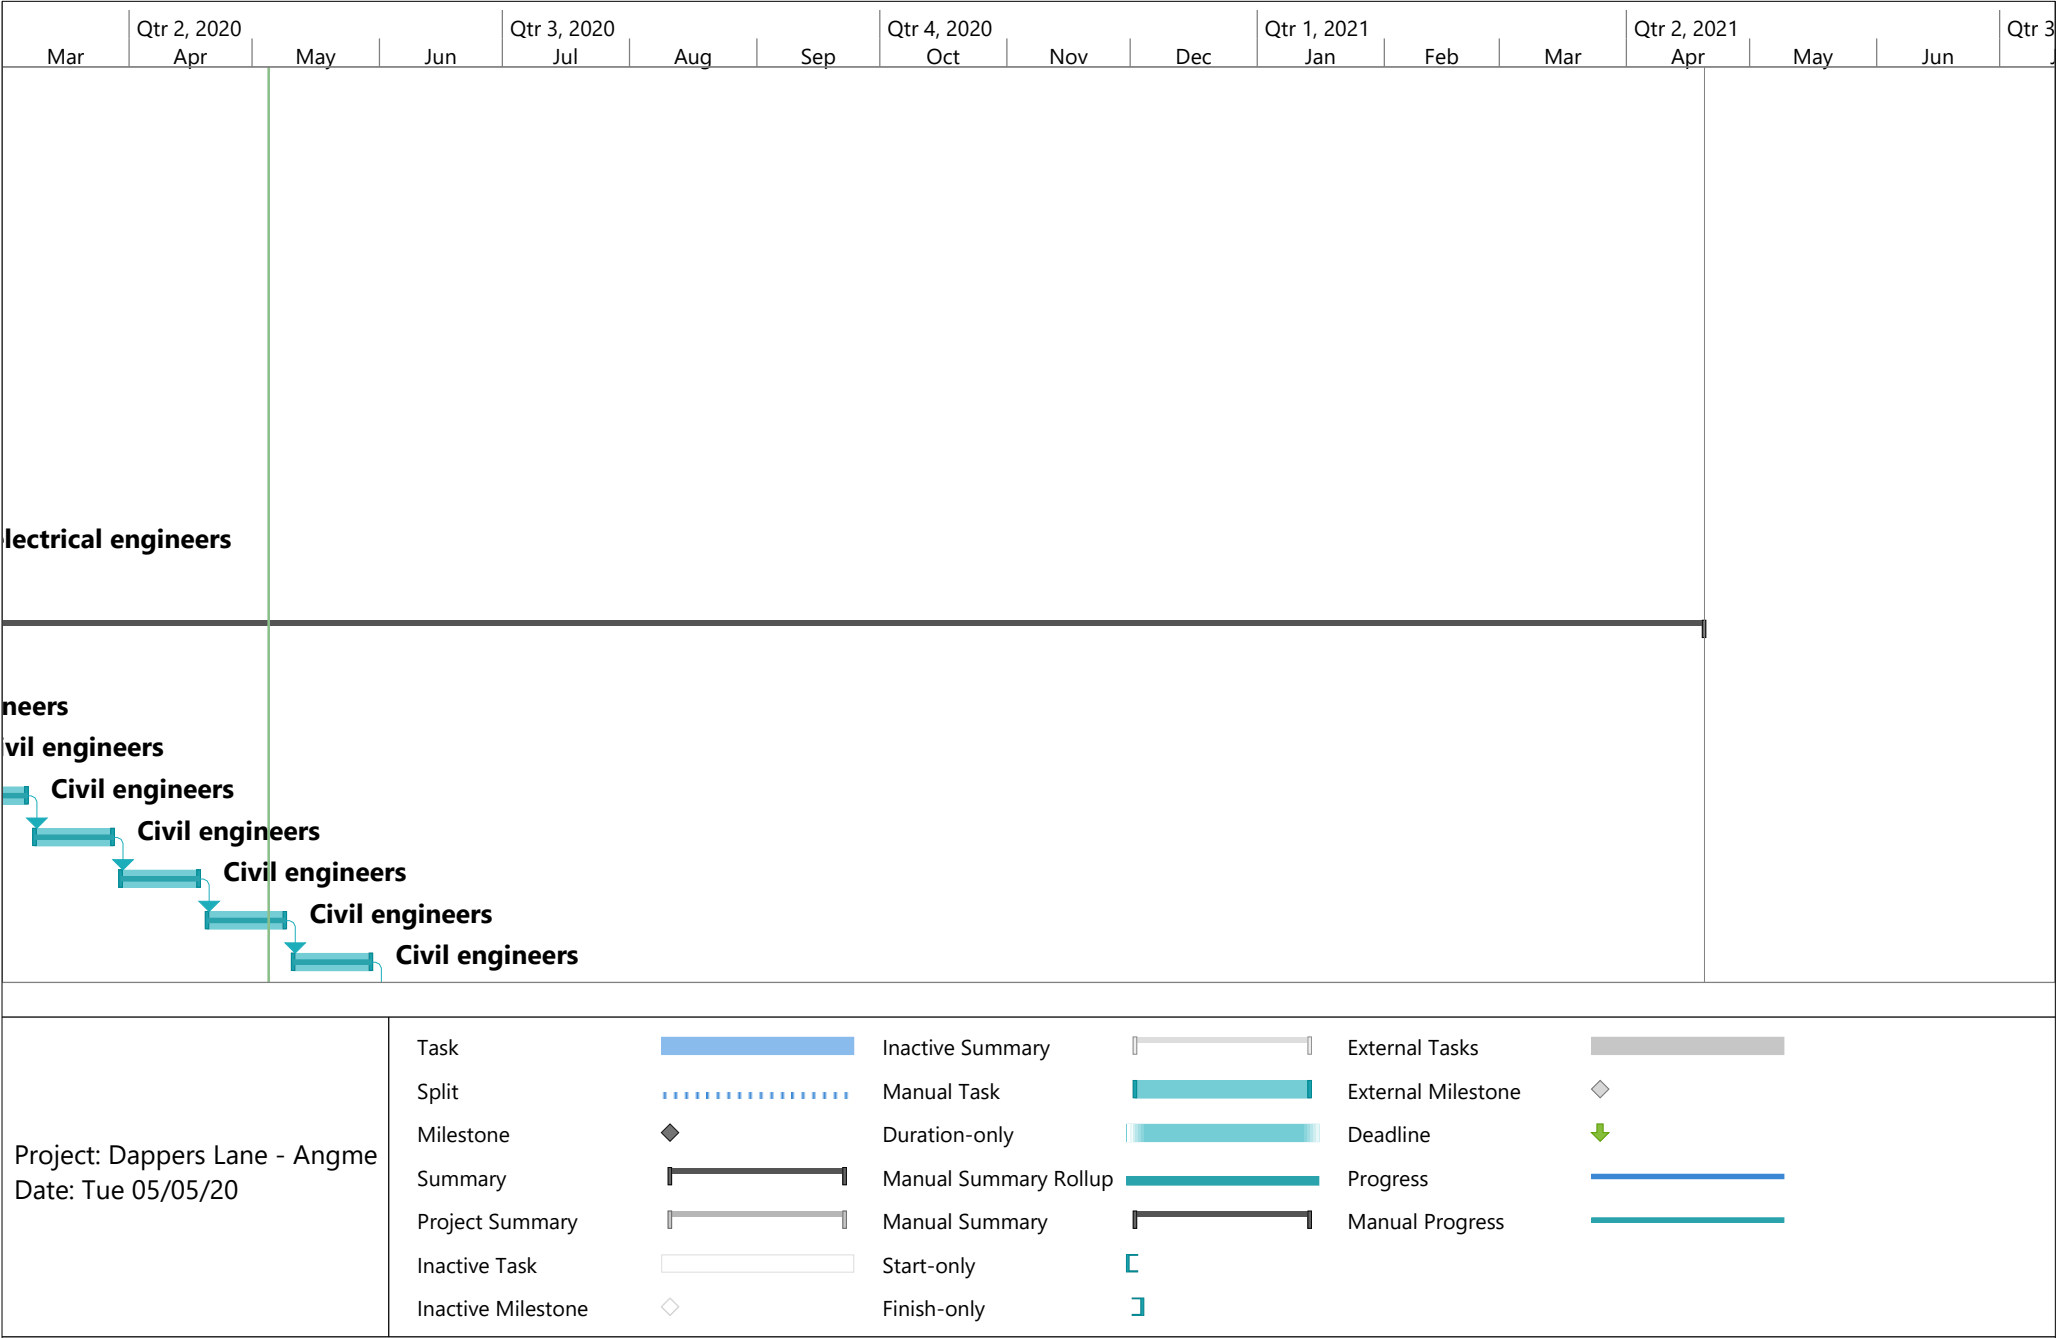

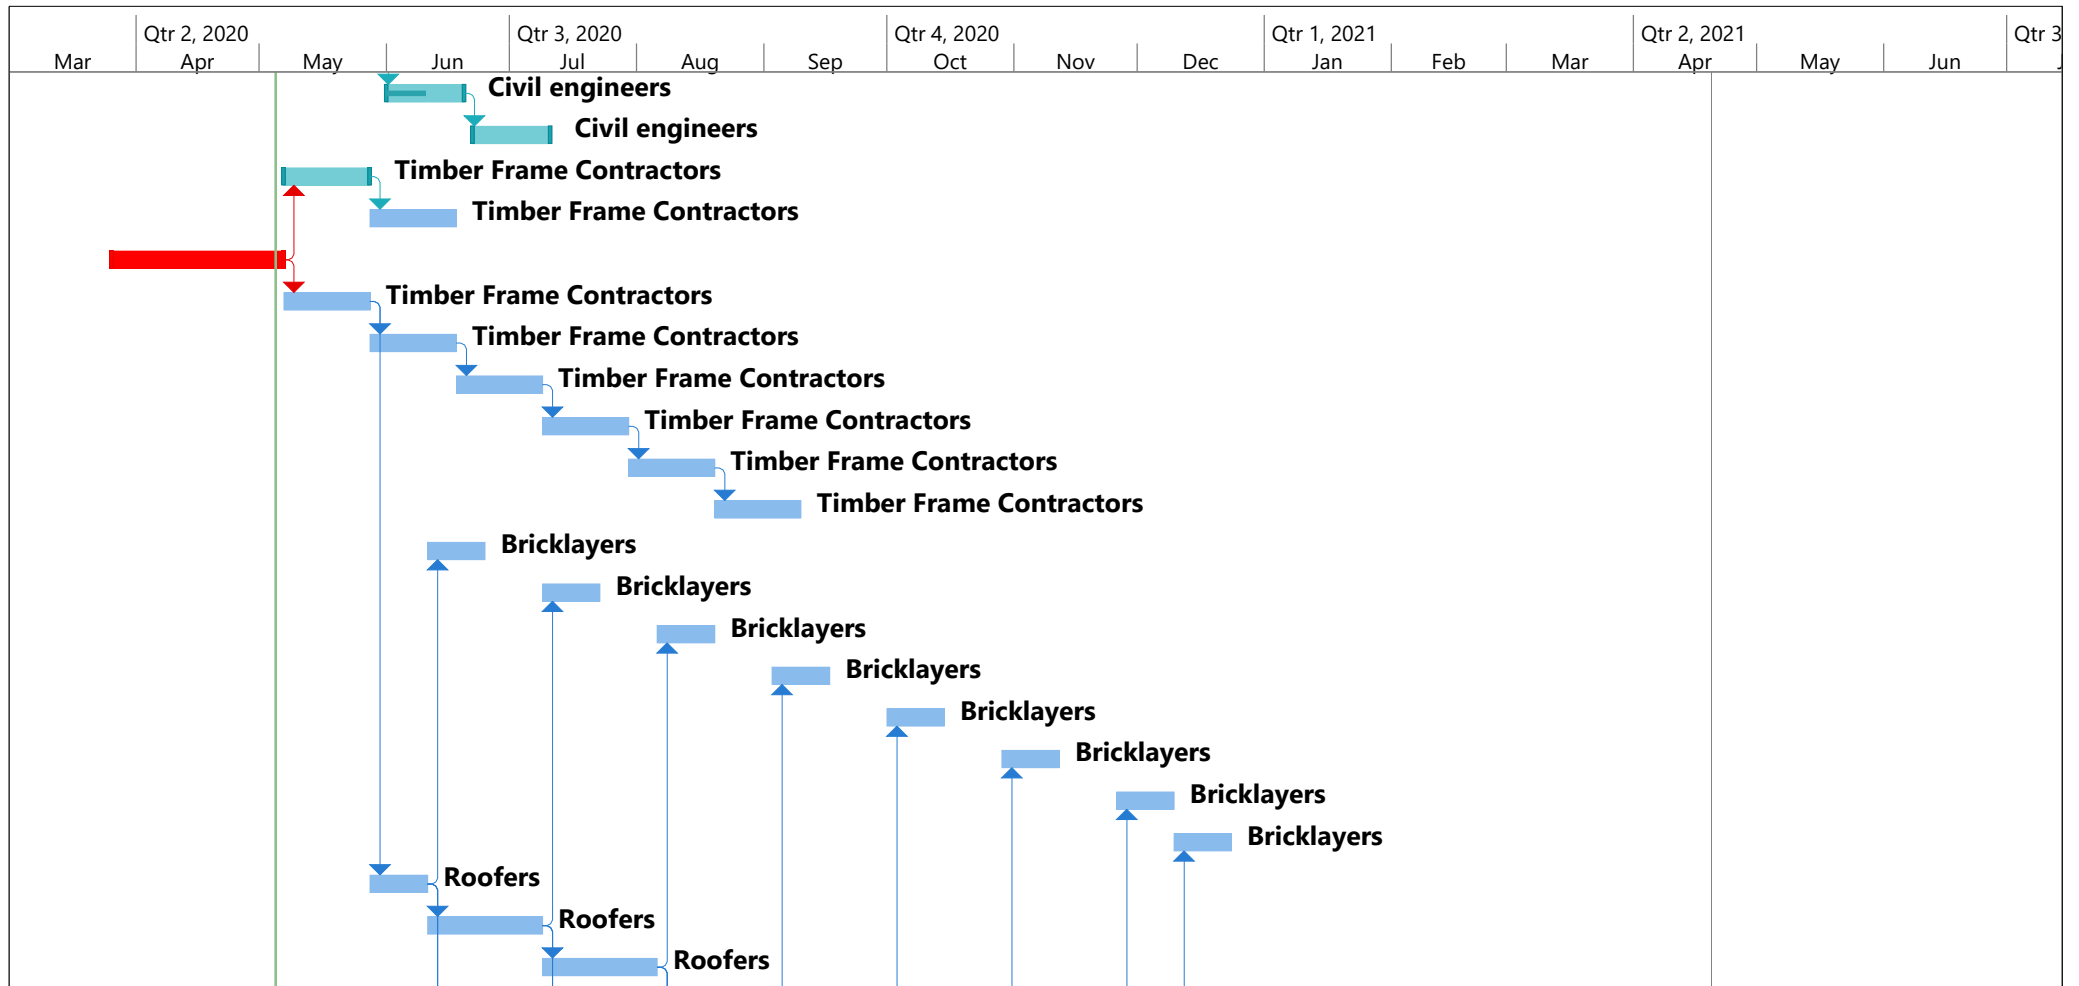


Project: Dappers Lane - Angme
Date: Tue 05/05/20


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

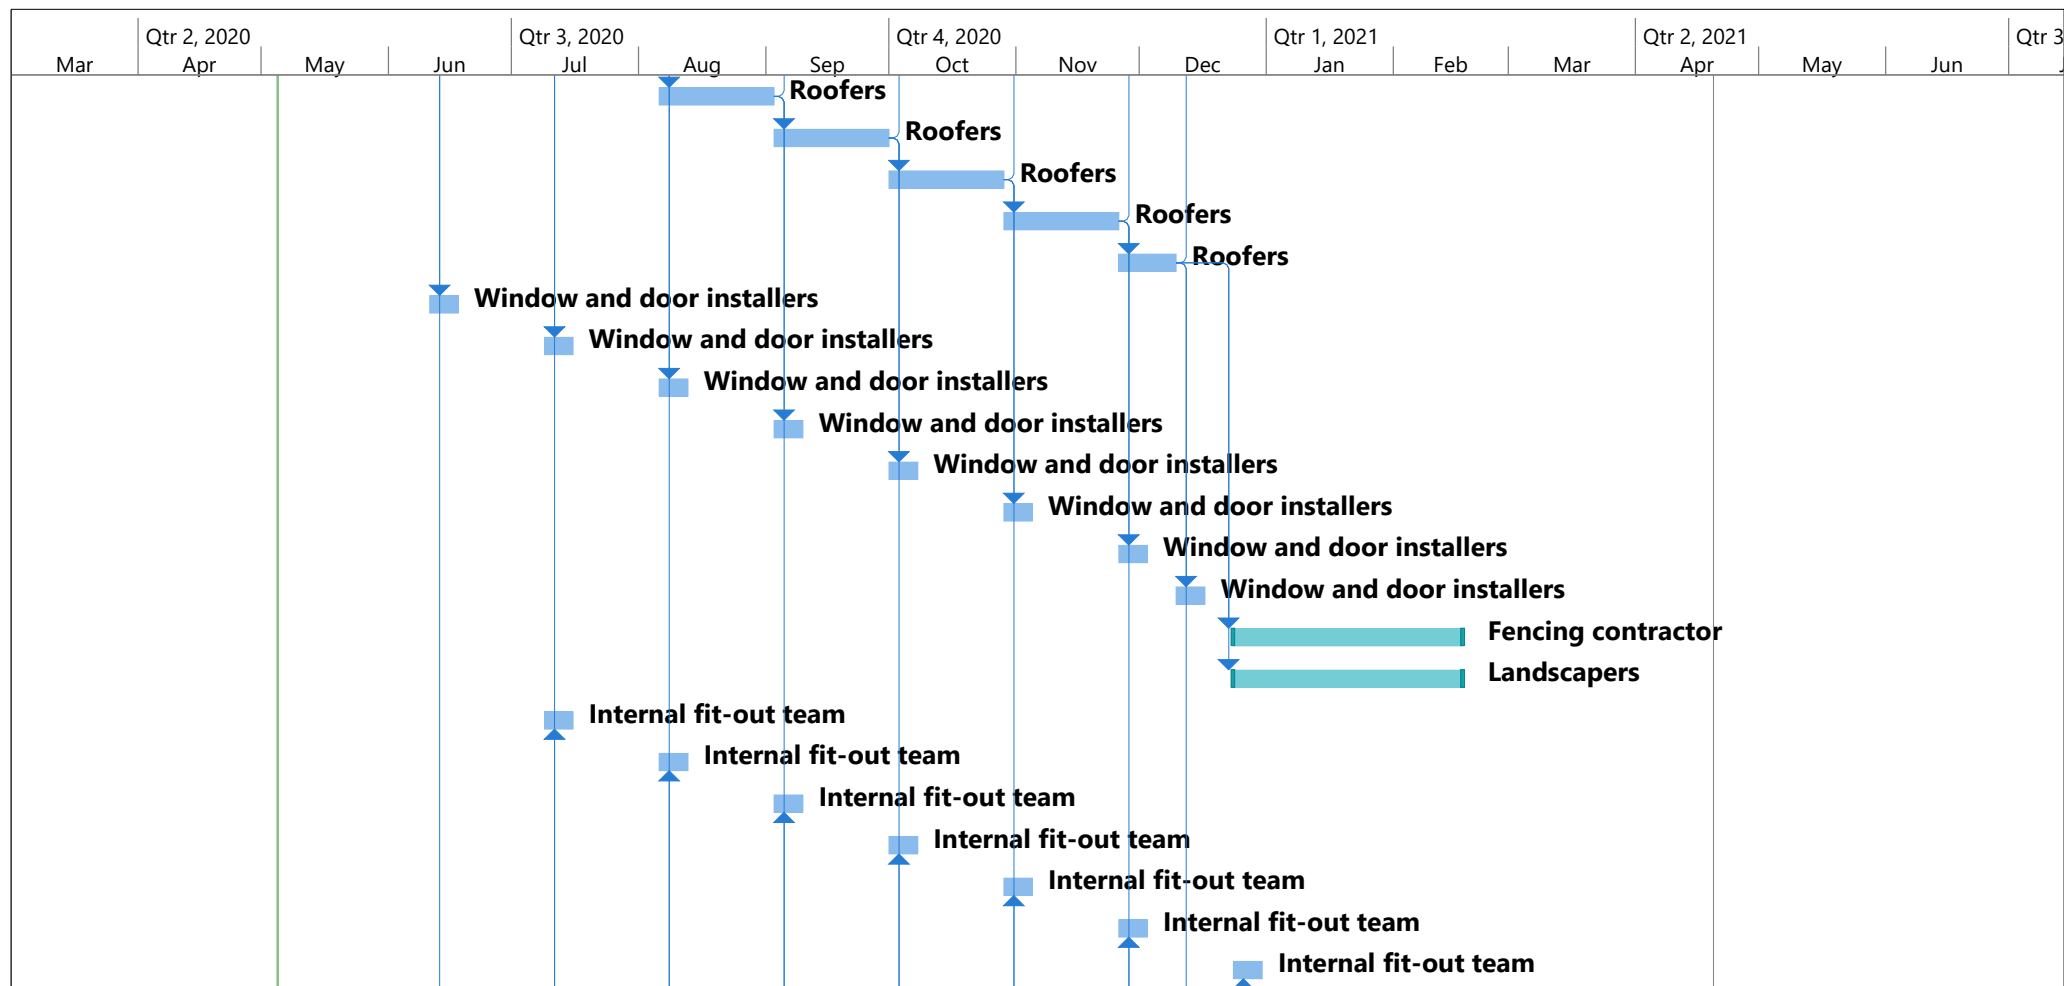


Project: Dappers Lane - Angme Date: Tue 05/05/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

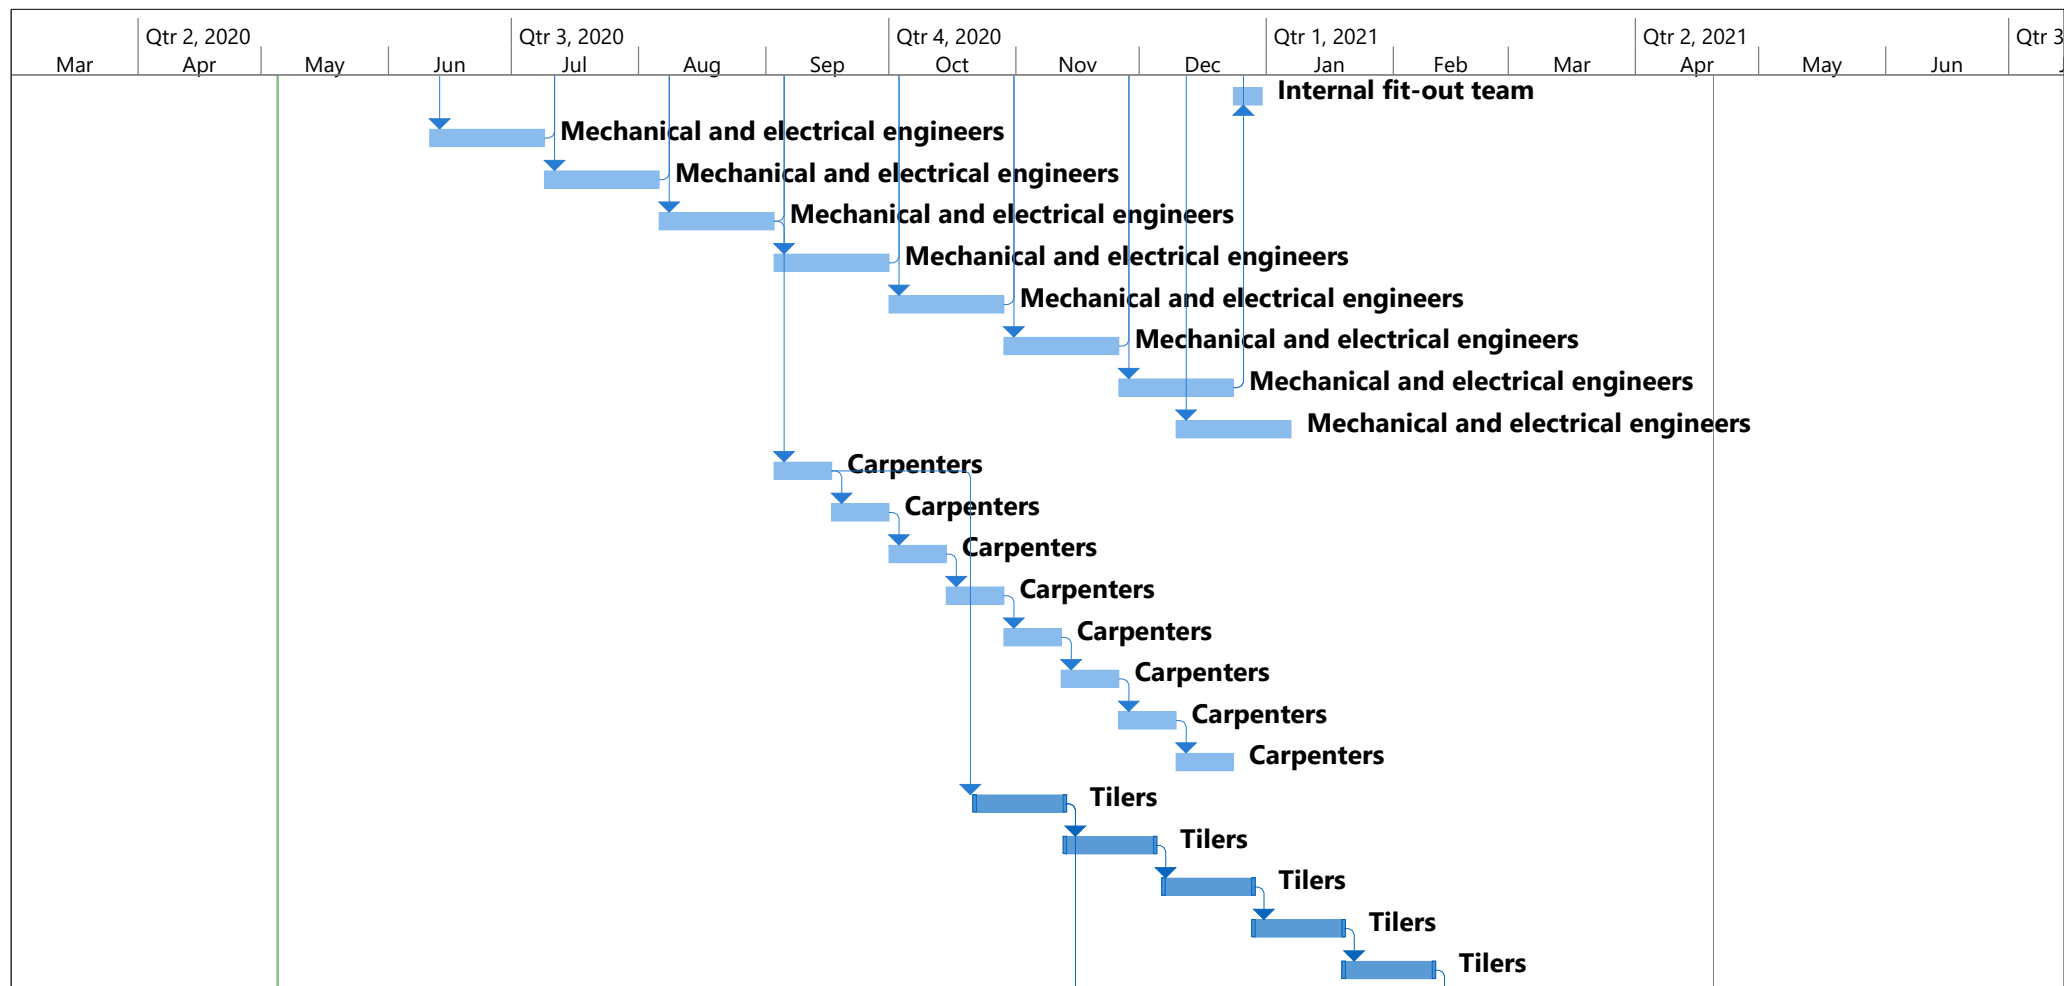

Project: Dappers Lane - Angme Date: Tue 05/05/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

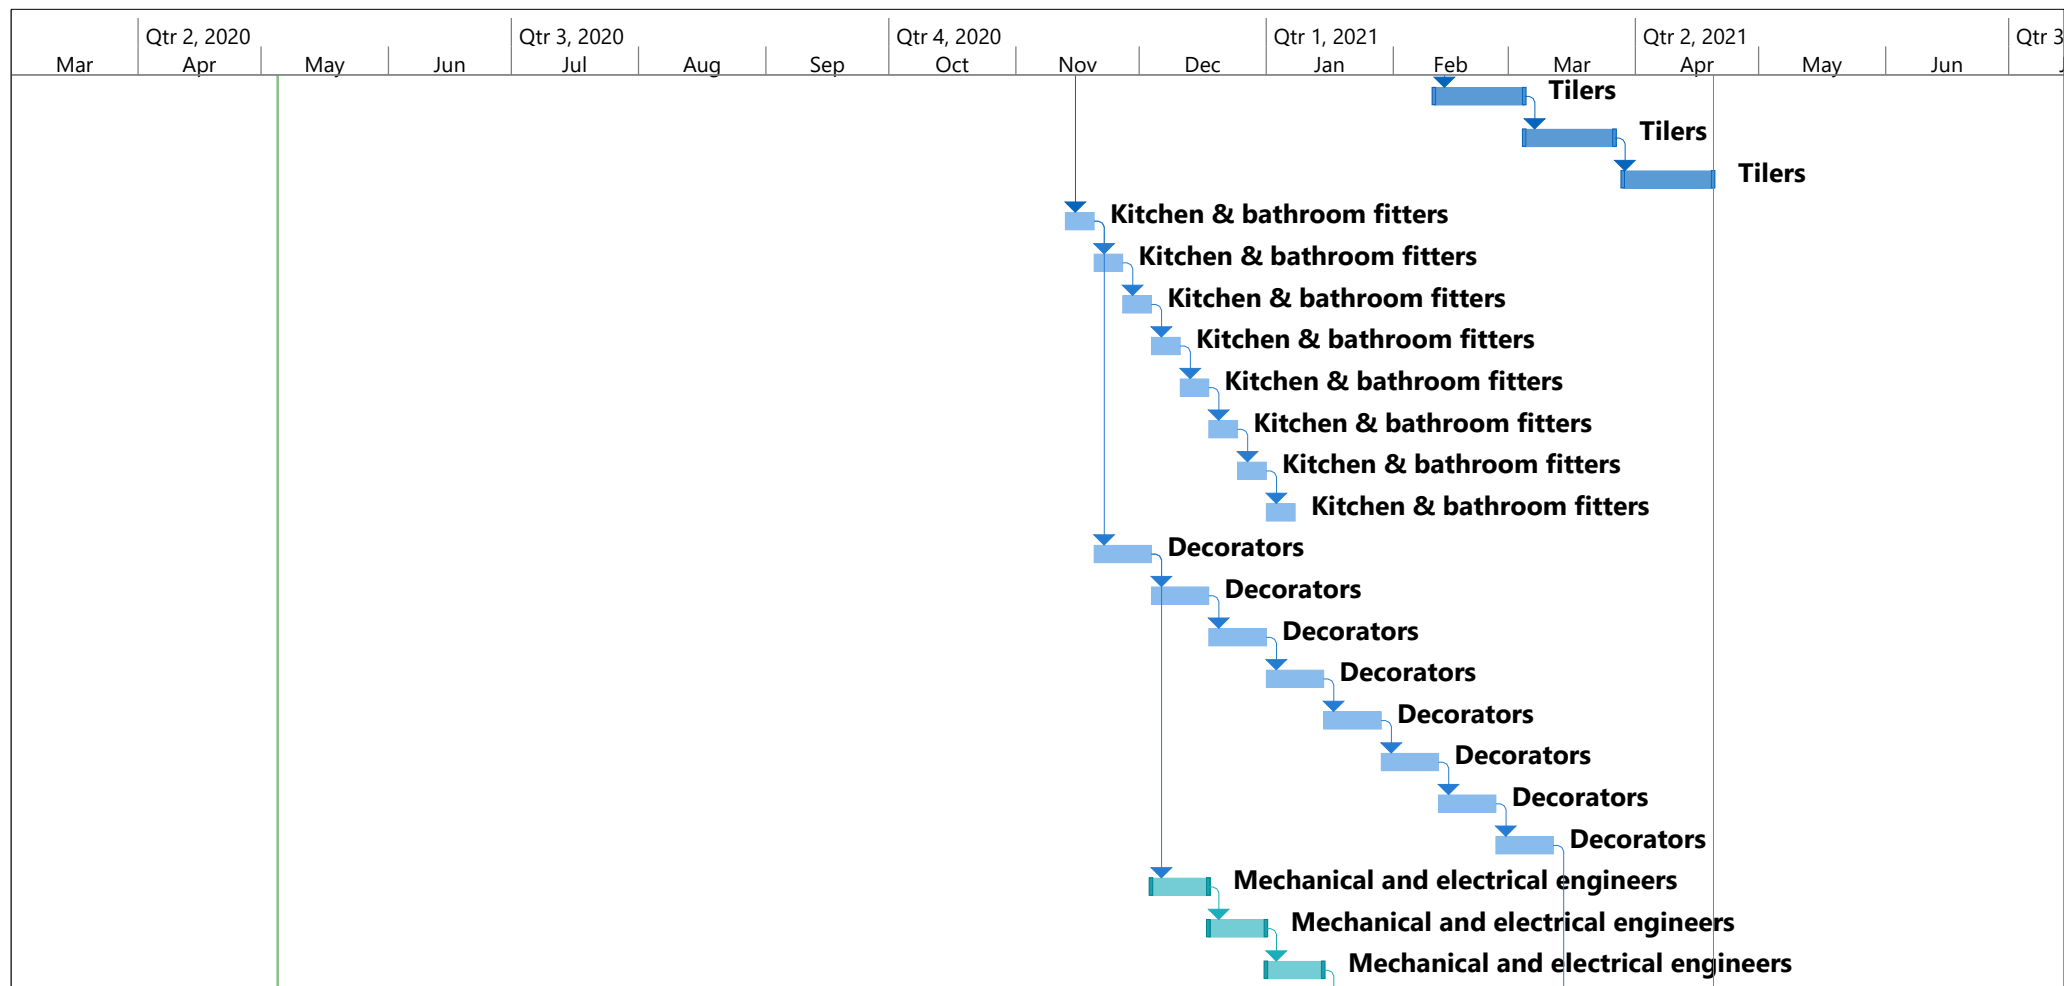

Project: Dappers Lane - Angme Date: Tue 05/05/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

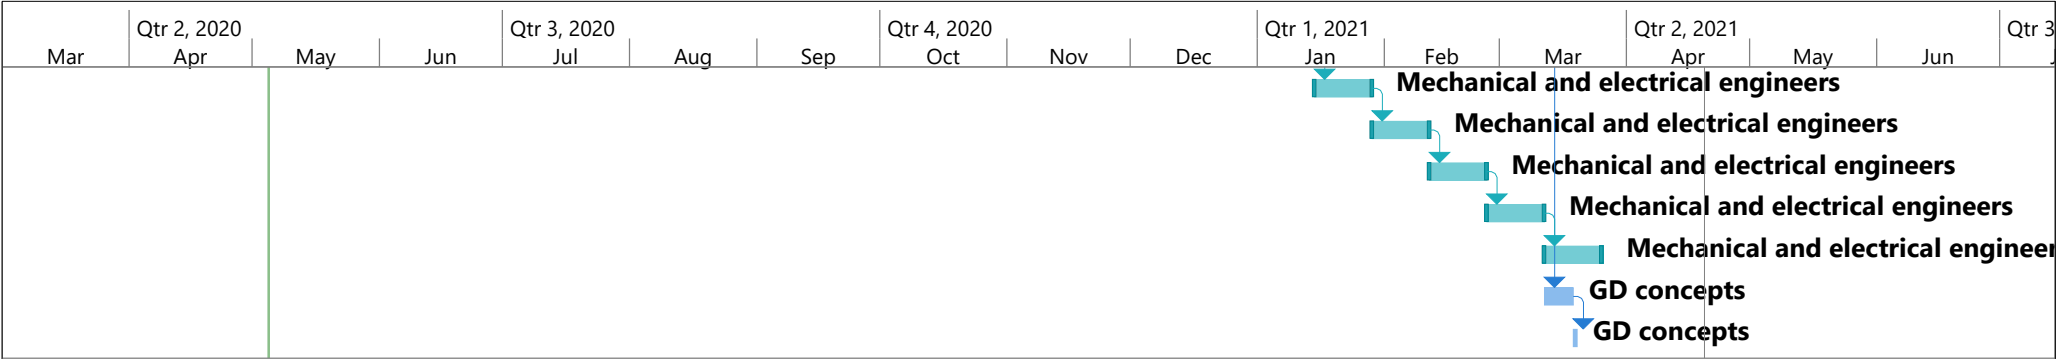

Project: Dappers Lane - Angme Date: Tue 05/05/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

[illegible]

[illegible]

[illegible]

Qtr 3, 2021

Jul

Aug

Sep

Qtr 4, 2021

Oct

Nov

Dec

Qtr 1, 2022

Jan

Feb

Mar

Qtr 2, 2022

Apr

May

Jun

Qtr 3, 2022

Jul

Aug

Sep

Qtr 4, 2022

Oct

Nov

Project: Dappers Lane - Angme

Date: Tue 05/05/20

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 23

Qtr 3, 2021			Qtr 4, 2021			Qtr 1, 2022			Qtr 2, 2022			Qtr 3, 2022			Qtr 4, 2022			Qtr 1, 2023		
Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
ers gineers																				
Project: Dappers Lane - Angme Date: Tue 05/05/20			Task		Inactive Summary		External Tasks													
			Split		Manual Task		External Milestone													
			Milestone		Duration-only		Deadline													
			Summary		Manual Summary Rollup		Progress													
			Project Summary		Manual Summary		Manual Progress													
			Inactive Task		Start-only															
			Inactive Milestone		Finish-only															
