


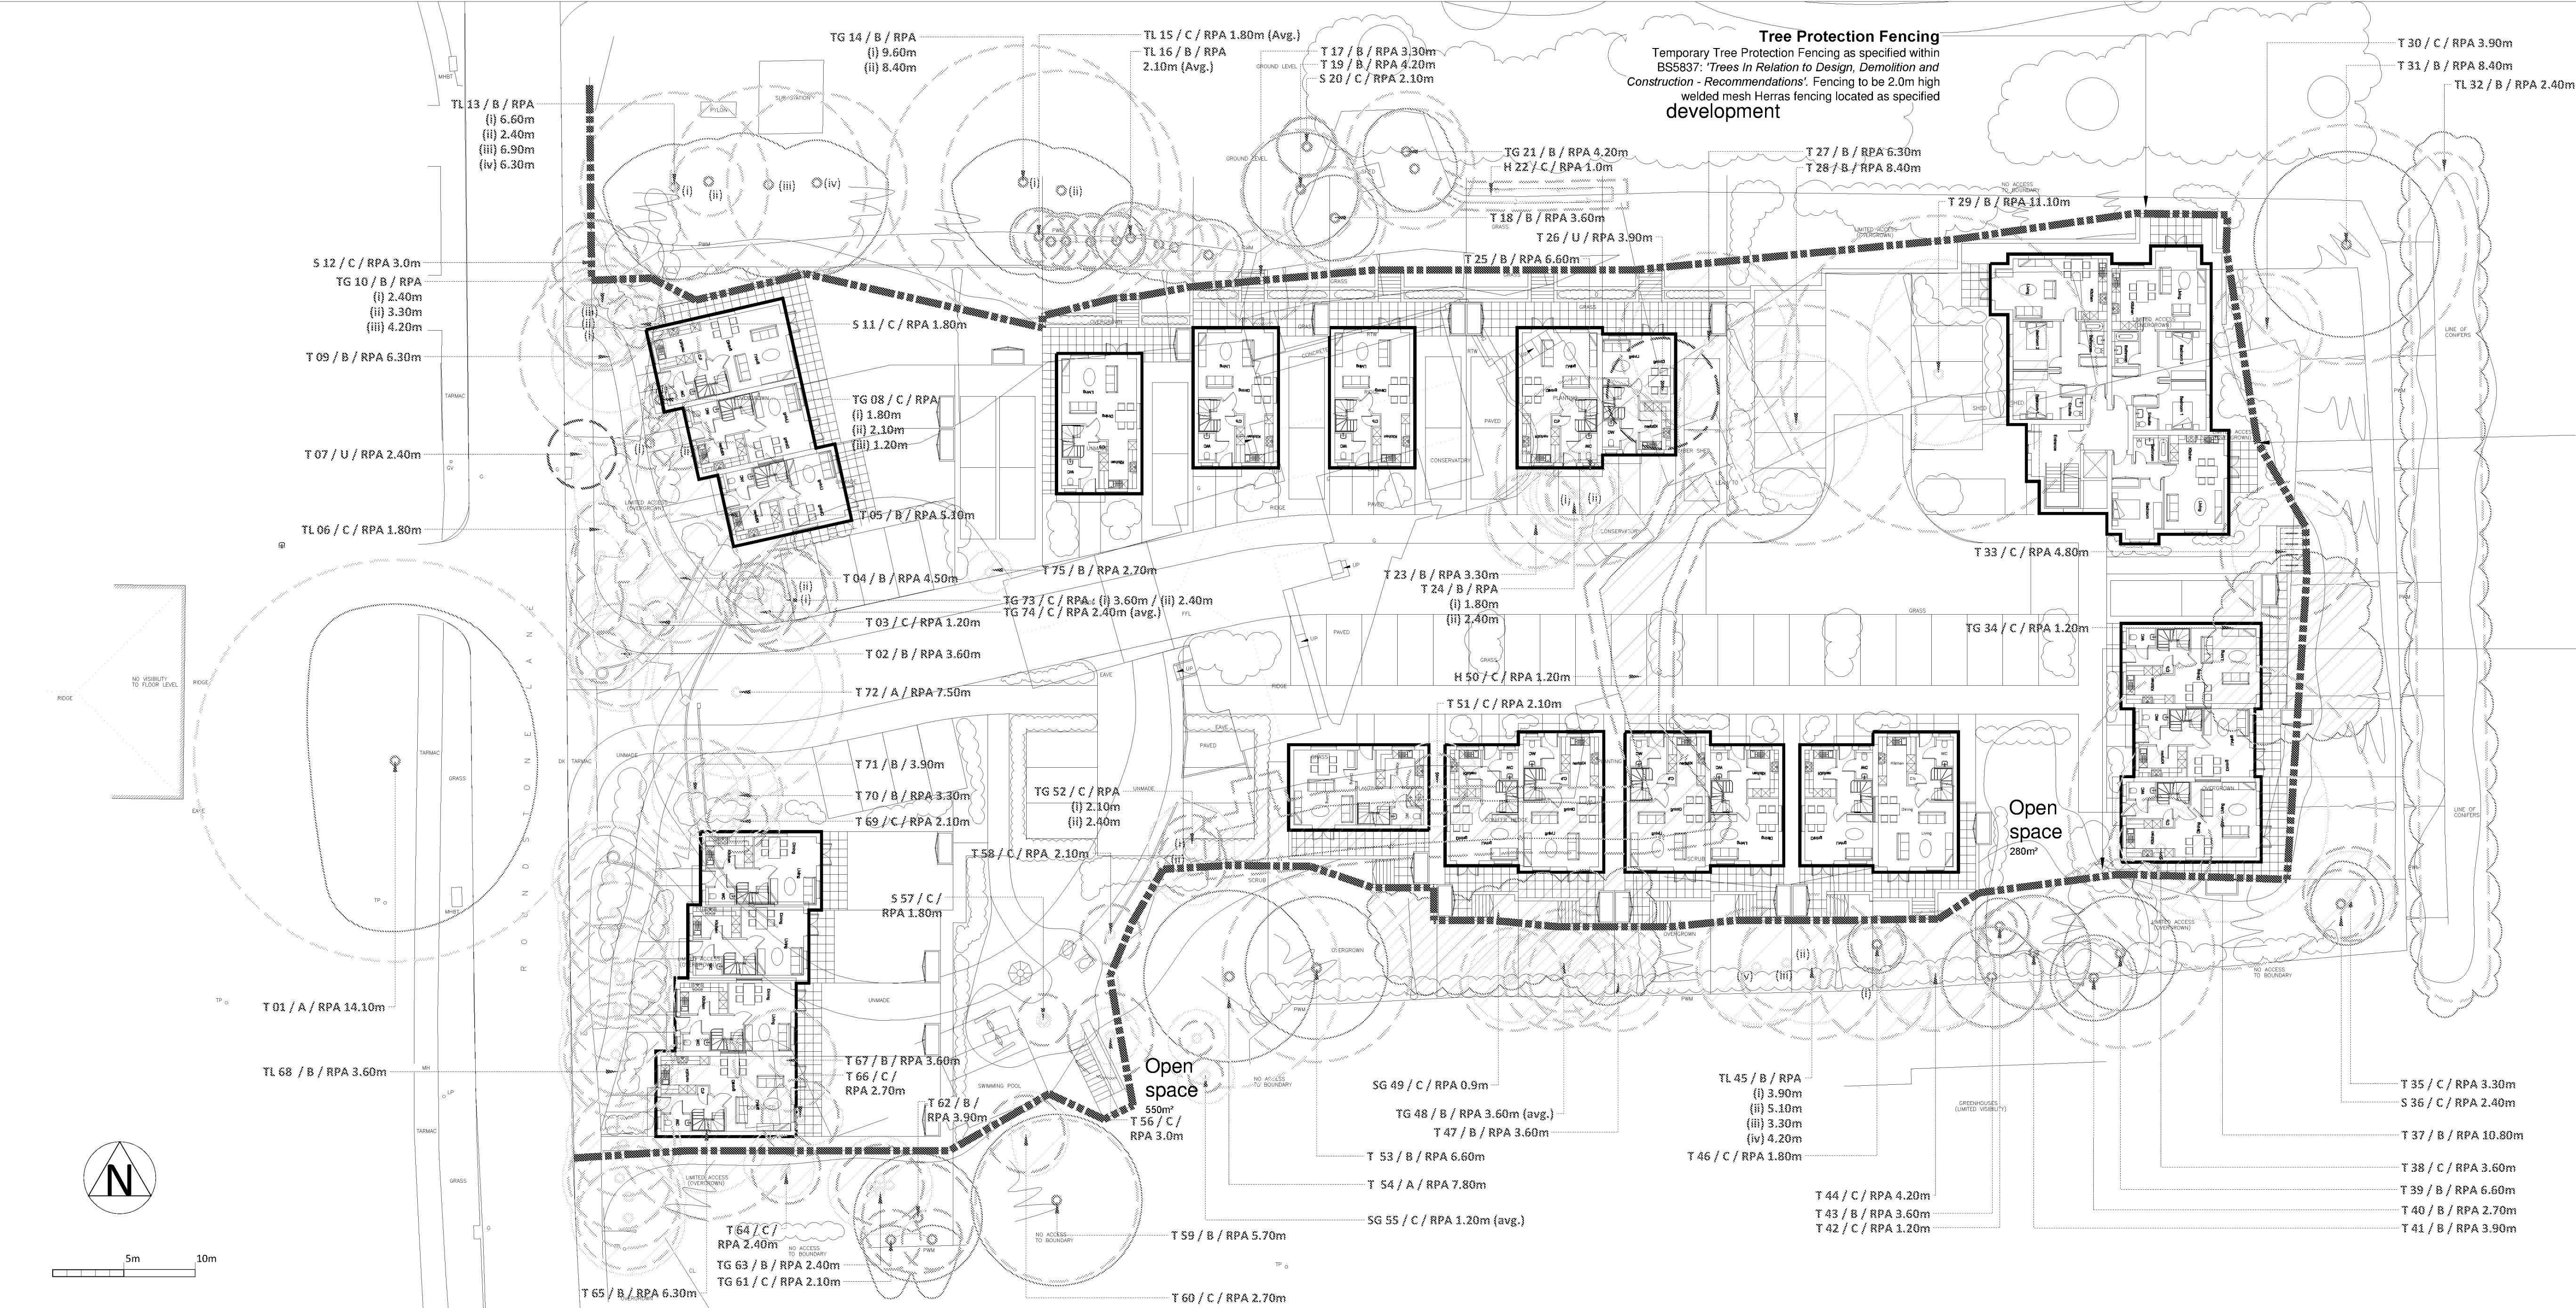

Tree Protection Fencing
Temporary Tree Protection Fencing as specified within BS5837: 'Trees In Relation to Design, Demolition and Construction - Recommendations'. Fencing to be 2.0m high welded mesh Herras fencing located as specified

Temporary Tree Protection Zone (Construction Phase)
Tree Protection Zone to temporary construction site access area. Designated areas to be protected with a Geotextile separation fabric overlain with 150mm min depth of Type 3 granular material in accordance with Highways Agency Specification: Clause 805 (Type 3).

Protection and Retention of Existing Vegetation
The Contractor is to exercise extreme care when undertaking operations below the canopy of existing trees / vegetation and within the specified Root Protection Areas designated for protection and at all times avoid damage to the roots, trunk and existing tree architecture.

Any excavations, cultivation and grading below the canopy of existing trees and within the specified Root Protection Areas of the existing trees / vegetation (including fencing) is to be carried out using hand tools only, taking great care not to damage or disturb any existing tree roots.

Tree roots measuring <25mm may be severed using specialist hand tools only and to the absolute minimum extent required - wherever possible tree roots must be left intact. Exposed roots should be immediately wrapped in dry hessian sacking or coconut matting in order to prevent drying and as a temporary measure can be surrounded with a loose granular fill prior to backfilling with the excavated topsoil.

All trees to be retained on site are to be protected with fencing erected as shown and in accordance with the guidelines as laid out in BS 5837- 2012: 'Trees in Relation to Design, Demolition and Construction - Recommendations'.

The fencing is to be installed and maintained during the entire construction program by the contractor who will be responsible for ensuring the area below the canopy of existing trees and within the specified Root Protection Areas is protected at all times.

The installed protective fencing is to be 2.0 metres height 'Heras' Welded Wire Mesh Fencing (or similar and approved) secured to a scaffolding framework, set into the existing ground and positioned to the outside edge of the existing tree Root Protection Areas as specified. All tree protection to be in accordance with BS 5837:2012 - 'Trees in Relation to Design, Demolition, and Construction recommendations'. The fencing is to be fixed securely and where possible attached to

fences, walls, knee rails etc to ensure a robust temporary fence line and a completely protected area.

Day-glo ribbons or similar are to be attached to the top of the fencing to ensure it is clearly visible and these will be maintained for the entirety of the construction program by the main contractor. Fencing will enclose the full tree root protection areas as specified.

All tree protection fencing is to be maintained for the full contract period. All excavations, earthworks and cultivation within the specified tree root protection areas and below the canopy spread of any existing tree; shrub or hedge will be undertaken with hand tools only. Repositioning of the protective fencing during the course of the construction

works as the contract works progress will be with the approval of the Landscape Architect.

Following the completion of the construction works, the Contractor will remove all temporary protective fencing from the site. All retained vegetation is to be healthy and thriving at the handover date.

Within the specified tree root protection area the following activities must not take place;

- No vehicles are to be used in the fenced off areas;
- No materials are to be stockpiled or stored;
- No chemicals are to be stored;
- No excavation / increase in soil levels will occur;
- No fires shall be lit on site.

Removal of Existing Vegetation
All existing trees designated for removal are to be removed in accordance with the Tree Protection and Retention Drawing. All tree work and removal is to be carried out in accordance with BS 5837: 2012; 'Trees in Relation to Design, Demolition, and Construction'. Trees designated for removal and felling are to be marked on site with white paint. Prior to the removal and felling of trees, the required work and tree positions are to be agreed on site with the Landscape Architect. Trees designated for removal are to be felled prior to the erection of any tree protective fencing. Great care should be taken to avoid damage to trees which are designated to be retained.


Stumps are to be removed and cut away so that the top of the stump is at least 450 mm (minimum) below the final topsoil level in order that the site can be leveled and grassed over. Stumps are to be treated with an approved herbicide to be agreed with the Landscape Architect.

Tree Surgery
Any significant defects found in the trees during the course of the scheduled work to be reported to the Landscape Architect. All work is to be undertaken by an approved and qualified tree surgeon in accordance with BS 3998:2010: Tree Work.


Tree Surgery.
Great care is to be taken to avoid damage to neighbouring trees which are to be retained. Branches in confined spaces are to be removed in sections. All arisings are to be transported and disposed of away from site.

Tree and Vegetation Management
For Tree and Vegetation Retention and Removal Proposals refer to the attached Existing Tree Schedule and Schedule of Tree Works. For any tree and vegetation management proposals refer to the Tree Surgery and Management Recommendations contained within the Existing Tree Schedule.


KEY




Proposed Residential Dwellings
Refer to Crowther Architect drawings and specifications for further details.




Existing Tree / Shrub Groups to be Removed
Existing tree / shrub groups to be removed prior to any construction activities on site.




Category B Trees
Existing trees (root protection areas) assessed to be 'Category B': moderate quality and value.




Temporary Tree Protection Zone (Construction Phase)
Tree Protection Zone to temporary construction site access area. Designated areas to be protected with a Geotextile separation fabric overlain with 150mm min depth of Type 3 granular material in accordance with Highways Agency Specification: Clause 805 (Type 3).




Tree and Shrub Numbers
Tree No. / Category / Tree Root Protection Area.




Existing Hedgerows
Existing hedgerows to be retained and protected within the proposed development scheme.




Category C Trees
Existing trees (root protection areas) assessed to be 'Category C': low quality and value.




Existing Tree Specimens to be Retained
Existing tree specimens to be retained and protected within the proposed development scheme.



Existing Hedgerows to be Removed
Existing hedgerows to be removed prior to any construction activities on site.




Category U Trees to be Removed
Existing trees (root protection areas) assessed to be 'Category U': unsuitable for retention.



Existing Tree Specimens to be Removed
Existing tree specimens to be removed prior to any construction activities on site.



Category A Trees
Existing trees (root protection areas) assessed to be 'Category A': high quality and value.



Tree Protection Fencing
Temporary Tree Protection Fencing as specified within BS5837: 'Trees In Relation to Design, Demolition and Construction - Recommendations'. Fencing to be 2.0m high welded mesh Herras fencing located as specified.

NOTES

All tree surgery works are to be carried out by an appropriately qualified tree surgeon to BS 3998: 2010; Tree Surgery. Refer to accompanying Existing Tree Schedule for further details.

The information contained within this drawing and accompanying Existing Tree Schedule is not intended as a safety audit and should not be interpreted as such.

REV	DESCRIPTION	DATE	INITIALS
01	Layout issued for planning	03-02-17 AR	
02	Layout amended following comments	05-07-17 AR	



The Studio, 68 Cuckfield Road, Hurstpierpoint, West Sussex, BN6 9SB
T: 01273 834 198 M: 07973 776047 E: landscape@ramsayandco.com

Project Title: Quiet Waters, Roundstone Lane, Angmering, W. Sussex Nova Developments Ltd.
Drawing Title: Tree Protection Drawing Planning Issue

Scale: 1:250@A1	Drawn: AR	Date: 05-01-17
Drawing Number: RCO 193 / 01	Revision: 02	
