

Arbortrack Systems Ltd
The Granary Studio
Crewe Lane
Kenilworth
Warwickshire
CV8 2LA



Arboricultural Impact Assessment

& Method Statement:

10 Felpham Gardens
Felpham
Bognor Regis
West Sussex
PO22 8QS

REPORT PREPARED FOR:

Sussex Building Consultancy Ltd
3 Northcote Road
Bognor Regis
PO21 5LZ

REPORT PREPARED BY

James Bell
MSc. (Env). Arbor. A. Tech. Cert.

Ref: jwmb/ rpt1/ 10felphamgdns/ AIAAMS

Date: 13th December 2018

The content and format of this report are for the exclusive use of the client. It may not be sold, lent, hired out or divulged to any third party not directly involved in the subject matter without the written consent of Arbortrack Systems Ltd.

CONTENTS

1.0	Introduction	3
1.1	Purpose & Use of the Report	3
1.2	Terms of Reference	3
1.3	Development Proposals & Impact Assessment	3
1.4	Sequence of Works	4
1.5	Site Supervision	4
1.6	Site Monitoring & Contact Information	4
1.7	Statement Adoption	5
2.0	Pre Development Site Preparation	5
2.1	Arboricultural Works	5
2.2	Preparation of Surfaces	5
2.3	Installation of Tree Protection Barrier	5
2.4	Pre Development Site Inspection	6
3.0	Development Phase	6
3.1	General Precautions	6
3.2	Root Protection Areas	6
3.3	Site Access Accommodation & Storage	6
3.4	Routing & Installation of Services	7
3.5	Demolition Measures	7
3.6	Changes in Grade	7
3.7	Construction Measures	7
3.8	Removal of Tree Protection Barrier	7
3.9	Post Construction Landscaping	7
4.0	Summary of Proposed Methods	8
4.1	Table of Impacts & Mitigation	8
5.0	Completion	8
5.1	Completion Meeting	8
	Appendix A	Tree Protection Plan
	Appendix B	Tree Survey Schedule & Recommended Tree Works
	Appendix C	Fencing Specification to BS5837:2012
	Appendix D	Glossary & General Guidelines

1.0 Introduction

1.1 Purpose & Use of the Method Statement

- 1.1.1 This impact assessment & method statement report has been prepared for submission to Arun District Council (ADC) to accompany a planning application for two 3 bedroom detached dwellings with attached single garages and a shared two bay detached carport at 10 Felpham Gardens, Felpham, Bognor Regis, PO22 8QS. This statement is intended to demonstrate the feasibility of construction without harm to the retained tree resource adjoining the site. See material accompanying this report for full scheme details.
- 1.1.2 This document lays down the methodology for any proposed works that may have an effect upon the trees on and adjacent to the site. It is essential within the scope of any contracts related to the development proposals that this method statement is observed and adhered to. It is recommended that this document form part of the work schedule and specification issued to the building contractors and can be used to form part of the contract.
- 1.1.3 Copies of this document should be available for inspection on site. The developer will inform the local planning authority within twenty-four hours if the designated arboriculturist is replaced.

1.2 Terms of Reference

- 1.2.1 I am instructed by Sussex Building Consultancy Ltd acting on behalf of Mr Tom Barnes to prepare an arboricultural impact assessment & method statement report to accompany a planning application for a proposed development at 10 Felpham Gardens, Felpham, Bognor Regis, PO22 8QS with reference to BS5837:2012 Trees in relation to design, demolition & construction-Recommendations (BS5837:2012).

1.3 Development Proposals & Impact Assessment

- 1.3.1 See section 1.1.1 accompanying material for full details of the development proposals.
- 1.3.2 None of the surveyed trees will be removed to allow or facilitate development. Minor cutting back of overhanging branch tips of trees 11 & 13 is recommended to improve separation with the proposed dwellings. The dwellings will have a very similar relationship with offsite surveyed trees to that currently present at 7 Felpham Gardens.
- 1.3.3 Some soft ground within the root protection area (RPA) of trees 11 & 13 principally will be converted to hard standing (driveway) at the end of development. Levels will be made up using loose granular fill as per guidance in BS5837:2012 section 7.4.4.4. Finished surfaces will be constructed to a conventional specification with a porous surface to allow water infiltration to those areas of the RPA of tree 11 principally.
- 1.3.4 The great majority of site works will take place beyond the RPA of retained trees and canopies. Retained trees will be protected through the course of development by fencing to the specifications recommended by BS5837:2012-see Appendix C for details.

1.4 Sequence of Works

1.4.1 The sequence of works should be as follows:

- ¿ laying of service runs as required
- ¿ erection of tree protection barrier (TPB) on advised line(s)
- ¿ main construction including driveway & carport construction
- ¿ removal of TPB
- ¿ soft landscaping as proposed

1.5 Site Supervision

1.5.1 Site supervision – an individual e.g. the Site Agent, must be nominated to be responsible for all arboricultural matters on site. This person must:

- ¿ be present on site for the majority of the time
- ¿ be aware of the arboricultural responsibilities
- ¿ have the authority to stop any work that is causing, or has the potential to cause, harm to any retained tree
- ¿ be responsible for ensuring that all site operatives are aware of their responsibilities toward trees on site and the consequences of the failure to observe these responsibilities
- ¿ make immediate contact with the local authority and/or the designated arboriculturist in the event of any tree related problems occurring, whether actual or potential

1.6 Site Monitoring

1.6.1 The site agent will be responsible for monitoring all arboricultural works, inspecting protective fencing and monitoring any works within exclusion zones. The designated arboriculturist will be available for site visits on a basis to be agreed between client and planning authority when/ if appropriate or required i.e. if required by condition. A record of site visits will be maintained for inspection on site and copies forwarded to the developer/ agent and to the local planning authority. A certificate of practical completion should be produced for sites deemed by all parties to merit this.

1.6.2 Principal contact information: 1/ James Bell, Arbortrack Systems Ltd, Arboricultural Consultant

5/5/ 4/ / Site agent details to be advised.

1.7 Statement Adoption

- 1.7.1 It is recommended that, in due course, acceptance of the recommendations in this report is demonstrated by, for example, the architect specifying in writing to the building contractor that tree care conditions apply in execution of the contract, and by an estimate or written undertaking from the contractor to the architect demonstrating that the practical aspects of observation of such recommendations have been priced in.
- 1.7.2 If conflicts between any part of a tree and the building arise in the course of development these can often be resolved quickly and at little cost if a qualified arboriculturist is consulted promptly. Lack of such care is often apparent quickly and decline and death of such trees can spoil design aims and can of course affect saleability, and reflect poorly on the construction and design personnel involved. Trees that have been the recipients of careful handling during construction add considerably to the appeal and value of the finished development.

2.0 Pre-Development Site Preparation

2.1 Arboricultural Works

- 2.1.1 See Appendix B for full details of tree works required to allow or facilitate development.

2.2 Preparation of Surfaces

- 2.2.1 n/a

2.3 Installation of Tree Protective Barrier

- 2.3.1 The TPB must be comprised of a vertical and horizontal scaffold framework, braced to resist impacts, with vertical tubes spaced at a maximum level of 3m. On to this weldmesh panels should be securely fixed with wire scaffold clamps: see section 6.2.2 and Figure 2 of BS5837:2012 (Appendix C). Hardboard or marine ply sheets can be used as an alternative to weldmesh panels but these must be firmly fixed to the framework. The location of the TPB is shown in Appendix A.
- 2.3.2 This TPB is to be erected before any construction work commences on site, is to remain 'in situ' undamaged for the duration of all work or each phase, and is only to be removed once all work is completed. If any work other than preparatory tree work is deemed necessary prior to the erection of fencing the designated arboriculturist should be informed to enable his/ her presence to oversee the work being carried out.
- 2.3.3 The only other exception is the completion of soft landscaping but if any excavations, however minor, are to be carried out as part of soft landscaping within RPAs, an arboricultural assessment must be carried out beforehand and any arboricultural protection measures incorporated. The TPB should carry waterproof warning notices denying access within RPAs.

-
- 2.3.4 The Tree Protection Plan in Appendix A illustrates where the protective fencing should be located to form the boundary of the Tree Protection Zone (TPZ). The TPZ is an exclusion zone and suitable steps should be taken to prevent access by pedestrians and vehicles and the storage of any works materials and equipment should be located outside of the TPZ.

2.4 Pre-Development Site Inspection

- 2.4.1 At the instigation of the client/site agent or ADC, upon erection of the fencing the designated arboriculturist will meet the relevant local authority member on site to check the standard of the work(s). If there are any amendments to the protective fencing these will be agreed at this meeting, confirmed in writing, and undertaken thereafter.

3.0 Development Phase

3.1 General Precautions

- 3.1.1 No fires shall be made on any part of the site, or within 10m of the furthest extent of the canopy of any tree or group tree to be retained on site or on land adjoining.
- 3.1.2 No spilling or pouring of fuels, oils, solvents or tar shall be made on any part of the site.
- 3.1.3 No materials that are likely to have an adverse effect on tree health such as oil, bitumen or cement will be stored or discharged within 10 metres of the trunk of a tree that is to be retained.
- 3.1.4 No spillage or discharge of wet mortar or concrete shall be made on any part of the site.
- 3.1.5 No storage of materials shall be made within the protective fences.
- 3.1.6 No breaching or moving of the protective fences shall occur without the approval of the designated arboriculturist.
- 3.1.7 Alterations in levels within the tree protection fence areas shall be avoided.

3.2 Root Protection Areas

- 3.2.1 The RPA is a desirable zone of protection around the trees' rooting system and these have been marked on the plan in Appendix A. The RPAs will lie within the TPZ and therefore, be fully fenced off (see Appendix A) unless where appropriate ground protection is offered.

3.3 Site Access, Accommodation & Storage

- 3.3.1 Many site activities are potentially damaging to trees e.g. material storage, parking, soil compaction and the use of plant machinery. In this latter example particular care is required to ensure that the operational arcs of excavation and lifting machinery, including their loads, do not physically damage trees when in use or in accessing the site.

3.4 Routing & Installation of Services

- 3.4.1 It is assumed that service runs will be brought into the site in a manner that avoids the RPAs of retained trees.
- 3.4.2 Where crown interference with mature trees is a possibility, over-ground services will be routed in an alternative direction. In relation to this, any landscaping taking place should accommodate the presence of over-ground services and take mature tree size into account.

3.5 Demolition Measures (n/a)

3.6 Changes in Grade

- 3.6.1 The upper layer of top soil (top 60cm) contains the majority of a tree's roots and if this is disturbed by a change in ground level, serious damage can be caused. On this basis, as a minimum, level changes should be avoided within RPAs.
- 3.6.2 If any significant section of ground level requires raising within RPAs, this should be achieved using coarse, granular material such as pebbles. See section 7.4.4.4 of BS5837:2012.
- 3.6.3 If ground levels need to be altered within 1.5 metres of any tree trunk prior agreement must be sought and given by the local authority tree officer.

3.7 Construction Measures

- 3.7.1 No specialist construction methods are required for the building footprints or associated infrastructure in terms of trees.

3.8 Removal of Tree Protective Barrier

- 3.8.1 The protective fencing may be removed only upon completion of the development phase when all drainage and service runs have been installed and any site machinery has been removed.

3.9 Post Construction Landscaping

- 3.9.1 Following the developing phase, some trees may be subject to either landscaping or seeding beneath their canopy but at this stage the protective fencing will have been removed.
- 3.9.2 Any approved landscaping works should avoid the changing of ground levels or deep digging. Mechanised cultivation such as tractor-mounted rotovation must not be used within the RPAs of existing trees.
- 3.9.3 Heavy machinery should not be used in the vicinity of any retained trees.
- 3.9.4 If herbicides are to be used they should be appropriate to their purpose and not in such a way as to damage any retained trees or vegetation.
- 3.9.5 Ideally, retained trees should be within a shrub area as this reduces the chances of compaction and disturbance of root systems.

4.0 Summary of Proposed Methods

4.1 Table of Impacts and Mitigation


4.1.1 The table below summarises the main areas where trees could become damaged by the proposed development and the methods that need to be adopted in order to prevent such damage:

<u>Impact</u>	<u>Mitigation</u>	<u>Reference</u>	<u>Trees Affected</u>
Passage of machinery and storage of materials over RPAs	Construction of protective fencing to acceptable standards	Sections 2.3. Fencing spec Appendix C, Tree Protection Plan Appendix A	1, 11 & 13

5.0 Completion

5.1 Completion Meeting

- 5.1.1 Following completion of the approved works on site, the designated arboriculturist will meet with a local authority representative and agree upon any remedial works deemed necessary (if any).
- 5.1.2 Any works agreed in the above meeting will be confirmed in writing and should be performed to BS3998:2010.
- 5.1.3 Any work proposed post development should be checked to avoid penalty for performing illegal work on a protected tree.

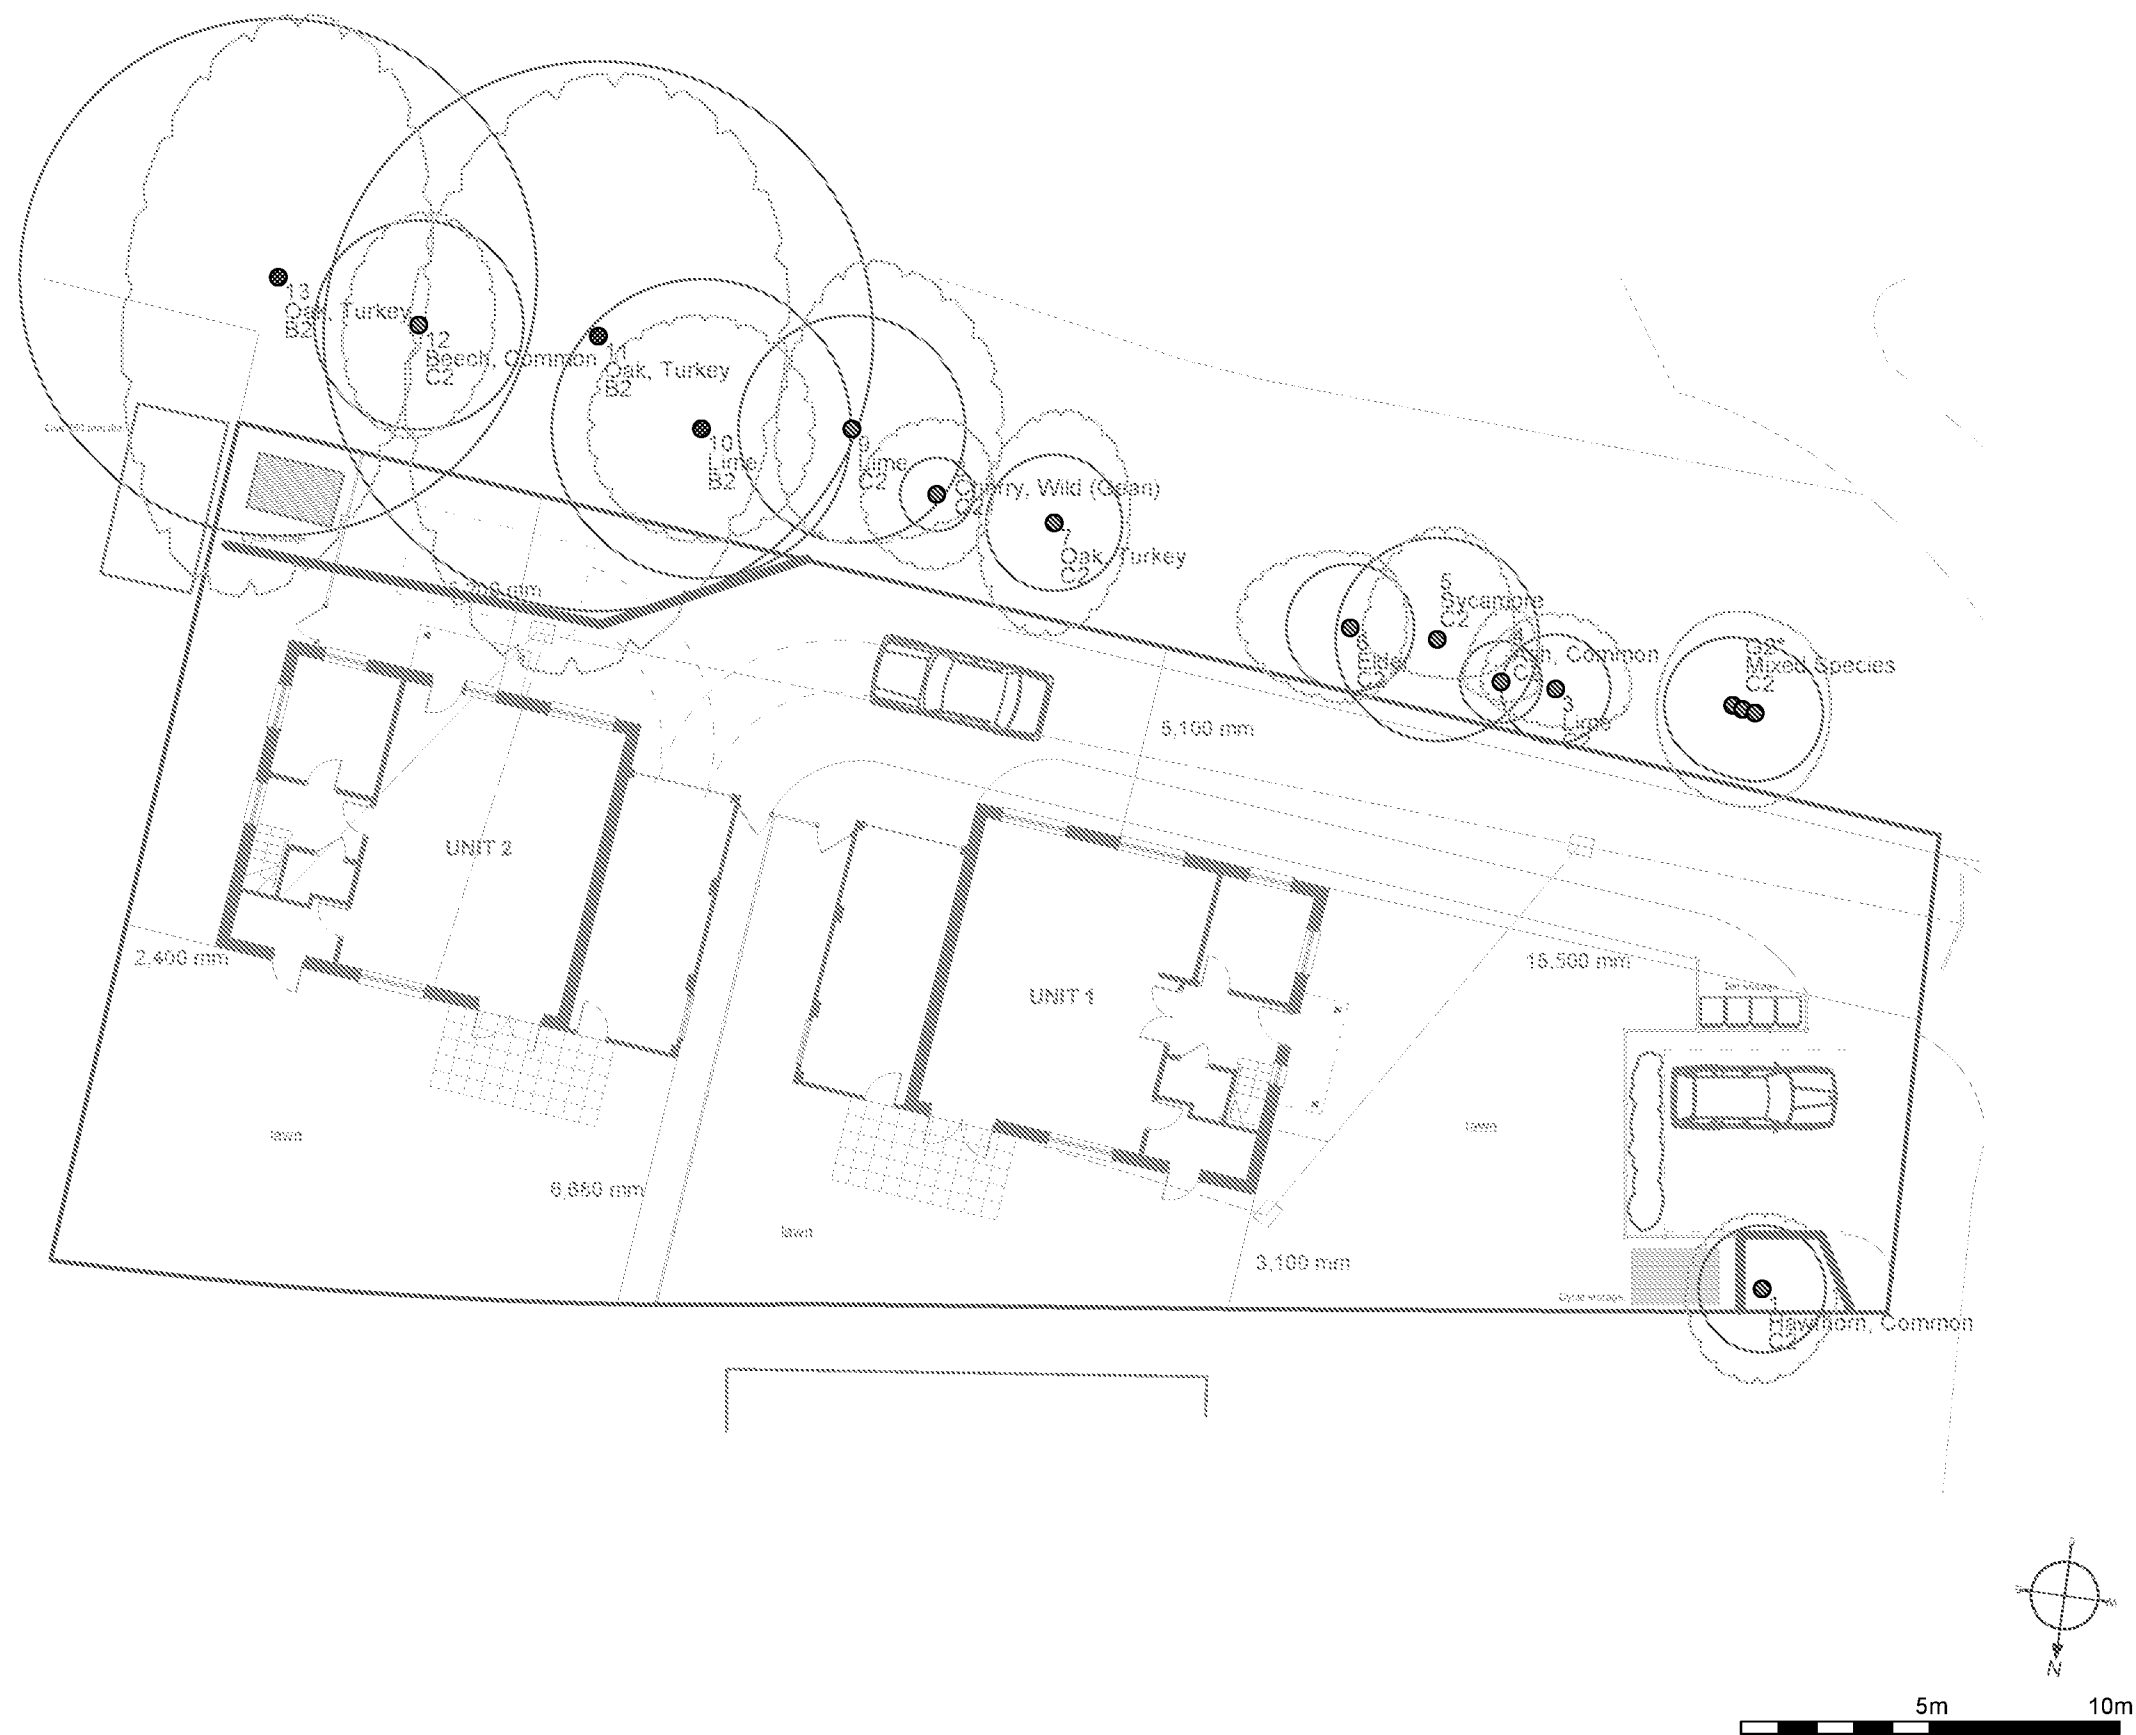

Arbortrack Systems Ltd

The Granary Studio, Crewe Lane, Kenilworth, CV8 2LA
07986 122074 / james.bell@arbortrack.com

Site: 10 Felpham Gardens

Drawing Title: Tree Protection Plan	1-200@A3
Appendix: A	Dec 2018

Key:

Category A	Category	Crown Spread
Category B	Tree Number	
Category C	Species	
Category U	Category	

NOTE: Tree/group numbers marked with an * have approximate locations.

Tree Protection Fencing

Site: 10 Felpham Gardens Bognor Regis

Appendix B

Date: 27th November 2018

BS5837:2012 Tree Survey Schedule

Surveyor(s): James Bell

Ref: jwmb/rpt1/10felphamgdns/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter	Protection Radius	Age Class	Growth Vitality	Structural Condition	B S Cat	Sub Cat	Useful Life	Comments
			N	S	E	W										
1	Hawthorn, Common	7.5	2.5	2	2	2	2.5	140	1.7	Semi-mature	Normal	Good	C	2	20+	Bark wounds
G2	Mixed Species	4	2.5	2.5	2	2	0.5	150 #	1.8	Semi-mature	Moderate	Fair	C	2	10+	Lime, ash sapling & field maple: suppressed by now removed ash; SD's are 160 (FM), 60 (ash) & 130 (lime)
3	Lime	3.5	1	2	2	2	1.75	120	1.4	Young	Normal	Fair	C	2	20+	Weak fork
4	Ash, Common	4	.5	2	1	1	1	90	1.1	Young	Normal	Good	C	2	20+	
5	Sycamore	8	1	3	2	2	1	224	2.7	Early Mature	Normal	Good	C	2	10+	
6	Elder	4.5	2	2	3	1.5	0.5	141 #	1.7	Early Mature	Normal	Good	C	2	10+	
7	Oak, Turkey	6	3	3	2	2	1	150	1.8	Semi-mature	Normal	Fair	C	2	10+	Small elder @ base to N

Site: 10 Felpham Gardens Bognor Regis

Date: 27th November 2018

Appendix B

BS5837:2012 Tree Survey Schedule

Arbortrack Systems Ltd

Surveyor(s): James Bell

Ref: jwmb/rpt1/10felphamgdns/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter	Protection Radius	Age Class	Growth Vitality	Structural Condition	B S Cat	Sub Cat	Useful Life	Comments
			N	S	E	W										
8	Cherry, Wild (Gean)	6	2	2	2	1.5	1.5	81	1.0	Young	Normal	Fair	C	2	10+	Sapling
9	Lime	8.5	3	4.5	2	4	2	250	3.0	Semi-mature	Normal	Good	C	2	20+	Ivy clad Divides to 4 @ 3m
10	Lime	12	3	3	3	3	0	330	4.0	Early Mature	Normal	Good	B	2	10+	Asymmetry (minor) Ivy clad
11	Oak, Turkey	17.5	9	7	5	5	3	606	7.3	Mature	Normal	Good	B	2	20+	Bifurcation @ 1.2m
12	Beech, Common	12	3	3	2	2	1.5	230	2.8	Semi-mature	Normal	Good	C	2	20+	Suppressed by nearby trees
13	Oak, Turkey	17	8.5	7	4	4	3.5	570	6.8	Mature	Normal	Good	B	2	20+	Ivy clad 13m ash 5.5m to E SD=44cm

Site: 10 Felpham Gardens Bognor Regis

Date: 27th November 2018

Appendix B

Recommended Tree Works

Arbortrack Systems Ltd

Surveyor(s): James Bell

Ref: jwmb/rpt1/10felphamgdns/AIAAMS



Tree No.	English Name	Height	Stem Diameter	Crown Spread				BS Cat	Sub Cat	Recommended Works	Comments / Reasons
				N	S	E	W				
11	Oak, Turkey	17.5	606	9	7	5	5	B	2	Cut back overhanging branch tips to North by 2m to improve clearance	Bifurcation @ 1.2m To facilitate development
13	Oak, Turkey	17	570	8.5	7	4	4	B	2	Cut back overhanging branch tips to North by 2m to improve clearance	Ivy clad 13m ash 5.5m to E SD=44cm

Appendix B

Notes on Tree Survey Schedule:

- ¿ Height describes the approximate height of the tree measured in metres from ground level.
- ¿ The Crown Spread refers to the crown radius in metres from the stem centre and is expressed as an average of N SE W aspect if symmetrical.
- ¿ Ground Clearance is the height in metres of crown clearance above adjacent ground level.
- ¿ Clear Stem Height is the distance between trunk base and first branch separation measured in metres.
- ¿ Stem Diameter is the diameter of the stem measured in millimetres at 1.5m from ground level for single stemmed trees. See section 4.6 for detail of treatment for multistems.
- ¿ Protection Radius is a radial distance in metres measured from the trunk centre.
- ¿ Growth Vitality - Normal growth, Moderate (below normal), Poor (sparse/ weak), Dead (dead or dying tree).
- ¿ Structural Condition - Good (no or only minor defects), Fair (remediable defects), Poor - Major defects present.
- ¿ B.S. Category refers to (British Standard 5837:2012 Table 1) and refers to tree/ group quality and value; 'A' - High, 'B' - Moderate, 'C' - Low, 'U' - Unsuitable for Retention.
- ¿ Sub Cat refers to the retention criteria values where 1 is mainly arboricultural qualities, 2 is mainly landscape qualities and 3 is mainly cultural values including conservation.
- ¿ Useful Life is the tree's estimated remaining contribution in years.
- ¿ First Significant Branch (FSB) is the height of the first significant branch above ground level taken at the trunk separation point.

Notes on Recommended Tree Works:

1, 2,3	Urgent (ASAP), Standard (6-12 months), Non-Urgent (2-3 years)
CB	Cut back to boundary/ clear from structure
CL#	Crown lift to given height in meters
CT#%	Crown Thinning by identified %
CCL	Crown clean (remove deadwood/ crossing & hazardous branches & stubs)
CR#%	Crown Reduce by given maximum percentage (of outermost branch & twig length)
DWD	Remove deadwood
Fell	Fell to ground level
FInv	Further Investigation (generally with decay detection equipment)
Pol	Pollard or re-pollard
Mon	Monitor ongoing condition (annually by staff/ owners & every 2-3 years by consultant). Svr Ivy/ Clr Bs Sever Ivy/ clear base and re-inspect base/ stem for concealed defects

Appendix C Tree Protective Fencing Detail (from BS5837:2012)

Figure 2 Default specification for protective barrier


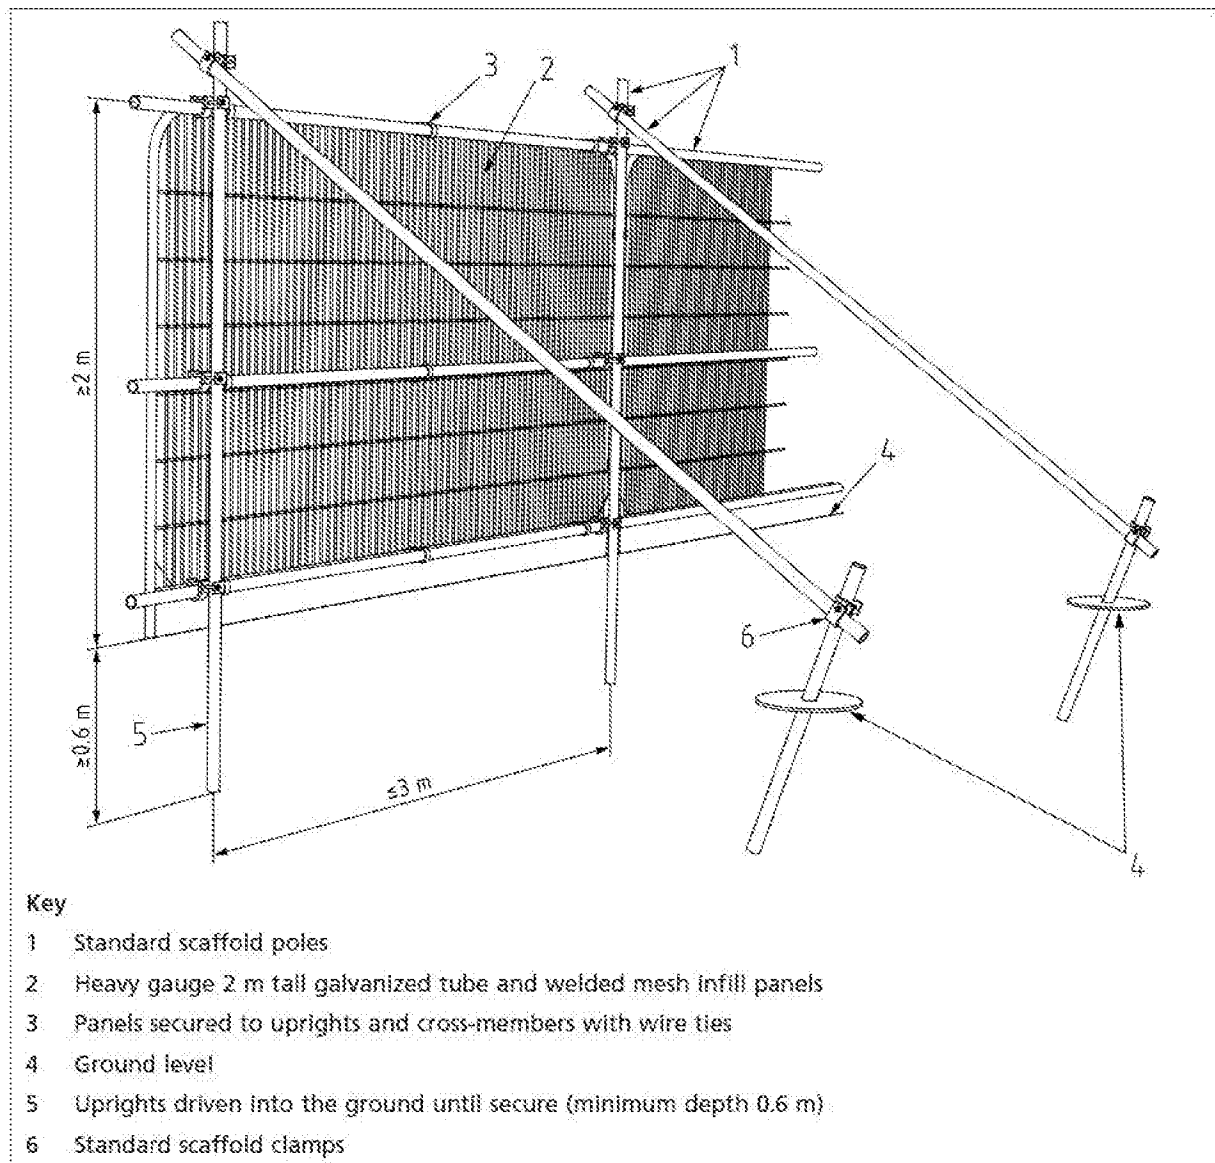


Figure 3 Examples of above-ground stabilizing systems

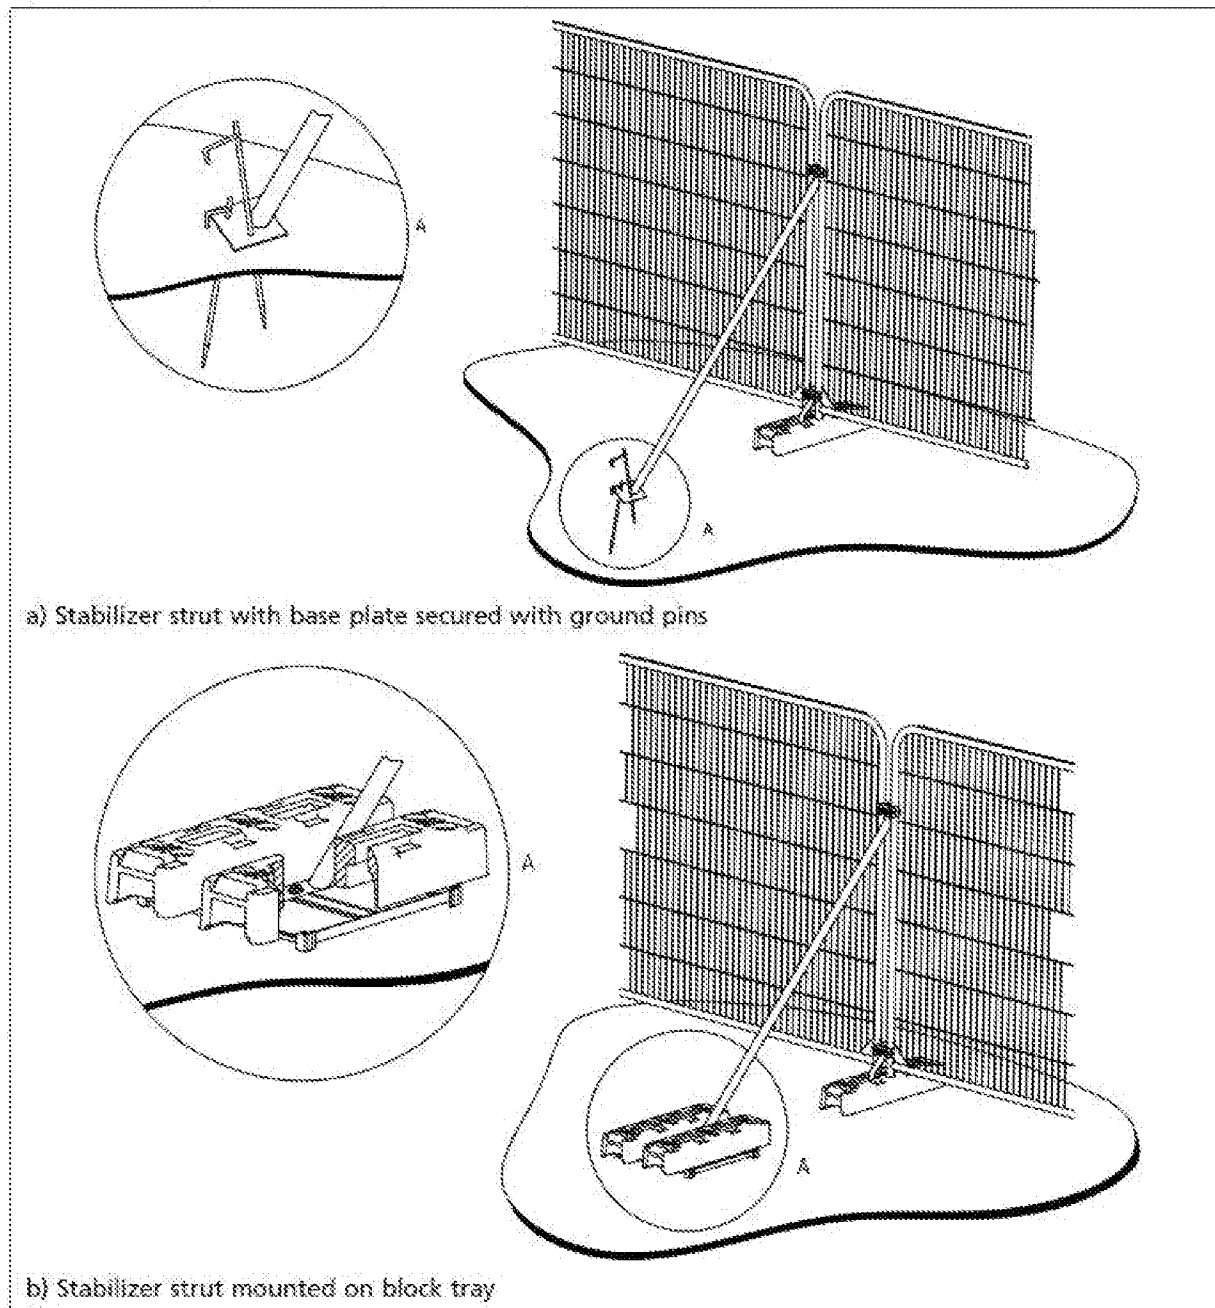

Appendix D

1.0 Glossary of Terms & Abbreviations

Canker	Disease damaged area of a tree, usually caused by fungus or bacteria.
Co-dominant Stem	A stem which has grown in direct competition to the main stem and which has formed a substantial size influencing the appearance of the tree.
Crown Lift	The removal of the lowest branches, usually to a given height. It allows more residual light and greater clearance underneath for vehicles etc.
Crown reduce	The reduction of a tree's height or spread while preserving its natural shape.
Crown thin	The removal of some of the density of a tree's crown, usually 5-25% allowing more light through its canopy and reducing wind resistance.
Deadwood	The removal of all dead, dying and diseased branches from a tree. Also, wood which is dead.
Dieback	Where branches are beginning to show signs of death usually at the tips in the crown.
Epicormic shoots	Small branches that grow in uncharacteristic clusters around the base or the stem of a tree, usually as a result of bad pruning or some other stress factor.
Formative pruning	The trimming of a tree to remove weaknesses and irregularities which may lead to problems. The formative pruning operation is aimed at reducing the potential for future weaknesses or problems within the tree's crown.
Included bark	Where the bark on two adjoining branches or stems is growing tight together, forming a joint with limited physical strength.
Pollarding	A method of tree management in which the main trunk of the tree is cut at about 4m, and the resulting branches are then cropped on a regular basis.
Remedial pruning	The removal of old stubs, deadwood, epicormic growth, rubbing or crossing branches and other unwanted items from the tree's crown. Sometimes referred to as crown cleaning.
Topping	Topping is a form of pruning that removes terminal growth leaving a 'stub' cut end. Topping causes serious health problems to a tree.

2.0 General Guidelines

- 2.1 All work must be to BS 3998:2010 – Tree work-Recommendations
- 2.2 Staff carrying out the work must be qualified, experienced and ideally be Arboricultural Association approved contractors, and should be covered by adequate public liability insurance.
- 2.3 Any defects seen by a contractor or the client that were not apparent to the consultant must be brought to the consultant's attention immediately.
- 2.4 No liability can be accepted by the consultant in respect of the trees unless the recommendations of this method statement are carried out under the supervision of the designated arboriculturist.
- 2.5 It is advisable to have trees inspected by designated arboriculturist regularly. On this site it is recommended that these inspections are made every year.
