

FELPHAM
WEST SUSSEX
PHASE 4 & 5 REPLAN

ARBORICULTURAL
IMPACT
ASSESSMENT
&
METHOD
STATEMENT

ACD
ENVIRONMENTAL

Ecology
Archaeology
Arboriculture
Landscape Architecture



BARRATT
HOMES

Written by:	M Welby
Checked by:	A Bigg
Date:	18.03.2015
Revision:	A:01.03.2016
Ref:	BDWS19795aia_amsA

Table of Contents

1. Executive Summary	3
2. Introduction	4
3. Arboricultural Impact Assessment.....	5
3.1. Overview of proposed development	5
3.2. Planning context	5
3.3. Trees proposed for removal	5
3.4. Demolition, site clearance & archaeology.....	5
3.5. Construction within RPAs	6
3.6. Access and working room within RPAs	6
3.7. Permanent hard surfaces within RPAs	6
3.8. Protection fencing.....	7
3.9. Services.....	7
4. Arboricultural Method Statement	8
4.1. Phasing of operations & site supervision.....	8
4.2. Construction exclusions zone	9
4.3. Tree protection barriers	10
4.4. Ground protection.....	13
4.5. Site storage, parking, welfare facilities, etc.....	15
4.6. Tree surgery and removal	15
4.7. Soft landscaping.....	16
4.8. Installation of underground services	17
4.9. Installation of no-dig surface.....	18
4.10. Excavation within RPAs.....	20
4.11. Installation of boundary fencing within protected areas	21
 Appendix 1: tree:fabric Tree Survey Reference Plan	 22
Appendix 2: Tree Work Schedule.....	23
Appendix 3: Tree Protection Plan	25

1. Executive Summary

- 1.1. ACD was supplied with existing tree data and instructed to assess the subject layout, advise on tree removals and retention, and draft proposals for tree protection during construction in line with recommendations of the British Standard.
- 1.2. This application is for a re-plan of an extant planning consent granted by Arun District Council, ref: FP/224/11 and is for a number of residential units, the layout of which can be seen on the appended Tree Protection Plan.
- 1.3. Trees to be removed are mainly limited to low quality trees that have a limited life and current landscape value. Some of which are covered by a TPO. Any loss that may be felt as a result of their removal will be more than mitigated through the new planting proposed for the site. It must be noted that the majority of the trees to be removed are of category U and would be removed, regardless of any development, as good arboricultural practice.
- 1.4. Some site supervision will be required during the installation of no-dig surfacing, and excavation for a road near to trees.
- 1.5. The arboricultural method statement and tree protection plan include details of all tree protection measures required.
- 1.6. The fencing must be erected after tree removals and surgery but before any demolition or construction contractor enter the site, and before any soil stripping takes place.
- 1.7. There will be no changes in levels, service routing, machine activity, storage of materials or site hut positioning within areas to be protected, and the protective fencing shall remain in position for the duration of the construction process.

2. Introduction

- 2.1. Barratt David Wilson instructed ACD Environmental in March 2015 to prepare the following impact assessment and method statement.
- 2.2. Following the recommendations of the British Standard¹, this report includes the necessary information to support a planning application. It demonstrates that the impact, both direct and indirect, of the proposed development within the site, has been assessed and where appropriate, mitigation and tree protection proposed.
- 2.3. The implementation of the protection methods recommended within this report are critical for ensuring the retained trees are successfully protected through the construction process and must be implemented prior to any work on site.
- 2.4. This assessment is based upon the supplied layout drawing, ref: SITE LAYOUT 29 - 2016 RANGE and tree survey data from *tree:fabrik* ref: tf 1007/TS/100, dated February 2015.
- 2.5. The controlling authority is Arun District Council, who can be contacted at: Arun District Council, Civic Centre, Planning Services, Maltravers Road, Littlehampton, BN17 5LF, Tel: 01243 863141.
- 2.6. This assessment considers the impact of the development on the constraints posed by the retained trees (both beneath ground: the root protection area (RPA), and above ground: the canopy).
- 2.7. Direct impact from development comes in six main forms: 1) Surface installation within RPAs, 2) Root loss from excavation for foundations, drainage and other utilities within RPAs, 3) Soil stripping, removal and level changes within RPAs, 4) Excessive access facilitation pruning to retained trees, 5) Soil compaction from storage and vehicle movements within RPAs, 6) Soil contamination.
- 2.8. Indirect impact can come from changes to the site hydrology, future pressure to prune or fell, failure of trees exposed by removal of neighbouring trees, and other environmental changes which can take several years to manifest.
- 2.9. The RPA for each tree represents a minimum area in m² that should be left undisturbed around each retained tree. This is initially represented by a circle but is often adjusted to account for constraints to root growth within the site (primarily highways and buildings). It is therefore important to ensure the protection of trees both above and below ground. Recommendations are provided in the British Standard as to the protection of existing trees before, during and after development. This is achieved by ensuring the tree protection plan and arboricultural method statement are implemented before any commencement on site.

¹ BS5837:2012 *Trees in relation to design, demolition and construction- Recommendations*, London: British Standards Institute

3. Arboricultural Impact Assessment

3.1. Overview of proposed development

3.1.1. The existing site is to be developed with a number of residential dwellings, the layout of which can be seen on the appended Tree Protection Plan.

3.2. Planning context

3.2.1. **Tree Preservation Orders/Conservation Area:** TPO F/1/07 covers some trees on the site. TPO reference numbers can be found on the plan next to the tree number.

3.2.2. **Previous planning applications and consents:** There is an extant consent for the site, planning ref: FP/224/11.

3.3. Trees proposed for removal

3.3.1. The trees proposed for removal and cutting back can be found at appendix 2.

3.3.2. In summary these comprise:

- Category B: 1
- Category C: 5 trees and 6 groups (or elements thereof)
- Category U: 13

3.3.3. Apart from the oak T51, all the category C trees listed for removal are of low quality and value and have only limited wider landscape significance with a limited life expectancy. It is noted that some of these trees are covered by the TPO, but given the holistic redevelopment of the entire area, this must be considered acceptable, especially given their low British Standard rating.

3.3.4. The removal of T51, the category B oak, will be more mitigated through the new planting proposed for the site. All remaining moderate to high quality trees are to be retained.

3.3.5. Of the trees listed, the category U trees are in such a poor condition that they are to be removed as good arboricultural practice regardless of any development.

3.4. Demolition, site clearance & archaeology

3.4.1. To ensure damage does not occur to trees highlighted for retention, tree protection fencing must be erected before ANY plant/vehicles entering site whatsoever. This should be subject to a pre-commencement site meeting between the developer, their project arboriculturist and a representative from the Local Authority.

3.4.2. No special demolition procedures need be observed on this site, other than respecting the tree protection fencing.

3.5. Construction within RPAs

3.5.1. The construction of all buildings is proposed outside the RPAs of retained trees.

3.5.2. The construction of the garages for plots 61-64 & 69, the corner of plot 87 encroaches slightly into the RPAs of adjacent trees. This encroachment is considered marginal and will not be to the detriment of the trees. Therefore special construction measures or adjustment of the plans are NOT required.

3.5.3. The corner of plot 67 encroaches slightly into the RPAs of adjacent trees. This encroachment is considered marginal and will not be to the detriment of the trees. Therefore special construction measures or adjustment of the plans are NOT required.

3.5.4. The adopted design must be approved for use by the project arboriculturist, detailed in the arboricultural method statement, and installed under their supervision

3.6. Access and working room within RPAs

3.6.1. Space is required for scaffold erection and working room within the RPA of Tx. Access is required across the RPA of Tx. Following the recommendations of 6.2.3 of the British Standard, ground protection will be employed to retain the underlying soil structure and avoid detriment to roots. This must be installed as per the method statement, and signed off by the project arboriculturist prior to the start of any work.

3.6.2. However, given the operational issues with implementing ground protection, an alternative solution is proposed, in that the protection areas is extended contiguous to the RPA². We are comfortable with this approach and that it will not be deleterious to the health of the tree. Nonetheless, should the Council wish to see the installation of ground protection, this can be enforced by a suitable worded planning condition.

3.7. Permanent hard surfaces within RPAs

3.7.1. In section 7.4 of the British Standard, permanent hard surfacing within the RPAs of retained trees is addressed, and recommendations made.

3.7.2. The parking bays for plots 97 & 97, the garden path for plot 97, the surface in front of plots 100 & 101, will require no-dig surfacing to avoid damage to underlying roots.

3.7.3. The main road runs past two oak trees T25 & 26 and will not be able to be installed using no-dig surfacing, partly due to the approved drainage runs underneath it, but also due to the restrictions applied by the highways department on road construction. Therefore the excavation of the road will be supervised and any roots that are found will be cleanly severed as per the appropriate section of the following method statement.

² Section 5.3a). *BS5837:2012 Trees in relation to design, demolition and construction- Recommendations*, London: British Standards Institute.

3.8. Protection fencing

3.8.1. Figure 2 of the British Standard recommends a standard fencing design for tree protection. This is a weld mesh panel design, mounted upon a well-braced scaffold framework. This is perfectly adequate for this site and all the retained trees can be suitably protected by its erection before any works start on site whatsoever.

3.9. Services

3.9.1. It is fundamental to tree protection that infrastructure design is sensitively approached, as trenching close to trees may damage roots and affect tree health and stability. Details of services have not been provided at the time of writing. The Tree Protection Plan, showing the constraints posed by retained trees will be passed to the infrastructure engineers to inform their design, ensuring that all services avoid areas of potential conflict. As per Figure 1 of the British Standard, once further details become available as part of the detailed/technical design for the site, the TPP and AMS may need to be revised to incorporate service details for inclusion in the tender documentation.

4. Arboricultural Method Statement

TO BE READ IN CONJUNCTION WITH THE APPENDED TREE PROTECTION PLAN REF: BDWS19795-03B

4.1. Phasing of operations & site supervision

4.1.1. The tree protection and other arboriculturally related works must be carried out in the following order:

Operation	Present	Notes
1 Pre-start meeting	ACD, site manager, groundwork, foreman, demolition foreman	To 'sign-off' protection prior to any plant activity, demolition & groundworks on site
2 Tree removals & surgery	Tree contractor	See Tree Protection Plan for trees to be removed
3 Protection barriers erected	Fencing contractor	See Tree Protection Plan for position and type of barriers
4 Supervised excavation from new road close to T25 & 26	ACD, groundwork contractor, site manager	See section 4.10 of method statement
5 No-dig path installation	ACD, groundwork contractor, site manager	See section 4.9 of method statement
6 Removal of protection barriers and landscape work	ACD, landscape contractor, site manager	See section 4.7 of method statement

4.1.2. Supervision is required should any unplanned access and/or work be required in the construction exclusion zone.

4.1.3. Supervision will require the arboriculturist to be present throughout the task, to ensure all the arboricultural objectives are met. If the task is to take a long period of time, provided the arboriculturist is satisfied, and after an initial 'tool-box talk', the supervision may be reduced to telephone contact between the site foreman/contractor and arboriculturist.

4.2. Construction exclusions zone

4.2.1. Barriers and/or ground protection must be used to protect all retained trees before any machinery or materials are brought onto the site, and before any demolition, development or stripping of soil commences.

4.2.2. Where all activity can be excluded from the RPA, vertical barriers must be erected to create the construction exclusion zone (CEZ). The default position of which is shown on the appended Tree Protection Plan.

4.2.3. Where, due to site constraints, construction activity cannot be fully or permanently excluded from all, or part of a tree's RPA, appropriate ground protection can be installed.

4.2.4. It is the responsibility of everyone engaged in the construction process to respect the tree protection measures and observe the necessary precautions within and adjacent to them.

4.2.5. Inside the exclusion zone, the following shall apply:

- No mechanical excavation whatsoever.
- No excavation by any other means without arboricultural site supervision.
- No hand digging without a written method statement having first been approved by the project arboriculturist.
- No lowering of levels for any purpose (except removal of grass sward using hand tools).
- No storage of plant or materials.
- No storage or handling of any chemical including cement washings.
- No vehicular access.
- No fire lighting.

4.2.6. In addition to the above, further precautions are necessary adjacent to trees:

- No substances injurious to tree health, including fuels, oil, bitumen, cement (including cement washings), builders sand, concrete mixing and other chemicals shall be stored or used within or directly adjacent to the protection area of retained trees.
- No fire shall be lit such that flames come within 5m of tree foliage.

4.3. Tree protection barriers

4.3.1. The construction exclusion zone will be protected as per the appended tree protection plan that shows the default alignment of the tree protection barriers, to be installed prior to any of the following taking place:

- Archaeology
- Demolition
- Plant and material delivery
- Soil stripping
- Utility installation
- Construction works
- Landscaping

4.3.2. Stages for installation of barriers:

- 1) Hand clearance of any vegetation to allow clear working access.
- 2) Setting out of node points
- 3) Barriers erected
- 4) Site meeting with project arboriculturist to 'sign-off' tree protection fencing.
- 5) Site accessible to demolition/construction traffic

4.3.3. Once erected, all barriers will be regarded as sacrosanct, and will not be removed or altered without prior recommendation by the project arboriculturist and approval of the local planning authority.

4.3.4. The default barrier construction is suitable for areas of high intensity development, and shall comprise of interlocking weld-mesh panels, well braced to resist impacts by attachment to a scaffold framework that is set firmly into the ground. A detailed specification can be found on the TPP.

4.3.5. The images below are alternative barrier designs that have been successfully used on site and that ACD are happy to support if a variation from the default style is required. If such a variation is necessary, the approval of the project arboriculturist will be obtained prior to any implementation on site.

4.3.6. Once barriers and/or ground protection have protected the exclusion zone, construction work can commence.

4.3.7. All weather notices should be erected on the barriers (for example see figure below).



Tree protection sign (download from www.acdenv.co.uk)



Weld-mesh panels on scaffold uprights



Weld-mesh panels on wooden posts



Chain-link on angle-iron uprights

4.4. Ground protection

4.4.1. If required, ground protection is to be installed as follows. It must be capable of supporting the expected loads and avoiding rutting, compaction and damage to the soil: as advised in section 6.2.3 of the British Standard.

4.4.2. Stages for ground protection installation:

- 1) No plant machinery to be used in the area of ground protection for whatever reason
- 2) Discuss procedure with project arboriculturist
- 3) Dismantle primary TPF and re-erect in secondary location as shown on TPP (if required)
- 4) Any shrubs, saplings or trees to be removed, are to be cut, or ground out to just below ground level rather than grubbed or winched out, which can damage roots of retained trees.
- 5) Lay woven geotextile over existing ground surface by hand
- 6) Cover the area with compressible layer, woodchip for example, using hand tools only
- 7) Cover compressible layer with side butting scaffold boards or plywood boards
- 8) Confirm surface is acceptable for use with project arboriculturist
- 9) Area ready for construction access


4.4.3. Any scaffolding required within the area will be erected with the uprights placed on spreader boards.

4.4.4. The boarding will be left in place until the construction works are finished.

4.4.5. A single thickness of boarding laid on the soil surface will provide sufficient protection for pedestrian loads. However, for wheeled or tracked construction traffic movements within the RPA, ground protection will involve the use of temporary cellular confinement systems, reinforced concrete slabs or track-board systems details of which are to be specified by the project engineer and approved for use by the project arboriculturist and local authority before construction commences.

4.4.6. Track-boards can be sourced from Trakmats Europe Ltd, 0845 6435388, www.trakmatseurope.com, or groundguards.com

4.4.7. There is to be no-excavation within ground protection area whatsoever. This includes installation of services and associated utilities.

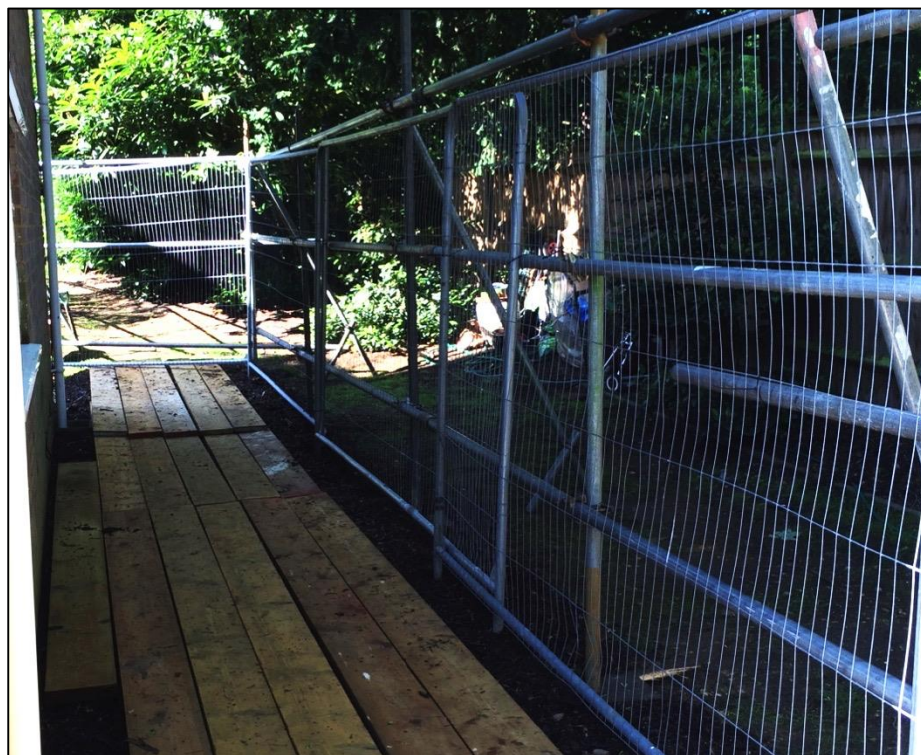

Scaffold board pedestrian ground protection



Vehicular ground protection trackway

4.5. Site storage, parking, welfare facilities, etc.

4.5.1. The site will require provision for; site storage, contractor parking, welfare facilities, temporary services/drainage, material drop off points, etc.

4.5.2. It is acceptable to place site cabins and walkways within the CEZ provided they are installed sensitively:

- Cabins must be placed on sleepers (or similar) to spread the load, avoiding point loading and associated soil compaction.
- The delivery of cabins should ensure that any unloading via 'hi-ab' crane can be carried out without impact on the crowns of retained trees.
- Walkways, if required, should be installed as per the ground protection specification.
- Any utilities for site compounds must be run above ground. For example, WC foul pipes/drainage and temporary electrical connections.

4.5.3. It is imperative that if cabins and walkways are installed, that fencing is erected to limit access to the protected areas. If amendments are made, the project arboriculturist should sign off the proposals prior to their implementation.

4.5.4. Contractor parking, storage and parking areas should be sited outside the CEZ.

4.6. Tree surgery and removal

4.6.1. All trees to be removed are indicated on the TPP, and listed at appendix 2.

4.6.2. If any further surgery work is proposed, details will be submitted to, and approved by, the council, before being carried out.

4.6.3. All work will be carried out in accordance with BS3998³ industry best practice and in line with any works already agreed with the council.

4.6.4. The tree surgeon shall ideally be chosen from The Arboricultural Association's Approved Contractor list. All work shall be undertaken at the appropriate time and with the consent and approval of the site agent.

4.6.5. The statutory protection^{4 5} will be adhered to. If further advice is required, particularly if bats are discovered during tree work, it will be obtained from Natural England or other competent persons and recommendations adhered to.

³ BS3998:2010- *Recommendations for Tree Work*. London: British Standards Institute

⁴ *Wildlife and Countryside Act*. (1981) London: HMSO.

⁵ *Countryside and Rights of Way Act*. (2000) London: HMSO.

4.6.6. The stumps of any trees removed from within the Construction Exclusion Zone or the RPAs of retained trees will be either cut flush to ground level and left in situ or ground out using a stump grinder. They will not be winched out.

4.7. Soft landscaping

4.7.1. All landscaping and associated ground preparation within exclusion zones will be carried out sensitively to ensure root damage is mitigated as much as is practicable. At no time is any heavy plant to be used within any protected area. Removal of existing vegetation will be carried out by hand. Turf may be removed using a mechanical turf stripper or with hand tools.

Turfing

4.7.2. Stages for turfing gardens and open spaces:

- 1) No plant/machinery to be used in the area for whatever reason.
- 2) Remove TPF to allow access to area.
- 3) Re-erect TPF to secondary location (if required and shown on plan).
- 4) Do not reduce any high spots or excavate in any way.
- 5) Existing poor quality turf may be removed with a turf stripper.
- 6) Use good quality top-soil to level any low-lying areas and hollows, and provide a fine tilth to lay turf on. This imported soil must not result in a level increase of more than 100mm in any area.
- 7) Import turves by hand in wheelbarrow.
- 8) Lay turves.

Planting

4.7.3. Should the soil be compacted or have a poor structure that may hinder the development of any new planting, soil decompaction techniques may be used upon consultation with the project arboriculturist.

4.7.4. Stages for planting within tree protection areas:

- 1) No plant machinery to be used in the area for whatever reason.
- 2) Remove TPF to allow access to area.
- 3) Re-erect TPF to secondary location (if required and shown on plan).
- 4) Remove existing vegetation by hand, turf may be removed using a mechanical turf stripper.
- 5) Do not reduce any high spots or excavate in any way.
- 6) Import good quality top-soil by hand (with wheelbarrow) into area.
- 7) Level to a depth of no more than 100mm with hand tools.
- 8) Dig individual planting pits for each plant by hand (including hedging which must not be trench planted).
- 9) Any mulch should also be imported and spread by hand.

4.7.5. No works will be carried out within any protected areas if the soil moisture is of a level likely to allow compaction to occur.

4.8. Installation of underground services

4.8.1. Mechanical trenching for the installation of underground apparatus and drainage severs any roots present and can change the local soil hydrology in a way that adversely affects the health of the tree. For this reason, particular care should be taken in the routing and methods of installation of all underground apparatus. Wherever possible, apparatus should be routed outside RPAs. Where this is not possible, it is preferable to keep apparatus together in common ducts. Inspection chambers should be sited outside the RPA.

4.8.2. Where underground apparatus is to pass within the RPA, detailed plans showing the proposed routeing should be drawn up in conjunction with the project arboriculturist. In such cases, trenchless insertion methods should be used: Microtunnelling, Surface-launched directional drilling, Pipe ramming or Impact moling (see BS5837:2012 Table 3), with entry and retrieval pits being sited outside the RPA. Provided that roots can be retained and protected, excavation using hand-held tools might be acceptable for shallow service runs. If this is the case, the following methodology must be followed:

4.8.3. Stages for installing services by hand within tree protection areas:

No plant machinery to be used in the area for whatever reason

- 1) Contact project arboriculturist to hold pre-start site meeting and 'toolbox' talk before starting work.
- 2) Remove just enough tree protection fencing to allow access to area and facilitate trenching.
- 3) Remove any surface vegetation or existing hard surfaces using hand tools.
- 4) Using an air-pick excavate the trench, keeping to minimum dimensions required.
- 5) Roots occurring in clumps of 25 mm diameter and over are encountered they will be retained, and kept damp by covering with hessian (re-wetted as required). If required, these should be severed only following consultation with an arboriculturist, as such roots might be essential to the tree's health and stability.
- 6) Feed in services.
- 7) Back fill trench with 200-300mm depth of excavated soil, or a mixture of excavated and imported top-soil to BS3882 (BSI, 2007), firming down with heels.
- 8) Repeat step 7 until trench is filled.
- 9) Re-erect tree protection fencing as per approved plan.


4.8.4. The method of excavation above, for trenching within RPAs, is using air excavation. This tool utilises compressed air to remove soil from around tree roots causing minimal damage and can be run off a typical site compressor. ACD can provide details of contractors supplying air excavation services if required.

4.8.5. Alternatively trenchless technology, such as thrust boring can be used in some instances and is particularly effective as it can pass directly under the tree, at a depth which is likely to avoid almost all impact on roots of the subject tree. As no access/thrust pits will be located within the RPAs of the subject trees, the need for arboricultural supervision is limited.

4.8.6. Reference can be made to NJUG Vol 4⁶ for guidance, but any approach must be approved by the project arboriculturist and brought to the attention of the local authority tree officer.

4.9. Installation of no-dig surface

4.9.1. To ensure that tree roots, within the ground under this proposed surface, continue to survive during and after construction a cellular system such a CellWeb⁷ of 75-200mm depth is to be used.

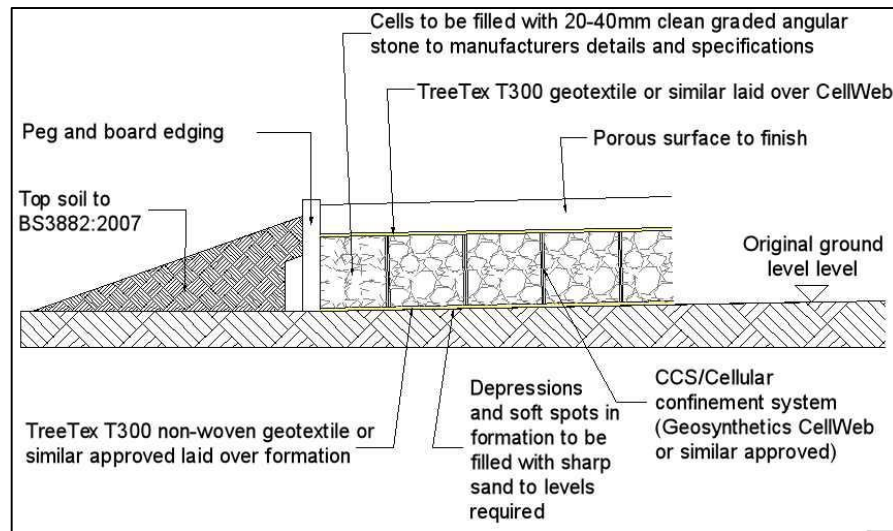

No-dig cross-section

4.9.2. Stages for Installation of the cellular confinement surface:

- 1) Contact project arboriculturist to hold pre-start site meeting and 'toolbox' talk before starting work
- 2) Dismantle TPF and re-erect in secondary location as shown on TPP
- 3) Remove existing vegetation by using a specific herbicide (as advised by a specialist) or manual removal with hand tools only. Agreed removal of shrubs, saplings or trees, within the protected areas of retained trees are to be cut, or ground out to just below ground level rather than grubbed or winched out, which can damage roots of retained trees.
- 4) Retain all original ground levels after vegetation removal. No excavation whatsoever.
- 5) Remove any existing hard surfaces (paving, tarmac etc.) Hand tools should be used if possible. If machinery is required for this operation, it must be used only on existing surfaces or outside the protection areas and tree canopies (approval from project arboriculturist must be sought before using machinery). The sub base of

⁶ National Joint Utilities Group. (2010). *Volume 4: NJUG Guidelines For The Planning, Installation And Maintenance Of Utility Apparatus In Proximity To Trees (Issue 2) – Operatives Handbook*. NJUG.

⁷ Geosynthetics Ltd, 01455 617139, www.geosyn.co.uk

existing surfaces or foundations should be left in situ where possible to avoid unnecessary root disturbance and provide a base for the new surface.

- 6) Install a non-woven Geotextile (such as TreeTex T300) directly over soil grade level (levelled where necessary, by non-compacted washed sand) and fix in place.
- 7) Lay the cellular system over the Geotextile, which is secured open under tension during the infill process with steel staples or wooden pegs.
- 8) Install kerbs and edgings directly on top of existing soil grade level. For light structures, a treated peg and board may be acceptable. For more substantial structures, railway sleepers, haunched concrete with road pins, drilled kerbstones, gabions or cast in situ kerbs will be appropriate.
- 9) Fill the cellular system ensuring any machinery works only on already filled areas. Typical infill consists of no fines angular granular material 20-40mm, which will remain un-compacted.
- 10) Cover with a non-woven Geotextile (such as TreeTex T300).
- 11) Install porous wearing surface.
 - Small Block Paving
 - Washed Gravel
 - Porous Asphalt

4.9.3. Any variation to the above specification must meet the following design criteria for low-invasive surfaces to provide the conditions for continued tree survival and growth:

- Maintain oxygen diffusion through new surface to rooting area (5-12% by volume⁸)
- Maintain sufficient passage of water to the rooting area (12-40% by volume⁹)
- Avoid compaction by maintaining a soil structure sufficient to sustain root growth (soil bulk density below 1.4g/cc¹⁰).

4.9.4. Site analysis of the soil type and its structural characteristics will be required prior to determining the specific depth of products to be adopted for example, footpaths normally require a depth of 75mm and, 100mm to 200mm depths are used for residential driveways, while greater depths may be required for the passage of heavier traffic such as for construction access and delivery vehicles.

4.9.5. If ground levels are to be raised more than 150mm this should be achieved by the use of a granular material, which does not inhibit vertical gaseous diffusion. For example: no-fines gravel, washed aggregate, structural soil (min. 20% sand content) or cobbles.

⁸ Smith, R. J. (2006). *Tree Roots in the Built Environment*. HSO

⁹ Coder, D. K. (2000). *Tree Root Growth Requirements*. University of Georgia

¹⁰ Harris, C. M. (2004). *Arboriculture, Tree Management of Shade Trees and Vines*.

4.10. Excavation within RPAs

4.10.1. Stages for excavation within RPAs:

- 1) Contact project arboriculturist to hold pre-start site meeting, 'toolbox' talk and supervise the operation.
- 2) Remove TPF to allow access to area (if required).
- 3) Identify sensitive area.
- 4) Remove hard surface if necessary (see relevant section of this report).
- 5) Excavate with no-tines bucket, or by hand, under close supervision.
- 6) If roots are found, clear by hand around them.
- 7) If roots found are greater than 25mm diameter then cover with damp hessian and keep moist until backfilled. If excavation requires all roots to be severed then proceed as below.
- 8) Cleanly sever roots with bypass secateurs, loppers or pull cut saw at right angles to root. Avoid tearing or ripping the root.
- 9) Backfill as soon as possible to cover cut root ends.

24.2. If, for whatever reason, the project arboriculturist feels that a tree's stability has been compromised during the operation, then the LPA shall be contacted and the arboricultural officer (or appropriate landscape officer) notified. A decision can then be made as to the best way forward.

4.11. Installation of boundary fencing within protected areas

4.11.1. Stages for installing wooden fence posts:

No plant machinery to be used in the area for whatever reason

- 1) Contact project arboriculturist to hold pre-start site meeting and 'toolbox' talk before starting work.
- 2) Remove TPF to allow access to area.
- 3) Dig postholes using hand tools, avoiding damage to the protective bark covering larger roots. Roots smaller than 25mm diameter may be pruned back using either secateurs or a hand saw, leaving a clean cut.
- 4) Damage or severance of roots above 25mm diameter must be avoided. If roots of this size are discovered, the hole should be relocated. If there are a large number of such roots it may be necessary to relocate the hole by half a fence panels length and adjust the fence panels accordingly.
- 5) Line hole with non-porous lining, for example durable polythene bag.
- 6) Insert post and fill post-hole with concrete to just below ground level.
- 7) Trim polythene to ground level and fill with clean topsoil.



Mark Welby Tech Cert (ArborA), Dip Arb (RFS), FArborA
Director
18th March 2015



LIMITATIONS OF USE AND COPYRIGHT

This assessment has been prepared for Barratt David Wilson. All rights in this report are reserved. No part of it may be reproduced or transmitted, in any form or by any means, electronic, mechanical, photocopying, recording or otherwise, or stored in any retrieval system of any nature, without our written permission. Its content and format are for the exclusive use of the addressee in dealing with Felpham, West Sussex, Phase 4 & 5 Re-plan. Until all invoices rendered by the Consultant to the Client have been paid in full, the copyright of any documents, forms, statements, maps, plans and other such material will remain vested in ACD Environmental and no unauthorised use of such material may be made by the Client or any person purporting to be acting on his/her behalf. It may not be sold, lent, hired out or divulged to any third party not directly involved in this site without the written consent of ACD Environmental ©

Appendix 1: *tree:fabric* Tree Survey Reference Plan

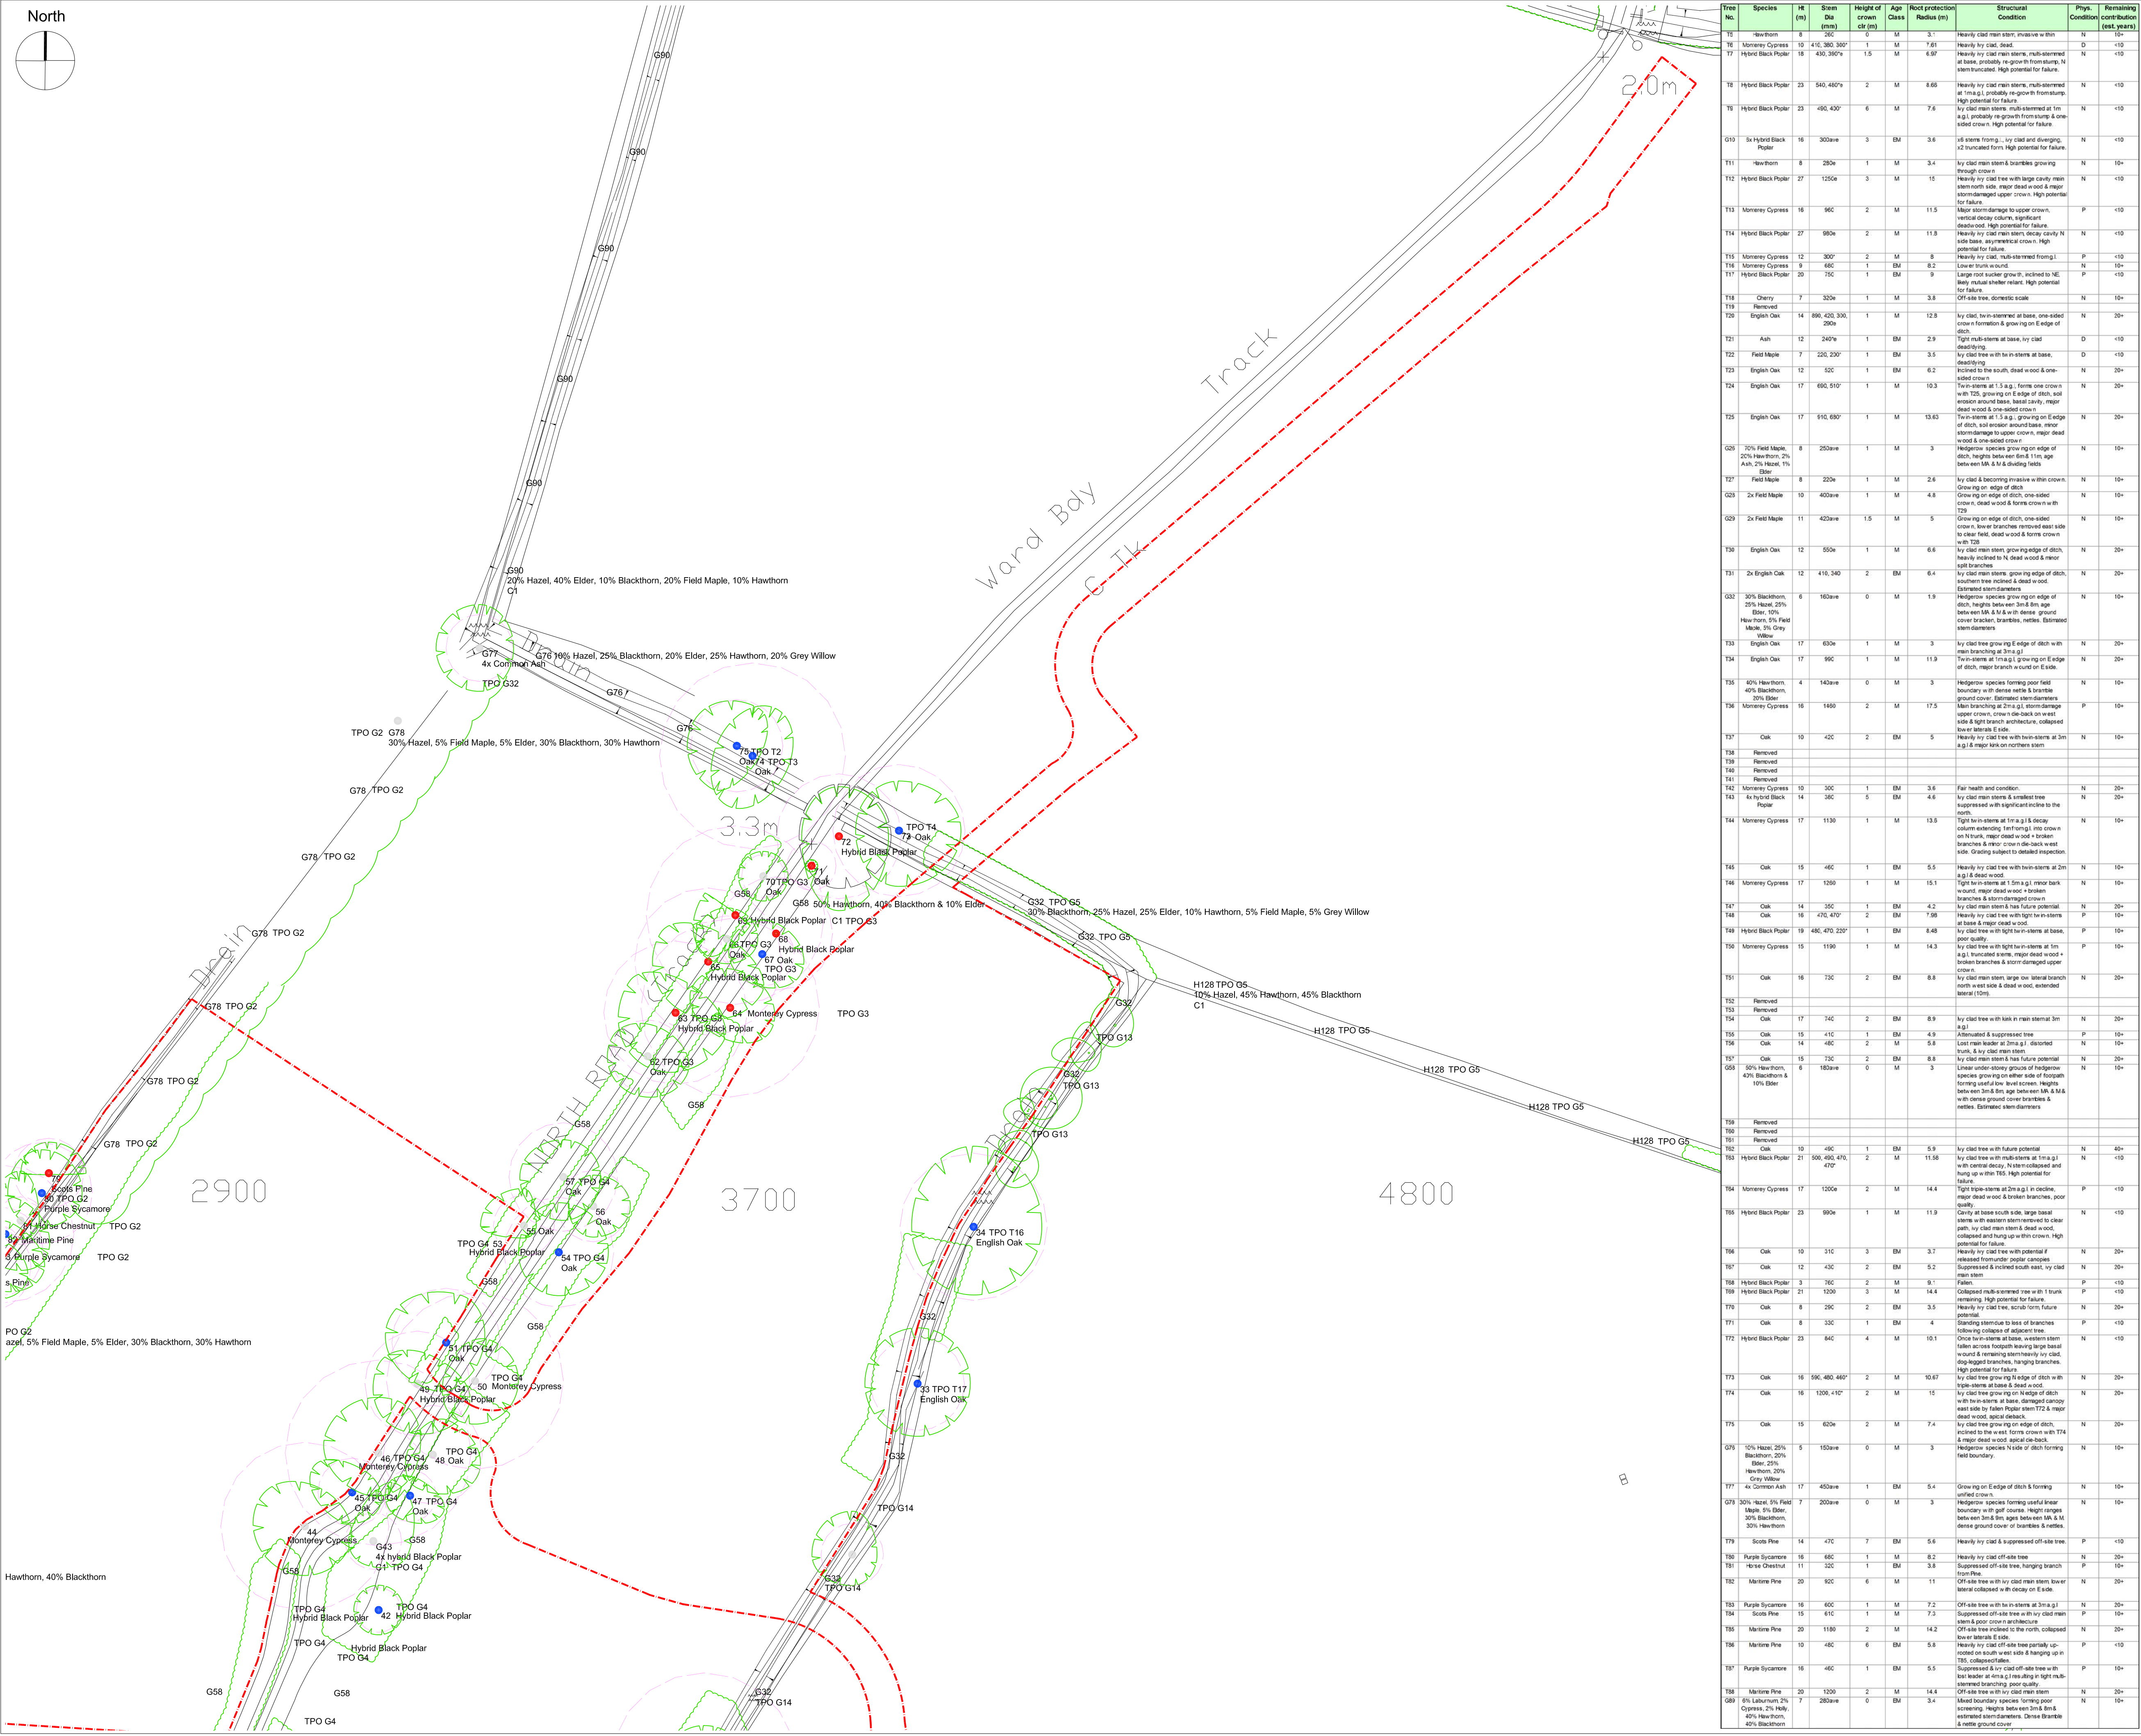

Notes

This drawing is the property of tree:fabrik Ltd. It must not be copied or reproduced without written consent. The original of this drawing was produced in colour - a monochrome copy should not be relied upon. Only figured dimensions are to be taken from this drawing. This is a basic data collection exercise for the sole use of identifying site constraints in context of the planning process and a record of the trees condition at the time of surveying. This is not a vegetation assessment for NH&C guidance or a higher level inspection (full hazard or risk assessment) and no guarantee, either expressed or implied can therefore be given with regards to identification, safety, stability or internal condition. Only trees listed within the adjacent schedule have been subject to re-assessment and updated with this plan.

General

This illustrative plan is intended to inform preliminary site layout & design and should be read in conjunction with the Tree Survey Schedule. Detailed assessment and site measurement may be required prior to final design. The assessment was carried out in accordance with the guidance and recommendations of British Standards 5837: (2012) 'Trees in relation to design, demolition and construction' and good arboricultural practice. Trees identified within this assessment were visually inspected from ground level by a person qualified and experienced in arboriculture. The tree's common name and its dimensions are recorded within the tree survey schedule together with their age, physiological, structural condition and a category code. All observations are confined to that which was visible from the site and areas of public access. Dense ivy/ground vegetation significantly hampered visual assessment of the trees quality and condition. This preliminary assessment may therefore be subject to amendment following additional detailed inspection.

It is recommended that following practical completion, a health & safety inspection of all retained trees is carried out in accordance with the change of land-use and any recommendations or remedial tree works (including deadwood) are implemented.

Site Boundary

Indicative site boundary

Statutory Designations (trees)

Selected trees and groups of trees are subject to Tree Preservation Order (TPO) F-1-07 administered by Arun District Council. As such, written consent must be obtained from the Council prior to carrying out tree works to trees subject to a TPO unless otherwise approved by the Council. The statutory designation of trees may change and it is recommended that the status of trees be checked with the Council prior to carrying out any tree works.

Tree Survey

Tree No. Trunk diameter

Common name

Quality & value of existing tree stock

The quality and value of each tree or group of trees assessed has been categorised in accordance with British Standards 5837 (2012) 'Trees in relation to design, demolition and construction'. The purpose of the tree categorization method is to allow informed decisions to be made concerning which trees should be removed or retained should development occur.

U Category tree: Trees in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years.

B Category tree: Trees of moderate quality and value.

A Category tree: Trees of high quality and value.

C Category tree: Trees of low quality and value.

Young trees with a stem diameter of less than 150mm should be considered for relocation subject to a comparison between costs of the of the various options. Similarly, appropriate mitigation through replacement tree planting elsewhere as part of the development is desirable.

BS Category

Age Class Distribution

Above and Below Ground Constraints

In addition to the tree's quality and condition, consideration needs to be given to the above ground constraints (crown spread) and the below ground constraints (root protection area) the trees pose by virtue of their size and position.

tree:fabrik

Lenten House
16 Lenten Street
Alton, Hampshire
GU34 1BD
T : 01420 593250
F : 01420 544243
E : alan@treefabrik.com

Project

FELPHAM
WEST SUSSEX

Drawing

TREE SURVEY REFERENCE PLAN
PHASE 5 - SHEET 1 of 2

Drawing sheet size - A1

Scale: 1:500 Date: FEB '15 Drawn: AR


Drawing No. tf 1007/TS/100 Revision

Legend

Preliminary
Issued for Planning Approval
Issued for Construction

Issued for Design/Information
Issued for Tender
As Built

Scale: 0 5 10 15 20 25 30 35 40 45 50

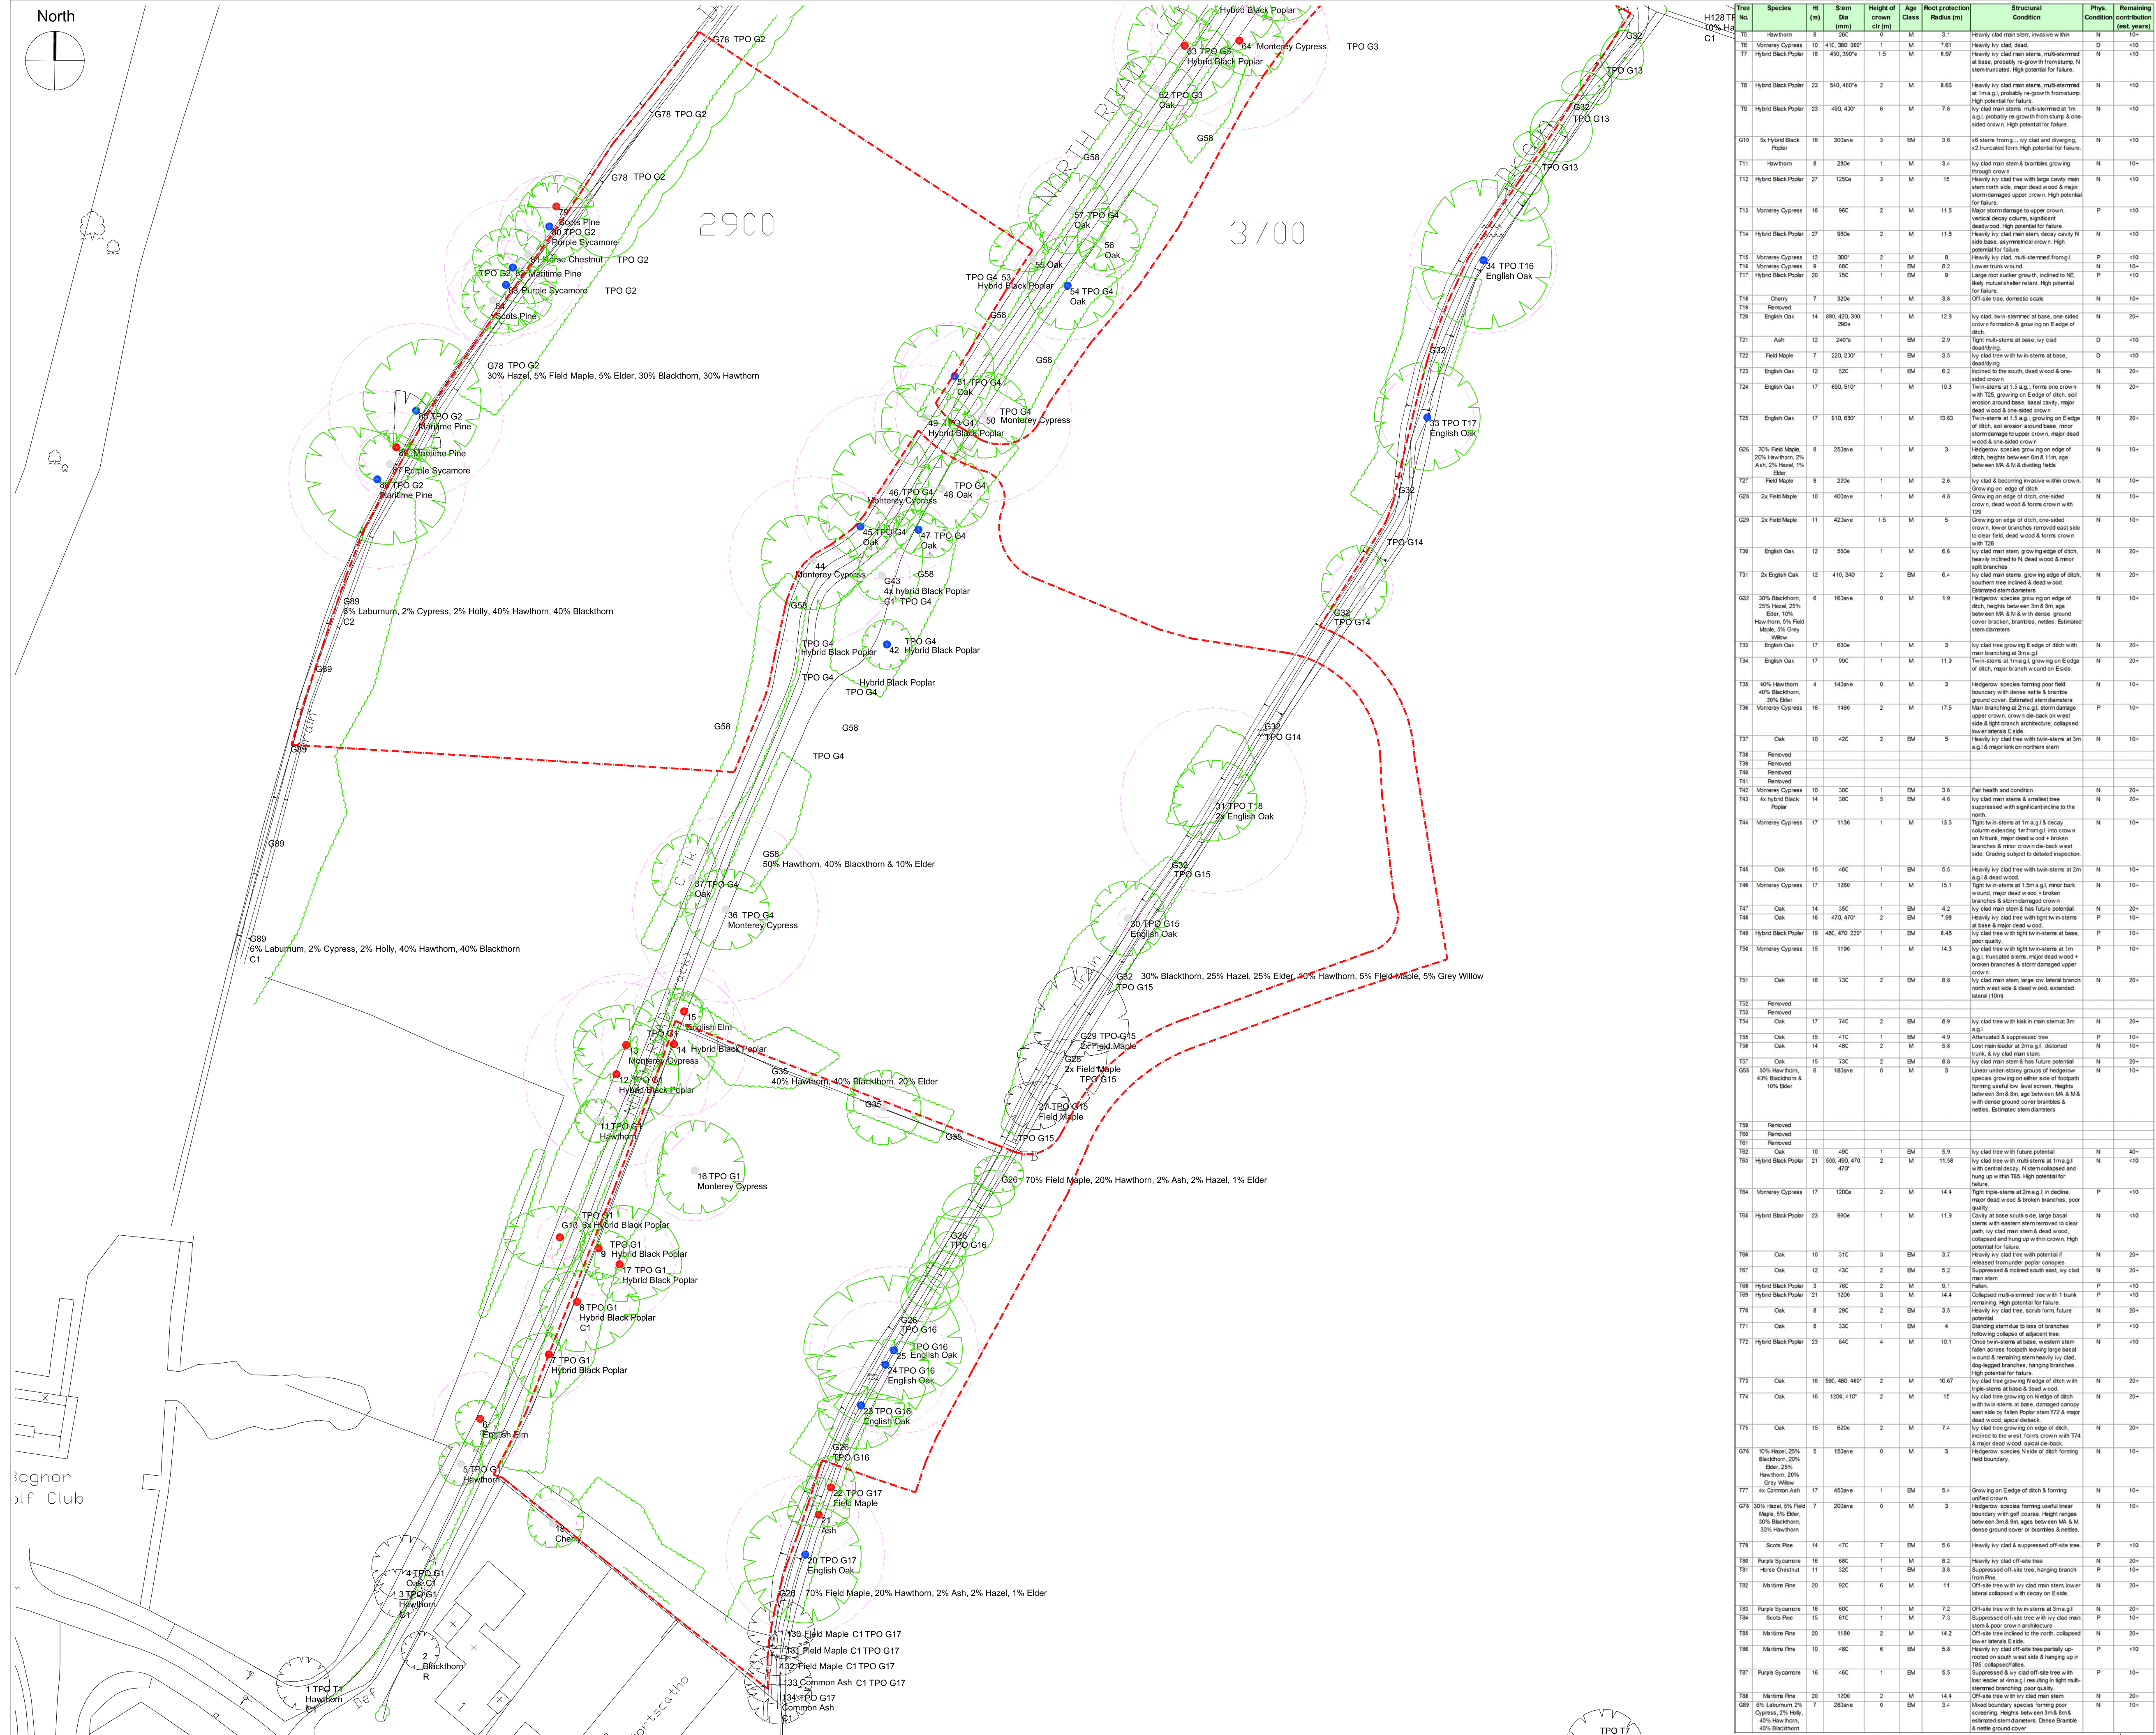

NOTES

This drawing is the property of tree:fabrik ltd. It must not be copied or reproduced without written consent. The original of this drawing was produced in colour - a monochrome copy should not be relied upon. Only figured dimensions are to be taken from this drawing. This is a basic data collection exercise for the sole use of identifying site constraints in context of the planning process and a record of the trees condition at the time of surveying. This is not a vegetation assessment for NNR guidance or a higher level inspection (full hazard or risk assessment) and no guarantee, either expressed or implied can therefore be given with regards to identification, safety, stability or internal condition. Only trees listed within the adjacent schedule have been subject to re-assessment and updated with this plan.

General

The illustrative plan is intended to inform preliminary site layout & design and should be read in conjunction with the Tree Survey Schedule. Detailed assessment and site measurement may be required prior to final design. The assessment was carried out in accordance with the guidance and recommendations of British Standards 5837: (2012) 'Trees in relation to design, demolition and construction' and good arboricultural practice. Trees identified within this assessment were visually inspected from ground level by a person qualified and experienced in arboriculture. The tree's common name and its dimensions are recorded within the tree survey schedule together with their age, physiological, structural condition and a category code. All observations are confined to that which was visible from the site and areas of public access. Dense ivy/ground vegetation significantly hampered visual assessment of the trees quality and condition. This preliminary assessment may therefore be subject to amendment following additional detailed inspection.

It is recommended that following practical completion, a health & safety inspection of all retained trees is carried out in accordance with the change of land-use and any recommendations or remedial tree works (including deadwood) are implemented.

Site Boundary

Indicative site boundary

Statutory Designations (trees)

Selected trees and groups of trees are subject to Tree Preservation Order (TPO) F-1-07 administered by Arun District Council. As such, written consent must be obtained from the Council prior to carrying out tree works to trees subject to a TPO unless otherwise approved by the Council. The statutory designation of trees may change and it is recommended that the status of trees be checked with the Council prior to carrying out any tree works.

Tree Survey

1 Tree No. Trunk diameter

Ash Common name

Quality & value of existing tree stock

The quality and value of each tree or group of trees assessed has been categorised in accordance with British Standards 5837 (2012) 'Trees in relation to design, demolition and construction'. The purpose of the tree categorization method is to allow informed decisions to be made concerning which trees should be removed or retained should development occur.

U Category tree
Trees in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years

B Category tree
Trees of moderate quality and value

A Category tree
Trees of high quality and value

C Category tree
Trees of low quality and value

Young trees

Young trees with a stem diameter of less than 150mm should be considered for relocation subject to a comparison between costs of the of the various options. Similarly, appropriate mitigation through replacement tree planting elsewhere as part of the development is desirable.

BS Category

21 0 22 32

Age Class Distribution

Early Mature 30% Mature 61%

Above and Below Ground Constraints

In addition to the tree's quality and condition, consideration needs to be given to the above ground constraints (crown spread) and the below ground constraints (root protection area) the trees pose by virtue of their size and position.

Crown spread

Preliminary root protection area

Illustrated as an area equivalent to a circle.

The root protection area (RPA) is a design tool indicating the area surrounding a tree that contains sufficient roots and rooting volume to maintain the trees viability, and where the protection of the tree roots and soil structure is treated as a priority.

tree:fabrik

Lenten House
16 Lenten Street
Alton, Hampshire
GU34 1BD

T: 01420 593250
F: 01420 544243
E: alan@treefabrik.com

Project

FELPHAM
WEST SUSSEX

Drawing

TREE SURVEY REFERENCE PLAN
PHASE 5 - SHEET 2 of 2

Drawing sheet size - A1

Scale

1:500

Date

FEB '15

Drawn

AR

Drawing No.

tf 1007/TS/100

Revision

Legend

Preliminary
Issued for Planning Approval
Issued for Construction

Issued for Design/Information
Issued for Tender
As Built

Table

Tree No.	Species	Ht (m)	Stem Dia (mm)	Height of crown (m)	Age Class	Root protection Radius (m)	Structural Condition	Phys. Condition	Remaining (est. years)
15	Hawthorn	8	260	0	M	3.1	Heavily clad main stem, invasive w/ thin	N	<10
16	Monterey Cypress	10	410, 380, 380	1	M	7.61	Heavily ivy clad, dead	D	<10
17	Hybrid Black Poplar	18	430, 300	1.5	M	8.9	Heavily ivy clad main stems, multi-stemmed at base, probably re-grow in front of them. N stem damaged, high potential for failure	N	<10
18	Hybrid Black Poplar	23	540, 480	2	M	8.65	Heavily ivy clad main stems, multi-stemmed at 1m a.g.l, probably re-grow in front of them. High potential for failure	N	<10
19	Hybrid Black Poplar	23	490, 420	6	M	7.6	Ivy clad main stems, multi-stemmed at 1m a.g.l, probably re-grow in front of them. N stem damaged, high potential for failure	N	<10
20	Hybrid Black Poplar	18	300	3	BM	3.6	18 stems forming, ivy clad and diverging, 12 truncated forks. High potential for failure	N	<10
21	Hawthorn	8	280	1	M	3.4	Ivy clad main stem & branches growing through crown	N	<10
22	Hybrid Black Poplar	27	1250	3	M	15	Heavily ivy clad tree with large cavity main stem north side, major dead wood & major storm-damaged upper crown. High potential for failure	N	<10
23	Monterey Cypress	18	980	2	M	11.5	Major storm-damage to upper crown, vertical decay column, significant deadwood. High potential for failure	P	<10
24	Hybrid Black Poplar	27	980	2	M	11.8	Heavily ivy clad main stem, decay cavity N side base, asymmetrical crown. High potential for failure	N	<10
25	Monterey Cypress	12	300	2	M	8	Heavily ivy clad, multi-stemmed from l.	P	<10
26	Monterey Cypress	8	480	1	BM	8.2	Lower trunk wound	N	<10
27	Hybrid Black Poplar	20	750	1	BM	9	Large root sucker growth, inclined to NE base, major shaker rot, high potential for failure	P	<10
28	Cherry	7	320	1	M	3.8	Off-site tree, domestic scale	N	<10
29	Removed								
30	English Oak	14	890, 420, 330, 290	1	M	12.8	Ivy clad, twin-stemmed at base, one-sided crown formation & growing on E edge of ditch	N	<20
31	Ash	12	240	1	BM	2.9	Tight multi-stems at base, ivy clad deadwood	D	<10
32	Field Maple	7	220, 220	1	BM	3.5	Ivy clad tree with twin-stems at base, deadwood	D	<10
33	English Oak	12	520	1	BM	6.2	Inclined to the south, dead wood & one-sided crown	N	<20
34	English Oak	17	690, 510	1	M	10.3	Twin-stems at 1.5 a.g.l, forms one crown w/ 125, growing on E edge of ditch, soil erosion around base, basal cavity, major dead wood & one-sided crown	N	<20
35	English Oak	17	910, 680	1	M	13.65	Twin-stems at 1.5 a.g.l, growing on E edge of ditch, soil erosion around base, minor storm-damage to upper crown, major dead wood & one-sided crown	N	<20
36	25% Field Maple, 25% Hawthorn, 2% Ash, 2% Hazel, 1% Elm	8	250	1	M	3	Hedgehog species growing on edge of ditch, heights between 6m & 11m age	N	<10
37	Field Maple	8	220	1	M	2.6	Ivy clad & becoming invasive w/ thin crown, growing on edge of ditch	N	<10
38	2x Field Maple	10	400	1	M	4.8	Growing on edge of ditch, one-sided crown, lower branches, removed east side to clear field, dead wood & forms crown w/ 125	N	<10
39	2x Field Maple	11	420	1.5	M	5	Growing on edge of ditch, one-sided crown, lower branches, removed east side to clear field, dead wood & forms crown w/ 125	N	<10
40	English Oak	12	550	1	M	6.6	Ivy clad main stem, growing edge of ditch, heavily inclined to N, dead wood & minor split branches	N	<20
41	2x English Oak	12	410, 340	2	BM	6.4	Ivy clad main stems, growing edge of ditch, southern tree inclined & dead wood	N	<20
42	30% Blackthorn, 25% Hazel, 25% Elder, 20% Hawthorn, 5% Field Maple, 5% Grey Willow	6	160	0	M	1.9	Hedgehog species growing on edge of ditch, heights between 3m & 6m age between 1M & 6M w/ dense ground cover bracken, brambles, nettles. Estimated stem diameters	N	<10
43	English Oak	17	630	1	M	3	Ivy clad tree growing E edge of ditch with main branching at 3m a.g.l	N	<20
44	English Oak	17	990	1	M	11.9	Twin-stems at 1m a.g.l, growing on E edge of ditch, major crown decay & E side	N	<20
45	40% Hawthorn, 40% Blackthorn, 20% Elder	4	140	0	M	3	Hedgehog species forming poor field boundary w/ dense nettle & bramble ground cover. Estimated stem diameters	N	<10
46	Monterey Cypress	16	1480	2	M	17.5	Main branching at 2m a.g.l, storm-damage upper crown, crown die-back on west side & light branch architecture, collected lower lateral E side	P	<10
47	Oak	10	420	2	BM	5	Heavily ivy clad tree with twin-stems at 3m a.g.l & major bark on northern stem	N	<10
48	Removed								
49	Removed								
50	Monterey Cypress	10	300	1	BM	3.6	Fair health and condition	N	<20
51	4x Hybrid Black Poplar	14	380	5	BM	4.6	Ivy clad main stems & smallest tree suppressed with significant decline to the north	N	<20
52	Monterey Cypress	17	1130	1	M	13.5	Tight twin-stems at 1m a.g.l & decay column extending 1m from l. into crown on N trunk, major crown decay & broken branches & minor crown die-back west side. Grading subject to detailed inspection	N	<10
53	Oak	15	460	1	BM	5.5	Heavily ivy clad tree with twin-stems at 2m a.g.l & dead wood	N	<10
54	Monterey Cypress	17	1260	1	M	15.1	Tight twin-stems at 1.5m a.g.l, minor bark wound, major dead wood & broken branches & storm-damaged crown	N	<10
55	Oak	14	380	1	BM	4.2	Ivy clad main stem & low future potential	N	<20
56	Oak	16	470, 470	2	BM	7.68	Heavily ivy clad tree with tight twin-stems at base & major dead wood	P	<10
57	Hybrid Black Poplar	19	480, 470, 220	1	BM	8.48	Ivy clad tree with tight twin-stems at base, poor quality	P	<10
58	Monterey Cypress	15	1190	1	M	14.3	Ivy clad tree with tight twin-stems at 1m a.g.l, truncated stems, major dead wood & broken branches & storm-damaged upper crown	P	<10
59	Oak	16	730	2	BM	8.8	Ivy clad main stem, large on lateral branch north west side & dead wood, extended lateral (10m)	N	<20
60	Removed								
61	Removed								
62	Oak	17	740	2	BM	8.9	Ivy clad tree with bark in main stem at 3m a.g.l	N	<20
63	Oak	15	410	1	BM	4.9	Almond & suppressed tree	P	<10
64	Oak	14	480	2	M	5.8	Low main leader at 2m a.g.l, disjunct trunk, & ivy clad main stem	N	<10
65	Oak	15	730	2	BM	8.8	Ivy clad main stem & low future potential	N	<20
66	50% Hawthorn, 40% Blackthorn, 10% Elder	6	160	0	M	3	Linear under-storey groups of hedgehog species growing on either side of footpath forming a low level screen. Heights between 3m & 6m age between 1M & 6M w/ dense ground cover brambles & nettles. Estimated stem diameters	N	<10
67	Removed								
68	Removed								
69	Oak	10	490	1	BM	5.9	Ivy clad tree with future potential	N	<40
70	Hybrid Black Poplar	21	680, 480, 470, 470	2	M	11.58	Ivy clad tree with multi-stems at 1m a.g.l with central decay, N stem collapsed and hung up within TBS. High potential for failure	N	<10
71	Monterey Cypress	17	1200	2	M	14.4	Tight tripe-stems at 2m a.g.l in decline, major dead wood & broken branches, poor quality	P	<10
72	Hybrid Black Poplar	23	980	2	M	11.9	Cavity at base south side, large basal stems with eastern stem removed to clear path, ivy clad main stem & dead wood collapsed and hung up within crown. High potential for failure	N	<10
73	Oak	10	310	3	BM	3.7	Heavily ivy clad tree with potential if released from under-pole canopy	N	<20
74	Oak	12	430	2	BM	5.2	Suppressed & inclined south east, ivy clad main stem	N	<20
75	Hybrid Black Poplar	3	760	2	M	9.1	Fallen	P	<10
76	Hybrid Black Poplar	21	1200	3	M	14.4	Collapsed multi-stemmed tree w/ in 1 trunk remaining. High potential for failure	P	<10
77	Oak	8	290	2	BM	3.5	Heavily ivy clad tree, acute form, future potential	N	<20
78	Oak	8	330	1	BM	4	Standing stem due to loss of branches following collapse of adjacent tree	N	<10
79	Hybrid Black Poplar	23	840	4	M	10.1	Once twin-stems at base, western stem falls across footpath leaving large basal wound & remaining stem ivy ivy clad, dog-legged branches, hanging branches. High potential for failure	N	<10
80	Oak	16	990, 480, 440	2	M	10.67	Ivy clad tree growing on E edge of ditch with tripe-stems at base & dead wood	N	<20
81	Oak	16	1200, 410	2	M	15	Ivy clad tree growing on E edge of ditch with twin-stems at base, damaged canopy east side by fallen Poplar stem T24 & major dead wood, special detach	N	<20
82	Oak	15	600	2	M	7.4	Ivy clad tree growing on edge of ditch, inclined to the west, forms crown with T14 & major dead wood, special detach	N	<20
83	10% Hazel, 25% Blackthorn, 20% Elder, 20% Hawthorn, 20% Grey Willow	5	150	0	M	3	Hedgehog species 1 side of ditch forming field boundary	N	<10
84	Common Ash	17	450	1	BM	5.4	Growing on E edge of ditch & forming unfused crown	N	<10
85	30% Hazel, 5% Field Maple, 5% Elder, 20% Blackthorn, 40% Hawthorn	7	200	0	M	3	Hedgehog species forming useful boundary w/ w/ golf course. Height canopy between 3m & 6m age between 1M & 6M dense ground cover of brambles & nettles	N	<10
86	Scots Pine	14	470	7	BM	5.6	Heavily ivy clad & suppressed off-site tree	P	<10
87	Purple Sycamore	16	680	1	M	8.2	Heavily ivy clad off-site tree	N	<20
88	Horse Chestnut	11	320	1	BM	3.8	Suppressed off-site tree, hanging branch from Phe	P	<10
89	Maritime Pine	20	920	6	M	11	Off-site tree with ivy clad main stem lower level collapsed w/ decay on E side	N	<20
90	Purple Sycamore	16	680	1	M	7.2	Off-site tree with twin-stems at 2m a.g.l	N	<20
91	Scots Pine	15	610	1	M	7.3	Suppressed off-site tree w/ ivy clad main stem & poor crown architecture	P	<10
92	Scots Pine	20	1180	2	M	14.2	Off-site tree inclined to the north, collapsed lower lateral E side	N	<20
93	Maritime Pine	10	480	6	BM	5.8	Heavily ivy clad off-site tree partially uprooted on south west side & hanging up in TBS, collected fallen	P	<10
94	Purple Sycamore	16	480	1	BM	5.5	Suppressed & ivy clad off-site tree with basal water at 0m a.g.l, resprouting in right multi-stemmed branching, poor quality	P	<10
95	Maritime Pine	20	1200	2	M	14.4	Off-site tree with ivy clad main stem	N	<20
96	10% Laburnum, 2% Cypress, 2% Holly, 40% Hawthorn, 40% Blackthorn	7	280	0	BM	3.4	Wood boundary species, forming poor screening. Heights between 3m & 6m & estimated stem diameters. Dense Bramble & nettle ground cover	N	<10

0 5 10 15 20 25 30 35 40 45 50

Scale

1:500

Appendix 2: Tree Work Schedule

No.	Name	Operation	Within or outside red-line boundary	BS Cat	TPO F/1/07
51	Oak	Remove	Outside	B	G4
G35	Hawthorn, Blackthorn, Elder	Remove as much of group as necessary from within site to allow road construction	Inside	C	
G26	Field maple, ash, hawthorn, hazel, elder	Remove as much as required to allow both access points to be constructed. Also cut back to allow 3m clearance from plot 97	Inside	C	G16
16	Monterey cypress	Remove	Inside	C	G1
46	Monterey cypress	Remove	Outside	C	G4
49	Poplar	Remove	Inside	C	G4
50	Monterey cypress	Remove	Outside	C	G4
53	Poplar	Remove	Inside	C	G4
G58	Hawthorn, Blackthorn, Elder	Remove as much as necessary within site to allow construction of garage for plot 57 and back to the boundary for plot 68/69	Inside	C	
G78	30% Hazel, 5% Field Maple, 5% Elder, 30% Blackthorn, 30% Hawthorn	Cut back to western site boundary to provide useable garden spaces	Inside	C	G2

Continued over...

No.	Name	Operation	Within or outside red-line boundary	BS Cat	TPO F/1/07
G89	6% Laburnum, 2% Cypress, 2% Holly, 40% Hawthorn, 40% Blackthorn	Cut back to western site boundary to provide useable garden spaces	Inside	C	
G32	30% Blackthorn, 25% Hazel, 25% Elder, 10% Hawthorn, 5% Field Maple, 5% Grey Willow	Cut back to allow 3m clearance from plots 90 & 2m clearance from plot 90's garage. Also cut back to boundary within plot 87's garden and parking area	Outside/Inside	C	
12	Poplar	Remove	Outside	U	G1
13	Monterey cypress	Remove	Outside	U	
14	Poplar	Remove	Inside	U	G1
15	Elm	Remove	Outside	U	
9	Poplar	Remove	Inside	U	G1
17	Poplar	Remove	Inside	U	G1
8	Poplar	Remove	Inside	U	G1
7	Poplar	Remove	Inside	U	G1
63	Poplar	Remove	Outside	U	G3
64	Poplar	Remove	Outside	U	G4
65	Poplar	Remove	Outside	U	G5
68	Poplar	Remove	Outside	U	G6
69	Poplar	Remove	Outside	U	G7

Appendix 3: Tree Protection Plan

BDWS19795-03B


Construction Exclusion Zone

Root protection areas (RPA) of retained trees within which all construction activity is restricted.

All trees that are being retained on site must be protected by barriers and/or ground protection before any materials or machinery are brought onto the site, and before any demolition, development or stripping of soil commences. Where all activity can be excluded from the RPA, vertical barriers must be erected to create a construction exclusion zone. Where, due to site constraints, construction activity cannot be fully or permanently excluded in this manner from all or part of a tree's RPA, appropriate ground protection can be installed.

Default position for the tree protection barriers.

BS5837:2012 Figure 2 - barrier specification

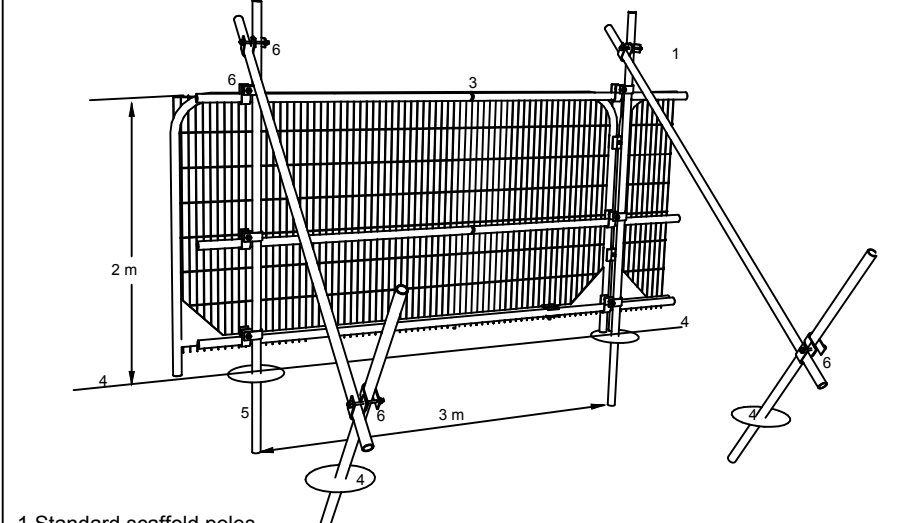


- 1 Standard scaffold poles
- 2 Heavy gauge 2m tall galvanized tube and weld mesh infill panels
- 3 Panels secured to uprights and cross-members with wire ties
- 4 Ground level
- 5 Uprights driven into the ground until secure (minimum depth 0.6m)
- 6 Standard scaffold clamps

Examples of alternative barrier designs can be found in the method statement. Should an alternative design be more viable and appropriate, it must be agreed with the project arboriculturist before its implementation.

Ground Protection

Where the set-back of the tree protection barrier would expose unmade ground to construction damage, new temporary ground protection should be installed as part of the implementation of physical tree protection measures prior to work starting on site.

Foot traffic

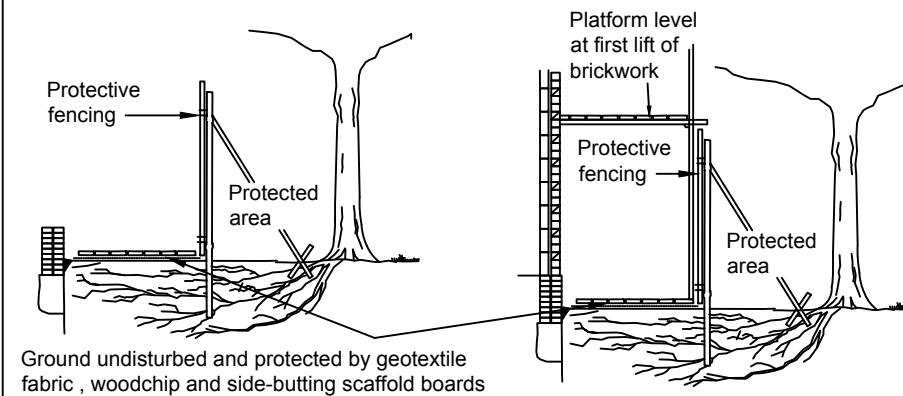

For **pedestrian movements** only, a single thickness of scaffold boards should be placed either on top of a driven scaffold frame, so as to form a suspended walkway, or on top of a compression-resistant layer (e.g. 100 mm depth of woodchip), laid onto a geotextile.

For **pedestrian operated plant** up to a gross weight of 2 t, proprietary, inter-linked ground protection boards should be placed on top of a compression-resistant layer (e.g. 150 mm depth of woodchip), laid onto a geotextile.


For **wheeled or tracked construction traffic** exceeding 2 t gross weight, an alternative system (e.g. pre-cast reinforced concrete slabs) should be employed to an engineering specification designed in conjunction with arboricultural advice to accommodate the likely loading to which it will be subjected.

TEMPORARY FENCING

The fencing is used to protect areas of special detail. It is to be installed with the main tree protection fence and is only to be removed when the detail is installed as per the method statement & under the supervision of the project arboriculturist. It shall be weld-mesh panels on boots, secured to the ground with road pins (or similar).

NO-DIG SURFACE

Cellular confinement system (CCS) to be used to create this area of hard surface, above the existing ground level. Topsoil to be retained. Depth of CCS to be 50-75mm for pedestrian surfaces and 100-200 for vehicular surfaces. Surface to be porous to approved details and specifications. To be installed under arboricultural supervision. **All specifications subject to engineering design.**

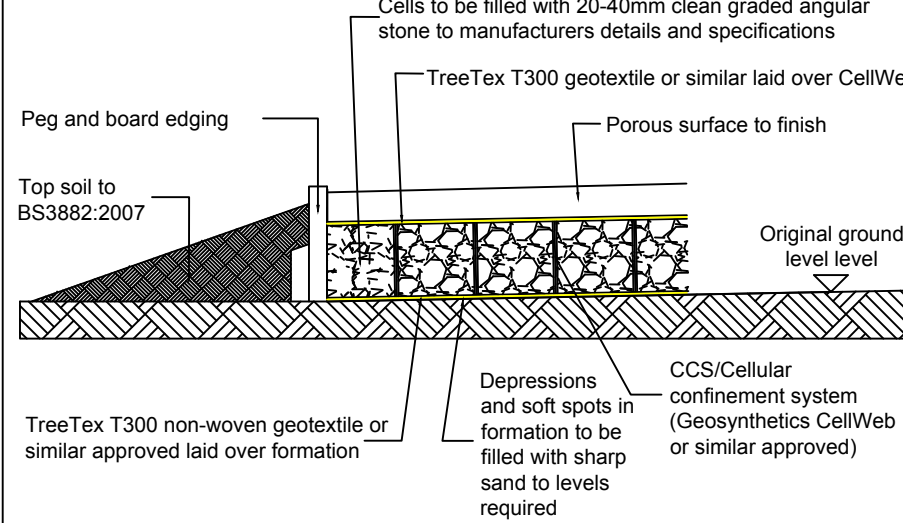

TREE TO BE REMOVED

- A CATEGORY TREE
 - B CATEGORY TREE
 - C CATEGORY TREE
 - U CATEGORY TREE
- ROOT PROTECTION AREA (RPA) FOR RETAINED TREES**

SUPERVISED EXCAVATION

This area of highway is to be installed within the RPA of adjacent retained trees. Therefore, to minimise impact any excavation shall be as per the method statement & under the supervision of the project arboriculturist.

RESTRICTIONS WITHIN TREE PROTECTION AREAS

Inside the exclusion area of the fencing, the following shall apply:

- No mechanical excavation whatsoever
- No excavation by any other means without arboricultural site supervision
- No hand digging without a written method statement having first been approved by the project arboriculturist.
- No lowering of levels for any purpose (except removal of grass sward using hand tools)
- No storage of plant or materials
- No storage or handling of any chemical including cement washings
- No vehicular access
- No fire lighting

In addition to the above, further precautions are necessary adjacent to trees:

- No substances injurious to tree health, including fuels, oil, bitumen, cement (including cement washings), builders sand, concrete mixing and other chemicals shall be stored or used within or directly adjacent to the protection areas of retained trees
- No fire shall be lit such that flames come within 5m of tree foliage.


PHASING & SUPERVISION OF DEVELOPMENT

Before any work starts on site, the tree protection measures shown on this plan are to be installed and a pre-start site meeting with the project arboriculturist, groundwork contractors and site manager held.

Additional site supervision and input from the project arboriculturist is to occur:


1. During the no-dig drive surfacing
2. During the excavation for the new road within the RPAs of T25 & T26

Supervision is also required should any unplanned access and/or work be required in the construction exclusion zone

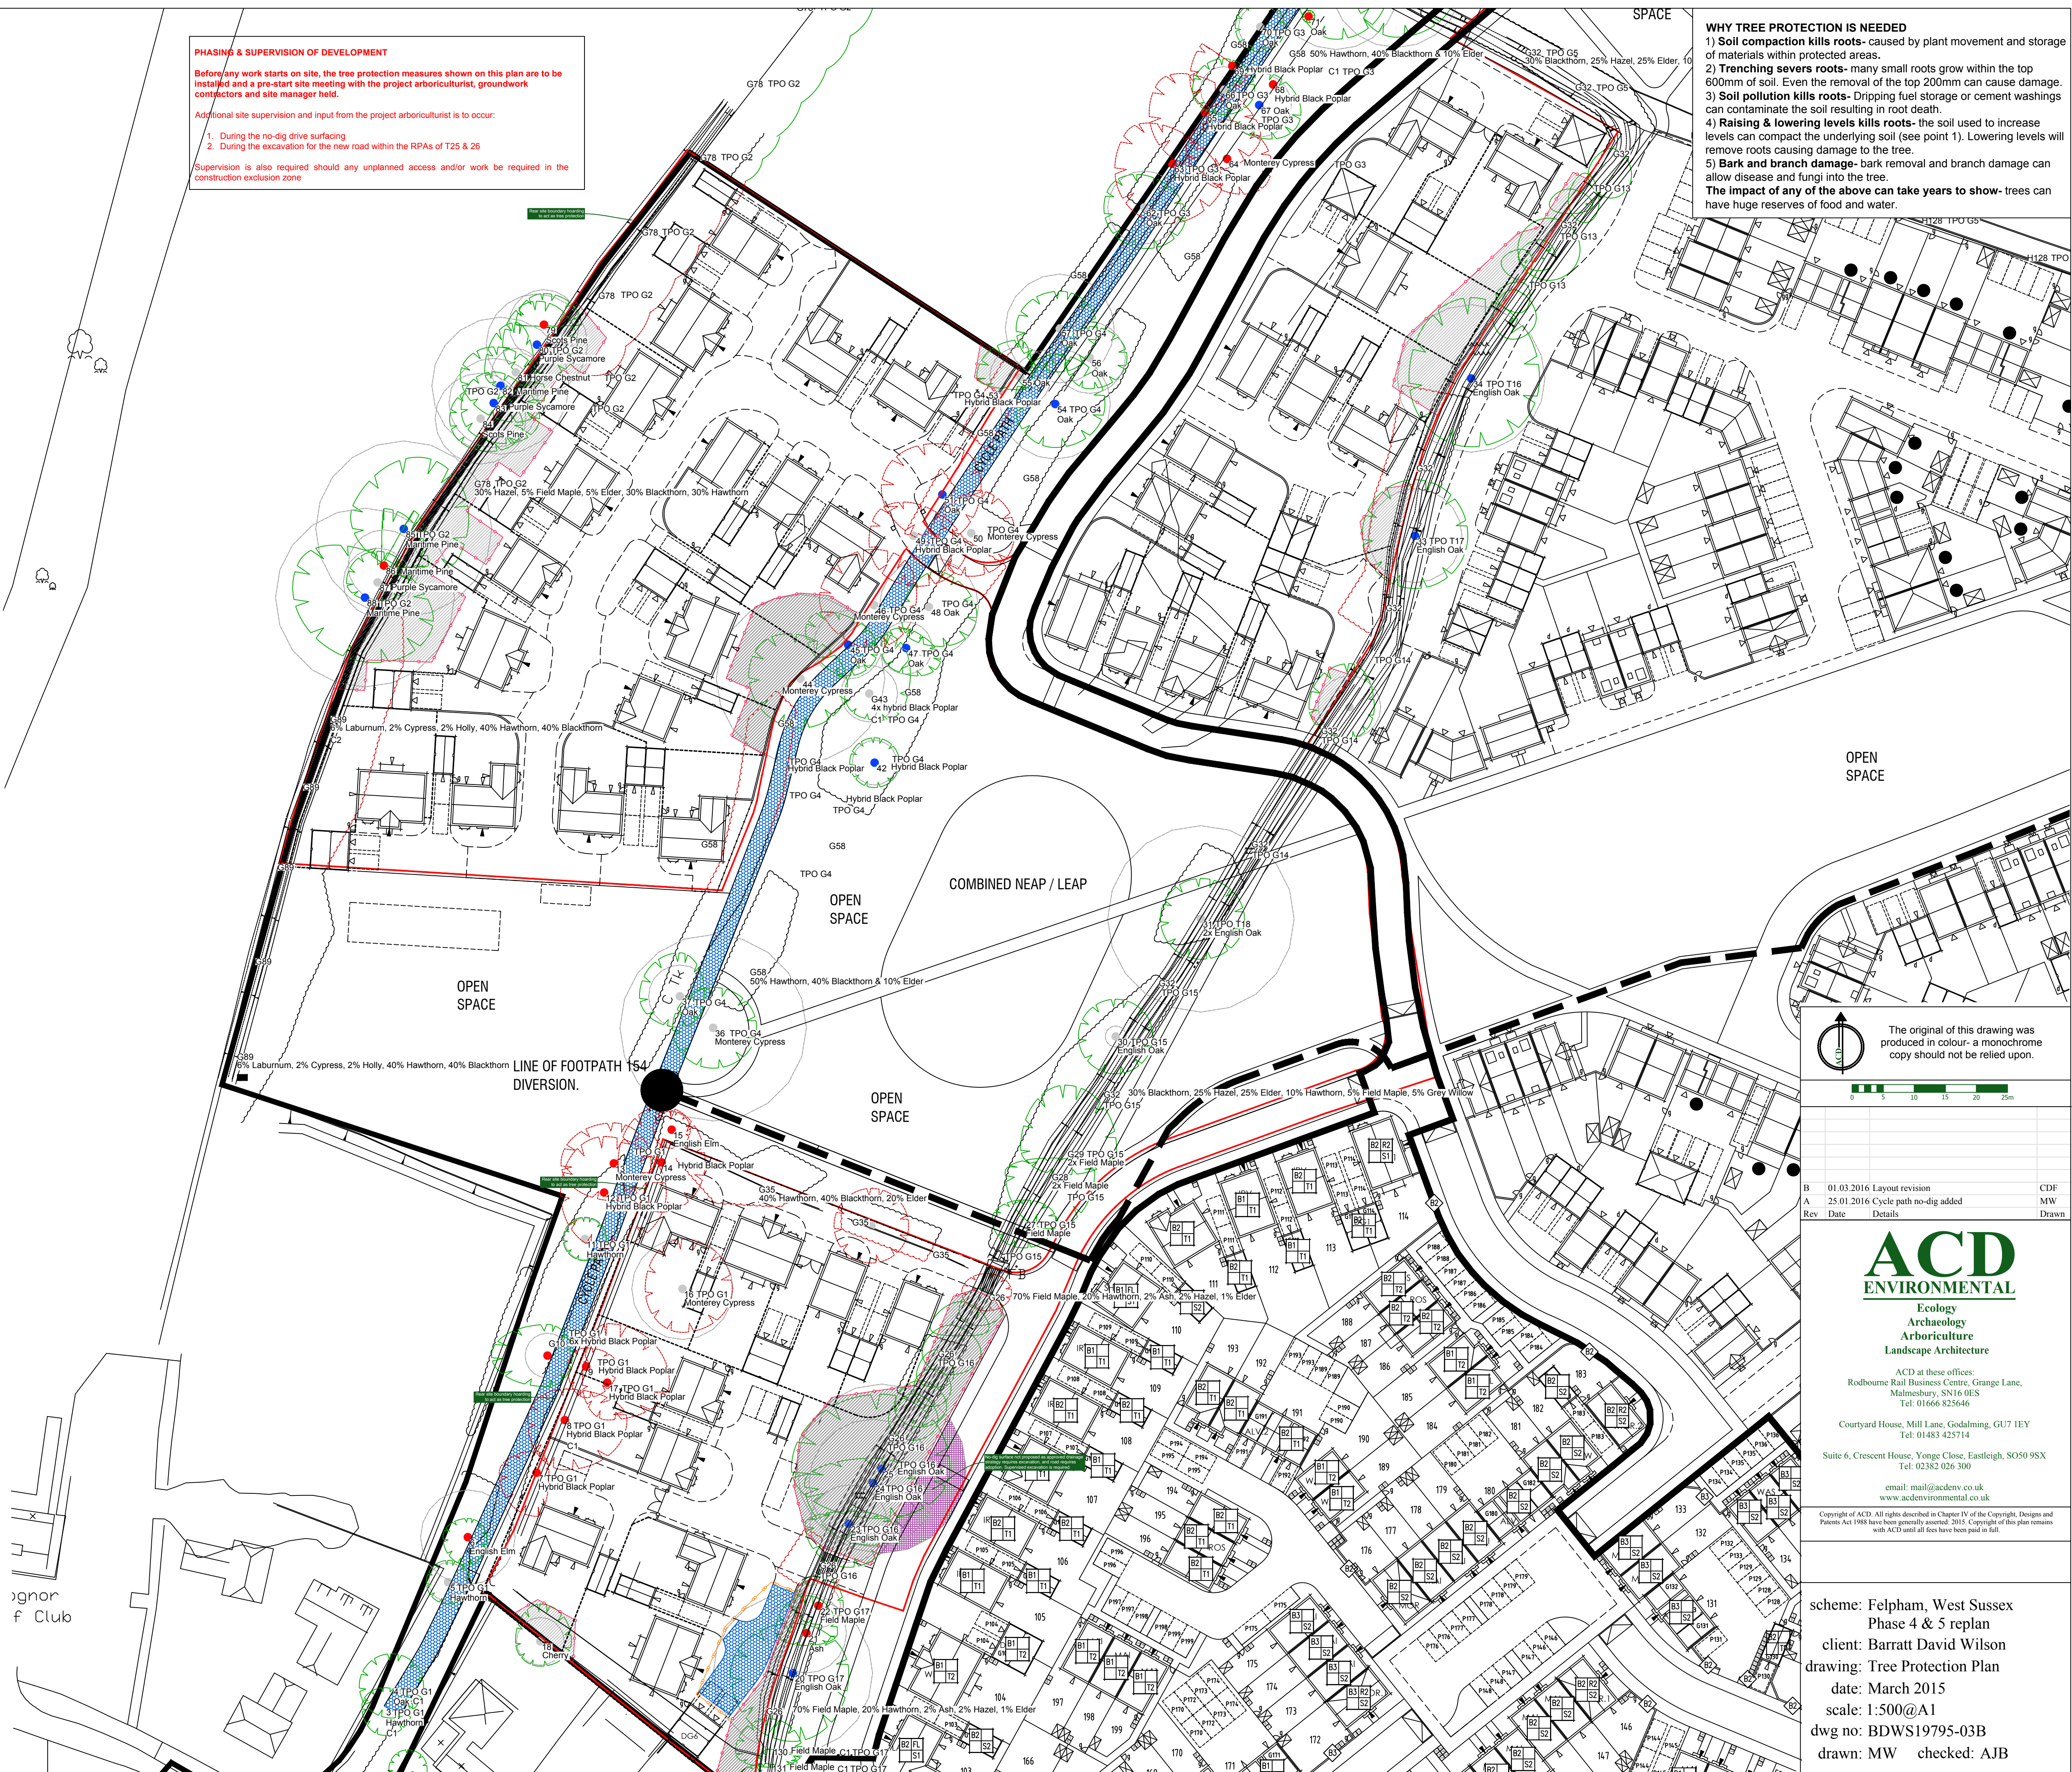

WHY TREE PROTECTION IS NEEDED

- 1) **Soil compaction kills roots** - caused by plant movement and storage of materials within protected areas.
 - 2) **Trenching severs roots** - many small roots grow within the top 600mm of soil. Even the removal of the top 200mm can cause damage.
 - 3) **Soil pollution kills roots** - Dripping fuel storage or cement washings can contaminate the soil resulting in root death.
 - 4) **Raising & lowering levels kills roots** - the soil used to increase levels can compact the underlying soil (see point 1). Lowering levels will remove roots causing damage to the tree.
 - 5) **Bark and branch damage** - bark removal and branch damage can allow disease and fungi into the tree.
- The impact of any of the above can take years to show** - trees can have huge reserves of food and water.



B	01.03.2016	Layout revision	CDF
A	25.01.2016	Cycle path no-dig added	MW
Rev	Date	Details	Drawn

ACD ENVIRONMENTAL

Ecology
Archaeology
Arboriculture
Landscape Architecture

ACD at these offices:
Rodbourne Rail Business Centre, Grange Lane,
Malmesbury, SN16 0ES
Tel: 01666 825646


Courtyard House, Mill Lane, Godalming, GU7 1EY
Tel: 01483 425714

Suite 6, Crescent House, Yongs Close, Eastleigh, SO50 9SX
Tel: 02382 026 300

email: mail@acdenv.co.uk
www.acdenvironmental.co.uk

Copyright of ACD. All rights described in Chapter IV of the Copyright, Designs and Patents Act 1988 have been generally asserted. 2015 Copyright of this plan remains with ACD until all fees have been paid in full.

scheme: Felpham, West Sussex
Phase 4 & 5 replan
client: Barratt David Wilson
drawing: Tree Protection Plan
date: March 2015
scale: 1:500@A1
dwg no: BDWS19795-03B
drawn: MW checked: AJB



Head Office

Rodbourne Rail Business Centre
Grange Lane
Malmesbury
SN16 0ES
Tel: 01666 825646

Surrey Office

Courtyard House
Mill Lane
Godalming
GU7 1EY
Tel: 01483 425714

Hampshire Office

Suite 6
Crescent House
Yonge Close
Eastleigh
SO50 9SX
Tel: 02382 026 300

Email: mail@acdenv.co.uk
Website: www.acdenvironmental.co.uk

ECOLOGICAL SURVEYS * PROTECTED SPECIES LICENSING * MITIGATION * IMPACT ASSESSMENT
ARBORICULTURAL SITE MONITORING AND SUPERVISION * ARCHAEOLOGY
LANDSCAPE & VISUAL IMPACT ASSESSMENT * LANDSCAPE AUDIT * PROJECT MANAGEMENT
EXPERT WITNESS* LANDSCAPE DESIGN & PLANNING LANDSCAPE MANAGEMENT
