


Inspection Report

Date: 17/12/24	Job No:	Weather: Dry	Operator: Mick	Section Number 66	PLR:
Present:	Vehicle: WM69 YNA	Camera: Camera 1	Preset:	Cleaned: YES	Grade:
Site; Tye Lane Place: Warblington		Division: District: S.W Tape No: 1		Start MH: S14 End MH: S13 Total Length:	
Purpose: Use: Catchment:	Structural Defects STORM P1 Schedule	Size/Shape: Circular dia 375mm Material: PLASTIC Lining: Category:			

Position Code Observation

0.0M ST Start Of Survey
0.0M WL Water Level 0%

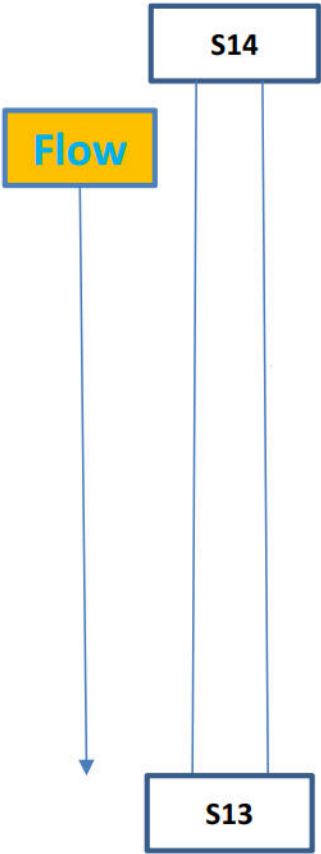

5.0M JN Line Drops In From The Left

6.2M JN Line Drops In From The Right From S 13.1

11.0M D Debris In Line, Unable To Pass

REM ; THE MANHOLE S13 IS FULL OF DEBRIS AND THIS IS TOO LARGE FOR THE LORRY TO SUCK OUT, THIS WILL NEED CONFINED SPACE ENTRY TO DIG OUT THE MANHOLE, ALSO S 12 IS LOCATED ON THE VERGE AND UNABLE TO GET LORRY NEAR ENOUGH TO JET AND ROAD IS NOT IN YET TO JET FROM S11 UP TO S 12

Structural Defects	Constructional Features
Service Defects	Miscellaneous Features
