



Storage and handling of harmful chemicals
Provision needs to be made to avoid the storage and handling of harmful chemicals in proximity to trees. Harmful chemicals include fuels, oils, builder's sand (which has a high salt content) and cement. Provision shall also be made to prevent fuelling or the handling of cement from occurring in areas proposed for further planting.

Cement mixing shall only occur where there is no potential for cement washings to leech into a root protection area. A designated fuelling station for plant machinery shall be selected that is either bunded or has provision to avoid spillages leeching into a construction exclusion zone.


Contractor facilities
A suitable location for site cabins, contractor parking and site facilities for operatives shall be agreed with the project arboriculturalist during a pre-commencement meeting. These facilities should be located outside the root protection areas of retained trees (unless on retained tarmac surfaces). Provision must also be taken to prevent exhaust fumes or hot air from generators or kitchen facilities from damaging the canopies of retained trees.

Construction exclusion zone
The areas protected by fencing or highlighted yellow shall be referred to as the construction exclusion zones. The following actions shall be prohibited within the construction exclusion zones:

- Vehicular access.
- Regular pedestrian access unless on suitable ground protection.
- Storage of construction materials.
- Storage or handling of harmful chemicals.
- Any change in ground level unless under the supervision of project arboriculturalist.
- Construction activities including hard, permanent surfacing.

All construction traffic (e.g. plant machinery and materials deliveries) to be routed through existing driveway for Longacre and retained paddock.

Heras fencing affixed with metal anti-tamper clamps (or equivalent construction fencing to be agreed with project arboriculturalist) to be installed around retained trees on construction area, prior to construction traffic entering site.

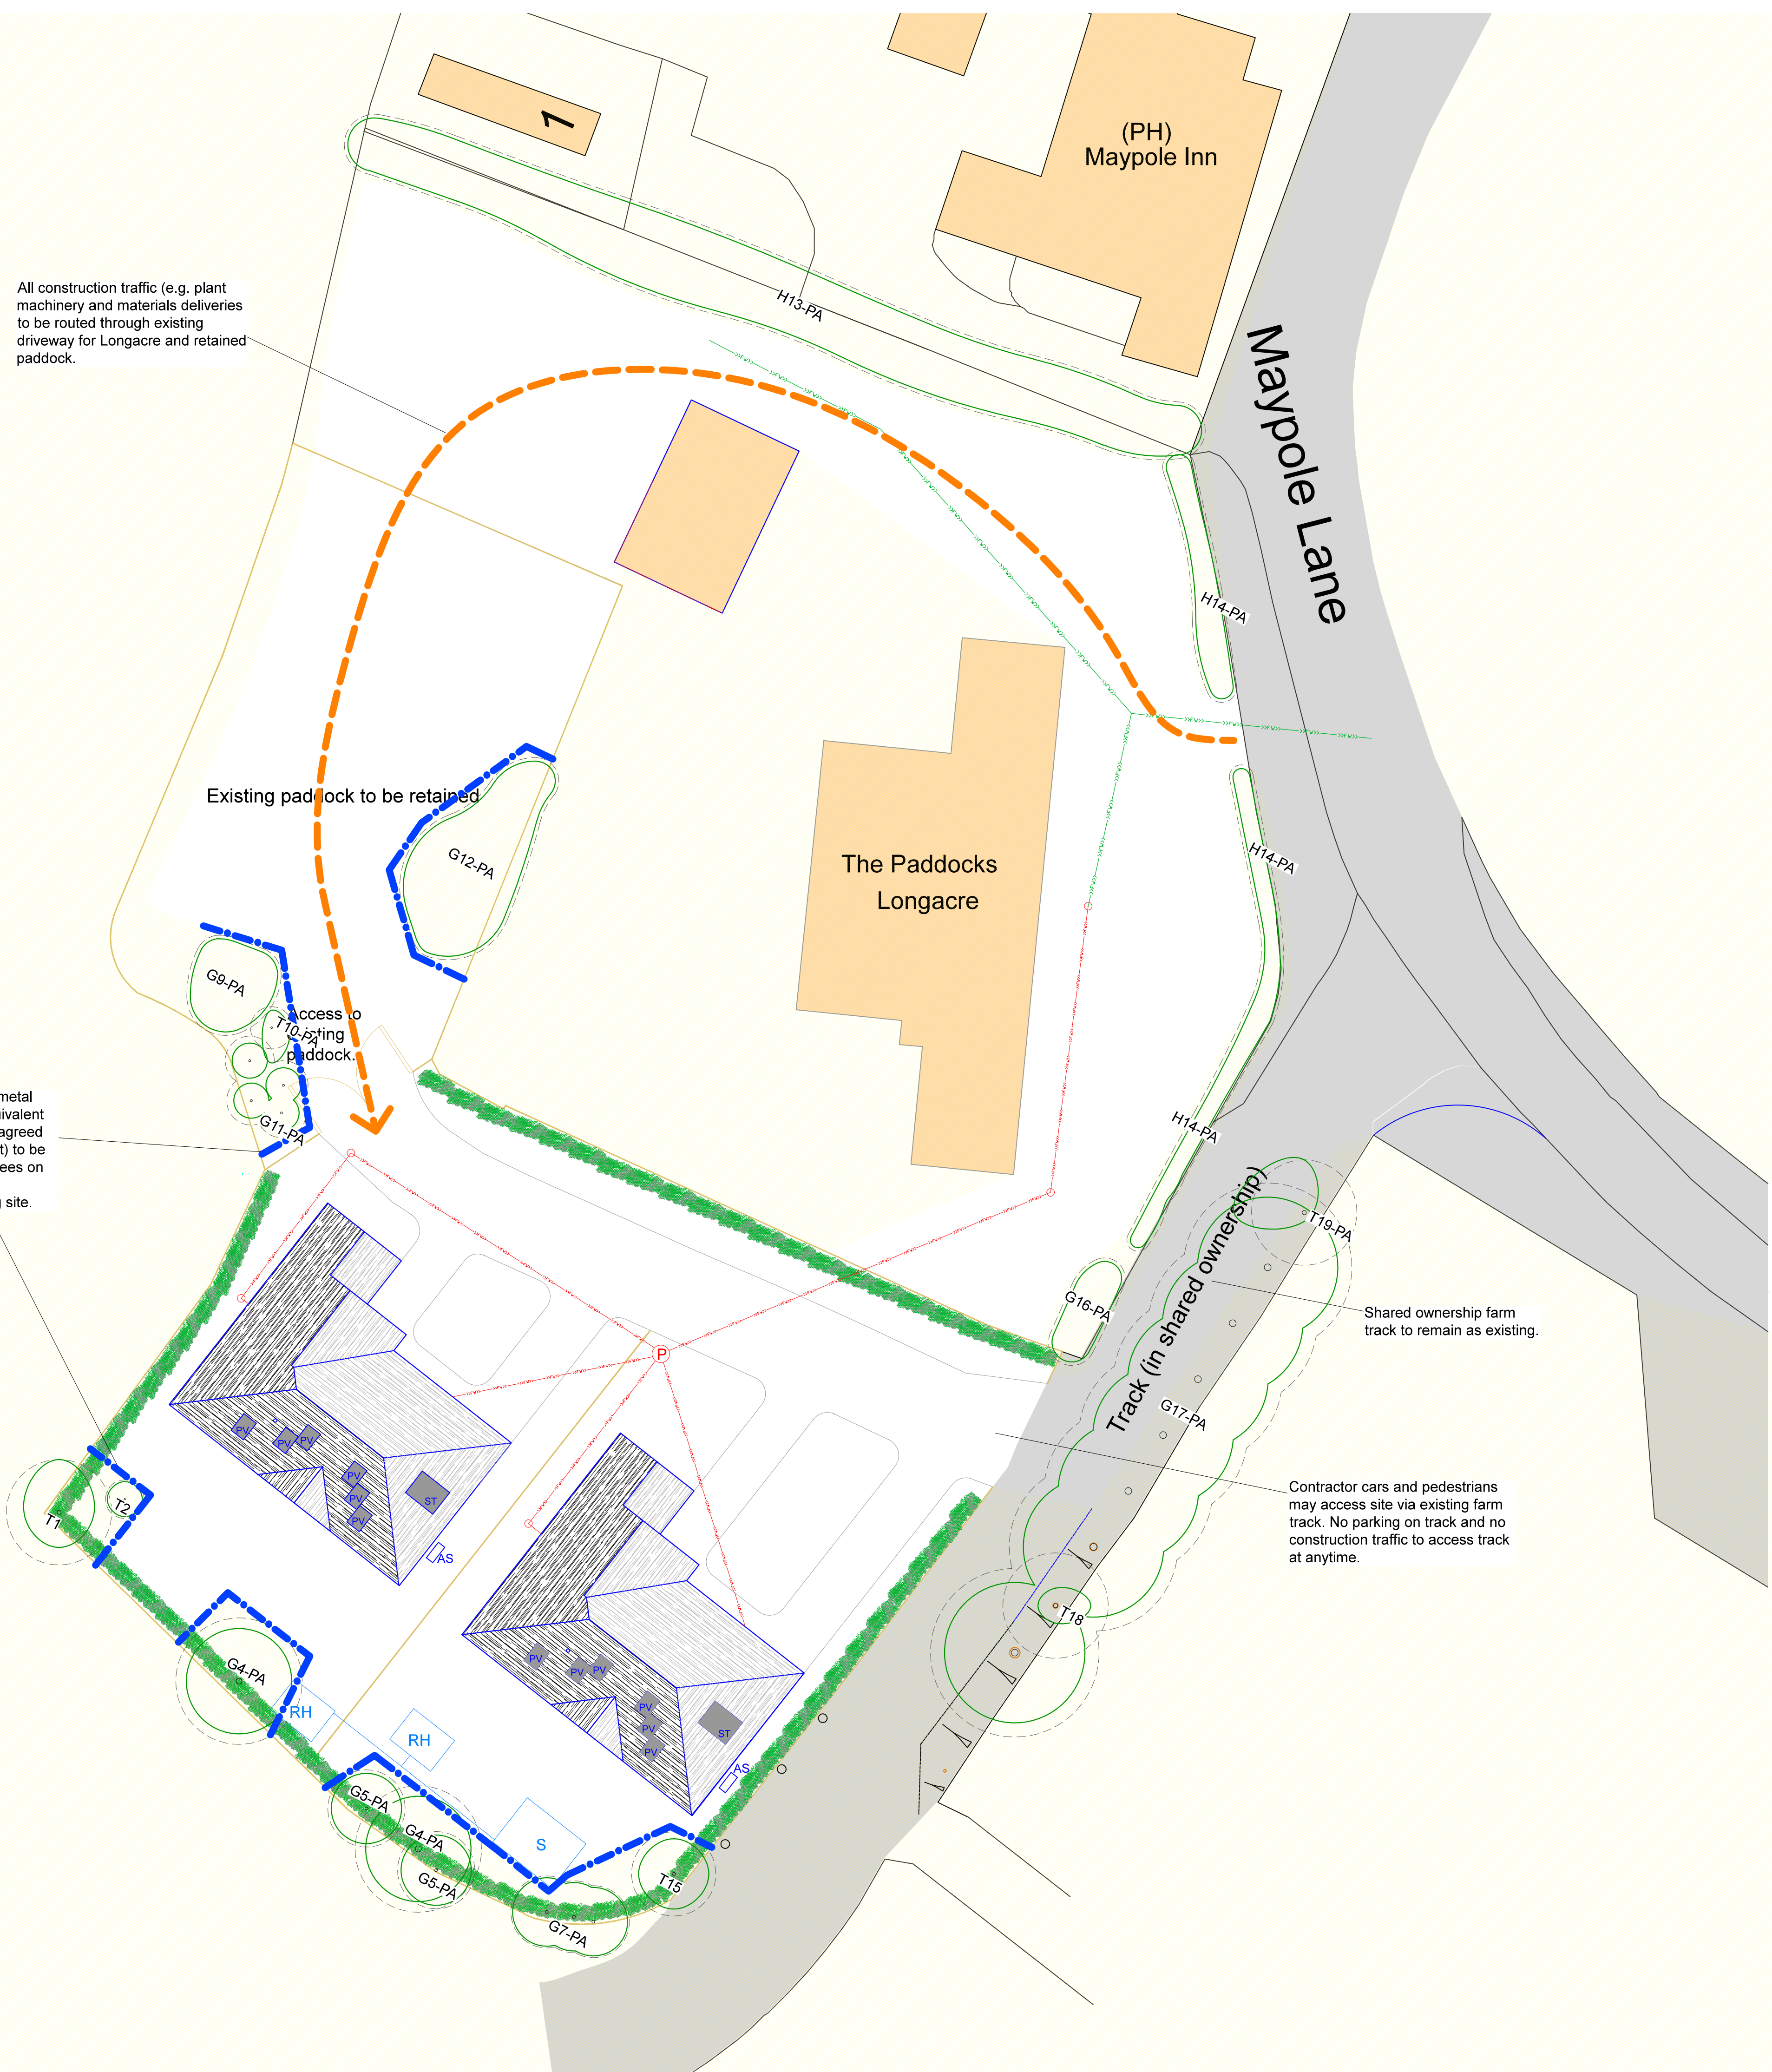

Key:

- RPA for retained tree
- Canopy of retained tree
- Tree protection fencing
- Construction exclusion zone
- Route of access for construction traffic

The Tree Survey Schedule shown on drawing ref. PJC/4366/17/A contains information and management recommendations for each tree.

This drawing should be viewed in colour.

Drawing no: PJC/4366/17/B Rev: - Sheet number: 1 of 1

Client and site:
Philips Surveyors


Land at Longacre
Maypole Lane
Yapton

Drawing title: Tree Protection Plan

Date drawn: 24/03/2017

Scale: 1:200 at A1

Drawn by: PD Checked by: NB



PJC Consultancy
Chapter House, Priestshaws Farm, Hailsham
Road, Polegate, East Sussex, BN26 6QU.
t: 01323 400311
e: contact@pjcconsultancy.com
w: www.pjcconsultancy.com
