



"YOUR-KEY LTD."

Portable and Security Cabins

SALE - HIRE - LEASE

A BS EN ISO 9002 COMPANY

P.O. Box 90
Bognor Regis
Sussex PO21 2UA

U.K. & The Channel Islands

NUMBER OF PAGES INCLUDING THIS ONE.....1.

PLEASE TELEPHONE 01243 841007 IF ALL PAGES NOT RECEIVED..

3.1.01.

FAX TO: David Tristram at Walberton Nurseries.

From John Yorke.

David,

Thank you for your verbal order for the manufacture and supply of:

1. No. 50ft x 12ft J/T Unit.

I am arranging for all the foundation and service detail that you required.

This will be forwarded to you in the very near future.

Having discussed the rainwater drainage with the factory, they have suggested that due to the size of the unit it will be better to have overhang roof section at each 12ft end with downpipes as this will disperse the water more efficiently than the H section guttering.

I have also discussed with them the position regarding the 3 phase 60 amp mains board.


The price differential is correct but it does include a 100amp RCD.

If however you have an RCD break somewhere else in your system then there is a cost saving of £104.00 net.

Perhaps you would be kind enough to confirm your acceptance regarding the above item.

Incorporating
Your-Key Southern. Your-Key Midlands. Your-Key Northern.
Your-Key Scotland. Your-Key Channel Islands.

A delivery schedule will be provided as soon as possible.



Your Key Ltd.

PO Box 90,



Your Key Ltd.

fax.

To: David Trotter, Wilberton Nursery. **From:** John Yorke

Page: One

Date: 26/01/01.

Re: Delivery of 60ft Portable Cabin. **CC:**

☐ Urgent ☐ For Review ☐ Please Comment ☐ Please Reply ☐ Please Recycle

● Comments:

David,

Just to confirm my recent telephone call to your office .

The new Cabin is programmed to arrive at site on Friday the 9th February 2001 at between 10am and 11am.

The crane will arrive at 9am in order to rig up.

Before the new unit arrives we will move the existing office away from the site and I would ask you to have the external services disconnected prior to our arrival.


The old unit will be removed from site either the same afternoon or at worst on the Monday morning.

January 26, 2001


I will be using a local Hiab Lorry for this move.

I trust that this meets with your approval.

If you have any further questions or queries do not hesitate to contact my office.







50' x 12'

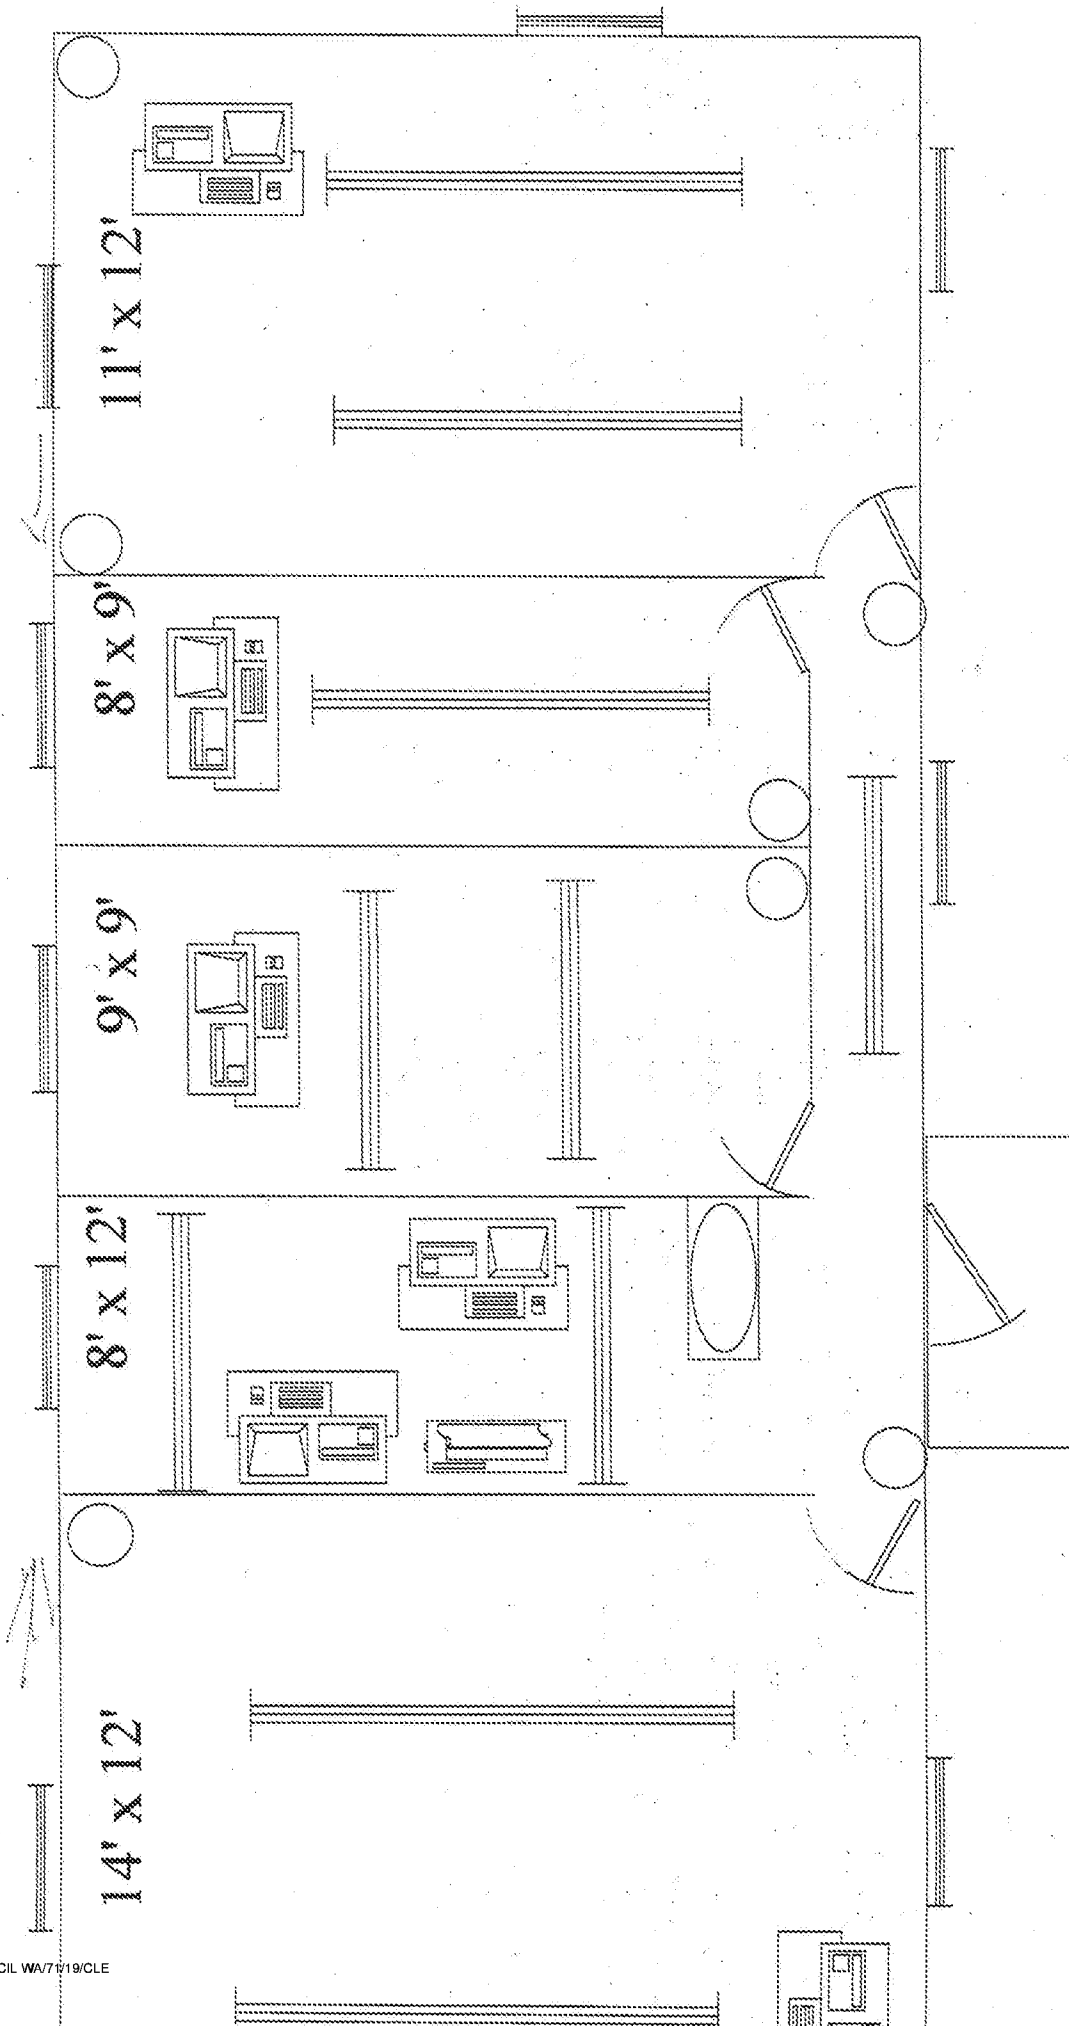

internal doors half glassed expect the out side door

sensors

ROOF WITH LOW PROFILE PLAS
 PANEL IN GMP SAFETY
 FALL TO BOTH ENDS

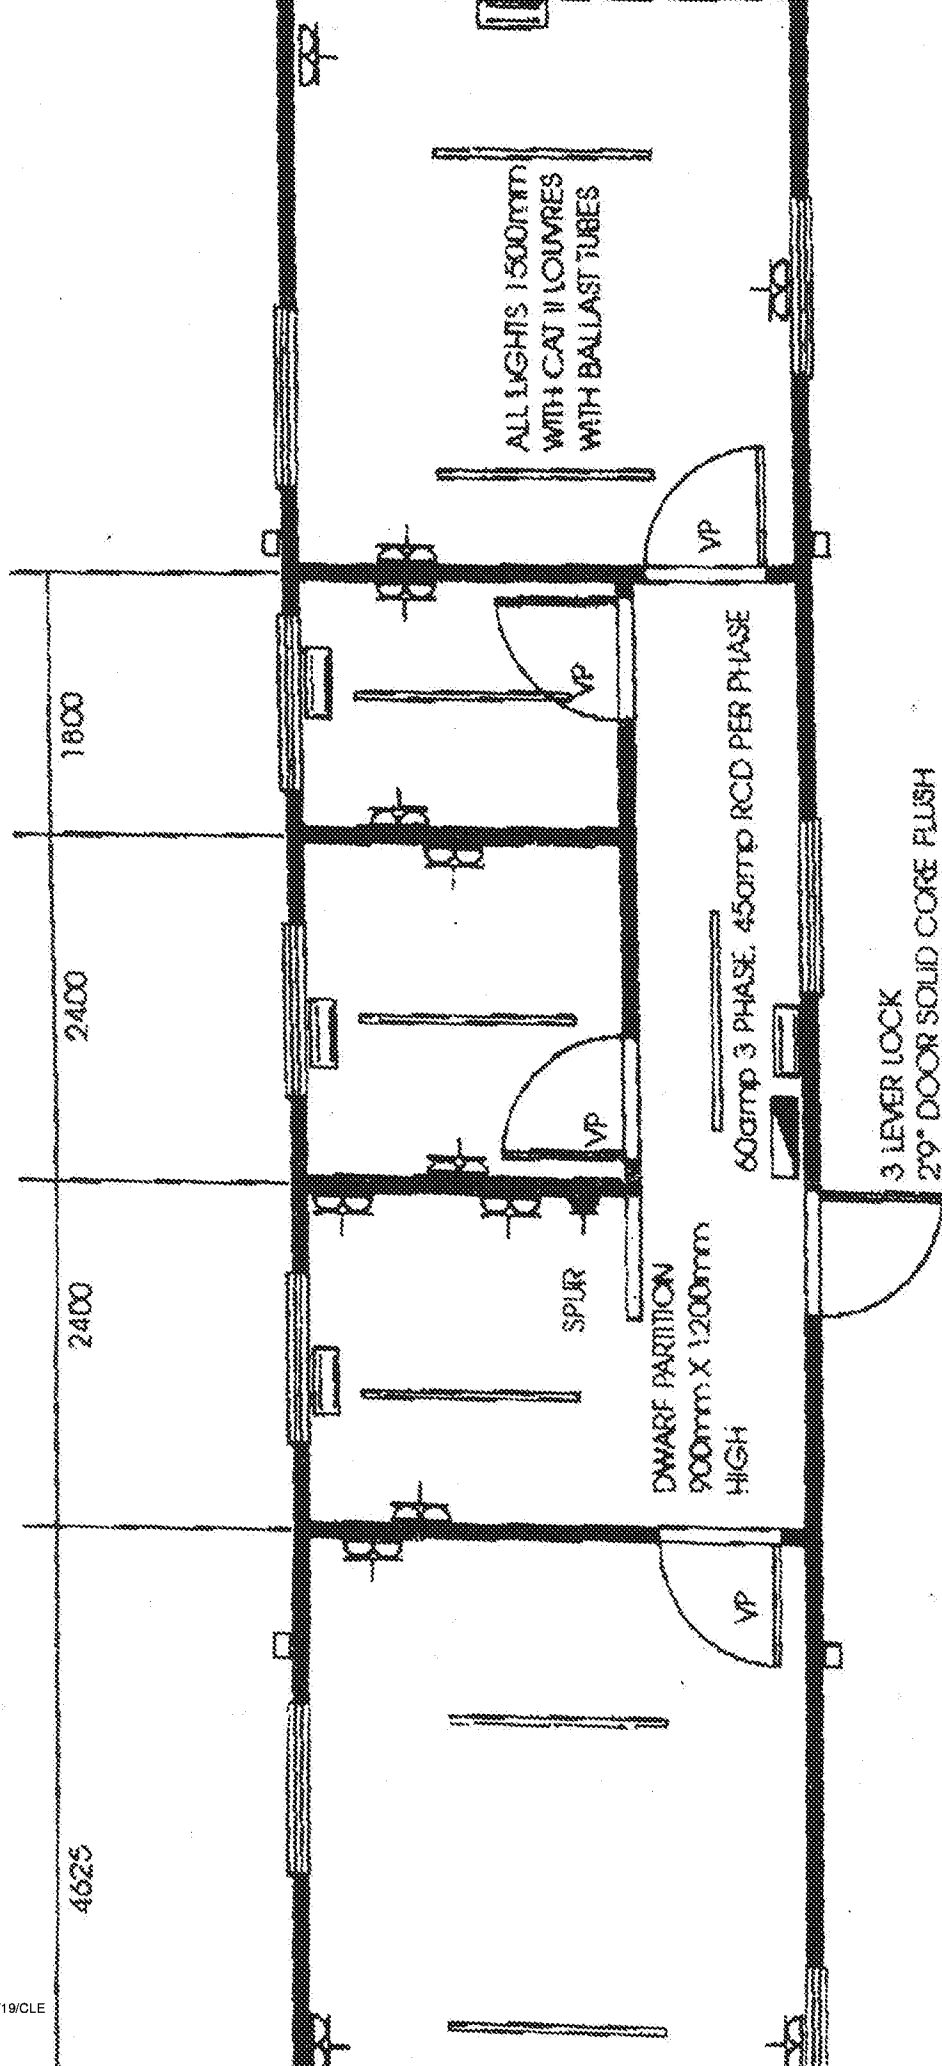

15250

YOUR-KEY LID - PROPOSED 50 X 12 JACKLEG UNIT
