



Section Inspection - 26/05/2021 - SP36X

Item No. 51	Insp. No. 1	Date 26/05/21	Time 14:59	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR SP36X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	SP36
Road:	Dappers Lane	Inspected Length:	4.00 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	4.00 m	Downstream Node:	F24
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation Grade

Depth: m

F24



0.00

MH

Start node, manhole, reference: F24

0.00

WL

Water level, 0% of the vertical dimension

2.50

LL

Line deviates left

3.50

LU

Line deviates up

4.00

MHF

Finish node, manhole, reference: SP36

SP36

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0


Dappers Lane

108




Section Pictures - 26/05/2021 - SP36X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
51	Upstream	SP36X		

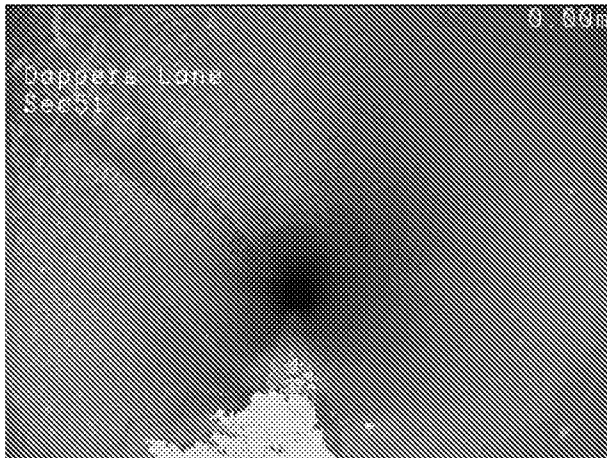


1, 00:00:00, 0.00 m
Start node, manhole, reference: F24

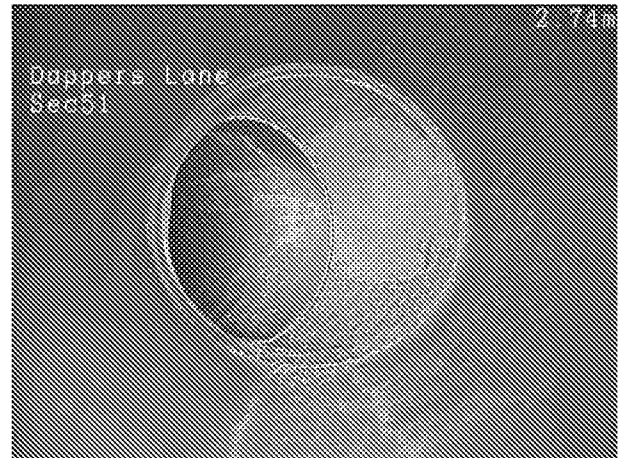

2, 00:00:16, 2.80 m
Line deviates left



3, 00:00:23, 3.60 m
Line deviates up

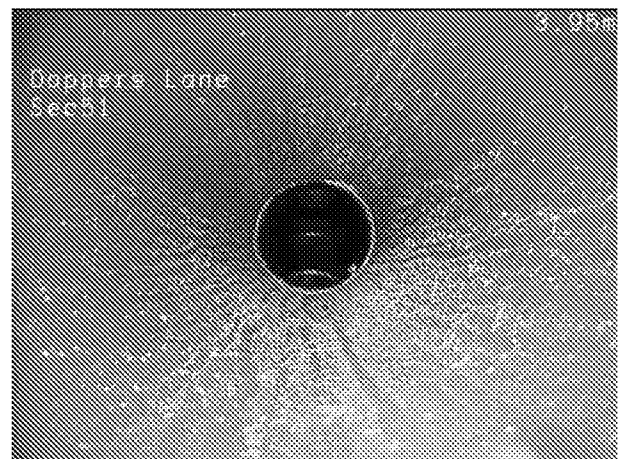

4, 00:00:29, 4.00 m
Finish node, manhole, reference: SP36



Section Inspection - 26/05/2021 - SP37X

Item No. 52	Insp. No. 1	Date 26/05/21	Time 15:01	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR SP37X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	SP37
Road:	Dappers Lane	Inspected Length:	7.50 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	7.50 m	Downstream Node:	F24
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:65 Position [m] Code Observation Grade

Depth: m

F24



0.00

MH

Start node, manhole, reference: F24

0.00

WL

Water level, 0% of the vertical dimension

6.60

LU

Line deviates up

7.50

MHF

Finish node, manhole, reference: SP37



SP37

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane

110



Section Pictures - 26/05/2021 - SP37X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
52	Upstream	SP37X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F24



2, 00:00:23, 6.60 m
Line deviates up



3, 00:00:32, 7.50 m
Finish node, manhole, reference: SP37



Section Inspection - 26/05/2021 - SP38X

Item No. 53	Insp. No. 1	Date 26/05/21	Time 15:03	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR SP38X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	SP38
Road:	Dappers Lane	Inspected Length:	6.00 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	6.00 m	Downstream Node:	F24
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:52 Position [m] Code Observation Grade

Depth: m

F24



0.00

MH

Start node, manhole, reference: F24

0.00

WL

Water level, 0% of the vertical dimension

0.10

LR

Line deviates right

5.40

LU

Line deviates up

6.00

MHF

Finish node, manhole, reference: SP38



SP38

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0


Dappers Lane

112



Section Pictures - 26/05/2021 - SP38X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
53	Upstream	SP38X		

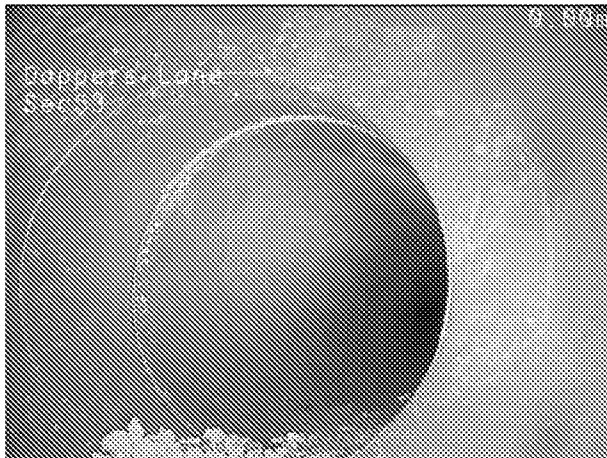



Section Inspection - 26/05/2021 - F24X

Item No. 54	Insp. No. 1	Date 26/05/21	Time 15:04	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F24X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F24
Road:	Dappers Lane	Inspected Length:	4.10 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	4.10 m	Downstream Node:	F25
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation Grade

Depth: m

F24



0.00

MH

Start node, manhole, reference: F24

0.00

WL

Water level, 0% of the vertical dimension

0.10

LL

Line deviates left

0.10

LD

Line deviates down

1.30

WL

Water level, 5% of the vertical dimension

1.50

WL

Water level, 15% of the vertical dimension

1.60

WL

Water level, 20% of the vertical dimension

1.70

WL

Water level, 50% of the vertical dimension

2.00

CUW

Loss of vision, camera under water

4.10

MHF

Finish node, manhole, reference: F25: Debris in chamber

F25

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations


STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane

114

Section Pictures - 26/05/2021 - F24X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
54	Downstream	F24X		

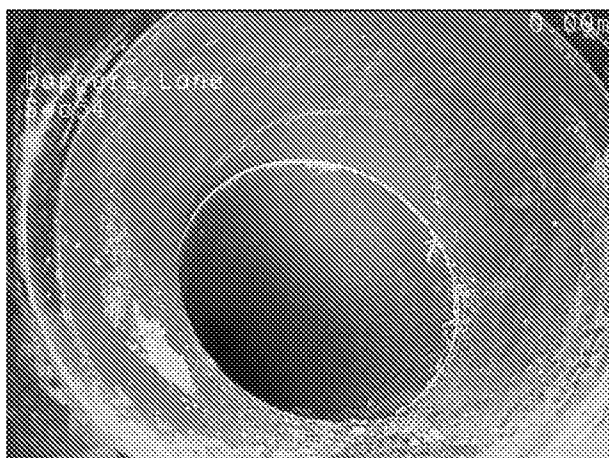

1, 00:00:00, 0.00 m
Start node, manhole, reference: F24



2, 00:00:13, 1.30 m
Water level, 5% of the vertical dimension



3, 00:00:18, 1.50 m
Water level, 15% of the vertical dimension



4, 00:00:20, 1.60 m
Water level, 20% of the vertical dimension



5, 00:00:21, 1.70 m
Water level, 50% of the vertical dimension



6, 00:00:39, 4.10 m
Finish node, manhole, reference: F25, Debris in chamber



Section Inspection - 26/05/2021 - SP39X

Item No. 55	Insp. No. 1	Date 26/05/21	Time 15:25	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR SP39X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	SP39
Road:	Dappers Lane	Inspected Length:	2.20 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	2.20 m	Downstream Node:	F26
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation Grade



Depth: m


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane

116

Section Pictures - 26/05/2021 - SP39X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
55	Upstream	SP39X		

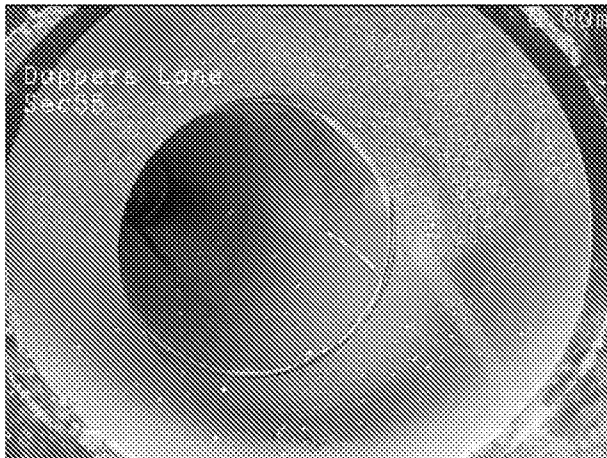

1, 00:00:00, 0.00 m
Start node, manhole, reference: F26



2, 00:00:13, 0.80 m
Line deviates left

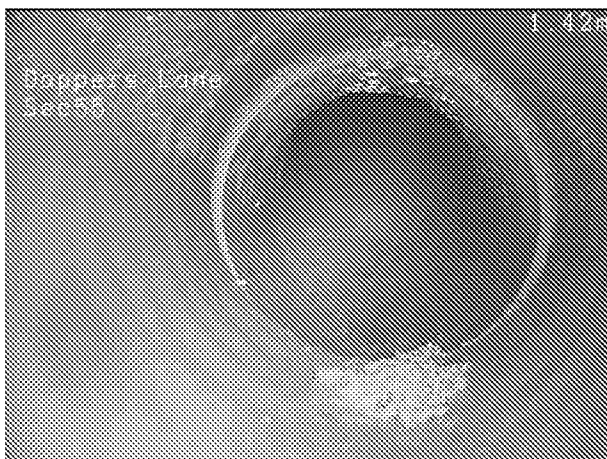

3, 00:00:19, 1.50 m
Line deviates up



4, 00:00:25, 2.20 m
Finish node, manhole, reference: SP39



Section Inspection - 26/05/2021 - SP40X

Item No. 56	Insp. No. 1	Date 26/05/21	Time 15:27	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR SP40X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	SP40
Road:	Dappers Lane	Inspected Length:	8.00 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	8.00 m	Downstream Node:	F26
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:69 Position [m] Code Observation Grade

Depth: m

F26



0.00

MH

Start node, manhole, reference: F26

0.00

WL

Water level, 0% of the vertical dimension

1.60

LR

Line deviates right

2.50

LR

Line deviates right

7.60

LU

Line deviates up

8.00

MHF

Finish node, manhole, reference: SP40

SP40

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations


STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane


118

Section Pictures - 26/05/2021 - SP40X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
56	Upstream	SP40X		

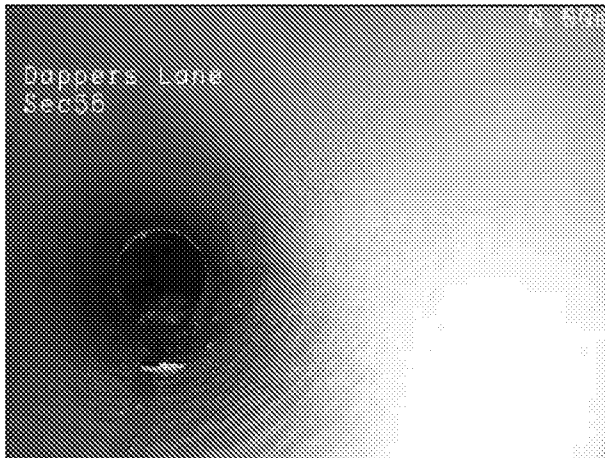

1, 00:00:00, 0.00 m
Start node, manhole, reference: F26

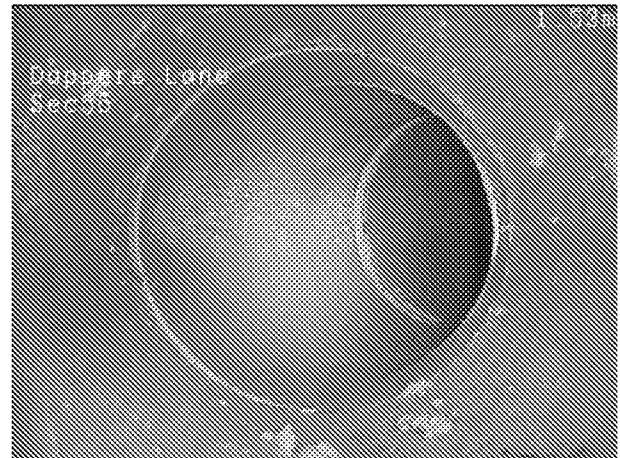

2, 00:00:25, 1.60 m
Line deviates right

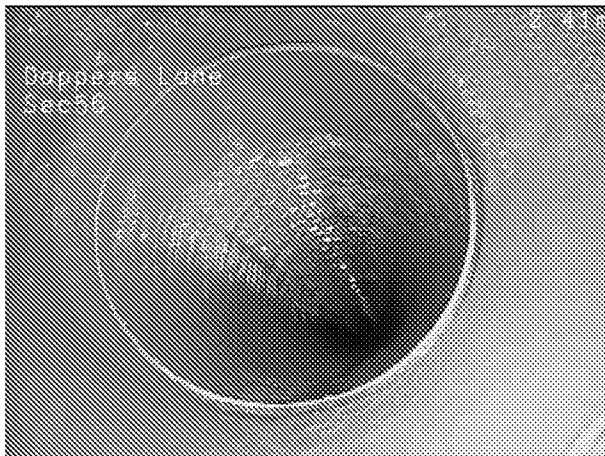

3, 00:00:32, 2.50 m
Line deviates right



4, 00:00:48, 7.60 m
Line deviates up



5, 00:00:54, 8.00 m
Finish node, manhole, reference: SP40



Section Inspection - 26/05/2021 - F26X


Item No. 57	Insp. No. 1	Date 26/05/21	Time 15:28	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F26X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F26
Road:	Dappers Lane	Inspected Length:	2.40 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	2.40 m	Downstream Node:	JN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation Grade

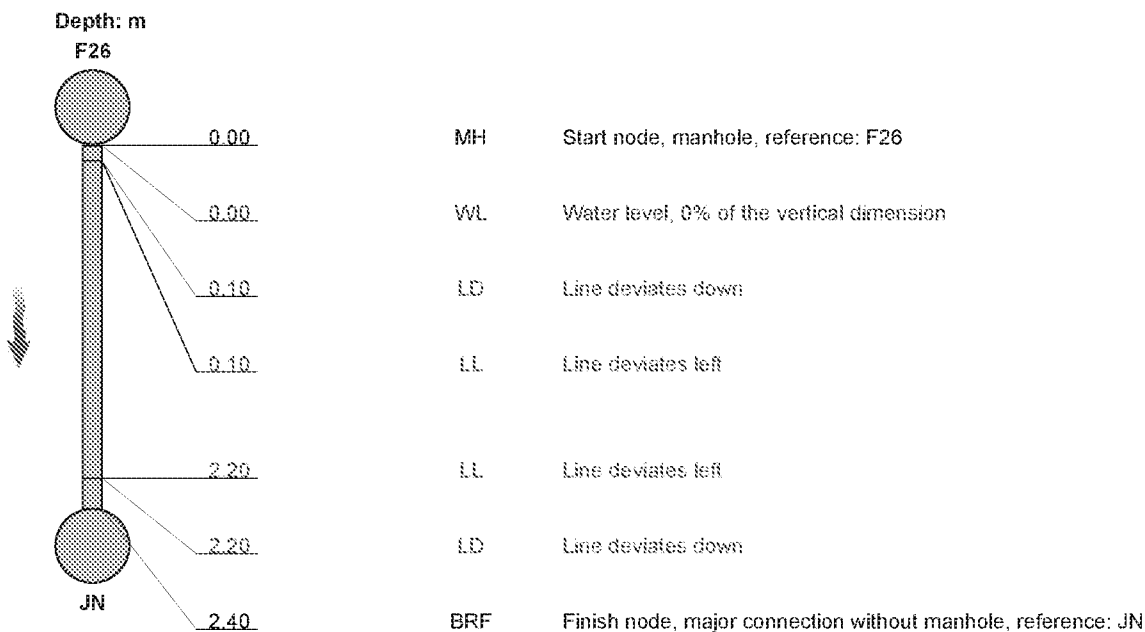

Depth: m

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0


Dappers Lane

120




Section Pictures - 26/05/2021 - F26X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
57	Downstream	F26X		

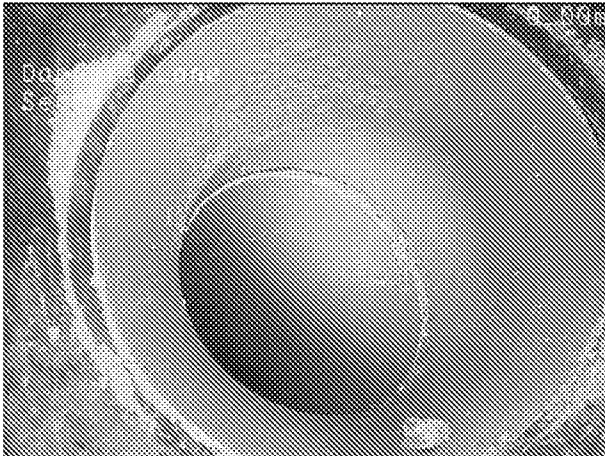

1, 00:00:01, 0.00 m
Water level, 0% of the vertical dimension

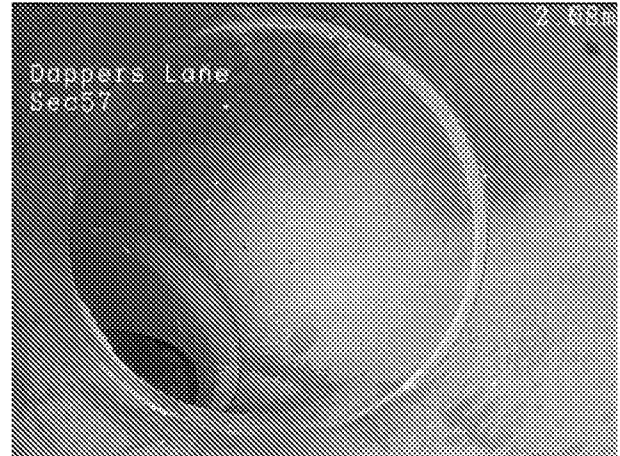

2, 00:00:22, 2.20 m
Line deviates left

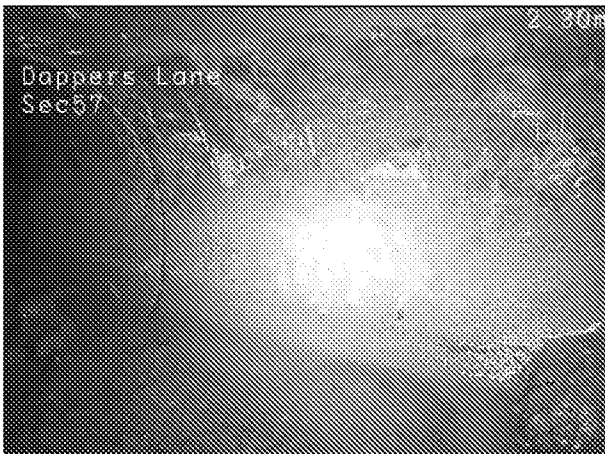

3, 00:00:27, 2.40 m
Finish node, major connection without manhole, reference: JN



Section Inspection - 26/05/2021 - SP41X

Item No. 58	Insp. No. 1	Date 26/05/21	Time 15:33	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR SP41X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	SP41
Road:	Dappers Lane	Inspected Length:	2.00 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	2.00 m	Downstream Node:	F27
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation Grade



Depth: m


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane

122

Section Pictures - 26/05/2021 - SP41X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
58	Upstream	SP41X		

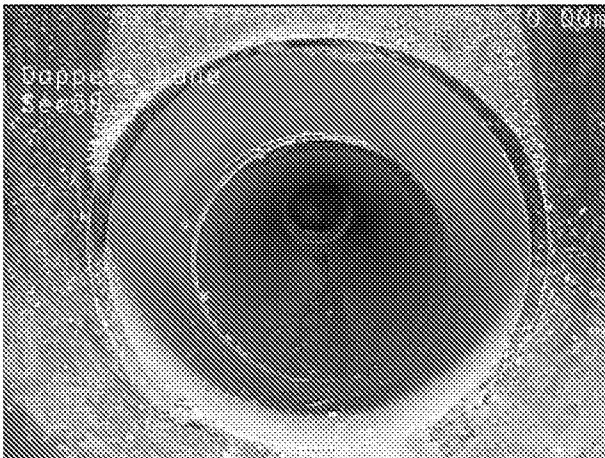

1, 00:00:00, 0.00 m
Start node, manhole, reference: F27



2, 00:00:20, 1.60 m
Line deviates up



3, 00:00:27, 2.00 m
Finish node, manhole, reference: SP41



Section Inspection - 26/05/2021 - SP42X

Item No. 59	Insp. No. 1	Date 26/05/21	Time 15:34	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR SP42X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	SP42
Road:	Dappers Lane	Inspected Length:	8.20 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	8.20 m	Downstream Node:	F27
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:71 Position [m] Code Observation Grade

Depth: m

F27



0.00

MH

Start node, manhole, reference: F27

0.00

WL

Water level, 0% of the vertical dimension

0.70

LR

Line deviates right

2.00

LR

Line deviates right

7.80

LU

Line deviates up

8.20

MHF

Finish node, manhole, reference: SP42

SP42

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane


124

Section Pictures - 26/05/2021 - SP42X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
59	Upstream	SP42X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F27

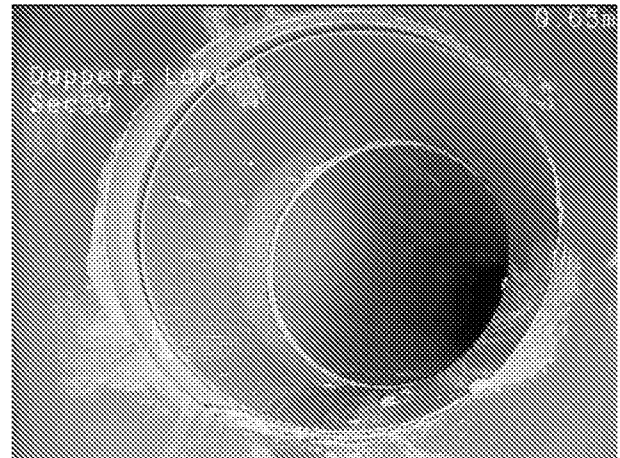

2, 00:00:16, 0.70 m
Line deviates right

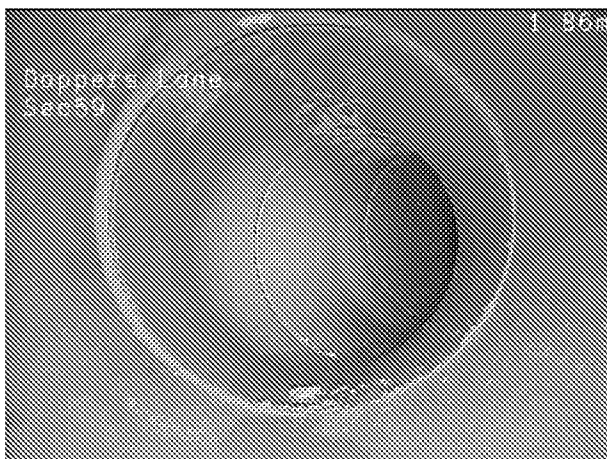

3, 00:00:26, 2.00 m
Line deviates right



4, 00:00:43, 7.80 m
Line deviates up



5, 00:00:46, 8.20 m
Finish node, manhole, reference: SP42



Section Inspection - 26/05/2021 - F27X


Item No. 60	Insp. No. 1	Date 26/05/21	Time 15:36	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F27X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F27
Road:	Dappers Lane	Inspected Length:	2.50 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	2.50 m	Downstream Node:	JN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation Grade

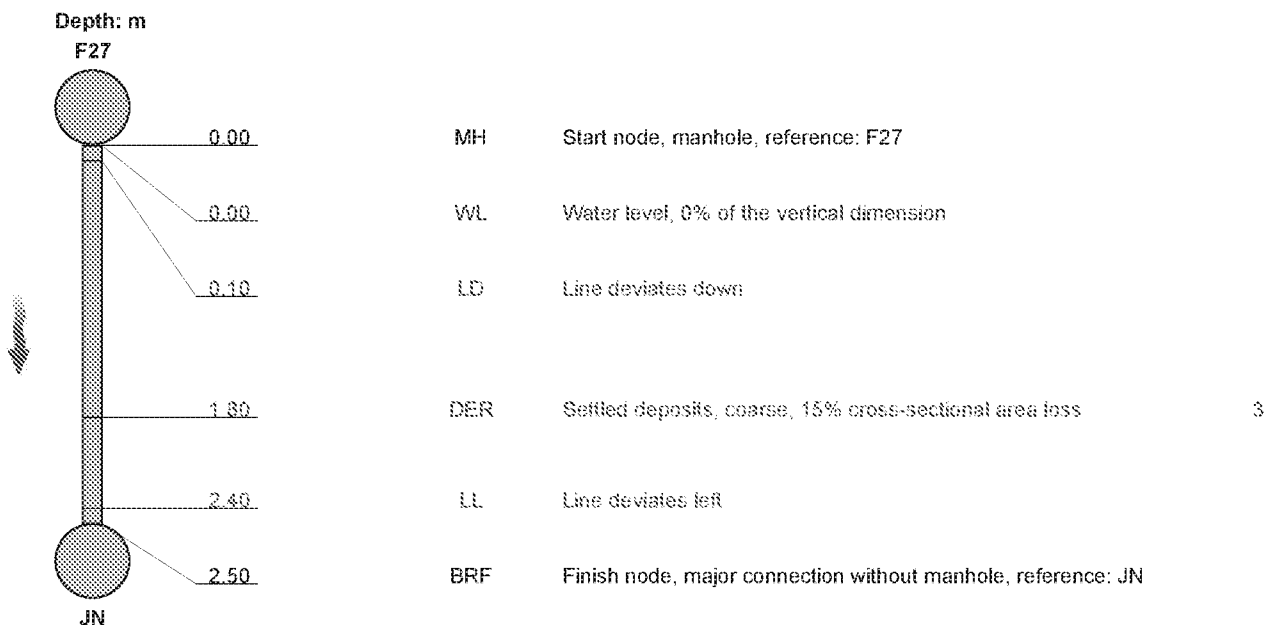

Depth: m


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	1	2.0	0.0	2.0	3.0

Dappers Lane


126

Section Pictures - 26/05/2021 - F27X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
60	Downstream	F27X		

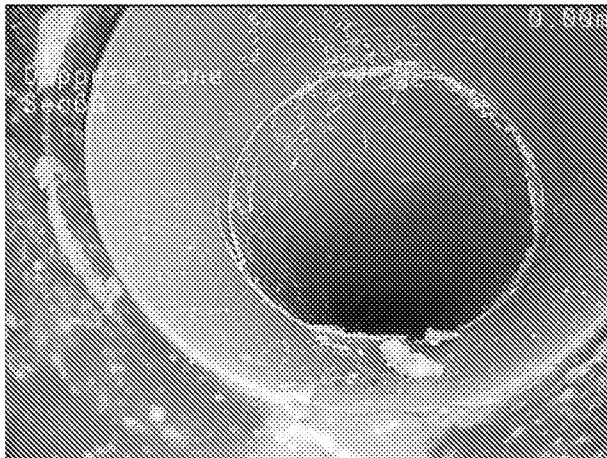


1, 00:00:00, 0.00 m
Start node, manhole, reference: F27

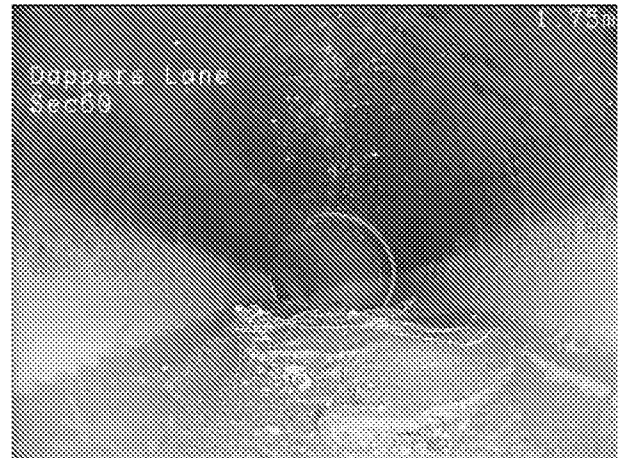

2, 00:00:23, 1.80 m
Settled deposits, coarse, 15% cross-sectional area loss



3, 00:00:30, 2.40 m
Line deviates left

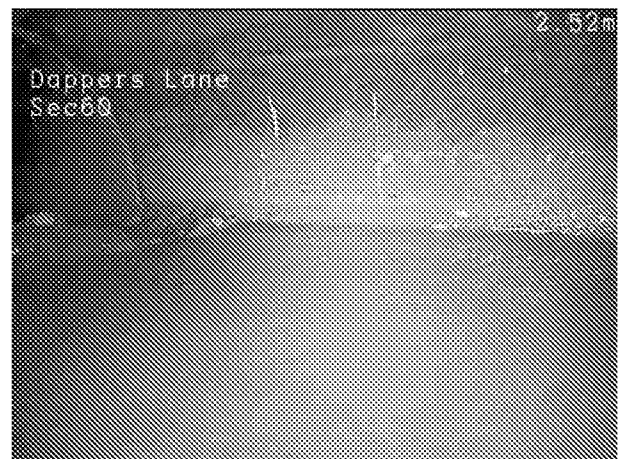

4, 00:00:44, 2.50 m
Finish node, major connection without manhole, reference: JN



Section Inspection - 26/05/2021 - SP43X


Item No. 61	Insp. No. 1	Date 26/05/21	Time 15:42	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR SP43X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	SP43
Road:	Dappers Lane	Inspected Length:	1.90 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	1.90 m	Downstream Node:	F28
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation Grade

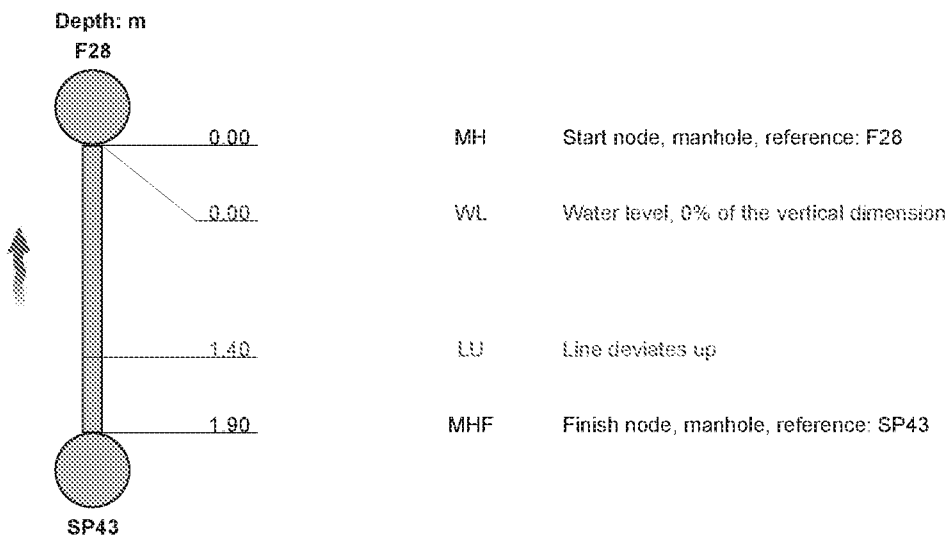

Depth: m

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane

128



Section Pictures - 26/05/2021 - SP43X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
61	Upstream	SP43X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F28



2, 00:00:17, 1.40 m
Line deviates up



3, 00:00:20, 1.90 m
Finish node, manhole, reference: SP43



Section Inspection - 26/05/2021 - SP44X

Item No. 62	Insp. No. 1	Date 26/05/21	Time 15:43	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR SP44X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	SP44
Road:	Dappers Lane	Inspected Length:	8.10 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	8.10 m	Downstream Node:	F28
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:70 Position [m] Code Observation Grade

Depth: m

F28



0.00

MH

Start node, manhole, reference: F28

0.00

WL

Water level, 0% of the vertical dimension

1.80

LR

Line deviates right

7.80

LU

Line deviates up

8.10

MHF

Finish node, manhole, reference: SP44

SP44

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane

130



Section Pictures - 26/05/2021 - SP44X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
62	Upstream	SP44X		




1, 00:00:00, 0.00 m
Start node, manhole, reference: F28



2, 00:00:20, 1.90 m
Line deviates right

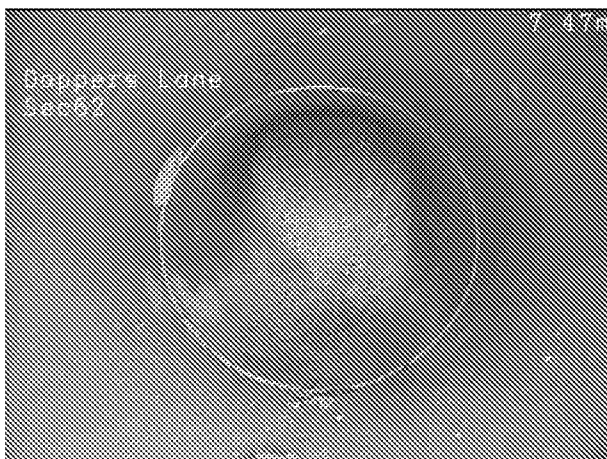

3, 00:00:36, 7.60 m
Line deviates up

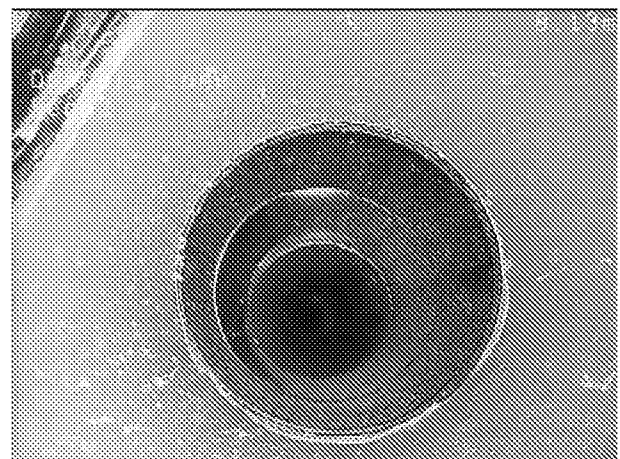

4, 00:00:40, 8.10 m
Finish node, manhole, reference: SP44



Section Inspection - 26/05/2021 - F28X


Item No. 63	Insp. No. 1	Date 26/05/21	Time 15:45	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F28X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F28
Road:	Dappers Lane	Inspected Length:	2.70 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	2.70 m	Downstream Node:	JN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation Grade

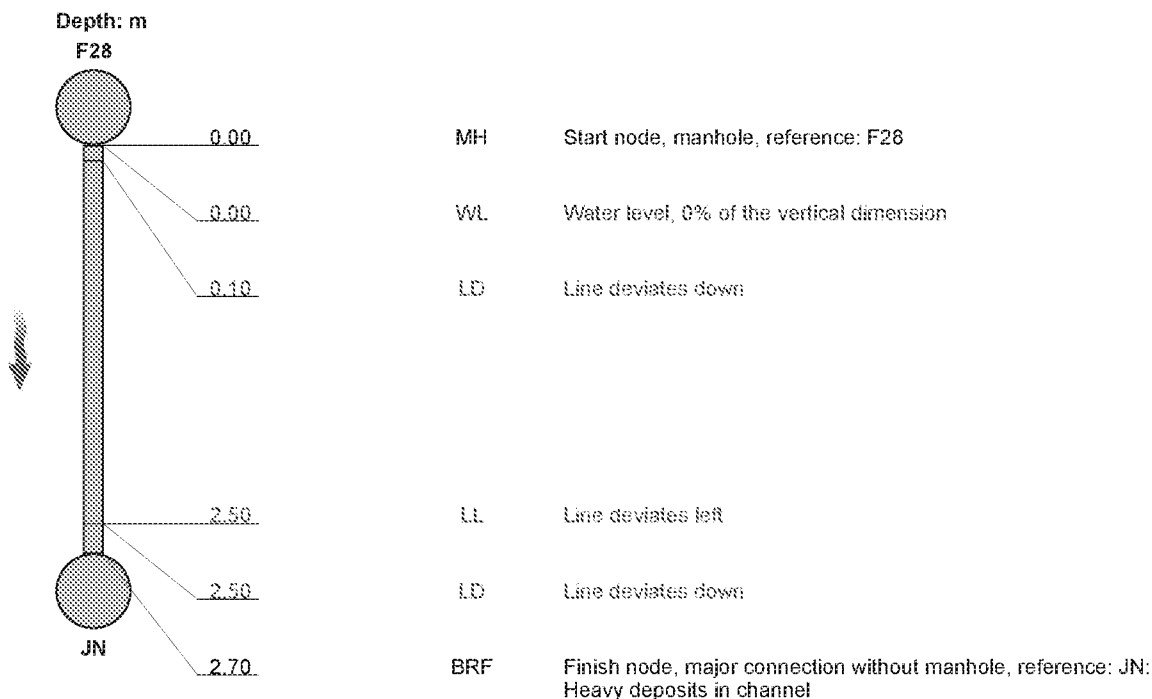

Depth: m


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane


132

Section Pictures - 26/05/2021 - F28X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
63	Downstream	F28X		

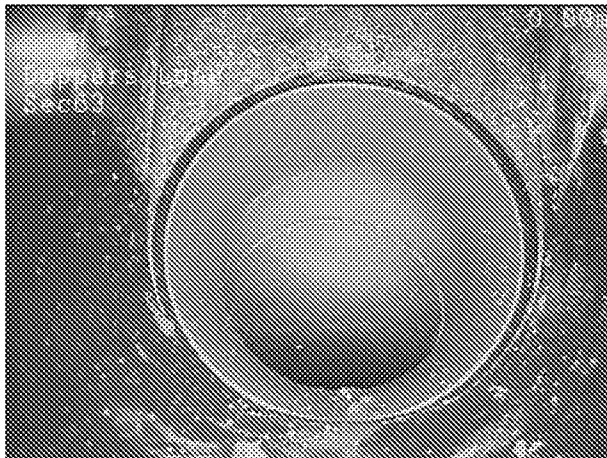

1, 00:00:00, 0.00 m
Start node, manhole, reference: F28

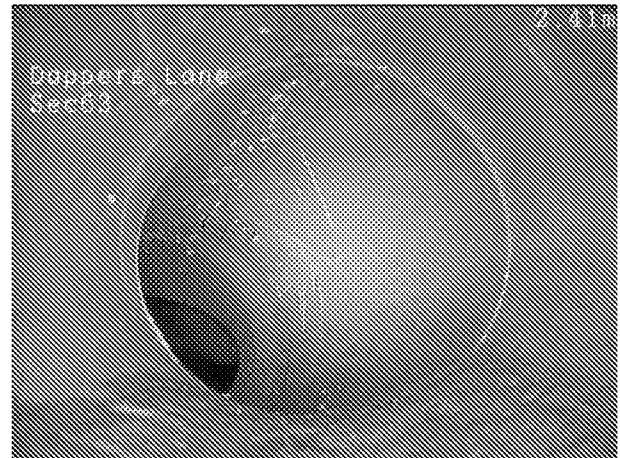

2, 00:00:33, 2.50 m
Line deviates left



3, 00:00:40, 2.70 m
Finish node, major connection without manhole, reference: JN,
Heavy deposits in channel



Section Inspection - 27/05/2021 - RE4X

Item No. 64	Insp. No. 1	Date 27/05/21	Time 8:46	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RE4X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RE4
Road:	Dappers Lane	Inspected Length:	10.10 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	10.10 m	Downstream Node:	S15
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:88	Position [m]	Code	Observation	Grade
Depth: m				
S15				
	0.00	MH	Start node, manhole, reference: S15	
	0.00	WL	Water level, 0% of the vertical dimension	
	0.20	LR	Line deviates right	
	1.20	JN	Junction at 3 o'clock, 100mm dia	
	1.60	WL	Water level, 5% of the vertical dimension	
	5.60	JN	Junction at 3 o'clock, 100mm dia	
	9.70	JN	Junction at 3 o'clock, 100mm dia	
	9.90	LU	Line deviates up	
RE4	10.10	MHF	Finish node, manhole, reference: RE4	
Depth: m				

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane

134




Section Pictures - 27/05/2021 - RE4X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
64	Upstream	RE4X		




1, 00:00:00, 0.00 m
Start node, manhole, reference: S15

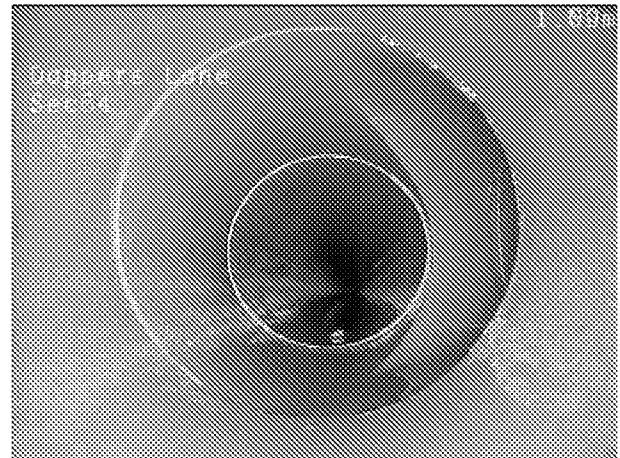

2, 00:00:13, 1.20 m
Junction at 3 o'clock, 100mm dia

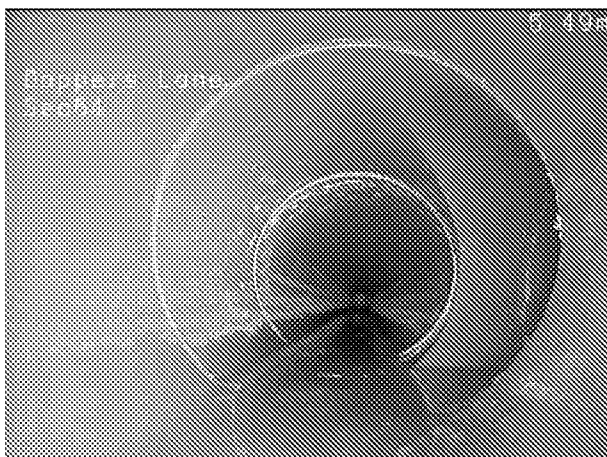

3, 00:00:47, 5.60 m
Junction at 3 o'clock, 100mm dia

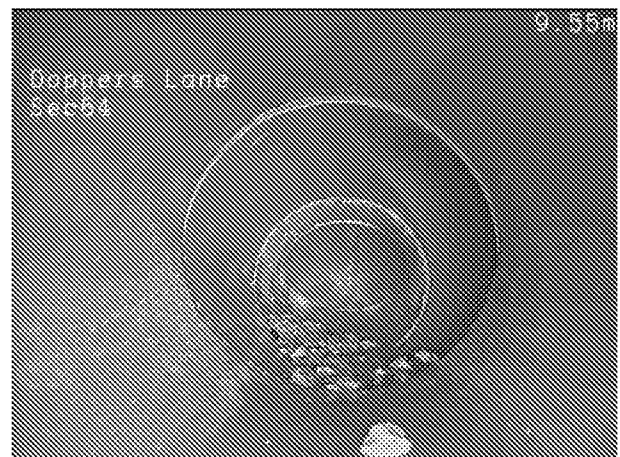

4, 00:01:09, 9.70 m
Junction at 3 o'clock, 100mm dia



5, 00:01:14, 10.10 m
Finish node, manhole, reference: RE4



Section Inspection - 27/05/2021 - S17X

Item No. 65	Insp. No. 1	Date 27/05/21	Time 8:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR S17X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	S17
Road:	Dappers Lane	Inspected Length:	11.90 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	11.90 m	Downstream Node:	S1
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:103 Position [m] Code Observation Grade

Depth: m

S17



0.00

MH

Start node, manhole, reference: S17

0.00

WL

Water level, 0% of the vertical dimension

7.30

WL

Water level, 5% of the vertical dimension

8.80

WL

Water level, 0% of the vertical dimension

11.90

MHF

Finish node, manhole, reference: S1



S1

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane


136

Section Pictures - 27/05/2021 - S17X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
65	Downstream	S17X		




1, 00:00:03, 0.00 m
Water level, 0% of the vertical dimension

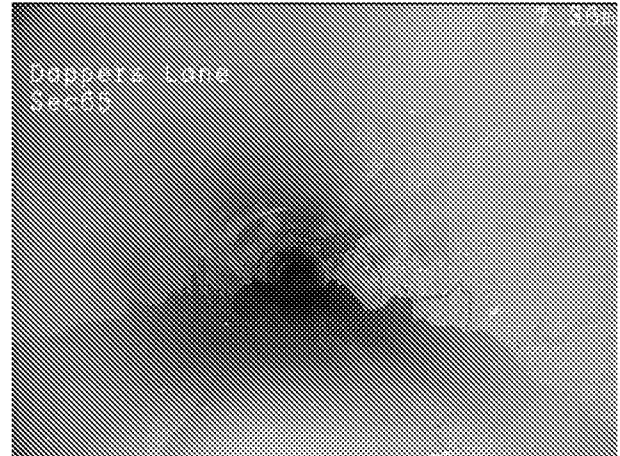

2, 00:00:36, 7.30 m
Water level, 5% of the vertical dimension

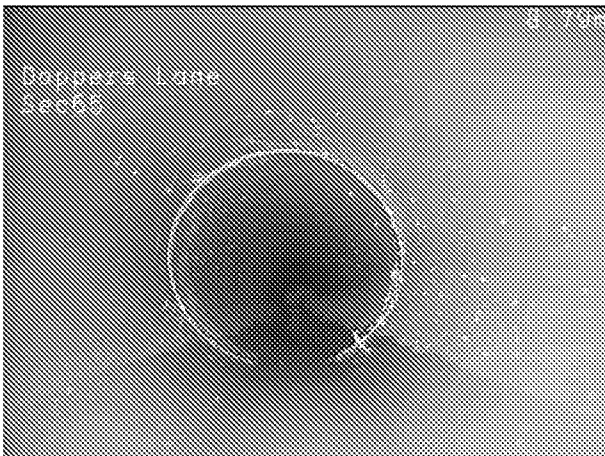

3, 00:00:49, 8.80 m
Water level, 0% of the vertical dimension

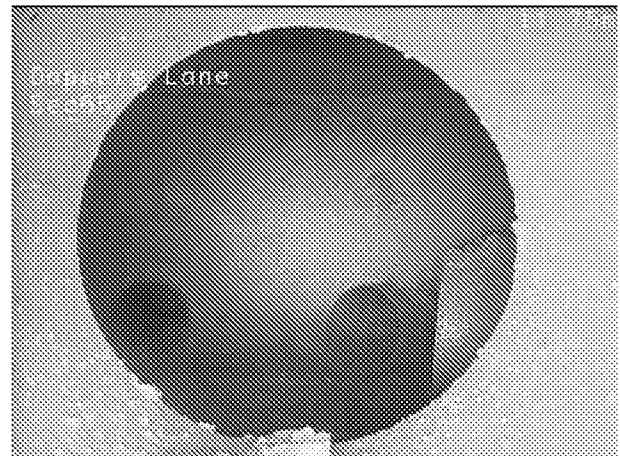

4, 00:01:06, 11.90 m
Finish node, manhole, reference: S1



Section Inspection - 27/05/2021 - RE6X

Item No. 66	Insp. No. 1	Date 27/05/21	Time 9:32	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RE6X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RE6
Road:	Dappers Lane	Inspected Length:	26.20 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	26.20 m	Downstream Node:	S1
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:226	Position [m]	Code	Observation	Grade
Depth: m				
S1				
0.00		MH	Start node, manhole, reference: S1	
0.00		WL	Water level, 0% of the vertical dimension	
8.60		JN	Junction at 3 o'clock, 100mm dia	
13.10		JN	Junction at 10 o'clock, 100mm dia	
15.10		JN	Junction at 3 o'clock, 100mm dia	
15.60		JN	Junction at 3 o'clock, 100mm dia	
16.20		WL	Water level, 5% of the vertical dimension	
17.30		WL	Water level, 10% of the vertical dimension	
19.00		WL	Water level, 5% of the vertical dimension	
19.80		WL	Water level, 0% of the vertical dimension	
22.80		JN	Junction at 9 o'clock, 100mm dia	
23.50		JN	Junction at 9 o'clock, 100mm dia	
25.80		LU	Line deviates up	
26.20		MHF	Finish node, manhole, reference: RE6	
RE6				
Depth: m				

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane

138

Section Pictures - 27/05/2021 - RE6X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
66	Upstream	RE6X		




1, 00:00:13, 0.00 m
Water level, 0% of the vertical dimension



2, 00:00:43, 8.60 m
Junction at 3 o'clock, 100mm dia



3, 00:01:04, 13.10 m
Junction at 10 o'clock, 100mm dia

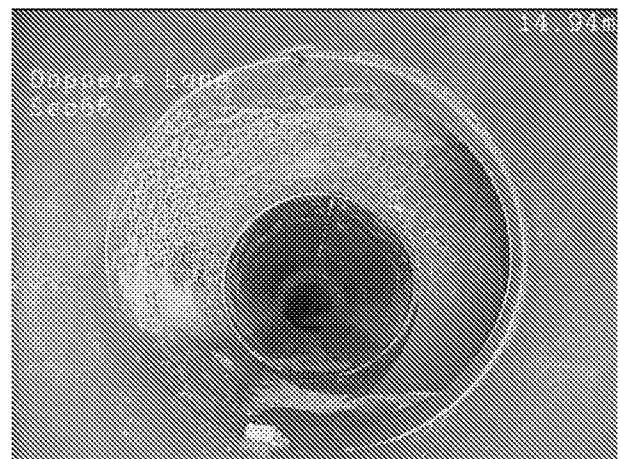

4, 00:01:11, 15.10 m
Junction at 3 o'clock, 100mm dia



5, 00:01:15, 15.60 m
Junction at 3 o'clock, 100mm dia




6, 00:01:19, 16.20 m
Water level, 5% of the vertical dimension



Section Pictures - 27/05/2021 - RE6X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
66	Upstream	RE6X		

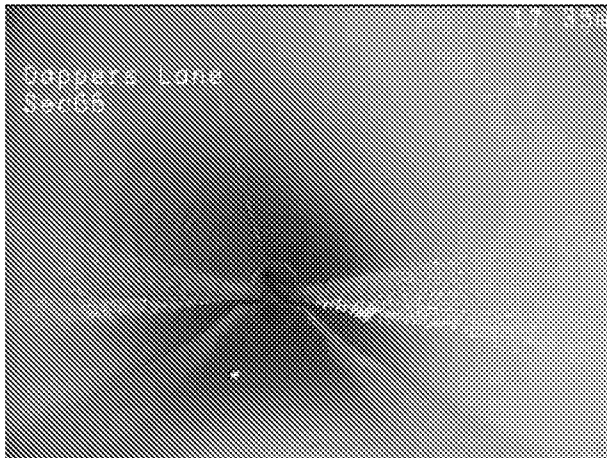

7, 00:01:27, 17.30 m
Water level, 10% of the vertical dimension



8, 00:01:41, 19.00 m
Water level, 5% of the vertical dimension




9, 00:01:51, 19.80 m
Water level, 0% of the vertical dimension



10, 00:02:04, 22.80 m
Junction at 9 o'clock, 100mm dia



11, 00:02:10, 23.50 m
Junction at 9 o'clock, 100mm dia

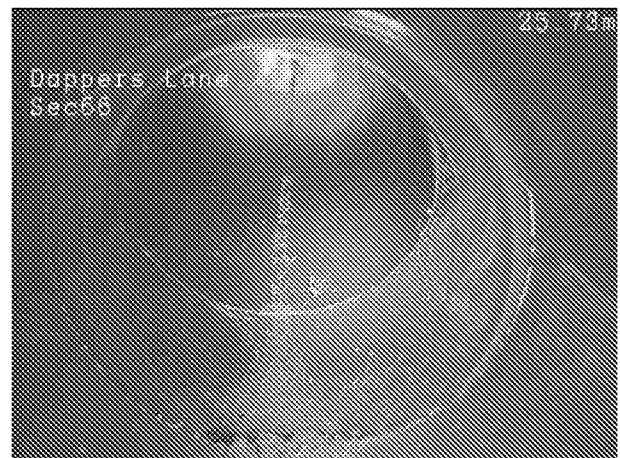

12, 00:02:22, 25.80 m
Line deviates up



Section Pictures - 27/05/2021 - RE6X

Item No.
66

Inspection Direction
Upstream

PLR
RE6X

Client's Job Ref

Contractor's Job Ref



13, 00:02:28, 26.20 m
Finish node, manhole, reference: RE6



Section Inspection - 27/05/2021 - S19X

Item No. 67	Insp. No. 1	Date 27/05/21	Time 9:38	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR S19X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	S19
Road:	Dappers Lane	Inspected Length:	12.40 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	12.40 m	Downstream Node:	S1
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:107 Position [m] Code Observation Grade

Depth: m

S1



0.00

MH

Start node, manhole, reference: S1

0.00

WL

Water level, 0% of the vertical dimension

5.30

LL

Line deviates left

12.10

LR

Line deviates right

12.40

MHF

Finish node, manhole, reference: S19

S19

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane

142



Section Pictures - 27/05/2021 - S19X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
67	Upstream	S19X		




1, 00:00:26, 0.00 m
Water level, 0% of the vertical dimension



2, 00:00:55, 5.30 m
Line deviates left

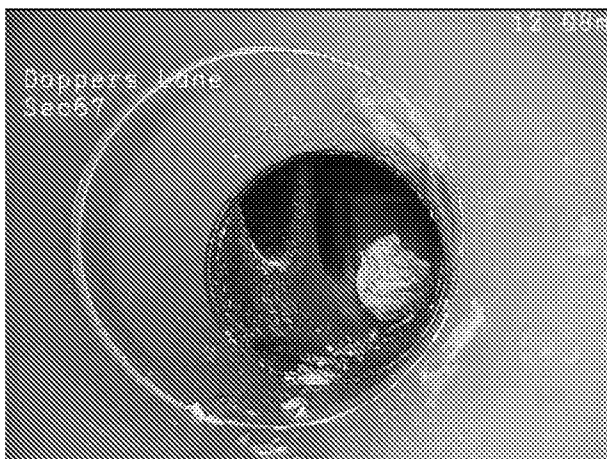

3, 00:01:20, 12.10 m
Line deviates right

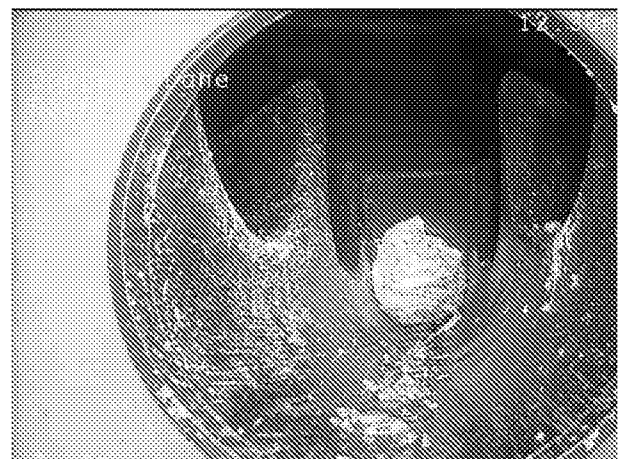

4, 00:01:27, 12.40 m
Finish node, manhole, reference: S19



Section Inspection - 27/05/2021 - RGX


Item No. 68	Insp. No. 1	Date 27/05/21	Time 9:57	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RGX
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RG
Road:	Dappers Lane	Inspected Length:	2.20 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	2.20 m	Downstream Node:	S1
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation Grade

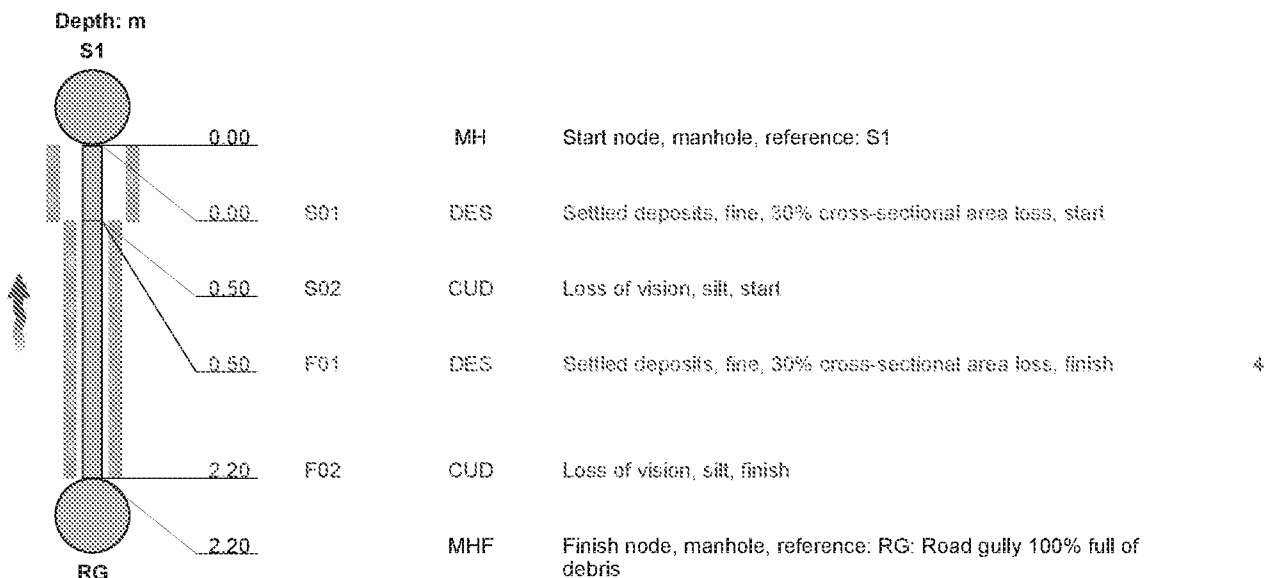

Depth: m

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	1	5.0	2.3	5.0	4.0

Dappers Lane

144



Section Pictures - 27/05/2021 - RGX

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
68	Upstream	RGX		



1, 00:00:00, 0.00 m
Start node, manhole, reference: S1



2, 00:00:00, 0.00 m
Settled deposits, fine, 30% cross-sectional area loss, start



3, 00:00:26, 2.20 m
Finish node, manhole, reference: RG, Road gully 100% full of debris



Section Inspection - 27/05/2021 - S1X

Item No. 69	Insp. No. 1	Date 27/05/21	Time 10:07	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR S1X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	S1
Road:	Dappers Lane	Inspected Length:	15.40 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	15.40 m	Downstream Node:	S2
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:133 Position [m] Code Observation Grade

Depth: m

S1



0.00

MH

Start node, manhole, reference: S1

0.00

WL

Water level, 0% of the vertical dimension

6.80

WL

Water level, 5% of the vertical dimension

6.80

WL

Water level, 10% of the vertical dimension

8.20

WL

Water level, 5% of the vertical dimension

14.00

WL

Water level, 0% of the vertical dimension

15.40

MHF

Finish node, manhole, reference: S2

S2

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Dappers Lane

146



Section Pictures - 27/05/2021 - S1X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
69	Downstream	S1X		

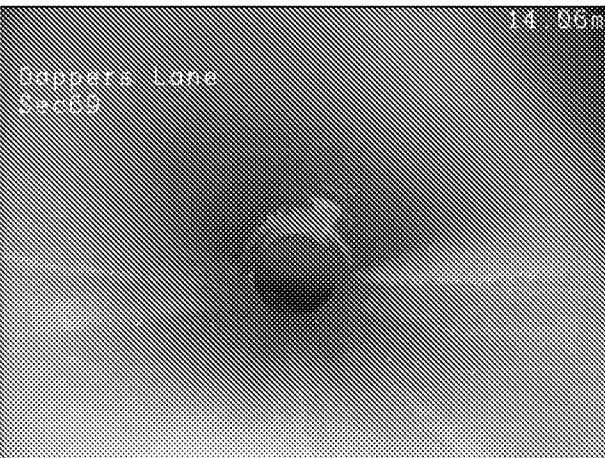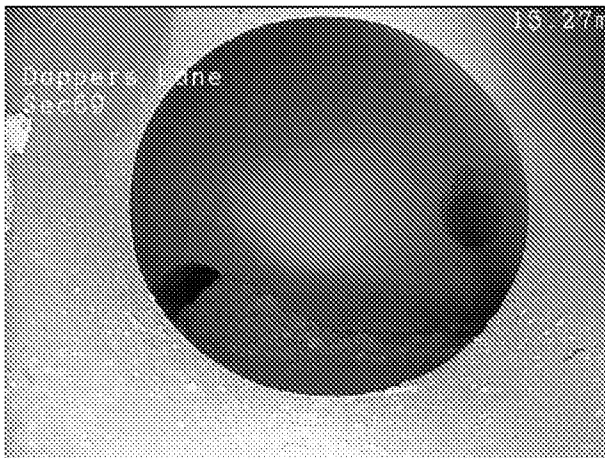 1, 00:00:01, 0.00 m Water level, 0% of the vertical dimension	 2, 00:00:48, 6.60 m Water level, 5% of the vertical dimension
 3, 00:00:50, 6.80 m Water level, 10% of the vertical dimension	 4, 00:01:05, 8.20 m Water level, 5% of the vertical dimension
 5, 00:01:22, 14.00 m Water level, 0% of the vertical dimension	 6, 00:01:26, 15.40 m Finish node, manhole, reference: S2



Section Inspection - 27/05/2021 - LDX

Item No. 70	Insp. No. 1	Date 27/05/21	Time 11:00	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR LDX
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	LD
Road:	Dappers Lane	Inspected Length:	14.60 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	14.60 m	Downstream Node:	S22
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:126 Position [m] Code Observation Grade

Depth: m

S22



0.00

MH

Start node, manhole, reference: S22

0.00

WL

Water level, 0% of the vertical dimension

14.60

REF

Finish node, rodding eye, reference: LD: Assumed end point

LD

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations


STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane


148

Section Pictures - 27/05/2021 - LDX

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
70	Upstream	LDX		

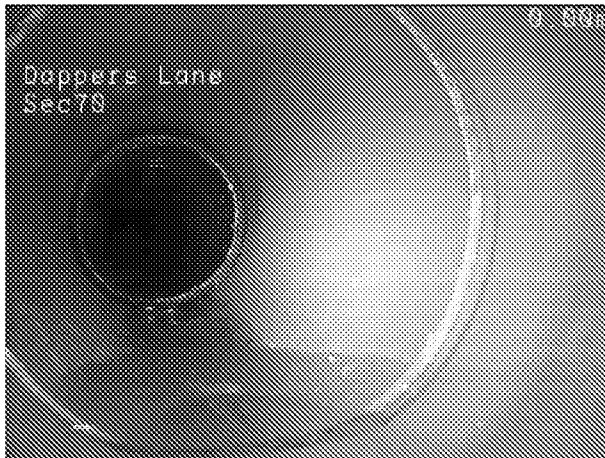

1, 00:00:00, 0.00 m
Start node, manhole, reference: S22

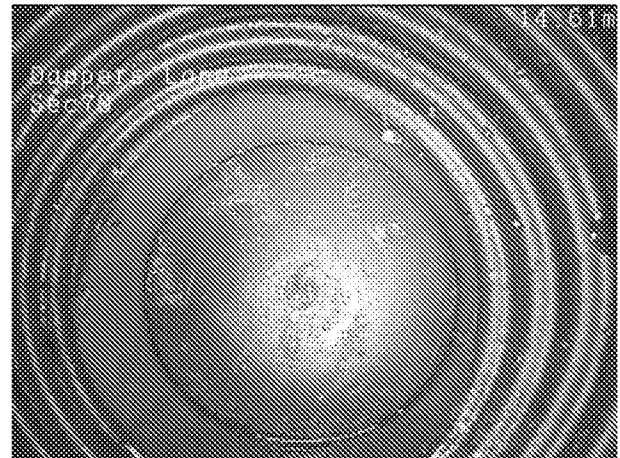

2, 00:01:11, 14.60 m
Finish node, rodding eye, reference: LD, Assumed end point



Section Inspection - 27/05/2021 - RE8X

Item No. 71	Insp. No. 1	Date 27/05/21	Time 11:01	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RE8X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RE8
Road:	Dappers Lane	Inspected Length:	11.50 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	11.50 m	Downstream Node:	S22
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:100 Position [m] Code Observation Grade

Depth: m

S22



0.00

MH

Start node, manhole, reference: S22

0.00

WL

Water level, 0% of the vertical dimension

5.60

JN

Junction at 9 o'clock, 100mm dia

11.40

JN

Junction at 9 o'clock, 100mm dia

11.50

SA

Survey abandoned: Capped, rodding eye not installed

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0


Dappers Lane

150



Section Pictures - 27/05/2021 - RE8X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
71	Upstream	RE8X		

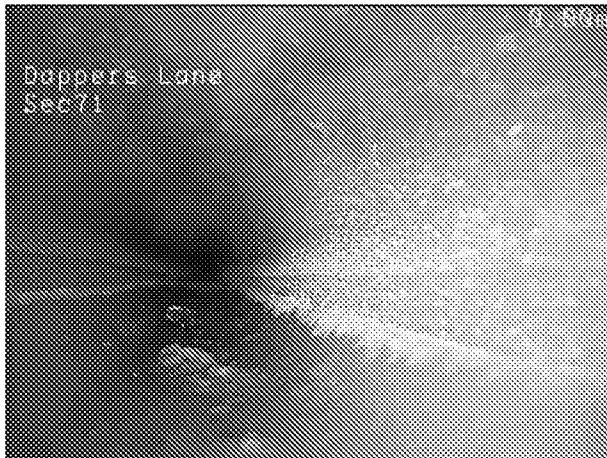

1, 00:00:00, 0.00 m
Start node, manhole, reference: S22



2, 00:00:20, 5.60 m
Junction at 9 o'clock, 100mm dia

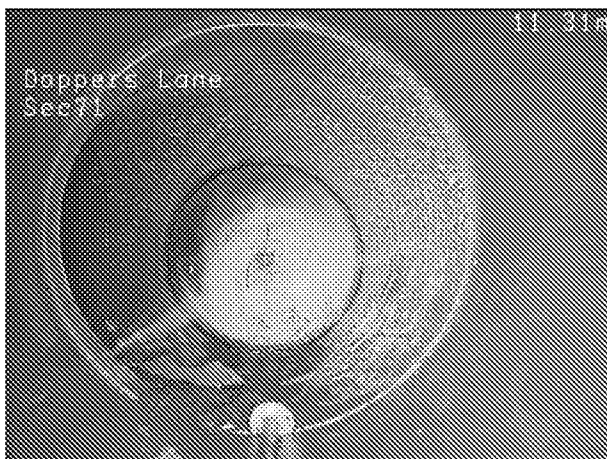

3, 00:00:33, 11.40 m
Junction at 9 o'clock, 100mm dia



4, 00:00:39, 11.50 m
Survey abandoned, Capped, rodding eye not installed



Section Inspection - 27/05/2021 - RE9X

Item No. 72	Insp. No. 1	Date 27/05/21	Time 11:04	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RE9X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RE9
Road:	Dappers Lane	Inspected Length:	13.30 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	13.30 m	Downstream Node:	S22
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:115 Position [m] Code Observation Grade

Depth: m

S22



0.00

MH

Start node, manhole, reference: S22

0.00

WL

Water level, 10% of the vertical dimension

2.40

JN

Junction at 3 o'clock, 100mm dia

3.70

WL

Water level, 5% of the vertical dimension

6.00

WL

Water level, 0% of the vertical dimension

8.10

JN

Junction at 3 o'clock, 100mm dia

13.20

JN

Junction at 3 o'clock, 100mm dia

13.30

SA

Survey abandoned: Capped, rodding eye not installed

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0


Dappers Lane

152




Section Pictures - 27/05/2021 - RE9X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
72	Upstream	RE9X		

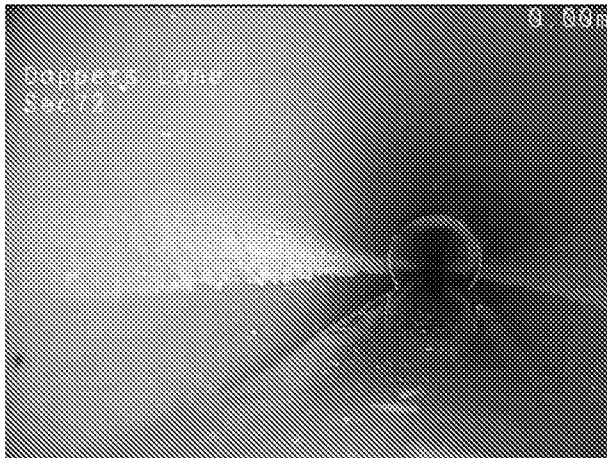

1, 00:00:11, 0.00 m
Water level, 10% of the vertical dimension

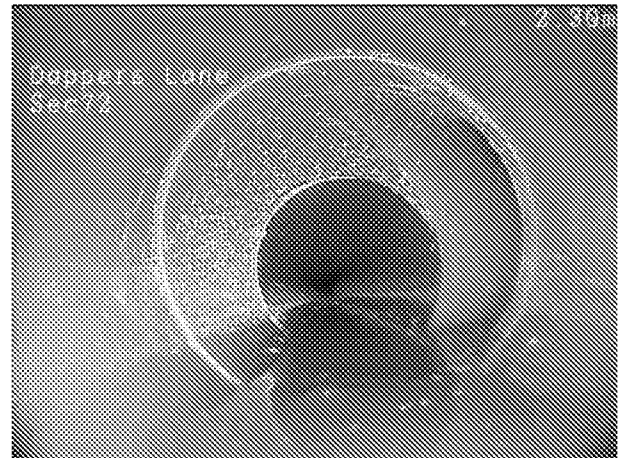

2, 00:00:39, 2.40 m
Junction at 3 o'clock, 100mm dia

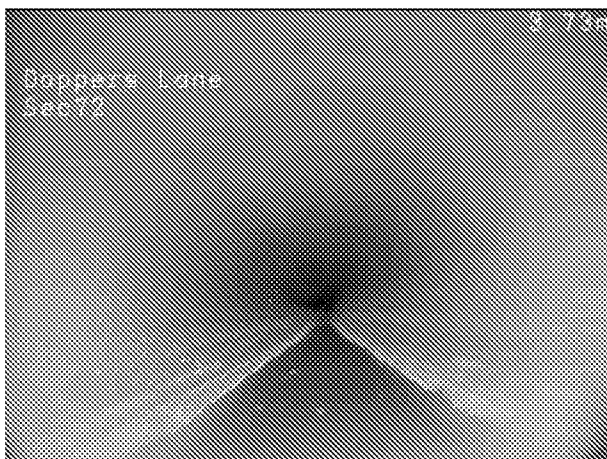

3, 00:00:48, 3.70 m
Water level, 5% of the vertical dimension



4, 00:01:05, 8.10 m
Junction at 3 o'clock, 100mm dia



5, 00:01:17, 13.20 m
Junction at 3 o'clock, 100mm dia



6, 00:01:21, 13.30 m
Survey abandoned, Capped, rodding eye not installed



Section Inspection - 27/05/2021 - LD 2X

Item No. 73	Insp. No. 1	Date 27/05/21	Time 11:08	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR LD 2X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	LD 2
Road:	Dappers Lane	Inspected Length:	14.40 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	14.40 m	Downstream Node:	S22
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:125 Position [m] Code Observation Grade

Depth: m

S22



0.00

MH

Start node, manhole, reference: S22

0.00

WL

Water level, 0% of the vertical dimension

0.10

LR

Line deviates right

14.30

LU

Line deviates up

14.40

MHF

Finish node, manhole, reference: LD 2

LD 2

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations


STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane


154

Section Pictures - 27/05/2021 - LD 2X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
73	Upstream	LD 2X		

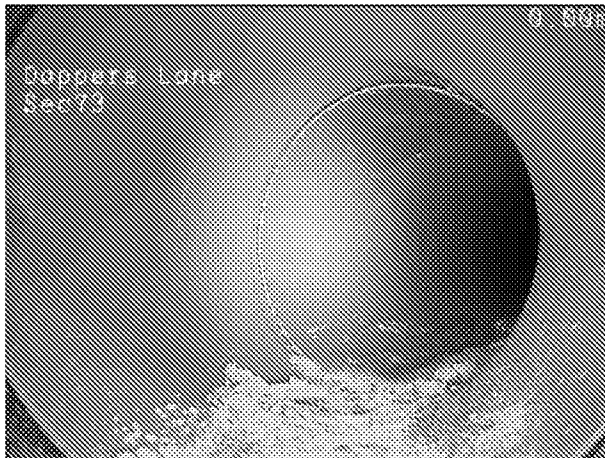

1, 00:00:00, 0.00 m
Start node, manhole, reference: S22

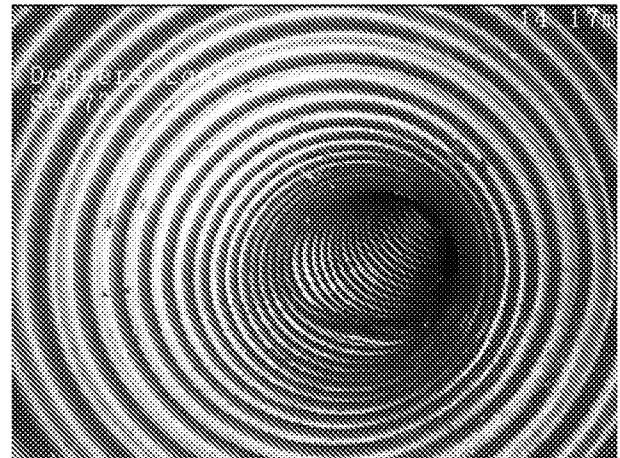

2, 00:01:43, 14.30 m
Line deviates up

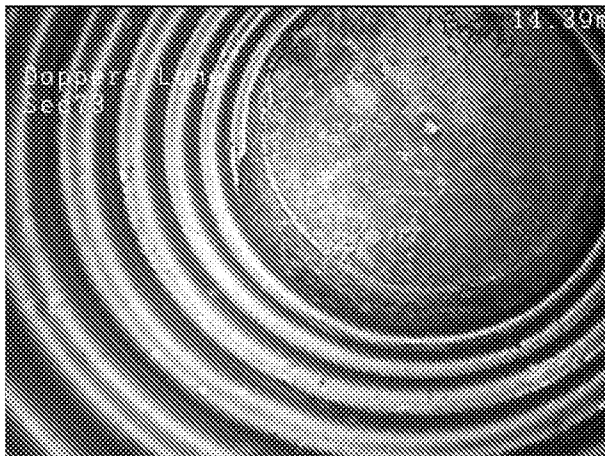

3, 00:01:50, 14.40 m
Finish node, manhole, reference: LD 2



Section Inspection - 27/05/2021 - S22X

Item No. 74	Insp. No. 1	Date 27/05/21	Time 11:15	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR S22X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	S22
Road:	Dappers Lane	Inspected Length:	21.80 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	21.80 m	Downstream Node:	S2
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:186	Position [m]	Code	Observation	Grade
Depth: m				
S22				
0.00		MH	Start node, manhole, reference: S22	
0.00		WL	Water level, 0% of the vertical dimension	
1.10		JN	Junction at 3 o'clock, 100mm dia	
8.50		DER	Settled deposits, coarse, 5% cross-sectional area loss	3
9.20		WL	Water level, 10% of the vertical dimension	
10.20		WL	Water level, 20% of the vertical dimension. Continuous	
10.70		JN	Junction at 1 o'clock, 100mm dia	
11.30		WL	Water level, 10% of the vertical dimension	
12.50	S01	DER	Settled deposits, coarse, 10% cross-sectional area loss, start	
17.00	F01	DER	Settled deposits, coarse, 10% cross-sectional area loss, finish	3
17.60		WL	Water level, 5% of the vertical dimension	
19.90		LL	Line deviates left	
21.80		MHF	Finish node, manhole, reference: S2	
S2				
Depth: m				

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	2	2.0	0.6	12.0	3.0

Dappers Lane

156




Section Pictures - 27/05/2021 - S22X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
74	Downstream	S22X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: S22

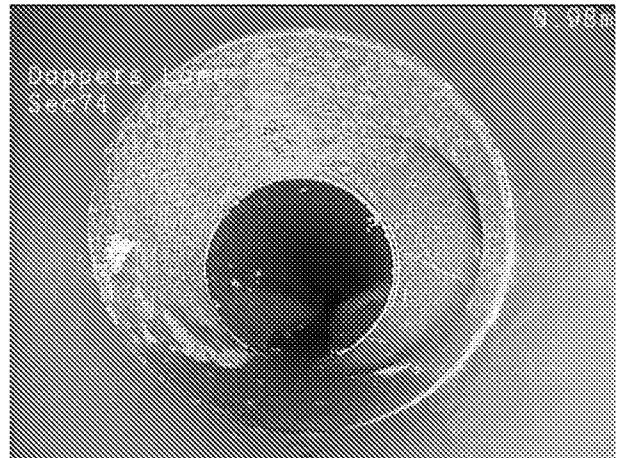

2, 00:00:13, 1.10 m
Junction at 3 o'clock, 100mm dia

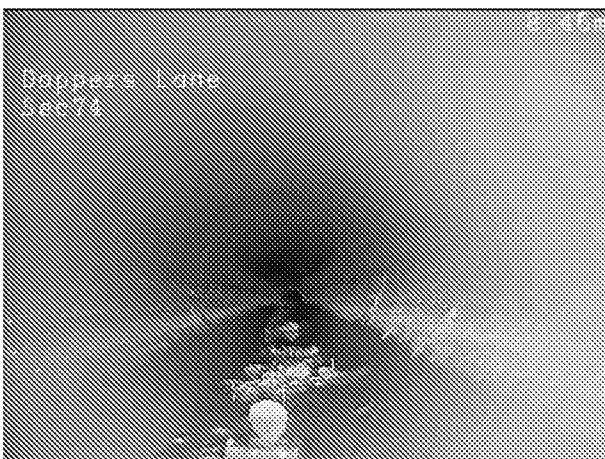


3, 00:00:48, 8.50 m
Settled deposits, coarse, 5% cross-sectional area loss



4, 00:00:53, 9.20 m
Water level, 10% of the vertical dimension




5, 00:01:00, 10.20 m
Water level, 20% of the vertical dimension, Continuous

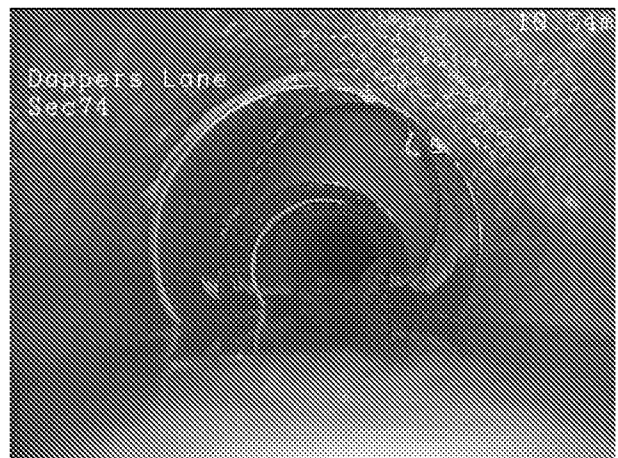

6, 00:01:06, 10.70 m
Junction at 1 o'clock, 100mm dia

Section Pictures - 27/05/2021 - S22X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
74	Downstream	S22X		

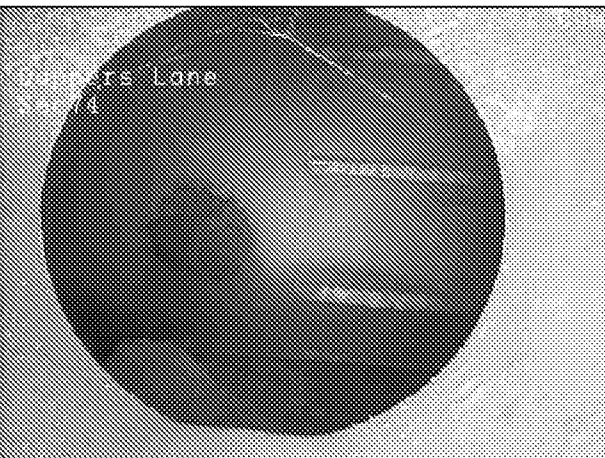	
7, 00:01:47, 11.30 m Water level, 10% of the vertical dimension	8, 00:01:56, 12.50 m Settled deposits, coarse, 10% cross-sectional area loss, start
	
9, 00:02:27, 17.60 m Water level, 5% of the vertical dimension	10, 00:02:35, 19.90 m Line deviates left
	
11, 00:02:43, 21.80 m Finish node, manhole, reference: S2	



Section Inspection - 27/05/2021 - RGX

Item No. 75	Insp. No. 1	Date 27/05/21	Time 11:36	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RGX
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RG
Road:	Dappers Lane	Inspected Length:	2.90 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	2.90 m	Downstream Node:	S2
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	Grade
		0.00	MH	Start node, manhole, reference: S2	
		0.00	WL	Water level, 0% of the vertical dimension	
		0.00	S01	DER	Settled deposits, coarse, 10% cross-sectional area loss, start
		1.40	C01	DER	Settled deposits, coarse, 15% cross-sectional area loss, change 4
		2.90	F01	DER	Settled deposits, coarse, 15% cross-sectional area loss, finish 3
		2.90	MHF	Finish node, manhole, reference: RG: Road gully full	

Depth: m

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	2	7.0	3.8	11.0	4.0

Dappers Lane

159




Section Pictures - 27/05/2021 - RGX


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
75	Upstream	RGX		



1, 00:00:00, 0.00 m
Start node, manhole, reference: S2

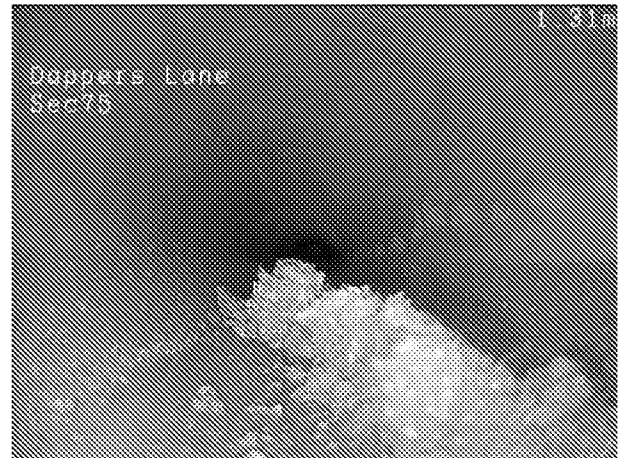

2, 00:00:45, 1.40 m
Settled deposits, coarse, 15% cross-sectional area loss, change

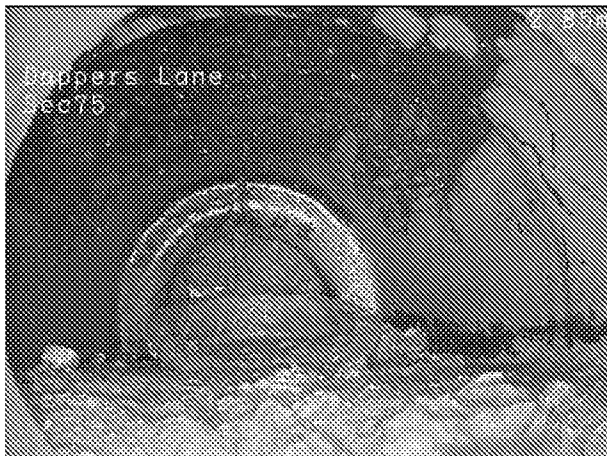

3, 00:01:09, 2.90 m
Finish node, manhole, reference: RG, Road gully full



Section Inspection - 20/07/2021 - S21X

Item No. 76	Insp. No. 1	Date 20/07/21	Time 9:10	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR S21X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	S21
Road:	Dappers Lane	Inspected Length:	12.40 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	12.40 m	Downstream Node:	S2
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:107 Position [m] Code Observation Grade

Depth: m

S21



0.00

MH

Start node, manhole, reference: S21

0.00

WL

Water level, 0% of the vertical dimension

0.10

LL

Line deviates left

6.80

LR

Line deviates right

7.00

WL

Water level, 10% of the vertical dimension

7.20

JN

Junction at 2 o'clock, 100mm dia

12.40

MHF

Finish node, manhole, reference: S2

S2

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations


STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0

Dappers Lane


161

Section Pictures - 20/07/2021 - S21X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
76	Downstream	S21X		

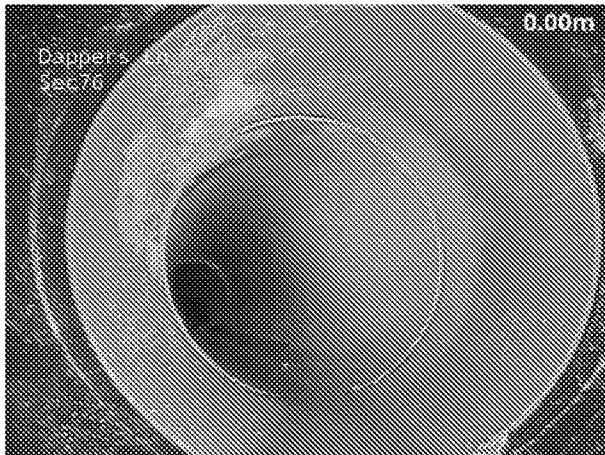

1, 00:00:02, 0.10 m
Line deviates left

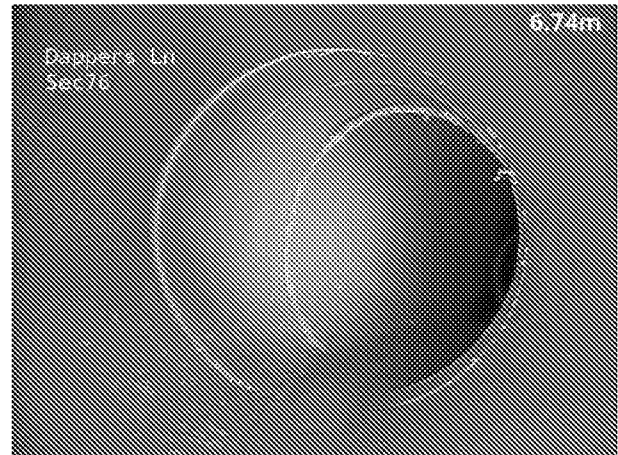


2, 00:00:21, 6.90 m
Line deviates right



3, 00:00:28, 7.00 m
Water level, 10% of the vertical dimension



4, 00:00:32, 7.20 m
Junction at 2 o'clock, 100mm dia

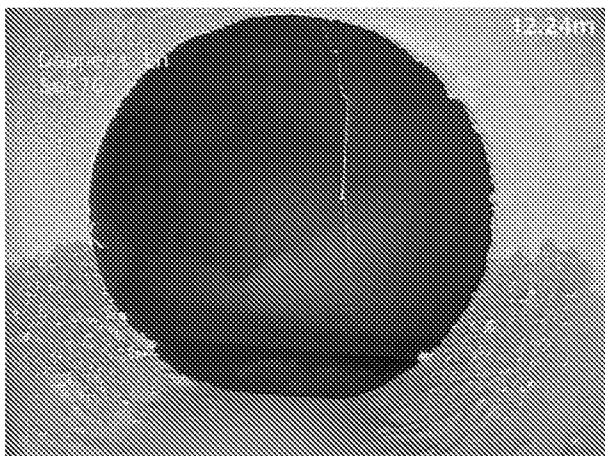

5, 00:00:53, 12.40 m
Finish node, manhole, reference: S2



Section Inspection - 27/05/2021 - S2X

Item No. 77	Insp. No. 1	Date 27/05/21	Time 11:45	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR S2X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	S2
Road:	Dappers Lane	Inspected Length:	8.50 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	8.50 m	Downstream Node:	S4
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:74 Position [m] Code Observation Grade

Depth: m

S2



0.00

MH

Start node, manhole, reference: S2

0.00

WL

Water level, 0% of the vertical dimension

8.50

MHF

Finish node, manhole, reference: S4

S4

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0


Dappers Lane

163




Section Pictures - 27/05/2021 - S2X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
77	Downstream	S2X		

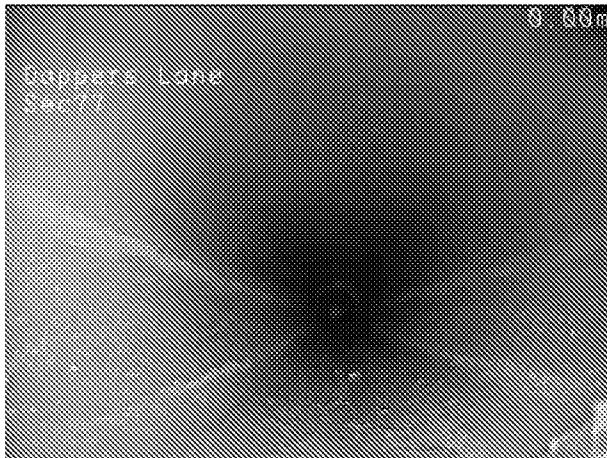

1, 00:00:20, 0.00 m
Water level, 0% of the vertical dimension

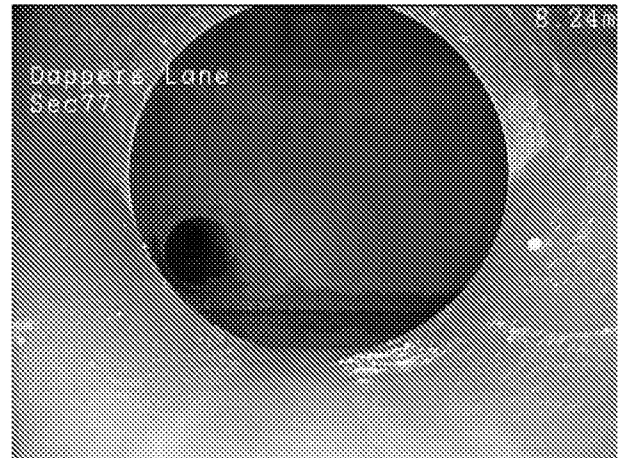

2, 00:01:14, 8.50 m
Finish node, manhole, reference: S4


Section Inspection - 27/05/2021 - RE12X

Item No. 78	Insp. No. 1	Date 27/05/21	Time 12:05	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RE12X
Operator Luke		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Private Drain	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RE12
Road:	Dappers Lane	Inspected Length:	17.70 m	Upstream Pipe Depth:	
Location:	Property or buildings	Total Length:	17.70 m	Downstream Node:	S26
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

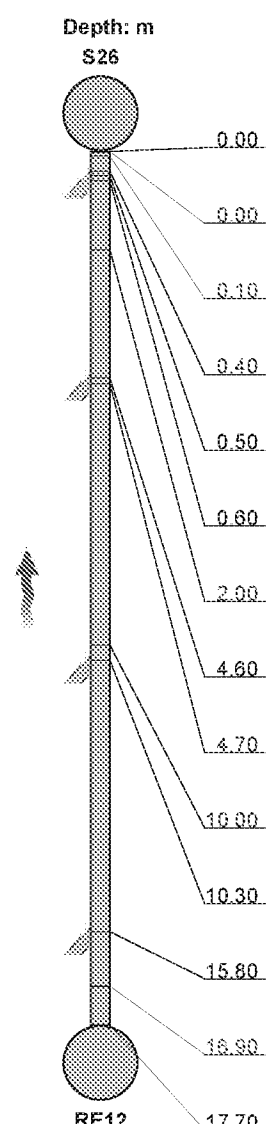Scale: 1:153	Position [m]	Code	Observation	Grade
Depth: m S26 				
	0.00	MH	Start node, manhole, reference: S26	
	0.00	WL	Water level, 0% of the vertical dimension	
	0.10	LR	Line deviates right	
	0.40	WL	Water level, 5% of the vertical dimension	
	0.50	JN	Junction at 3 o'clock, 100mm dia	
	0.60	SR	Sealing ring intruding, loop hanging above centre from 12 o'clock to 3 o'clock	1 / 4
	2.00	WL	Water level, 0% of the vertical dimension	
	4.60	JN	Junction at 3 o'clock, 100mm dia	
	4.70	WL	Water level, 10% of the vertical dimension	
	10.00	WL	Water level, 0% of the vertical dimension	
	10.30	JN	Junction at 3 o'clock, 100mm dia	
	15.80	JN	Junction at 3 o'clock, 100mm dia	
	16.90	LU	Line deviates up	
	17.70	MHF	Finish node, manhole, reference: RE12	
	Depth: m			

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	5.0	0.3	5.0	1.0	1	5.0	0.3	5.0	4.0


Dappers Lane

165




Section Pictures - 27/05/2021 - RE12X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
78	Upstream	RE12X		

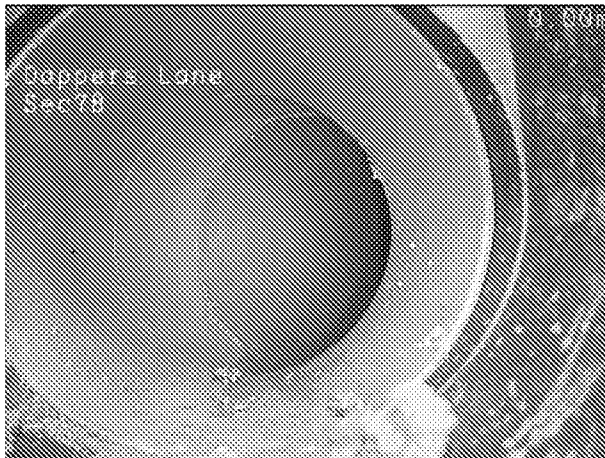

1, 00:00:00, 0.00 m
Start node, manhole, reference: S26

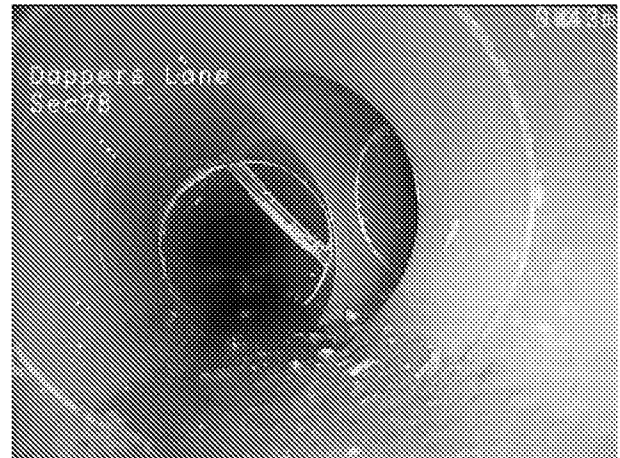


2, 00:00:17, 0.50 m
Junction at 3 o'clock, 100mm dia

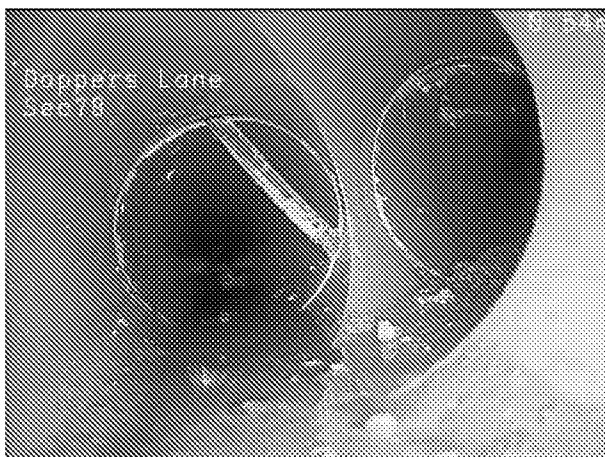

3, 00:00:22, 0.60 m
Sealing ring intruding, loop hanging above centre from 12 o'clock to 3 o'clock



4, 00:00:47, 4.60 m
Junction at 3 o'clock, 100mm dia

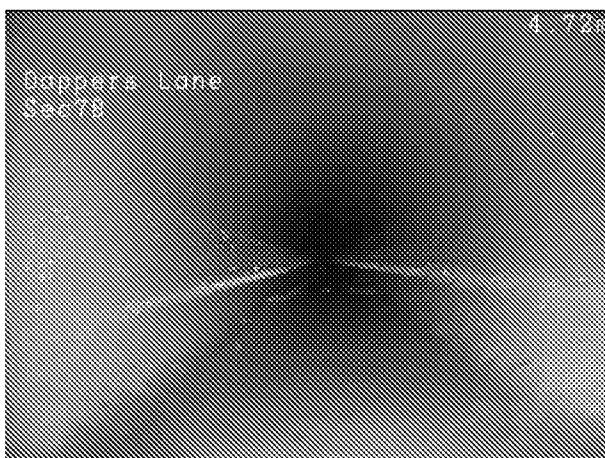

5, 00:00:51, 4.70 m
Water level, 10% of the vertical dimension



6, 00:01:29, 10.30 m
Junction at 3 o'clock, 100mm dia



Section Pictures - 27/05/2021 - RE12X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
78	Upstream	RE12X		

