


Inspection Report

Date: 17/12/24	Job No:	Weather: Dry	Operator: Mick	Section Number 29	PLR:
Present:	Vehicle: WM69 YNA	Camera: Camera 1	Preset:	Cleaned: YES	Grade:
Site; Tye Lane Place: Warblington		Division: District: S.W Tape No: 1		Start MH: F30.1 End MH: MAIN Total Length:	
Purpose: Use: Catchment:	Structural Defects FOUL P1 Schedule	Size/Shape: Circular dia 100mm Material: PLASTIC Lining: Category:			

Position Code Observation

0.0M ST Start Of Survey
0.0M WL Water Level 0%

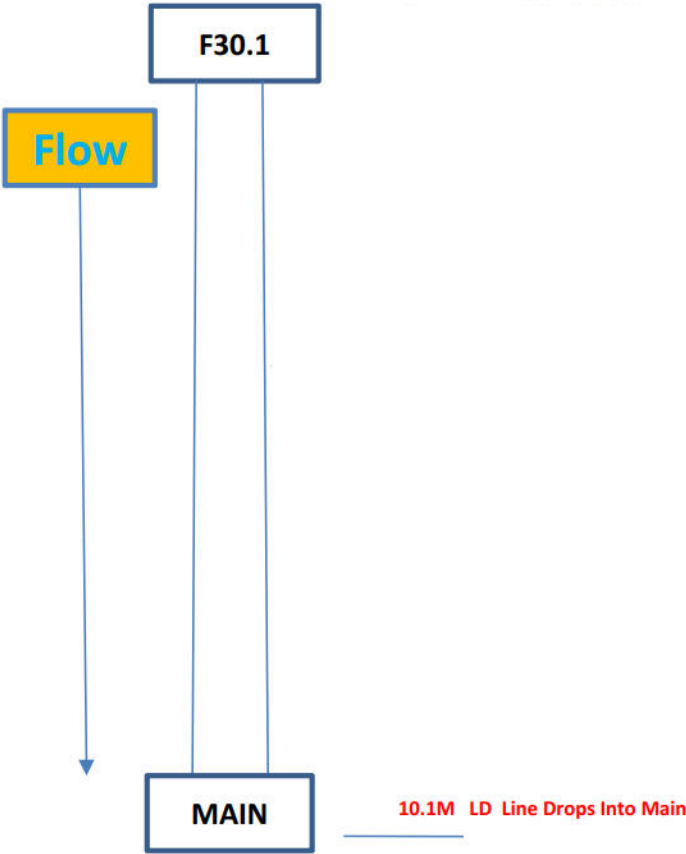

REM ; THERE ARE NO DEFECTS WITH THIS SECTION OF PIPE

Structural Defects	Constructional Features
Service Defects	Miscellaneous Features
