


LOCATION	Pipe I.D.	Pipe Depth	Pipe Height AGL	A.O.D. Ground Level	DATE Some rain in the week and Sat	DATE Heavy rain on some days	DATE Heavy rain start of week	DATE Rained all day on Thursday	DATE Dry mostly all week	DATE No Rain DRY sunny cold week	DATE Heavy rain at end of week	DATE Rain at end of week	DATE Some rain in the week	DATE Heavy rain early in the week
#2 Downview Road YAPTON					8.5	35.0	21.5	25	3.5	0.0	37.0	35.0	17.0	45.0
Weekly Rainfall Amount at BN16 (mm)					on Sun 30th	on Sat 6th	on Sat 13th	on Sat 20th	on Sat 27th	on Sat 3rd	on Sat 10th	on Sat 17th	on Sat 24th	on Sat 31st
Weekly Rainfall Recording Date					Wednesday 3-Dec	Saturday 6-Dec	Saturday 13-Dec	Saturday 20-Dec	Saturday 27-Dec	Saturday 3-Jan	Saturday 10-Jan	Saturday 17-Jan	Saturday 24-Jan	Saturday 31-Jan
Maximum Depth	GWP #1	3010	430		2502	2355	2286	2087	2152	2527	2420	2242	2167	1997
Below Ground Level	(east)	-2580			-2072	-1925	-1856	-1657	-1722	-2097	-1990	-1812	-1737	-1567
Level Above O.D.		3.585		6.595	4.523	4.670	4.739	4.938	4.873	4.498	4.605	4.783	4.858	5.028
Change from Previous						147	69	199	-65	-375	107	178	75	170
Reading BGL on GWP Install														

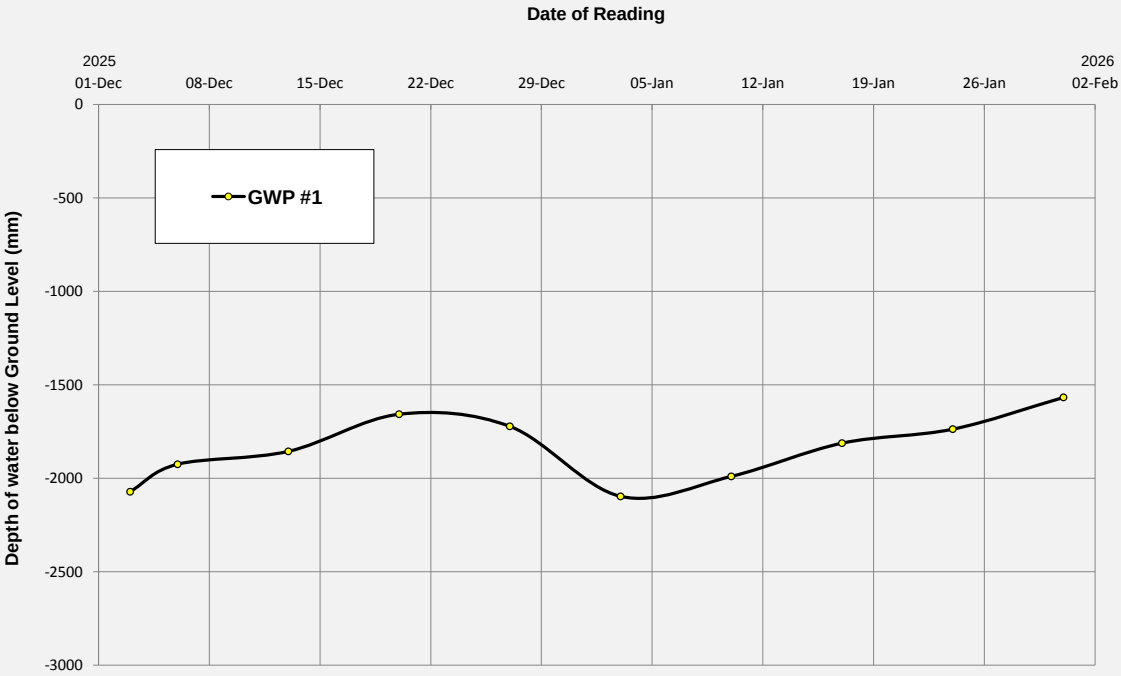

Groundwater Monitoring -- in Groundwater Point GWP#1
