

Water Service SPT

Barratt David Wilson Southampton Limited
Tars Farm, Marshall Close, Barnham, PO22 0DQ
Job Number: MU3602



Developed and implemented by:

Connect it Utility Services Ltd
Foundation House, Hamilton Business Park
Hedge End, SO30 2JR
[REDACTED]
www.cius.co.uk

WATER SERVICE SPT

RAMS

I have read the RAMs and completed a POWRA Yes

INSTALLATION DETAILS

Job number	MU3602
Worksheet Name	Water Service SPT
Nav Reference	.
Water Company	IWNL
House / Plot / Flat	Plot
Plot Number	3
Additional Plot Non Standard Information	
Postal Address	Gospond Road Barnham, Bognor Regis, PO22 0EU
Quantity	1
Task reference	012 - Water Service Complete Inc SPT Per Plot
Comment	.

PRE CONNECTION CHECKS

Stop Cock Fitted Yes

Photo of Stop Cock Fitted



Tracer Wire Connected	N/A
Service Connection Flushed Through	Yes

TEST DETAILS

For service tee connections to PE mains, a two-minute hydraulic pressure test at 1.5 times the nominal pressure rating of the pipe or fitting which ever is the lower shall be applied to the fused fitting prior to tapping in accordance with our WIRs procedure.

Test Pass or Fail

Pass

MAIN CONNECTION DETAILS

Photo Confirming service pipe at correct depth and insulated



Photo of connection onto Main



Photo of Water Meter box / Boundary Box



NEW METER DETAILS

Meter Serial Number	H25yu341409
As Installed Meter Reading	00000
Distance to LHS of front door (metres):	2.5
Distance to RHS of front door (metres):	
Distance to back of kerb (metres):	1.6

NEW METER LOCATION DETAILS

Location Ground Type	Unmade Ground
Service Pipe Length (m)	9.6
Service Pipe Size (mm)	25mm
Service Pipe Material	PE
Main Size	63mm

SIGN OFF

I confirm the above information is correct

Name	Kenny Clark
Signed Date	Fri Oct 03 2025 14:55 GMT





Photo of New Meter



Photo of Sketch

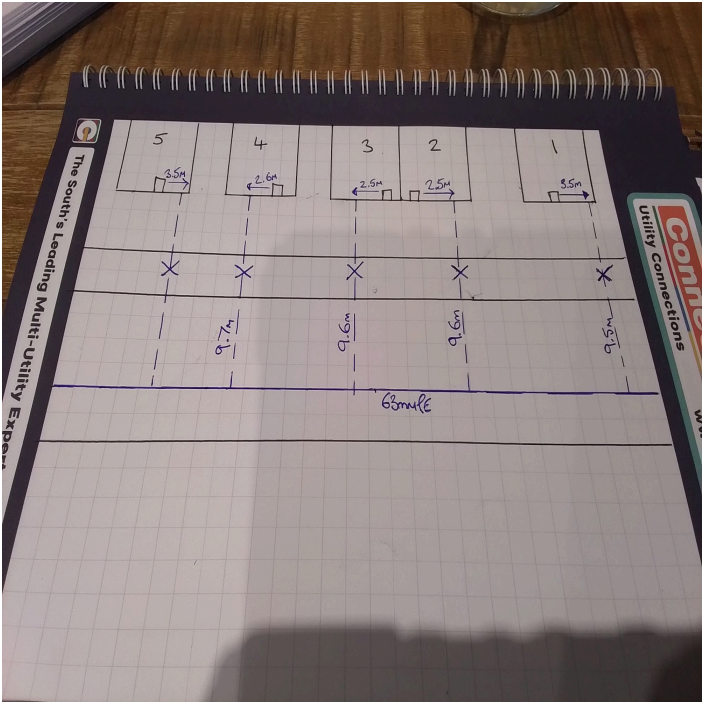

INSTALLATION DETAILS

Inspector Phone Number	07917344777
WRAS Membership No:	GW9507
Comments	.

SUPPLY DETAILS (SELF LAY)

Brief Description of Works	1x 25mm connection to self laid main. Service pipe has been laid to a depth of 750 on a bed of sand. A BS1010 tap installed within the property. The duct is foamed and lagged and run in a straight line from the property to the connection point.
Internal or External Meter	External
New or Replacement Service	New Supply

PHOTOS

Evidence Of Capped Pipe



Photo of WRAS Certificate

COMPLIANCE
Customer Reference Number: [blank] Internal ☐ External ☒

Water Company: [blank]
Application Reference Number: [blank]

Member's Name: KENNY CLARK Membership No: GW507
Company Name: C.I.O.S. Membership No: 616126

Customer Name: [REDACTED]
Address: [REDACTED]

Engineer Name: BREATH DAVID WILSON, TARS FARM, BARNHAM, GOSPOD ROAD, PO22 0EU
Plot No: 1 2 3 4 5 Plot No: 5

Name and address of the person who commissioned the work (the customer):
BREATH FLORE - BREATH DAVID WILSON, TARS FARM, BARNHAM, GOSPOD ROAD, PO22 0EU

Telephone Number: 0778313921 Email: BREATH.FLORE@BOWHAMS.CO.UK

Please give a brief description of the work completed and its location within the premises:
5 x NEW 25MM PE SERVICES - ON TO 63MM MAIN AS PER DESIGN.

Confirm that the work carried out complies with the Water Supply (Water Fittings) Regulations 1999, Water Supply (Water Fittings) (Scotland) Byelaws 2005 and any other relevant regulations. (Signature of Engineer)
[REDACTED] 31/10/25
[REDACTED] 23

SIGN OFF

I confirm that the work carried out complies with the Water Supply (Water Fittings) Regulations 1999, Water Supply (Water Fittings)(Scotland) Byelaws 2014 or Water Supply (Water Fittings) Regulations (Northern Ireland) 2009.

Name

Kenny Clark

Signed Date

Fri Oct 03 2025 16:01 GMT

