


Sussex Lime Plastering

New Place Bungalow
Arundel Road
Angmering
West Sussex
BN16 4ET



25-May-2021

Method Statement for Church House, Arundel Road, Angmering

Taking down and rebuilding the garden wall which runs along Arundel Road, due to an excessive lean towards the road. This will be done primarily with hand tools but not excluding some power tools. Removal of the capping bricks will be done in such a way that minimal damage is caused to the original brick so they can be used once again. All flints will be cleaned of mortar and kept as to use all original flints in the rebuild.

A hotlime mix (quicklime) will be used in the rebuild of the wall. A sample of the original mortar will be taken to get an aggregate as close to the original as we can, this will probably come from The Lime Centre in Winchester.

The wall will be reinstated to the existing height and width, any bricks that need to be replaced will be done so with an appropriate reclaimed brick. The patress plate will also be reinstated in its original position.

Sussex Lime Plastering


David Ayre


Photos

The length of flint wall along the western boundary.



The section of flint wall to be re-built.

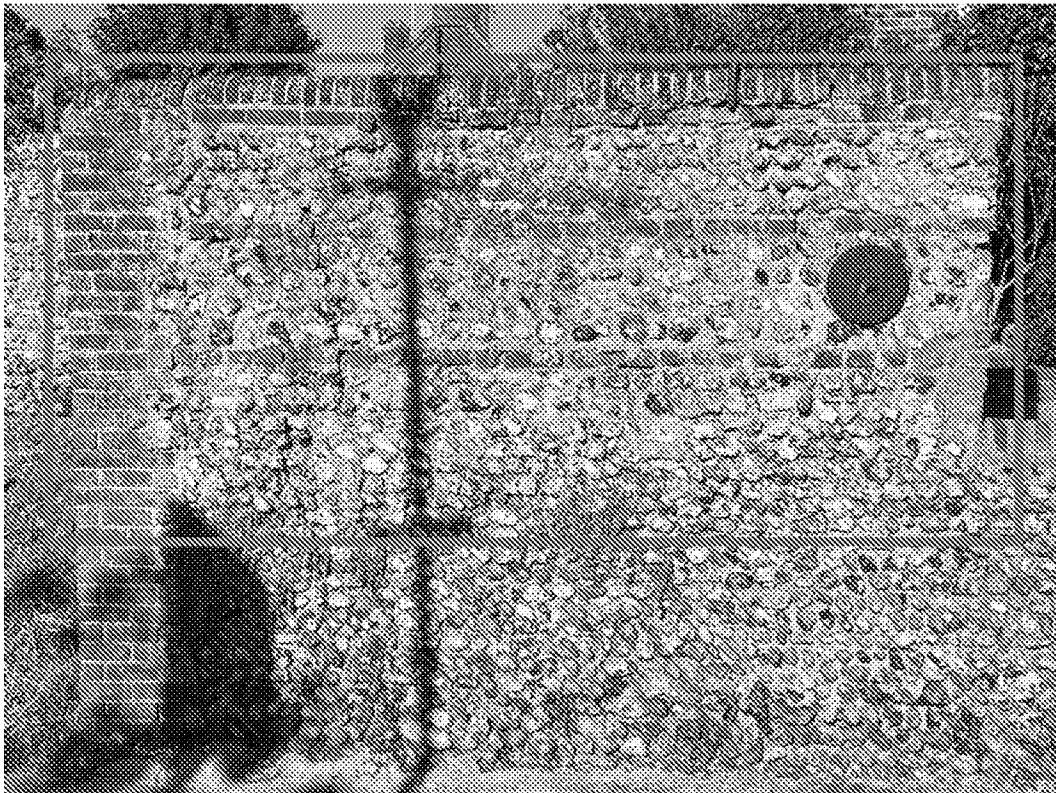

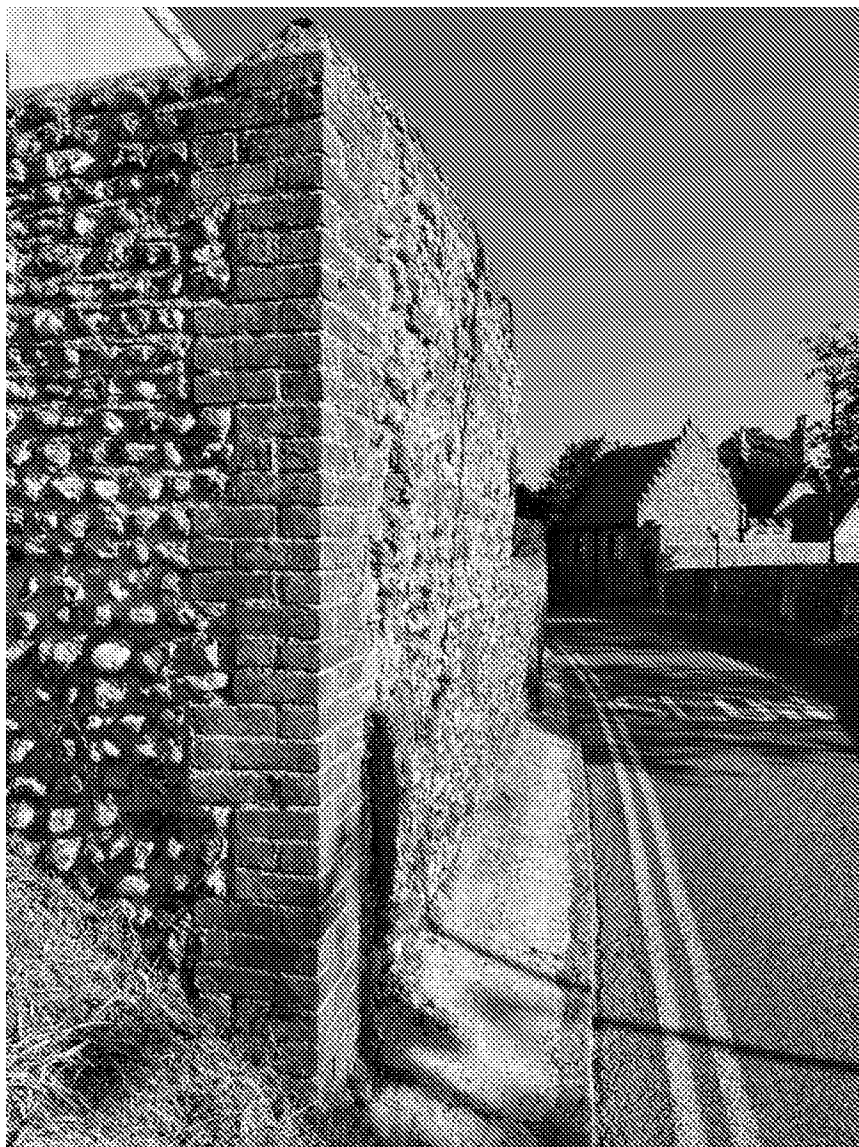**Access Statement**

Proposed works do not alter the accessibility of the building in any way.
