



Project

Project Name: Mackoy Ltd - Langmead Place Angmering

Project Date: 04/11/2025

Inspection Standard: MSCC5 Sewers & Drainage GB (SRM5 Scoring)






Table of Contents

Project Name	Project Number	Project Date
Mackoy Ltd - Langmead Place Angmering		04/11/2025
Project Information		P-1
Scoring Summary		P-2
Section Item 1: RG55 > MAIN (RG55X)		1
Section Item 2: RG50 > MAIN (RG50X)		3
Section Item 3: RG49 > 340 (RG49X)		5
Section Item 4: RG46 > MAIN (RG46X)		7
Section Item 5: RG44 > MAIN (RG44X)		9
Section Item 6: RG45 > MAIN (RG45X)		11
Section Item 7: RG59 > MAIN (RG59X)		13
Section Item 8: RG60 > MAIN (RG60X)		16
Section Item 9: RG58 > MAIN (RG58X)		18
Section Item 10: RG57 > MAIN (RG57X)		20
Section Item 11: RG56 > MAIN (RG56X)		22
Section Item 12: RG72 > 262 (RG72X)		24
Section Item 13: RG66 > 261 (RG66X)		26
Section Item 14: RG63 > MAIN (RG63X)		28
Section Item 15: RG61 > 264 (RG61X)		30
Section Item 16: RG62 > 264 (RG62X)		32
Section Item 17: RG77 > MAIN (RG77X)		34
Section Item 18: RG78 > MAIN (RG78X)		36
Section Item 19: RG80 > MAIN (RG80X)		38
Section Item 20: RG79 > MAIN (RG79X)		40
Section Item 21: RG73 > MAIN (RG73X)		42
Section Item 22: RG74 > MAIN (RG74X)		44
Section Item 23: RG75 > MAIN (RG75X)		46
Section Item 24: RE373 > 341 (RE373X)		48
Section Item 25: RE363 > 341 (RE363X)		50
Section Item 26: 224 > 225 (224X)		52
Section Item 27: 337 > 338 (337X)		54




Table of Contents

Project Name	Project Number	Project Date
Mackoy Ltd - Langmead Place Angmering		04/11/2025
Section Item 28: 338 > 340 (338X)		56
Section Item 29: 342 > S217 (342X)		58
Section Item 30: 321 > 322 (321X)		60
Section Item 31: 322 > 324 (322X)		62
Section Item 32: 324 > 326 (324X)		64
Section Item 33: 262 > 263 (262X)		66
Section Item 34: 263 > 264 (263X)		68
Section Item 35: 340 > 342 (340X)		70
Section Item 36: 341 > 342 (341X)		72
Section Item 37: 223 > 222 (223X)		74
Section Item 38: 223 > 225 (223X)		76
Section Item 39: 225 > S2706 (225X)		78
Section Item 40: 261 > 262 (261X)		80
Section Item 41: F7 > F8 (F7X)		82
Section Item 42: F22 > F23 (F22X)		84
Section Item 43: F23 > F24 (F23X)		86
Section Item 44: F42 > F43 (F42X)		88
Section Item 45: F43 > F47 (F43X)		90
Section Item 46: F18 > F19 (F18X)		92
Section Item 47: F19 > F20 (F19X)		94
Section Item 48: F20 > F21 (F20X)		96
Section Item 49: F39 > F40 (F39X)		98
Section Item 50: F40 > F41 (F40X)		100
Section Item 51: F41 > F42 (F41X)		102
Section Item 52: 32A > 32B (32AX)		104
Section Item 53: 325 > 326 (325X)		106
Section Item 54: 323 > 323A (323X)		108
Section Item 55: 330 > S215 (330X)		110
Section Item 56: 330 > S215 (330X)		112



Table of Contents		
Project Name	Project Number	Project Date
Mackoy Ltd - Langmead Place Angmering		04/11/2025

Section Item 57: 332B > 330 (332BX)	114
Section Item 58: FW348 > F41 (FW348X)	116
Section Item 59: FW332 > F41 (FW332X)	118
Section Item 60: FW355 > MAIN (FW355X)	120
Section Item 61: RWP > 330 (RWPX)	122
Section Item 62: FW230 > F18 (FW230X)	124
Section Item 63: FW230 > F18 (FW230X)	126
Section Item 64: FW209 > F39 (FW209X)	128
Section Item 65: RG69 > MAIN (RG69X)	130
Section Item 66: RG70 > MAIN (RG70X)	132
Section Item 67: RG68 > 323A (RG68X)	134
Section Item 68: RG53 > 337 (RG53X)	136
Section Item 69: RG52 > 338 (RG52X)	138
Section Item 70: RG51 > 338 (RG51X)	140
Section Item 71: RG65 > 261 (RG65X)	142
Section Item 72: RG54 > 337 (RG54X)	144



Project Information

Project Name	Project Number	Project Date
Mackoy Ltd - Langmead Place Angmering		04/11/2025

Client

Company: Mackoy Ltd
Department: Monks Brook Ind Park
Street: 10 School Close
Town or City: Chandlers Ford
County: Hampshire
Post Code: SO53 4RA




Site

Company: Mackoy Ltd
Street: Langmead Place
Town or City: Angmering
County: West Sussex



Contractor

Company: The Bloggs Ltd
Contact: Chris Blogg
Street: 144 Oak Road
Town or City: Bishops Waltham
County: Hampshire
Post Code: SO32 1EQ
Phone: 01489 307197
Mobile: 07934 890753
Email: thebloggsLtd@gmail.com





Scoring Summary

Project Name	Project Number	Project Date
Mackoy Ltd - Langmead Place Angmering		04/11/2025

Structural Defects

Item No.	PLR	Grade	Description
All inspected pipes are in an acceptable structural condition (< grade 3).			

Service / Operational Condition

Item No.	PLR	Grade	Description
All inspected pipes are in an acceptable service condition (< grade 3).			

Abandoned Surveys

Item No.	PLR	Description
All inspections complete, none are abandoned.		

Information

These scoring summaries are based on the SRM grading from the WRc.



Section Inspection - 04/11/2025 - RG55X

Item No. 1	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG55X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG55
Road:	Langmead Place	Inspected Length:	8.54 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	8.54 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:


Scale:	1:74	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG55							
	0.00	GY	Start node, gully, reference: RG55		00:00:00	1	
	0.00	WL	Water level, 0% of the vertical dimension				
	2.40	WL	Water level, 20% of the vertical dimension		00:00:14		
	8.54	MHF	Finish node, manhole, reference: MAIN		00:00:36	2	
MAIN Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
2	40.0	4.8	41.0	3.0	1	1.0	0.1	1.0	2.0



Section Pictures - 04/11/2025 - RG55X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
1	Downstream	RG55X		

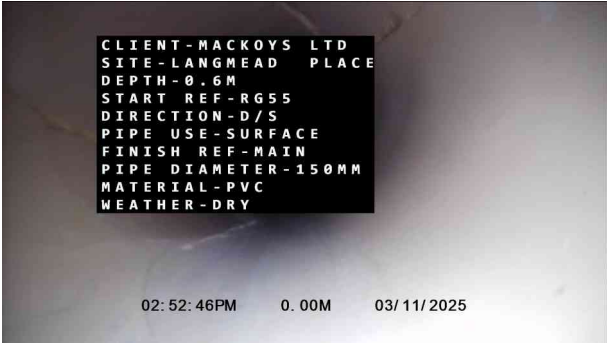

1, 00:00:00, 0.00 m
Start node, gully, reference: RG55



2, 00:00:36, 8.54 m
Finish node, manhole, reference: MAIN



Section Inspection - 04/11/2025 - RG50X

Item No. 2	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG50X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG50
Road:	Langmead Place	Inspected Length:	2.30 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	2.30 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG50	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		1.82	LR	Line deviates right	00:00:33		
		2.30	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:37	2	

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
6	131.0	57.8	133.0	4.0	2	2.0	0.9	2.0	3.0



Section Pictures - 04/11/2025 - RG50X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
2	Downstream	RG50X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG50



2, 00:00:37, 2.30 m
Finish node, major connection without manhole, reference: MAIN



Section Inspection - 04/11/2025 - RG49X

Item No. 3	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG49X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG49
Road:	Langmead Place	Inspected Length:	1.82 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.82 m	Downstream Node:	340
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG49	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:03		
		1.82	MHF	Finish node, manhole, reference: 340	00:00:15	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.5	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG49X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
3	Downstream	RG49X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG49



2, 00:00:15, 1.82 m
Finish node, manhole, reference: 340



Section Inspection - 04/11/2025 - RG46X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
4	1	04/11/25	10:19	Not Specified	No Rain Or Snow	Yes	RG46X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Vivax Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG46
Road:	Langmead Place	Inspected Length:	2.40 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	2.40 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation MPEG Photo Grade

Depth: 0.60 m
RG46



0.00

GY

Start node, gully, reference: RG46

00:00:00

1

0.00

WL

Water level, 0% of the vertical dimension

1.82

LD

Line deviates down

00:00:10

2.40

BRF

Finish node, major connection without manhole, reference: MAIN

00:00:13

2

MAIN
Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.4	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG46X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
4	Downstream	RG46X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG46



2, 00:00:13, 2.40 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG44X

Item No. 5	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG44X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG44
Road:	Langmead Place	Inspected Length:	2.88 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	2.88 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG44	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:06		
		2.88	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:18	2	

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



t [REDACTED]

Section Pictures - 04/11/2025 - RG44X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
5	Downstream	RG44X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG44



2, 00:00:18, 2.88 m
Finish node, major connection without manhole, reference:
MAIN



	PLR	
	RG45X	
	Alternative ID	
	Not Specified	

RG45
Depth: 0.600 m
MAIN
Depth:

Recommendations:

EG	Photo	Grade
0:00	1	
0:07		
0:19		
0:22	2	

res	
ervations	
SER Total	SER Grade
0.0	1.0



Section Pictures - 04/11/2025 - RG45X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
6	Downstream	RG45X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG45



2, 00:00:22, 4.60 m
Finish node, major connection without manhole, reference:
MAIN




Section Inspection - 04/11/2025 - RG59X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
7	1	04/11/25	10:19	Not Specified	No Rain Or Snow	Yes	RG59X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Vivax Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG59
Road:	Langmead Place	Inspected Length:	10.90 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	10.90 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:95	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG59							
							
	0.00	GY		Start node, gully, reference: RG59	00:00:00	1	
	0.00	WL		Water level, 0% of the vertical dimension			
	1.53	S01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:18	2	
	3.36	F01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:21		
	8.45	S02	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:29	3	
	9.41	F02	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:32		
	9.41	WL		Water level, 30% of the vertical dimension	00:00:32		
	9.41	CN		Connection other than junction at 2 o'clock, 100mm dia	00:00:32		
	10.60	RPL		Point repair, localised lining from 12 o'clock to 11 o'clock	00:00:35	4	
	10.90	BRF		Finish node, major connection without manhole, reference: MAIN	00:00:39	5	
				MAIN Depth: m			

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG59X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
7	Downstream	RG59X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG59



2, 00:00:18, 1.53 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:00:29, 8.45 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



4, 00:00:35, 10.60 m
Point repair, localised lining from 12 o'clock to 11 o'clock



Section Pictures - 04/11/2025 - RG59X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
7	Downstream	RG59X		



5, 00:00:39, 10.90 m
Finish node, major connection without manhole, reference:
MAIN




Section Inspection - 04/11/2025 - RG60X

Item No. 8	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG60X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG60
Road:	Langmead Place	Inspected Length:	10.11 m	Upstream Pipe Depth:	0.630 m
Location:	Road	Total Length:	10.11 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

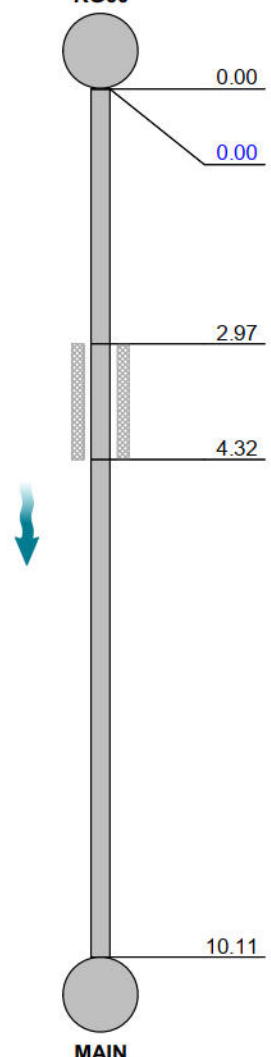Scale:	1:88	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.63 m RG60							
							
	0.00	GY		Start node, gully, reference: RG60	00:00:00	1	
	0.00	WL		Water level, 0% of the vertical dimension			
	2.97	S01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:11	2	
	4.32	F01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:13		
	10.11		BRF	Finish node, major connection without manhole, reference: MAIN	00:00:23	3	
MAIN Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG60X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
8	Downstream	RG60X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG60



2, 00:00:11, 2.97 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:00:23, 10.11 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG58X


Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
9	1	04/11/25	10:19	Not Specified	No Rain Or Snow	Yes	RG58X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Vivax Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG58
Road:	Langmead Place	Inspected Length:	2.78 m	Upstream Pipe Depth:	0.630 m
Location:	Road	Total Length:	2.78 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG58	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:09		
		1.44	WL	Water level, 20% of the vertical dimension	00:00:13		
		2.78	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:18	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.4	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG58X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
9	Downstream	RG58X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG58



2, 00:00:18, 2.78 m
Finish node, major connection without manhole, reference:
MAIN



Recommendations:



Section Pictures - 04/11/2025 - RG57X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
10	Downstream	RG57X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG57



2, 00:00:18, 3.64 m
Finish node, major connection without manhole, reference:
MAIN




Section Inspection - 04/11/2025 - RG56X


Item No. 11	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG56X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG56
Road:	Langmead Place	Inspected Length:	6.62 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	6.62 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

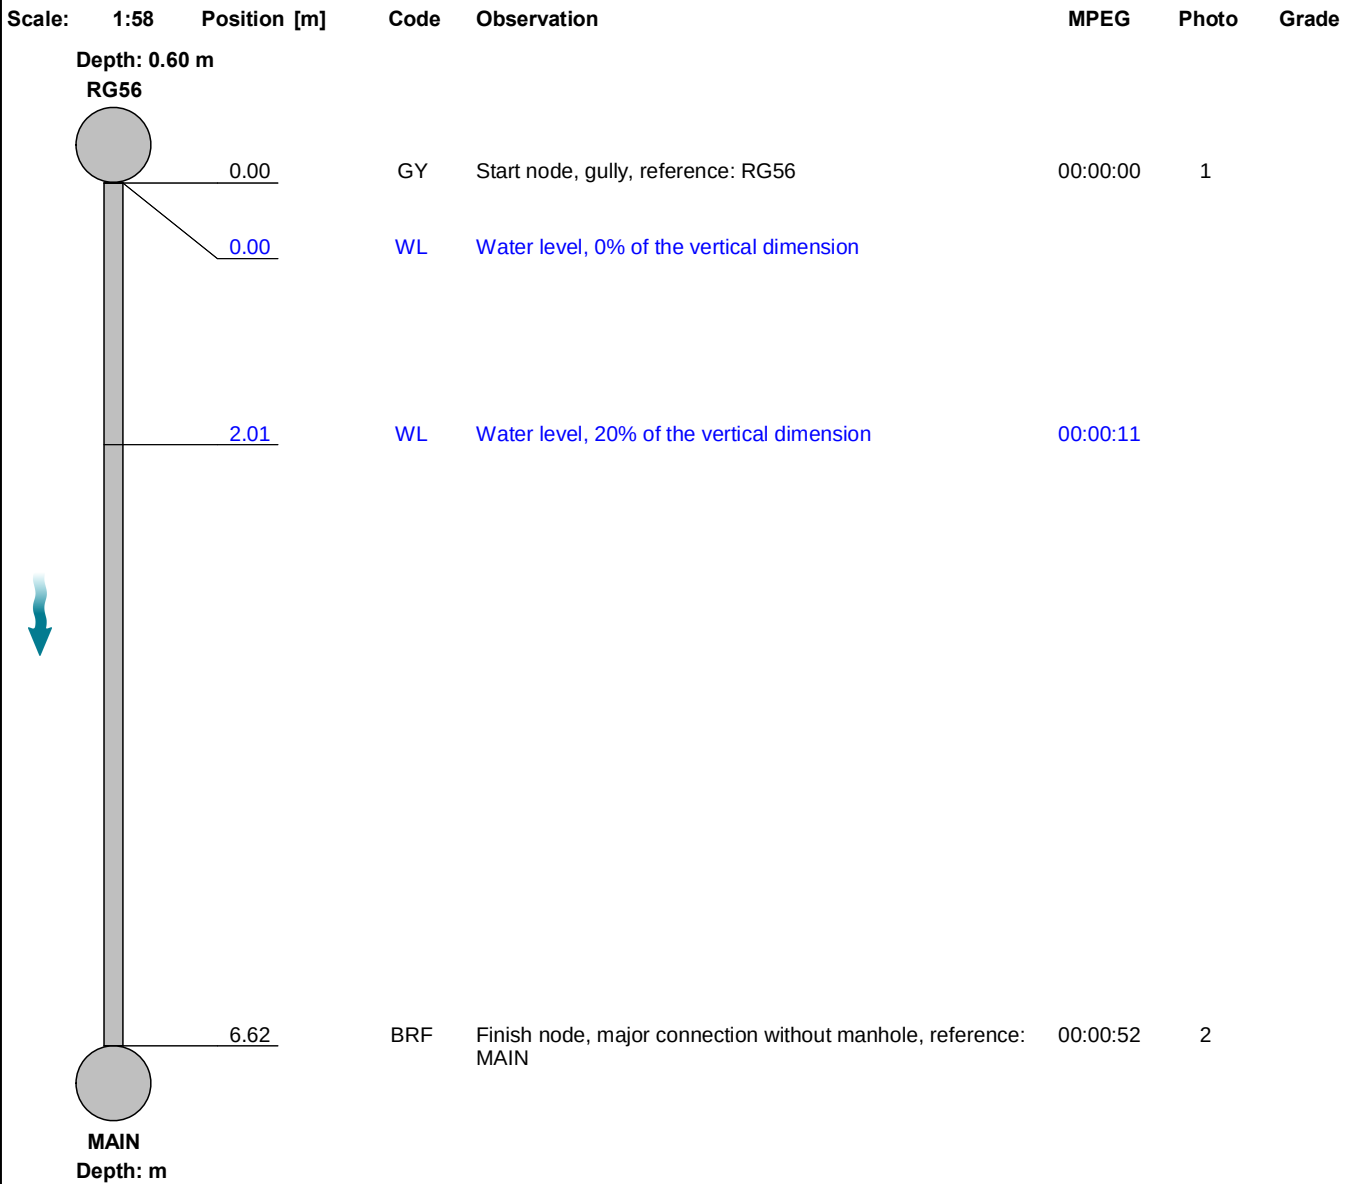

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
4	206.0	68.1	451.0	5.0	1	1.0	0.2	1.0	2.0



Section Pictures - 04/11/2025 - RG56X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
11	Downstream	RG56X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG56



2, 00:00:52, 6.62 m
Finish node, major connection without manhole, reference:
MAIN

Section Inspection - 04/11/2025 - RG72X

Item No. 12	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG72X
Operator C. Bloor		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG72
Road:	Langmead Place	Inspected Length:	8.85 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	8.85 m	Downstream Node:	262
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:77 Position [m] Code Observation MPEG Photo Grade

Depth: 0.60 m
RG72

0.00

0.00

GY Start node, gully, reference: RG72 00:00:00 1

WL Water level, 0% of the vertical dimension

7.77

WL Water level, 20% of the vertical dimension 00:00:30

8.85

MHF Finish node, manhole, reference: 262 00:00:34 2

262
Depth: m

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG72X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
12	Downstream	RG72X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG72



2, 00:00:34, 8.85 m
Finish node, manhole, reference: 262



Section Inspection - 04/11/2025 - RG66X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
13	1	04/11/25	10:19	Not Specified	No Rain Or Snow	Yes	RG66X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Vivax Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG66
Road:	Langmead Place	Inspected Length:	8.73 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	8.73 m	Downstream Node:	261
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:76	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG66							
	0.00	GY		Start node, gully, reference: RG66	00:00:00	1	
	0.00	WL		Water level, 0% of the vertical dimension			
	0.00	LD		Line deviates down	00:00:07		
	0.76	S01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:15	2	
	2.30	F01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:19		
	7.20	WL		Water level, 20% of the vertical dimension	00:00:29		
	8.73	MHF		Finish node, manhole, reference: 261	00:00:42	3	
261 Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG66X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
13	Downstream	RG66X		




1, 00:00:00, 0.00 m
Start node, gully, reference: RG66



2, 00:00:15, 0.76 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:00:42, 8.73 m
Finish node, manhole, reference: 261



Section Inspection - 04/11/2025 - RG63X

Item No. 14	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG63X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG63
Road:	Langmead Place	Inspected Length:	4.03 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	4.03 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:



Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.2	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG63X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
14	Downstream	RG63X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG63



2, 00:00:17, 4.03 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG61X

Item No. 15	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG61X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG61
Road:	Langmead Place	Inspected Length:	1.72 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.72 m	Downstream Node:	264
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG61							
	0.00	GY	Start node, gully, reference: RG61		00:00:00	1	
	0.00	WL	Water level, 0% of the vertical dimension				
	0.00	LD	Line deviates down		00:00:07		
	1.72	BRF	Finish node, major connection without manhole, reference: 264		00:00:35	2	
264 Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG61X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
15	Downstream	RG61X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG61



2, 00:00:35, 1.72 m
Finish node, major connection without manhole, reference:
264



Section Inspection - 04/11/2025 - RG62X

Item No. 16	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG62X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG62
Road:	Langmead Place	Inspected Length:	1.72 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.72 m	Downstream Node:	264
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:


Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG62	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.09	LD	Line deviates down	00:00:07		
		1.24	LD	Line deviates down	00:00:13		
		1.72	WL	Water level, 30% of the vertical dimension	00:00:15		
		1.72	BRF	Finish node, major connection without manhole, reference: 264	00:00:21	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.6	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG62X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
16	Downstream	RG62X		

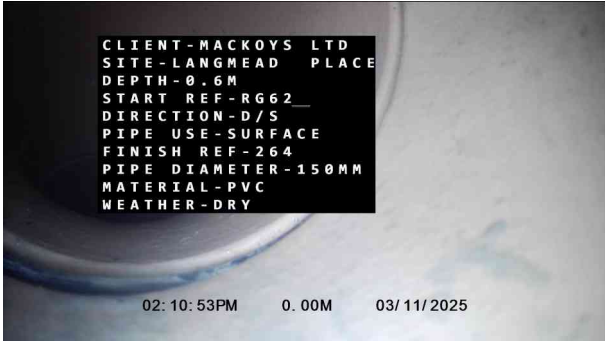

1, 00:00:00, 0.00 m
Start node, gully, reference: RG62



2, 00:00:21, 1.72 m
Finish node, major connection without manhole, reference:
264



Section Inspection - 04/11/2025 - RG77X


Item No. 17	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG77X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG77
Road:	Langmead Place	Inspected Length:	4.03 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	4.03 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG77	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:07		
		1.44	LD	Line deviates down	00:00:11		
		2.97	LR	Line deviates right	00:00:15		
		4.03	LD	Line deviates down	00:00:19		
		4.03	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:21	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
2	1.0	0.5	2.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG77X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
17	Downstream	RG77X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG77



2, 00:00:21, 4.03 m
Finish node, major connection without manhole, reference: MAIN



Section Inspection - 04/11/2025 - RG78X

Item No. 18	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG78X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG78
Road:	Langmead Place	Inspected Length:	1.35 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.35 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG78	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:06		
		1.35	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:12	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.7	1.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 04/11/2025 - RG78X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
18	Downstream	RG78X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG78

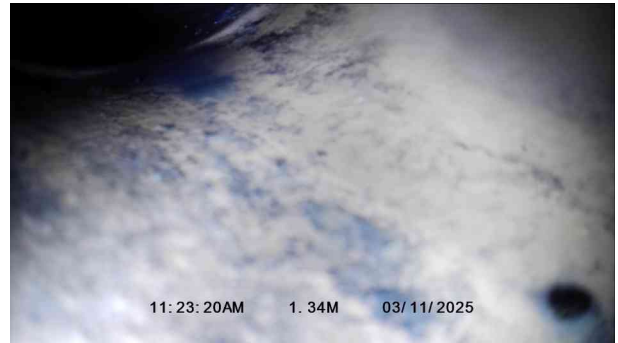

2, 00:00:12, 1.35 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG80X


Item No. 19	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG80X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG80
Road:	Langmead Place	Inspected Length:	1.53 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.53 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG80	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:06		
		1.44	JN	Junction at 2 o'clock, 150mm dia	00:00:19		
		1.53	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:31	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG80X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
19	Downstream	RG80X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG80



2, 00:00:31, 1.53 m
Finish node, major connection without manhole, reference: MAIN



Section Inspection - 04/11/2025 - RG79X

Item No. 20	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG79X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG79
Road:	Langmead Place	Inspected Length:	1.15 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.15 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG79	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:06		
		1.15	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:21	2	


Construction Features

Miscellaneous Features

Structural Defects


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.9	1.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 04/11/2025 - RG79X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
20	Downstream	RG79X		

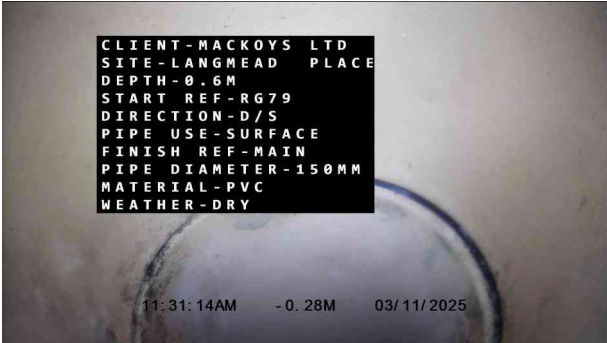

1, 00:00:00, 0.00 m
Start node, gully, reference: RG79

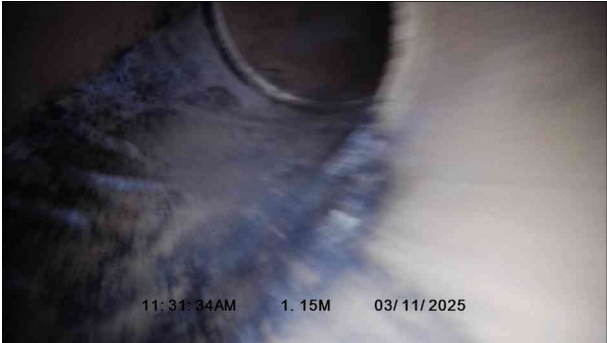

2, 00:00:21, 1.15 m
Finish node, major connection without manhole, reference:
MAIN



Item No. 21	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG73X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG73
Road:	Langmead Place	Inspected Length:	7.20 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	7.20 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Recommendations:

Scale: 1:63

Position [m]

Code

Observation

MPEG

Photo

Grade

Depth: 0.60 m

RG73

0.00

0.00

GY Start node, gully, reference: RG73 00:00:00 1

WL Water level, 0% of the vertical dimension

6.81

7.20

MAIN

Depth: m

00:00:25

MHF Finish node, manhole, reference: MAIN 00:00:29 2

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.1	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG73X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
21	Downstream	RG73X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG73



2, 00:00:29, 7.20 m
Finish node, manhole, reference: MAIN



Section Inspection - 04/11/2025 - RG74X

Item No. 22	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG74X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG74
Road:	Langmead Place	Inspected Length:	0.67 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	0.67 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG74							
		0.00	GY	Start node, gully, reference: RG74	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:12		
		0.38	LL	Line deviates left	00:00:13		
		0.67	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:14	2	
Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG74X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
22	Downstream	RG74X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG74



2, 00:00:14, 0.67 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG75X

Item No. 23	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG75X
Operator C.Blogg		Vehicle CV13 BYP		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG75
Road:	Langmead Place	Inspected Length:	1.30 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.30 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG75	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:05		
		1.30	BRF	Finish node, major connection without manhole, reference: MAIN			

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 04/11/2025 - RG75X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
23	Downstream	RG75X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG75



Section Inspection - 06/11/2025 - RE373X

Item No. 24	Insp. No. 1	Date 06/11/25	Time 13:50	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RE373X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Upstream	Upstream Node:	RE373
Road:	Langmead Place	Inspected Length:	9.20 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	9.20 m	Downstream Node:	341
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.000 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:80	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.00 m	341						
0.00		MH		Start node, manhole, reference: 341	00:00:00	1	
0.00		WL		Water level, 0% of the vertical dimension			
0.00	S01	RPL		Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:07	2	
0.86	F01	RPL		Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:14		
0.86		WL		Water level, 20% of the vertical dimension	00:00:14		
6.14		CN		Connection other than junction at 10 o'clock, 100mm dia	00:00:27		
7.01		JN		Junction at 10 o'clock, 150mm dia	00:00:29		
7.21		SC		Pipe size changes, new size(s), 100mm high	00:00:30	3	
8.40		LU		Line deviates up	00:00:39		
9.20		REF		Finish node, rodding eye, reference: RE373	00:00:55	4	
RE373							
Depth: m							

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - RE373X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
24	Upstream	RE373X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 341



2, 00:00:07, 0.00 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:00:30, 7.21 m
Pipe size changes, new size(s), 100mm high



4, 00:00:55, 9.20 m
Finish node, rodding eye, reference: RE373

Section Inspection - 06/11/2025 - RE363X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
25	1	06/11/25	13:50	Not Specified	No Rain Or Snow	Yes	RE363X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RE363
Road:	Langmead Place	Inspected Length:	7.19 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	7.19 m	Downstream Node:	341
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.000 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:63	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 341	00:00:00	1	
		0.00	WL	Water level, 20% of the vertical dimension			
		0.00	S01	RPL Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:08	2	
		0.19	S02	CUW Loss of vision, camera under water, start	00:00:10		
		0.32	F01	RPL Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:45		
		6.10	F02	CUW Loss of vision, camera under water, finish	00:00:45		
		6.49	LU	Line deviates up	00:00:48		
		7.19	REF	Finish node, rodding eye, reference: RE363	00:00:51	3	

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 06/11/2025 - RE363X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
25	Upstream	RE363X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 341

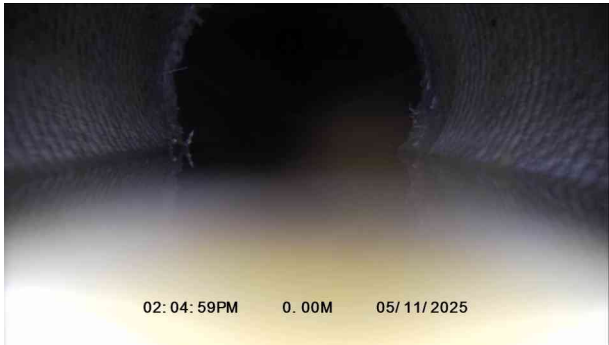

2, 00:00:08, 0.00 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start

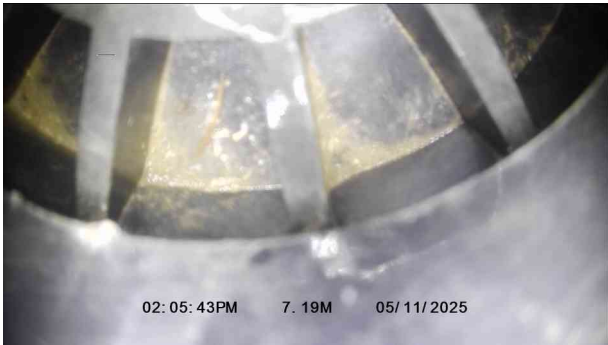

3, 00:00:51, 7.19 m
Finish node, rodding eye, reference: RE363


Section Inspection - 06/11/2025 - 224X

Item No. 26	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 224X
Operator C. Bloor		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	224
Road:	Langmead Place	Inspected Length:	10.11 m	Upstream Pipe Depth:	1.100 m
Location:	Road	Total Length:	12.45 m	Downstream Node:	225
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

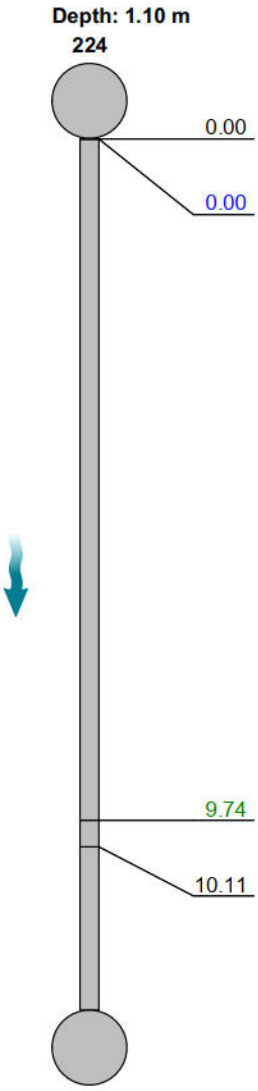Scale:	1:108	Position [m]	Code	Observation	MPEG	Photo	Grade
							
	0.00	MH	Start node, manhole, reference: 224	00:00:00	1		
	0.00	WL	Water level, 0% of the vertical dimension				
	9.74	LD	Line deviates down	00:01:57			
	10.11	MHF	Finish node, manhole, reference: 225	00:02:01			

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	10	0.1	10	10	1	50	0.4	50	40



Section Pictures - 06/11/2025 - 224X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
26	Downstream	224X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 224



Section Inspection - 06/11/2025 - 337X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
27	1	06/11/25	13:50	Not Specified	No Rain Or Snow	Yes	337X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	337
Road:	Langmead Place	Inspected Length:	10.44 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	10.44 m	Downstream Node:	338
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.400 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:91	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.40 m							
338							
	0.00		MH	Start node, manhole, reference: 338	00:00:00	1	
	0.00		WL	Water level, 15% of the vertical dimension			
	2.11		WL	Water level, 20% of the vertical dimension	00:00:14		
	10.44		MHF	Finish node, manhole, reference: 337	00:00:38	2	
337							
Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 337X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
27	Upstream	337X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 338



2, 00:00:38, 10.44 m
Finish node, manhole, reference: 337



Item No. 28	Insp. No. 1	Date 06/11/25	Time 13:50	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 338X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	338
Road:	Langmead Place	Inspected Length:	17.60 m	Upstream Pipe Depth:	1.400 m
Location:	Road	Total Length:	17.60 m	Downstream Node:	340
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:	
Recommendations:	

Scale:	1:153	Position [m]	Code	Observation	MPEG	Photo	Grade																																																							
Depth: 1.40 m 338 <table><tr><th>Code</th><th>Observation</th><th>MPEG</th><th>Photo</th><th>Grade</th></tr><tr><td>MH</td><td>Start node, manhole, reference: 338</td><td>00:00:00</td><td>1</td><td></td></tr><tr><td>WL</td><td>Water level, 0% of the vertical dimension</td><td></td><td></td><td></td></tr><tr><td>WL</td><td>Water level, 15% of the vertical dimension</td><td>00:00:11</td><td></td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 2 o'clock, 100mm dia</td><td>00:00:14</td><td></td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 2 o'clock, 100mm dia</td><td>00:00:19</td><td></td><td></td></tr><tr><td>S01</td><td>RPL Point repair, localised lining from 12 o'clock to 11 o'clock, start</td><td>00:00:19</td><td>2</td><td></td></tr><tr><td>F01</td><td>RPL Point repair, localised lining from 12 o'clock to 11 o'clock, finish</td><td>00:00:22</td><td></td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 2 o'clock, 100mm dia</td><td>00:00:27</td><td></td><td></td></tr><tr><td>LR</td><td>Line deviates right</td><td>00:00:57</td><td></td><td></td></tr><tr><td>MHF</td><td>Finish node, manhole, reference: 340</td><td>00:01:01</td><td>3</td><td></td></tr></table> 340 Depth: m								Code	Observation	MPEG	Photo	Grade	MH	Start node, manhole, reference: 338	00:00:00	1		WL	Water level, 0% of the vertical dimension				WL	Water level, 15% of the vertical dimension	00:00:11			CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:14			CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:19			S01	RPL Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:19	2		F01	RPL Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:22			CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:27			LR	Line deviates right	00:00:57			MHF	Finish node, manhole, reference: 340	00:01:01	3	
Code	Observation	MPEG	Photo	Grade																																																										
MH	Start node, manhole, reference: 338	00:00:00	1																																																											
WL	Water level, 0% of the vertical dimension																																																													
WL	Water level, 15% of the vertical dimension	00:00:11																																																												
CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:14																																																												
CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:19																																																												
S01	RPL Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:19	2																																																											
F01	RPL Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:22																																																												
CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:27																																																												
LR	Line deviates right	00:00:57																																																												
MHF	Finish node, manhole, reference: 340	00:01:01	3																																																											

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
2	1.0	0.1	2.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 338X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
28	Downstream	338X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 338



2, 00:00:19, 5.76 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:01:01, 17.60 m
Finish node, manhole, reference: 340



Section Inspection - 06/11/2025 - 342X

Item No. 29	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 342X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	342
Road:	Langmead Place	Inspected Length:	33.39 m	Upstream Pipe Depth:	1.900 m
Location:	Road	Total Length:	33.39 m	Downstream Node:	S217
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	300 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale: 1:290	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.90 m 342						
	0.00	MH	Start node, manhole, reference: 342	00:00:00		
	0.00	WL	Water level, 0% of the vertical dimension			
	2.28	CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:23		
	18.71	CN	Connection other than junction at 2 o'clock, 150mm dia	00:01:51		
	30.57	CN	Connection other than junction at 10 o'clock, 150mm dia	00:03:01		
	31.10	CN	Connection other than junction at 2 o'clock, 150mm dia	00:03:04		
	31.12	WL	Water level, 20% of the vertical dimension	00:03:08		
	33.39	MHF	Finish node, manhole, reference: S217	00:03:39	1	
S217 Depth: m						

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	1	5.0	0.1	5.0	4.0




Section Pictures - 06/11/2025 - 342X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
29	Downstream	342X		



1, 00:03:39, 33.39 m
Finish node, manhole, reference: S217



Section Inspection - 06/11/2025 - 321X

Item No. 30	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 321X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	321
Road:	Langmead Place	Inspected Length:	8.27 m	Upstream Pipe Depth:	1.600 m
Location:	Road	Total Length:	8.27 m	Downstream Node:	322
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:72	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 321	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		4.42	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:38		
		8.27	MHF	Finish node, manhole, reference: 322	00:00:59	2	

Construction Features

Miscellaneous Features

Structural Defects


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 06/11/2025 - 321X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
30	Downstream	321X		

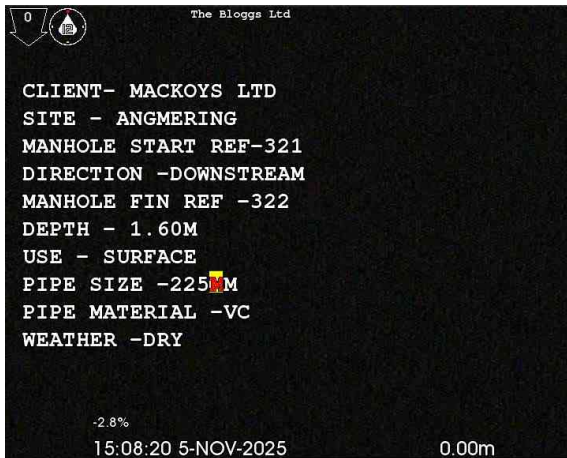

1, 00:00:00, 0.00 m
Start node, manhole, reference: 321

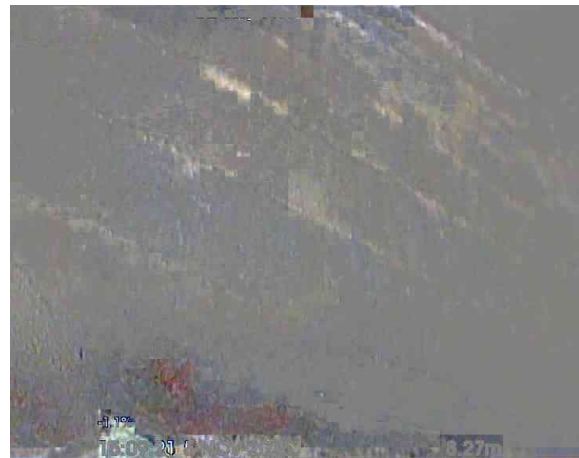

2, 00:00:59, 8.27 m
Finish node, manhole, reference: 322




Section Inspection - 06/11/2025 - 322X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
31	1	06/11/25	13:55	Not Specified	No Rain Or Snow	Yes	322X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	322
Road:	Langmead Place	Inspected Length:	28.19 m	Upstream Pipe Depth:	1.650 m
Location:	Road	Total Length:	28.19 m	Downstream Node:	324
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:245	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.65 m 322							
		0.00	MH	Start node, manhole, reference: 322	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		21.15	CN	Connection other than junction at 10 o'clock, 100mm dia	00:01:42		
		23.87	LL	Line deviates left	00:01:52		
		27.47	LR	Line deviates right	00:02:08		
324 Depth: m		28.19	MHF	Finish node, manhole, reference: 324	00:02:13	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 322X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
31	Downstream	322X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 322



2, 00:02:13, 28.19 m
Finish node, manhole, reference: 324



Section Inspection - 06/11/2025 - 324X

Item No. 32	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 324X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	324
Road:	Langmead Place	Inspected Length:	45.97 m	Upstream Pipe Depth:	1.800 m
Location:	Road	Total Length:	45.97 m	Downstream Node:	326
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	300 mm		
Flow Control:	No flow control	Material:	Concrete		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:399	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 324	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		4.97	CN	Connection other than junction at 2 o'clock, 150mm dia	00:00:41		
		15.88	CN	Connection other than junction at 2 o'clock, 150mm dia	00:01:52		
		19.27	CN	Connection other than junction at 2 o'clock, 150mm dia	00:02:12		
		27.47	CN	Connection other than junction at 2 o'clock, 150mm dia	00:03:08		
		38.32	CN	Connection other than junction at 2 o'clock, 150mm dia	00:04:22		
		39.07	CN	Connection other than junction at 2 o'clock, 150mm dia	00:04:27		
		45.97	MHF	Finish node, manhole, reference: 326	00:05:30	2	

Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 324X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
32	Downstream	324X		

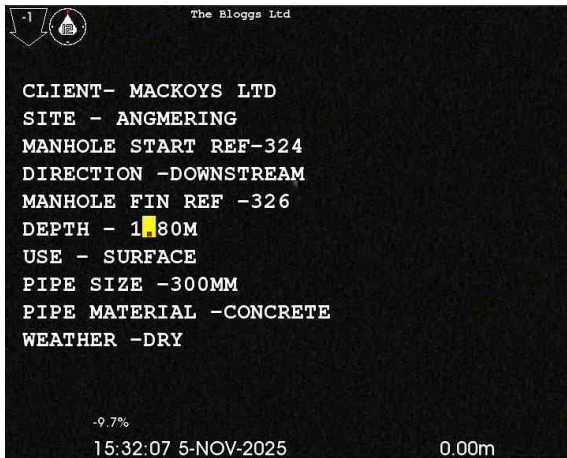

1, 00:00:00, 0.00 m
Start node, manhole, reference: 324



2, 00:05:30, 45.97 m
Finish node, manhole, reference: 326



Item No. 33	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 262X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	262
Road:	Langmead Place	Inspected Length:	11.09 m	Upstream Pipe Depth:	1.100 m
Location:	Road	Total Length:	11.09 m	Downstream Node:	263
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale: 1:97 Position [m] Code Observation MPEG Photo Grade

Depth: 1.10 m
262

0.00

0.00

WL Water level, 0% of the vertical dimension

11.09

263
Depth: m


Code	Observation	MPEG	Photo	Grade
MH	Start node, manhole, reference: 262	00:00:00	1	
MHF	Finish node, manhole, reference: 263	00:01:29	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 262X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
33	Downstream	262X		

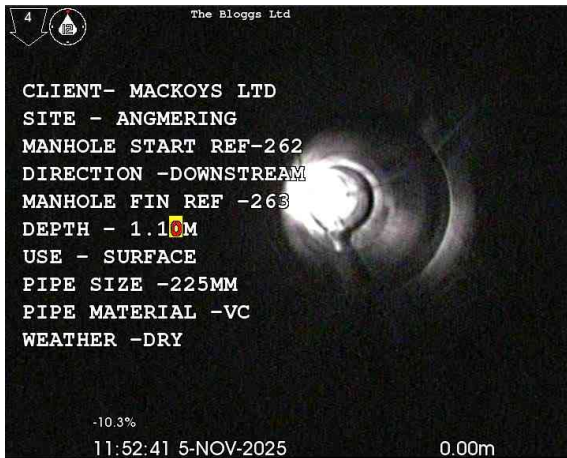

1, 00:00:00, 0.00 m
Start node, manhole, reference: 262



2, 00:01:29, 11.09 m
Finish node, manhole, reference: 263



Item No. 34	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 263X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	263
Road:	Langmead Place	Inspected Length:	57.18 m	Upstream Pipe Depth:	1.000 m
Location:	Road	Total Length:	57.18 m	Downstream Node:	264
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	300 mm		
Flow Control:	No flow control	Material:	Concrete		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:	
Recommendations:	


Scale:	1:496	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.00 m 263							
		0.00	MH	Start node, manhole, reference: 263	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		30.21	CN	Connection other than junction at 10 o'clock, 150mm dia	00:02:46		
		30.88	CN	Connection other than junction at 2 o'clock, 150mm dia	00:02:49		
		40.44	CN	Connection other than junction at 10 o'clock, 150mm dia	00:03:39		
		46.05	CN	Connection other than junction at 10 o'clock, 150mm dia	00:04:08		
		57.18	MHF	Finish node, manhole, reference: 264	00:06:21	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 263X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
34	Downstream	263X		

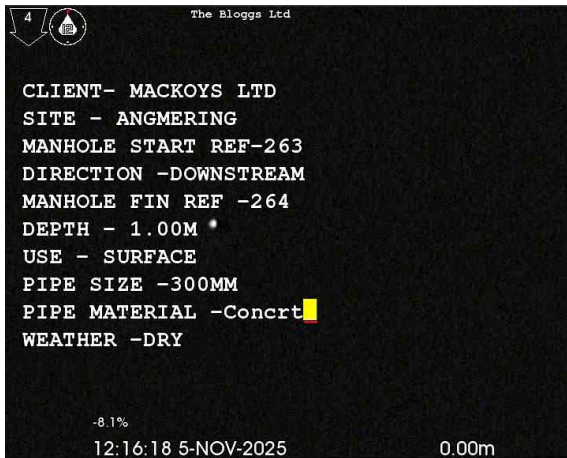

1, 00:00:00, 0.00 m
Start node, manhole, reference: 263



2, 00:06:21, 57.18 m
Finish node, manhole, reference: 264



Section Inspection - 06/11/2025 - 340X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
35	1	06/11/25	13:55	Not Specified	No Rain Or Snow	Yes	340X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	340
Road:	Langmead Place	Inspected Length:	13.90 m	Upstream Pipe Depth:	1.700 m
Location:	Road	Total Length:	13.90 m	Downstream Node:	342
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:121	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.70 m							
340							
	0.00	MH	Start node, manhole, reference: 340	00:00:00	1		
	0.00	WL	Water level, 0% of the vertical dimension				
	13.90	JN	Junction at 6 o'clock, 225mm dia: BACKDROP	00:01:24			
	13.90	MHF	Finish node, manhole, reference: 342	00:01:26	2		
342							
Depth: m							

Construction Features

Miscellaneous Features

Structural Defects


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 340X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
35	Downstream	340X		

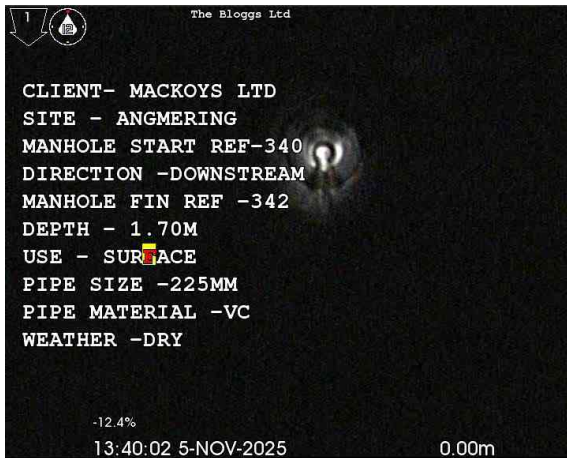

1, 00:00:00, 0.00 m
Start node, manhole, reference: 340



2, 00:01:26, 13.90 m
Finish node, manhole, reference: 342



Section Inspection - 06/11/2025 - 341X

Item No. 36	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 341X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	341
Road:	Langmead Place	Inspected Length:	24.61 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	24.67 m	Downstream Node:	342
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.800 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:214	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 342	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		4.61	CN	Connection other than junction at 10 o'clock, 150mm dia	00:00:43		
		5.41	WL	Water level, 15% of the vertical dimension	00:00:48		
		15.34	CN	Connection other than junction at 10 o'clock, 150mm dia	00:01:53		
		16.09	CN	Connection other than junction at 2 o'clock, 150mm dia	00:01:57		
		24.61	MHF	Finish node, manhole, reference: 341	00:03:17	2	

Construction Features

Miscellaneous Features

Structural Defects


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	1	0.0	0.2	5.0	1.0



Section Pictures - 06/11/2025 - 341X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
36	Upstream	341X		

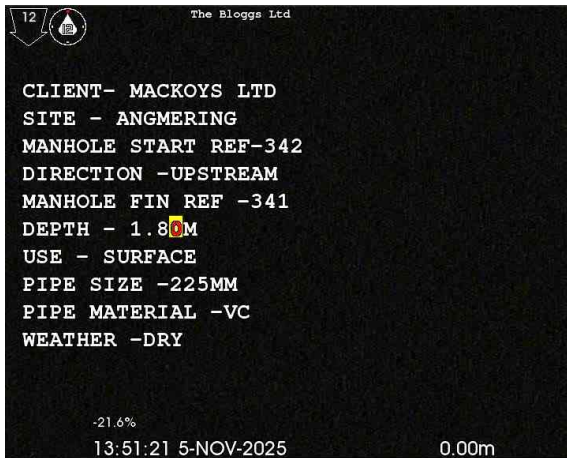

1, 00:00:00, 0.00 m
Start node, manhole, reference: 342




2, 00:03:17, 24.61 m
Finish node, manhole, reference: 341



Item No. 37	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 223X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	223
Road:	Langmead Place	Inspected Length:	46.87 m	Upstream Pipe Depth:	1.300 m
Location:	Road	Total Length:	46.87 m	Downstream Node:	222
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	450 mm		
Flow Control:	No flow control	Material:	Concrete		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:	
Recommendations:	


Scale:	1:406	Position [m]	Code	Observation	MPEG	Photo	Grade																																				
Depth: 1.30 m 223  0.00 0.00 8.79 11.46 14.16 17.21 30.22 32.36 46.87 222 Depth: m <table><tr><td>MH</td><td>Start node, manhole, reference: 223</td><td>00:00:00</td><td>1</td></tr><tr><td>WL</td><td>Water level, 0% of the vertical dimension</td><td></td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 10 o'clock, 100mm dia</td><td>00:00:58</td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 2 o'clock, 100mm dia</td><td>00:01:12</td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 2 o'clock, 100mm dia</td><td>00:01:26</td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 2 o'clock, 100mm dia</td><td>00:01:41</td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 2 o'clock, 100mm dia</td><td>00:02:47</td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 10 o'clock, 100mm dia</td><td>00:02:58</td><td></td></tr><tr><td>MHF</td><td>Finish node, manhole, reference: 222</td><td>00:04:15</td><td>2</td></tr></table>								MH	Start node, manhole, reference: 223	00:00:00	1	WL	Water level, 0% of the vertical dimension			CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:58		CN	Connection other than junction at 2 o'clock, 100mm dia	00:01:12		CN	Connection other than junction at 2 o'clock, 100mm dia	00:01:26		CN	Connection other than junction at 2 o'clock, 100mm dia	00:01:41		CN	Connection other than junction at 2 o'clock, 100mm dia	00:02:47		CN	Connection other than junction at 10 o'clock, 100mm dia	00:02:58		MHF	Finish node, manhole, reference: 222	00:04:15	2
MH	Start node, manhole, reference: 223	00:00:00	1																																								
WL	Water level, 0% of the vertical dimension																																										
CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:58																																									
CN	Connection other than junction at 2 o'clock, 100mm dia	00:01:12																																									
CN	Connection other than junction at 2 o'clock, 100mm dia	00:01:26																																									
CN	Connection other than junction at 2 o'clock, 100mm dia	00:01:41																																									
CN	Connection other than junction at 2 o'clock, 100mm dia	00:02:47																																									
CN	Connection other than junction at 10 o'clock, 100mm dia	00:02:58																																									
MHF	Finish node, manhole, reference: 222	00:04:15	2																																								

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 223X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
37	Downstream	223X		

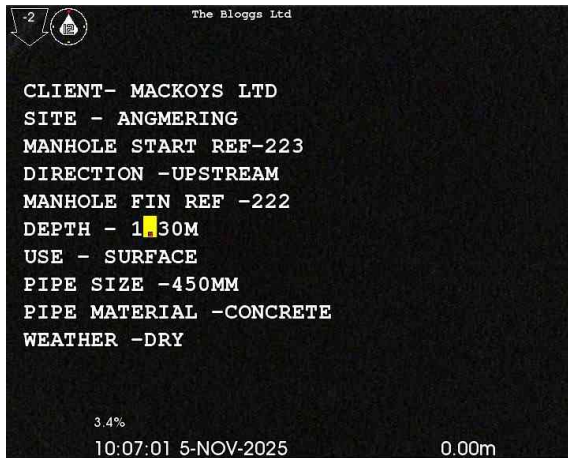

1, 00:00:00, 0.00 m
Start node, manhole, reference: 223



2, 00:04:15, 46.87 m
Finish node, manhole, reference: 222



Section Inspection - 06/11/2025 - 223X

Item No. 38	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 223X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	223
Road:	Langmead Place	Inspected Length:	25.13 m	Upstream Pipe Depth:	1.300 m
Location:	Road	Total Length:	25.13 m	Downstream Node:	225
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	450 mm		
Flow Control:	No flow control	Material:	Concrete		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:218	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.30 m	223						
0.00		MH	Start node, manhole, reference: 223	00:00:00	1		
0.00		WL	Water level, 0% of the vertical dimension				
5.61		CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:35			
5.81		CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:36			
8.92		CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:47			
25.13		MHF	Finish node, manhole, reference: 225	00:01:52	2		
225							
Depth: m							

Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 06/11/2025 - 223X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
38	Downstream	223X		

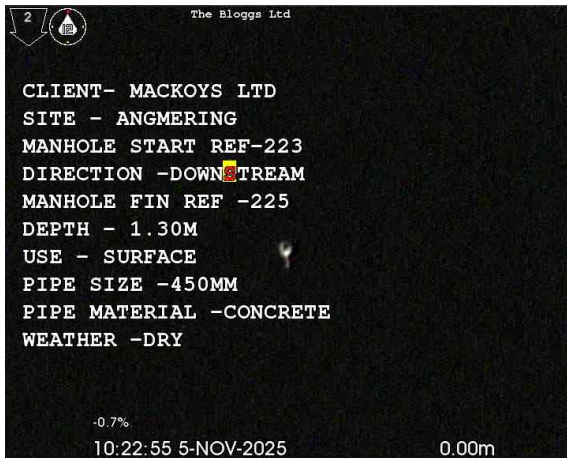

1, 00:00:00, 0.00 m
Start node, manhole, reference: 223

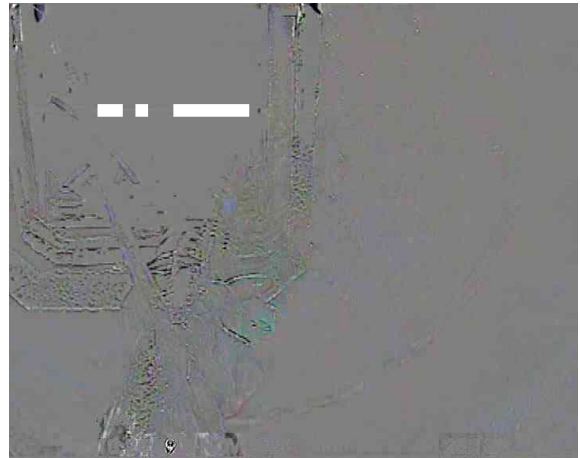

2, 00:01:52, 25.13 m
Finish node, manhole, reference: 225



Section Inspection - 06/11/2025 - 225X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
39	1	06/11/25	13:55	Not Specified	No Rain Or Snow	Yes	225X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	225
Road:	Langmead Place	Inspected Length:	30.88 m	Upstream Pipe Depth:	2.000 m
Location:	Road	Total Length:	30.88 m	Downstream Node:	S2706
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	450 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:268	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 2.00 m							
225							
	0.00	MH	Start node, manhole, reference: 225	00:00:00	1		
	0.00	WL	Water level, 0% of the vertical dimension				
	27.55	CN	Connection other than junction at 10 o'clock, 100mm dia	00:02:50			
	30.88	MHF	Finish node, manhole, reference: S2706	00:03:04	2		
S2706							
Depth: m							

Construction Features

Miscellaneous Features

Structural Defects

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 225X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
39	Downstream	225X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 225



2, 00:03:04, 30.88 m
Finish node, manhole, reference: S2706



Section Inspection - 06/11/2025 - 261X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
40	1	06/11/25	13:55	Not Specified	No Rain Or Snow	Yes	261X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	261
Road:	Langmead Place	Inspected Length:	27.70 m	Upstream Pipe Depth:	1.050 m
Location:	Road	Total Length:	27.70 m	Downstream Node:	262
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:240	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 261	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		2.69	CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:25		
		10.73	CN	Connection other than junction at 10 o'clock, 150mm dia	00:01:01		
		19.19	CN	Connection other than junction at 10 o'clock, 150mm dia	00:01:40		
		27.70	MHF	Finish node, manhole, reference: 262	00:02:21	2	
		262					
		Depth: m					

Construction Features

Miscellaneous Features

Structural Defects


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 261X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
40	Downstream	261X		

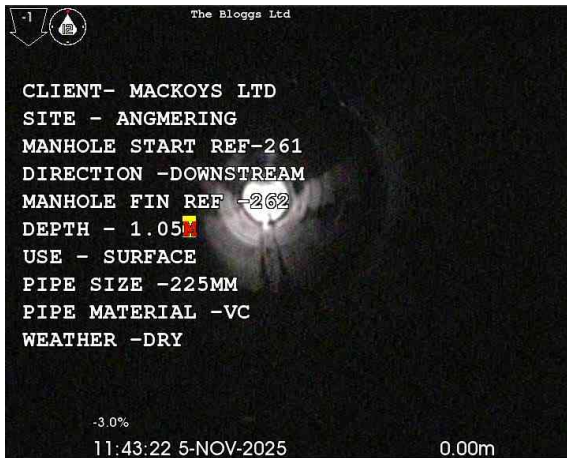

1, 00:00:00, 0.00 m
Start node, manhole, reference: 261



2, 00:02:21, 27.70 m
Finish node, manhole, reference: 262



Section Inspection - 11/11/2025 - F7X

Item No. 41	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F7X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F7
Road:	Langmead Place	Inspected Length:	13.98 m	Upstream Pipe Depth:	1.600 m
Location:	Road	Total Length:	13.98 m	Downstream Node:	F8
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:122	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.60 m F7 0.00 MH Start node, manhole, reference: F7 00:00:00 1 0.00 WL Water level, 0% of the vertical dimension 11.25 WL Water level, 20% of the vertical dimension 00:01:19 13.98 MHF Finish node, manhole, reference: F8 00:01:33 2 F8 Depth: m							

Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F7X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
41	Downstream	F7X		

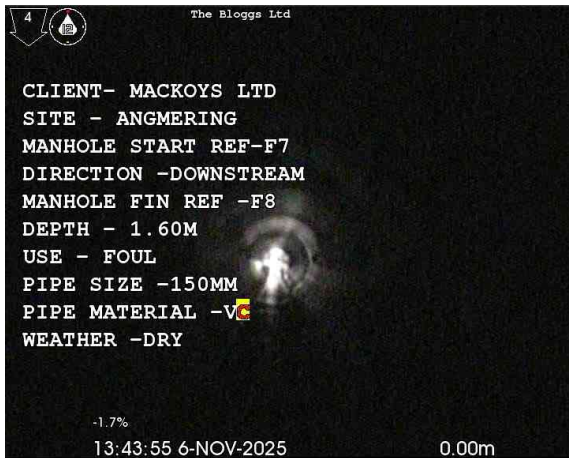

1, 00:00:00, 0.00 m
Start node, manhole, reference: F7



2, 00:01:33, 13.98 m
Finish node, manhole, reference: F8



Item No. 42	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F22X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Upstream	Upstream Node:	F22
Road:	Langmead Place	Inspected Length:	14.01 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	14.01 m	Downstream Node:	F23
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.400 m
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:	
Recommendations:	

Scale: 1:122 Position [m]

Depth: 1.40 m
F23


Code	Observation	MPEG	Photo	Grade
MH	Start node, manhole, reference: F23	00:00:00	1	
WL	Water level, 0% of the vertical dimension			
CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:46		
MHF	Finish node, manhole, reference: F22	00:02:18	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 11/11/2025 - F22X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
42	Upstream	F22X		

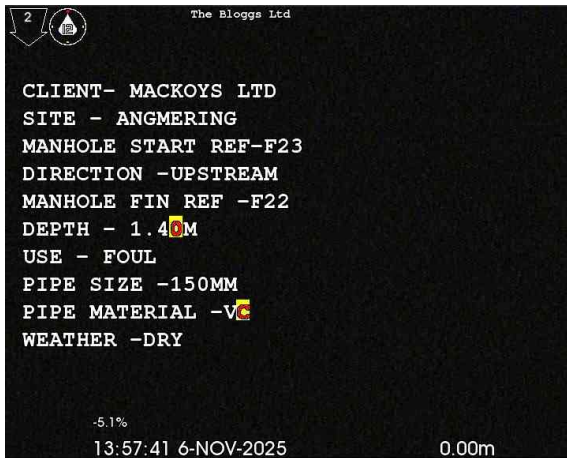

1, 00:00:00, 0.00 m
Start node, manhole, reference: F23

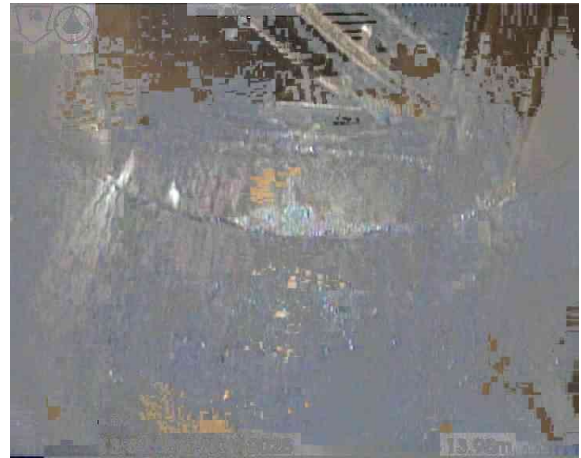

2, 00:02:18, 14.01 m
Finish node, manhole, reference: F22



Section Inspection - 11/11/2025 - F23X

Item No. 43	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F23X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	F23
Road:	Langmead Place	Inspected Length:	24.05 m	Upstream Pipe Depth:	1.400 m
Location:	Road	Total Length:	24.05 m	Downstream Node:	F24
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		


Comments:
Recommendations:

Scale:	1:209	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.40 m F23 0.00 0.00 8.44 24.05 F24 Depth: m							
		0.00	MH	Start node, manhole, reference: F23	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		8.44	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:30		
		24.05	MHF	Finish node, manhole, reference: F24	00:01:32	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F23X				
Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
43	Downstream	F23X		

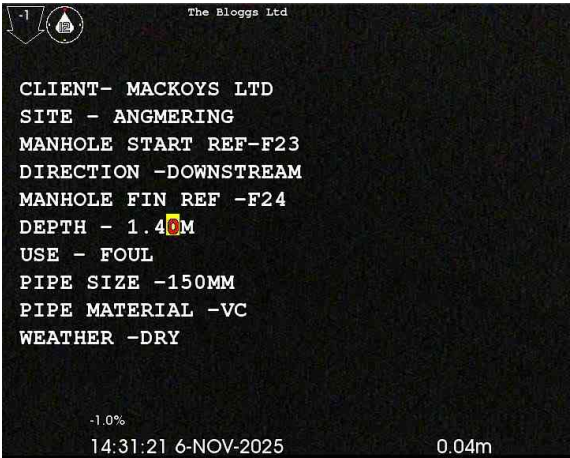

1, 00:00:00, 0.00 m
Start node, manhole, reference: F23



2, 00:01:32, 24.05 m
Finish node, manhole, reference: F24



Section Inspection - 11/11/2025 - F42X

Item No. 44	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F42X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F42
Road:	Langmead Place	Inspected Length:	14.70 m	Upstream Pipe Depth:	1.400 m
Location:	Road	Total Length:	14.70 m	Downstream Node:	F43
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:128	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.40 m F42 0.00 0.00 9.35 14.70 F43 Depth: m							
		0.00	MH	Start node, manhole, reference: F42	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		9.35	CN	Connection other than junction at 2 o'clock, 150mm dia	00:01:26		
		14.70	MHF	Finish node, manhole, reference: F43	00:01:59	2	

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F42X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
44	Downstream	F42X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F42



2, 00:01:59, 14.70 m
Finish node, manhole, reference: F43



Item No. 45	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F43X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F43X				
Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
45	Downstream	F43X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F43



2, 00:02:25, 20.42 m
Finish node, manhole, reference: F47



Item No. 46	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F18X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	F18
Road:	Langmead Place	Inspected Length:	7.41 m	Upstream Pipe Depth:	1.400 m
Location:	Road	Total Length:	7.41 m	Downstream Node:	F19
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul		Pipe Shape:	Circular	
Type of Pipe:	Gravity drain/sewer		Dia/Height:	150 mm	
Flow Control:	No flow control		Material:	Polyvinyl chloride	
Year Constructed:	Not Specified		Lining Type:	No Lining	
Inspection Purpose:	Routine inspection		Lining Material:	No Lining	

Comments:

Recommendations:

Scale: 1:65

Position [m]

Code

Observation

MPEG

Photo

Grade

Depth: 1.40 m

F18

0.00

0.00

MH

Start node, manhole, reference: F18

00:00:00

1

WL

Water level, 0% of the vertical dimension

7.41

MHF

Finish node, manhole, reference: F19

00:01:04

2

F19

Depth: m

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F18X				
Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
46	Downstream	F18X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F18



2, 00:01:04, 7.41 m
Finish node, manhole, reference: F19




Section Inspection - 11/11/2025 - F19X

Item No. 47	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F19X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	F19
Road:	Langmead Place	Inspected Length:	25.24 m	Upstream Pipe Depth:	1.400 m
Location:	Road	Total Length:	25.24 m	Downstream Node:	F20
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

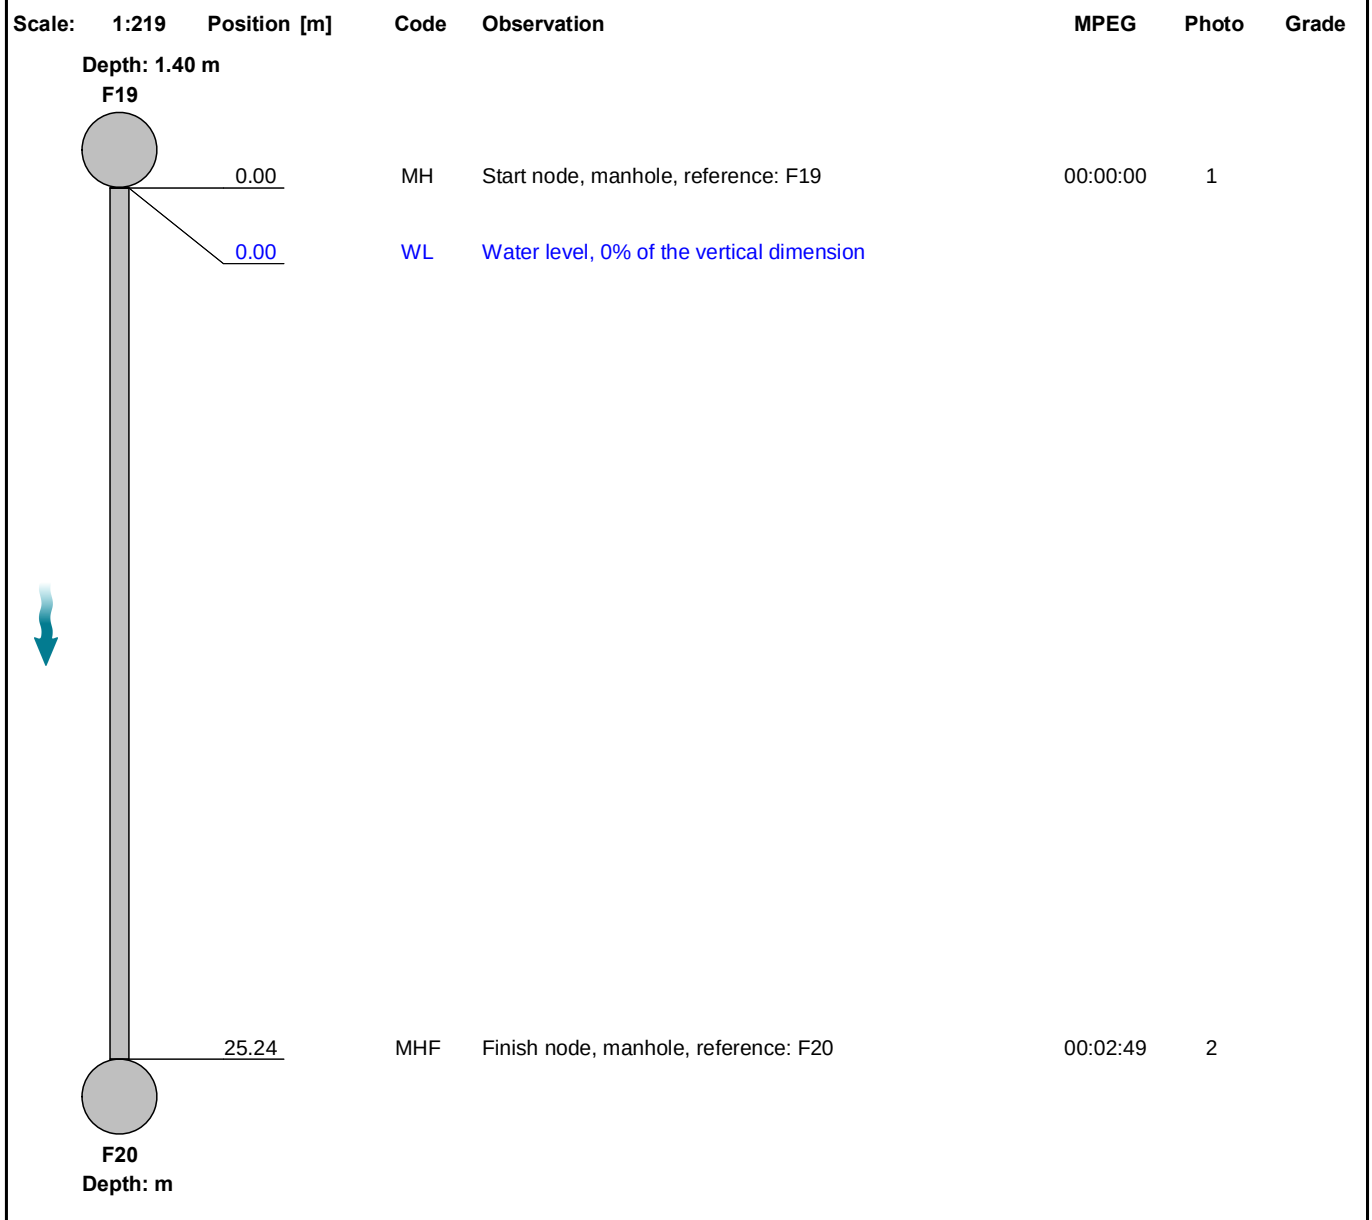

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F19X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
47	Downstream	F19X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F19



2, 00:02:49, 25.24 m
Finish node, manhole, reference: F20



Item No. 48	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F20X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	F20
Road:	Langmead Place	Inspected Length:	40.24 m	Upstream Pipe Depth:	1.400 m
Location:	Road	Total Length:	40.24 m	Downstream Node:	F21
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:	
Recommendations:	

Scale: 1:349 Position [m] Code Observation MPEG Photo Grade

Depth: 1.40 m
F20

0.00

0.00

40.24

F21
Depth: m

MH Start node, manhole, reference: F20 00:00:00 1

WL Water level, 0% of the vertical dimension


MHF Finish node, manhole, reference: F21 00:04:51 2

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F20X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
48	Downstream	F20X		

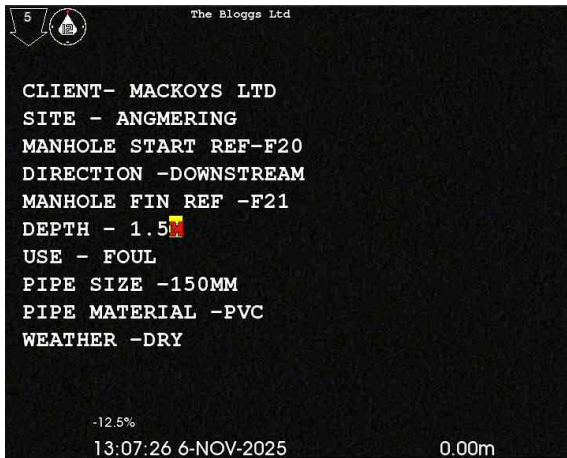

1, 00:00:00, 0.00 m
Start node, manhole, reference: F20



2, 00:04:51, 40.24 m
Finish node, manhole, reference: F21



Section Inspection - 11/11/2025 - F39X

Item No. 49	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F39X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F39
Road:	Langmead Place	Inspected Length:	16.91 m	Upstream Pipe Depth:	1.750 m
Location:	Road	Total Length:	16.91 m	Downstream Node:	F40
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:147	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.75 m F39						
0.00	MH	Start node, manhole, reference: F39	00:00:00	1		
0.00	WL	Water level, 0% of the vertical dimension				
16.01	WL	Water level, 20% of the vertical dimension	00:01:59			
16.91	MHF	Finish node, manhole, reference: F40	00:02:03	2		
F40 Depth: m						

Construction Features

Miscellaneous Features

Structural Defects


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 11/11/2025 - F39X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
49	Downstream	F39X		

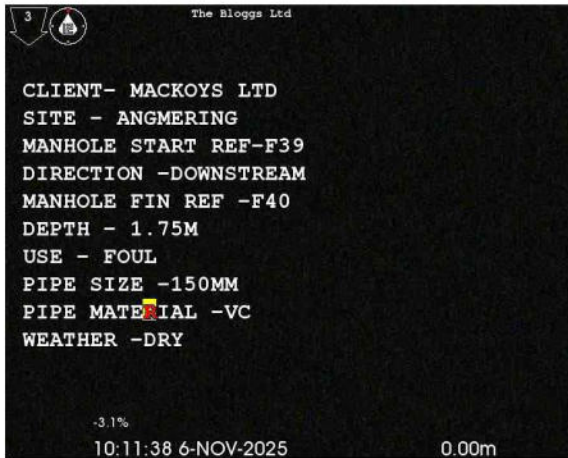

1, 00:00:00, 0.00 m
Start node, manhole, reference: F39

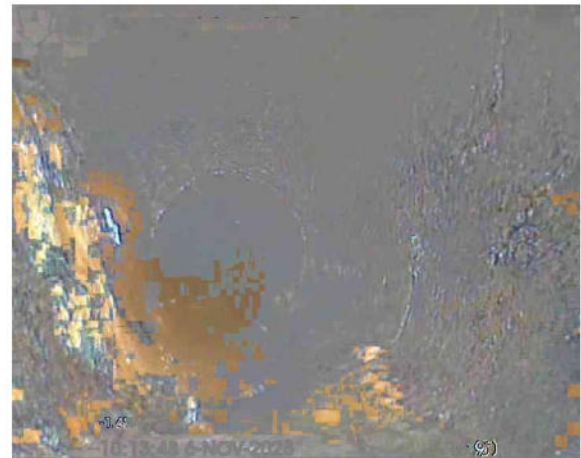

2, 00:02:03, 16.91 m
Finish node, manhole, reference: F40



Section Inspection - 11/11/2025 - F40X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
50	1	11/11/25	9:18	Not Specified	No Rain Or Snow	Yes	F40X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F40
Road:	Langmead Place	Inspected Length:	33.89 m	Upstream Pipe Depth:	1.600 m
Location:	Road	Total Length:	33.89 m	Downstream Node:	F41
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:294	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.60 m F40							
	0.00	MH	Start node, manhole, reference: F40	00:00:00	1		
	0.00	WL	Water level, 0% of the vertical dimension				
	33.81	JN	Junction at 6 o'clock, 150mm dia: BACKDROP	00:03:45			
	33.89	MHF	Finish node, manhole, reference: F41	00:03:48	2		
		F41	Depth: m				


Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	2	5.0	0.3	10.0	4.0



Section Pictures - 11/11/2025 - F40X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
50	Downstream	F40X		

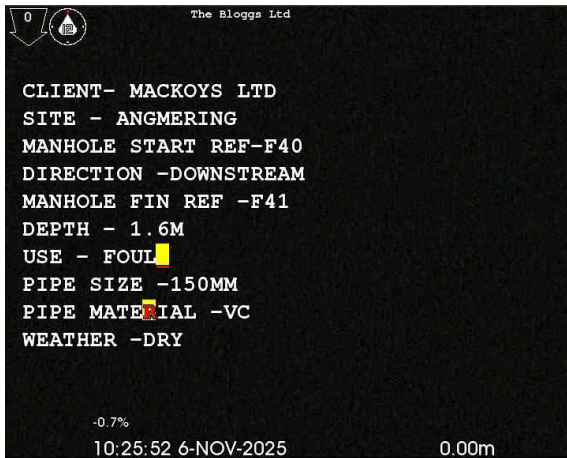

1, 00:00:00, 0.00 m
Start node, manhole, reference: F40



2, 00:03:48, 33.89 m
Finish node, manhole, reference: F41




Section Inspection - 11/11/2025 - F41X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
51	1	11/11/25	9:18	Not Specified	No Rain Or Snow	Yes	F41X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F41
Road:	Langmead Place	Inspected Length:	20.32 m	Upstream Pipe Depth:	1.800 m
Location:	Road	Total Length:	20.32 m	Downstream Node:	F42
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:176	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.80 m F41							
		0.00	MH	Start node, manhole, reference: F41	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	S01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:08	2
		0.86	F01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:16	
		14.94	CN	Connection other than junction at 2 o'clock, 150mm dia	00:01:58		
		20.32	MHF	Finish node, manhole, reference: F42	00:02:33	3	
F42 Depth: m							


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F41X				
Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
51	Downstream	F41X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F41

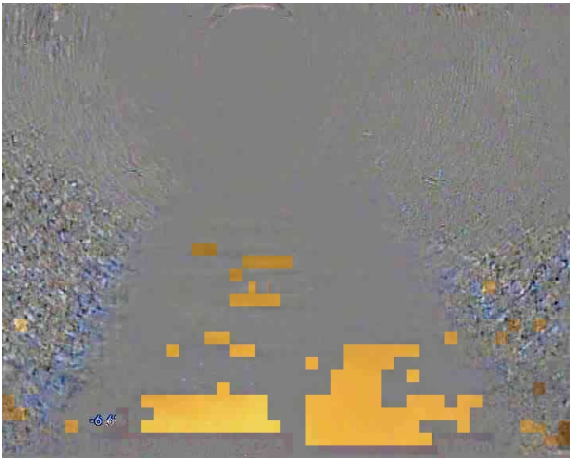

2, 00:00:08, 0.00 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:02:33, 20.32 m
Finish node, manhole, reference: F42




Section Inspection - 11/11/2025 - 32AX

Item No. 52	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 32AX
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Upstream	Upstream Node:	32A
Road:	Langmead Place	Inspected Length:	8.03 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	8.03 m	Downstream Node:	32B
Surface Type:		Joint Length:		Downstream Pipe Depth:	2.200 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

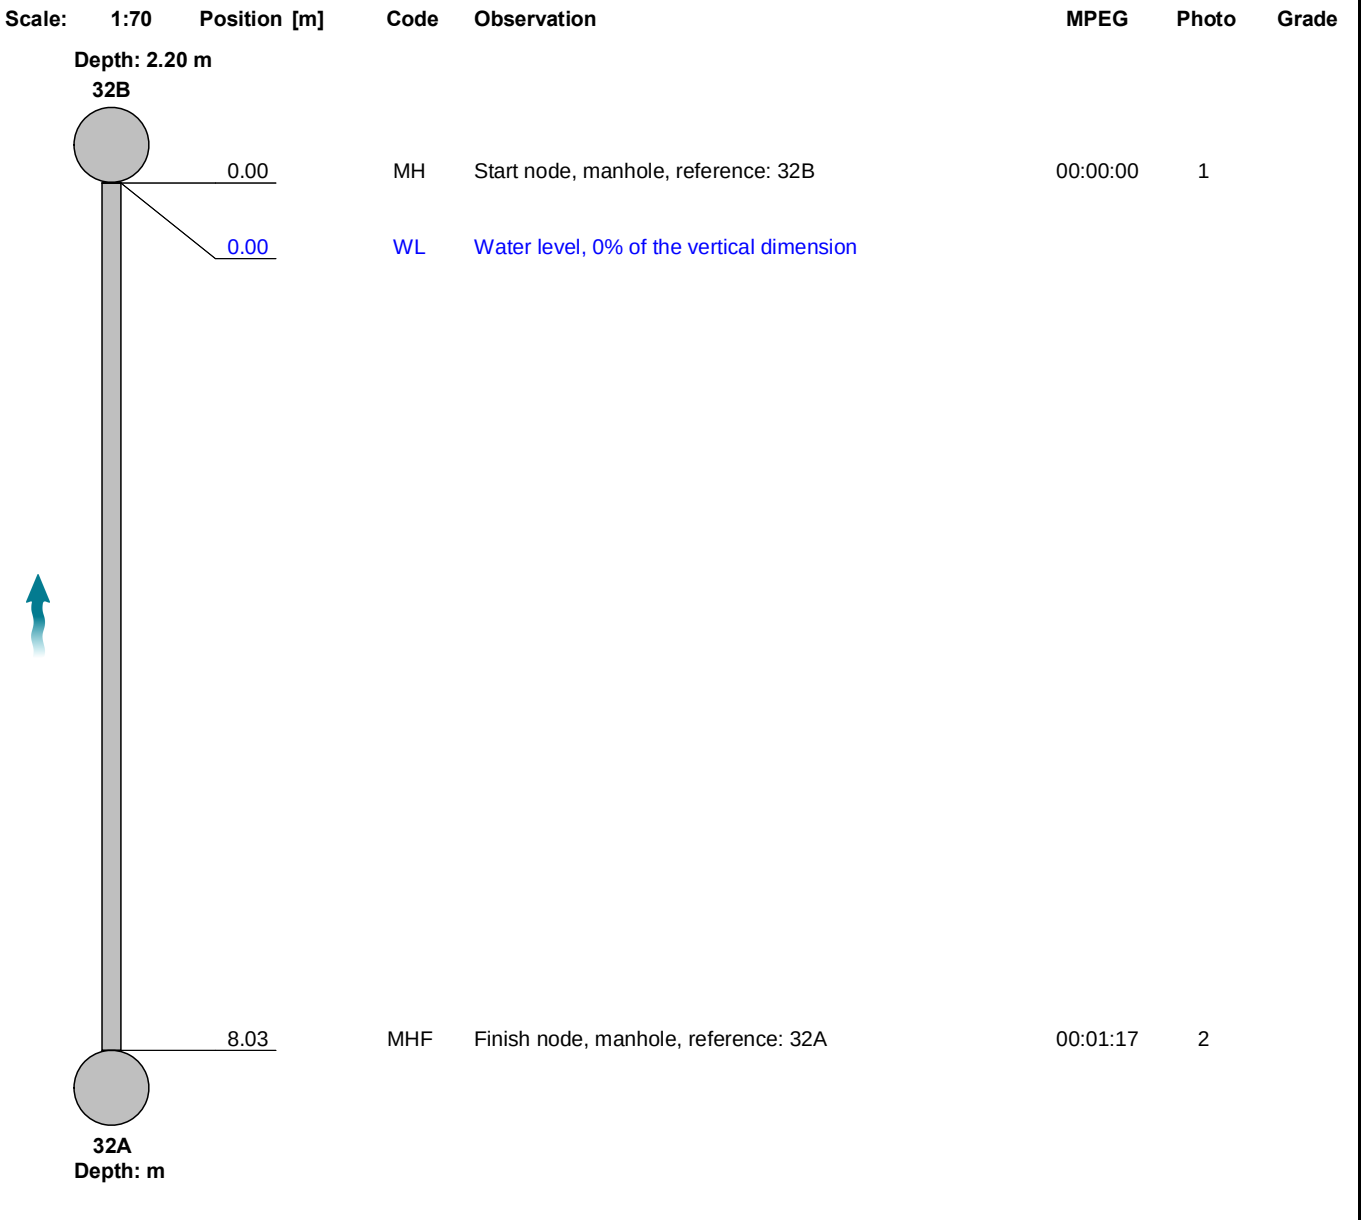

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - 32AX				
Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
52	Upstream	32AX		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 32B



2, 00:01:17, 8.03 m
Finish node, manhole, reference: 32A



Section Inspection - 11/11/2025 - 325X

Item No. 53	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 325X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	325
Road:	Langmead Place	Inspected Length:	29.80 m	Upstream Pipe Depth:	1.200 m
Location:	Road	Total Length:	29.80 m	Downstream Node:	326
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:259	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.20 m							
325							
	0.00	MH	Start node, manhole, reference: 325	00:00:00	1		
	0.00	WL	Water level, 0% of the vertical dimension				
	2.23	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:34			
	21.11	CN	Connection other than junction at 10 o'clock, 100mm dia	00:01:45			
	25.87	CN	Connection other than junction at 2 o'clock, 150mm dia	00:02:03			
	26.12	CN	Connection other than junction at 2 o'clock, 150mm dia	00:02:05			
	29.80	MHF	Finish node, manhole, reference: 326	00:02:20	2		
326							
Depth: m							

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
2	1.0	0.1	2.0	1.0	1	2.0	0.1	2.0	3.0



Section Pictures - 11/11/2025 - 325X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
53	Downstream	325X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 325



2, 00:02:20, 29.80 m
Finish node, manhole, reference: 326




Section Inspection - 11/11/2025 - 323X


Item No. 54	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 323X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	323
Road:	Langmead Place	Inspected Length:	17.48 m	Upstream Pipe Depth:	1.200 m
Location:	Road	Total Length:	17.48 m	Downstream Node:	323A
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

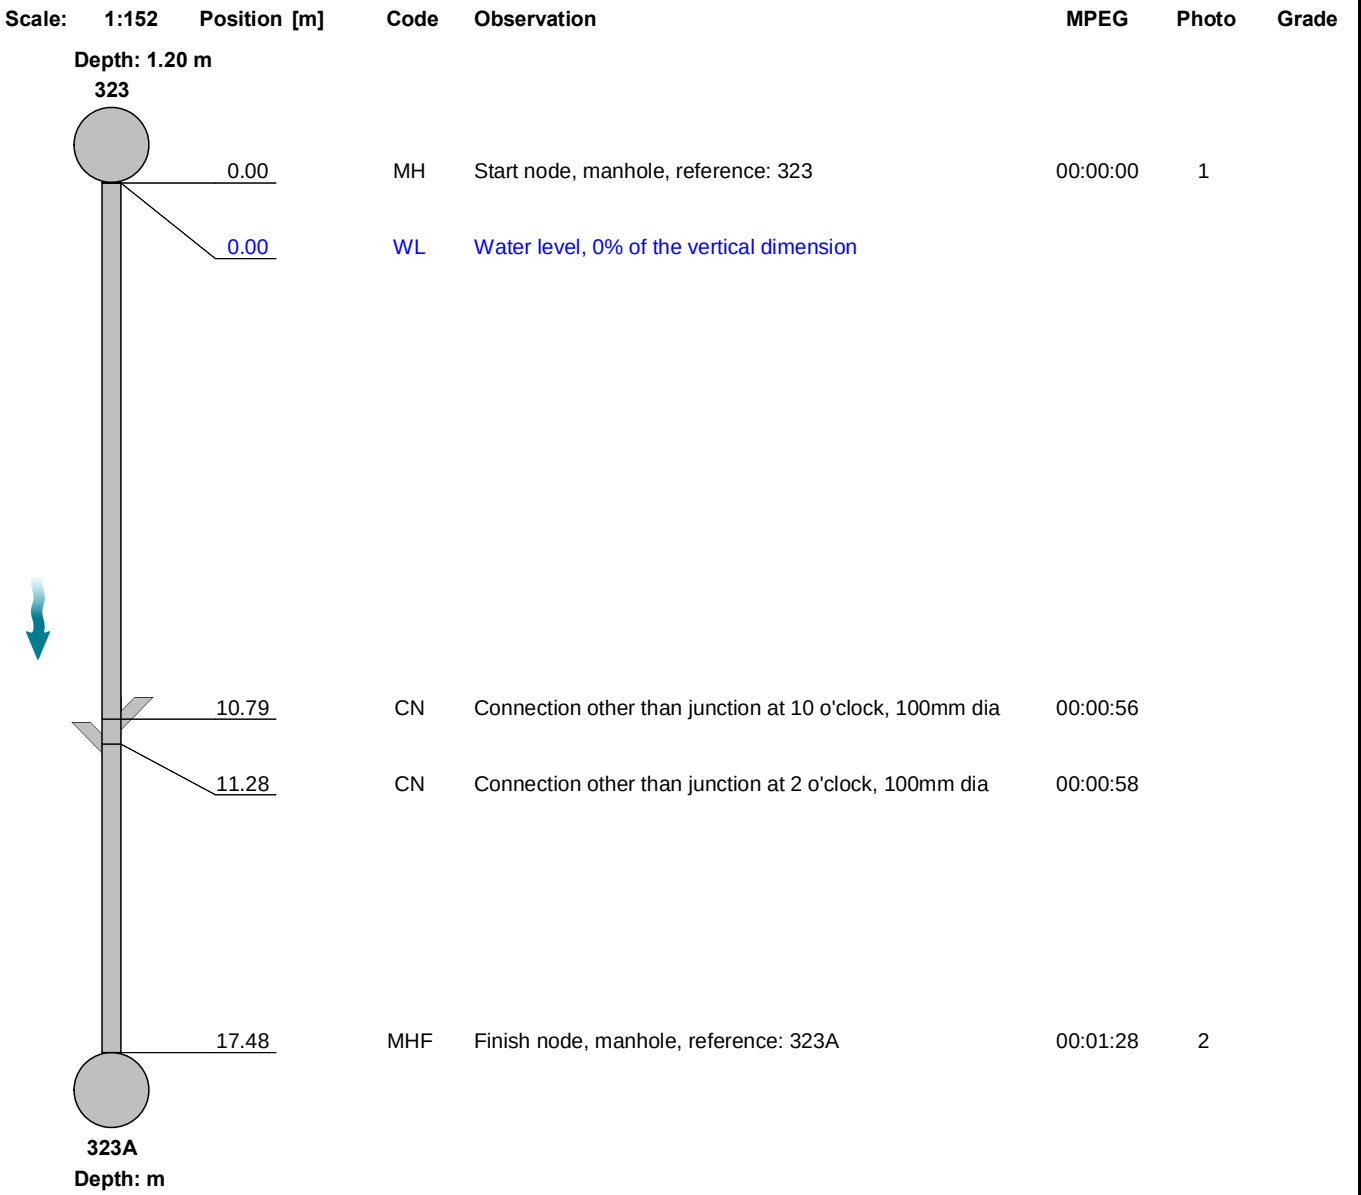

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - 323X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
54	Downstream	323X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 323



2, 00:01:28, 17.48 m
Finish node, manhole, reference: 323A



Section Inspection - 11/11/2025 - 330X

Item No. 55	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 330X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Upstream	Upstream Node:	330
Road:	Langmead Place	Inspected Length:	7.38 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	7.38 m	Downstream Node:	S215
Surface Type:		Joint Length:		Downstream Pipe Depth:	2.000 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:64	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 2.00 m S215 0.00 MH Start node, manhole, reference: S215 00:00:00 1 0.00 WL Water level, 0% of the vertical dimension 4.81 LU Line deviates up 00:00:37 7.38 MHF Finish node, manhole, reference: 330 00:02:04 2 330 Depth: m							

Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - 330X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
55	Upstream	330X		

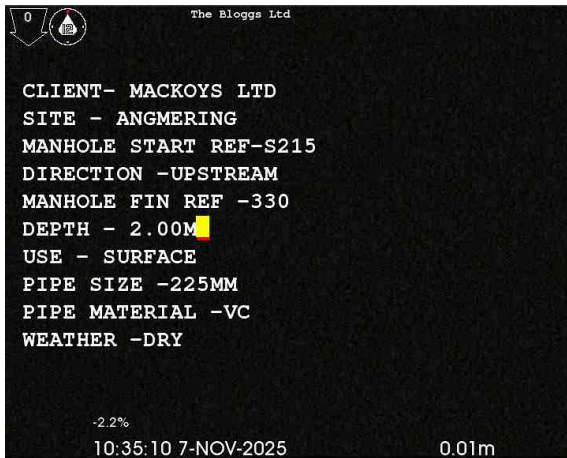

1, 00:00:00, 0.00 m
Start node, manhole, reference: S215



2, 00:02:04, 7.38 m
Finish node, manhole, reference: 330


Section Inspection - 11/11/2025 - 330X

Item No. 56	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 330X
Operator C. Bloor		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	330
Road:	Langmead Place	Inspected Length:	26.06 m	Upstream Pipe Depth:	2.000 m
Location:	Road	Total Length:	26.06 m	Downstream Node:	S215
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

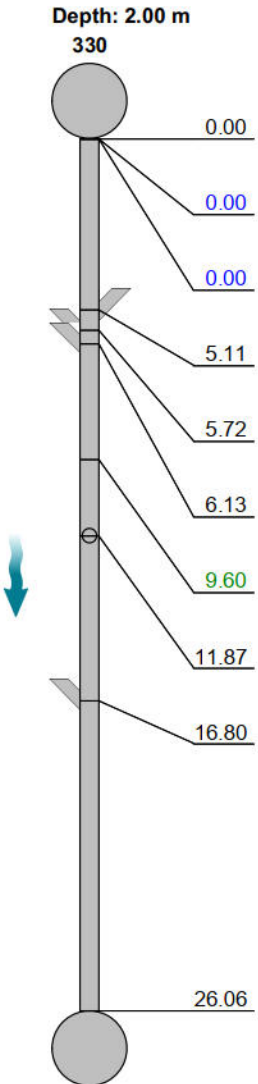Scale:	1:226	Position [m]	Code	Observation	MPEG	Photo	Grade																																								
Depth: 2.00 m 330  <table><tr><td>MH</td><td>Start node, manhole, reference: 330</td><td>00:00:00</td><td>1</td></tr><tr><td>WL</td><td>Water level, 0% of the vertical dimension</td><td></td><td></td></tr><tr><td>REM</td><td>General remark: overlap</td><td>00:00:08</td><td>2</td></tr><tr><td>CN</td><td>Connection other than junction at 10 o'clock, 100mm dia</td><td>00:00:52</td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 2 o'clock, 100mm dia</td><td>00:00:54</td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 2 o'clock, 100mm dia</td><td>00:00:56</td><td></td></tr><tr><td>LD</td><td>Line deviates down</td><td>00:01:24</td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 12 o'clock, 100mm dia</td><td>00:01:34</td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 1 o'clock, 100mm dia</td><td>00:01:53</td><td></td></tr><tr><td>MHF</td><td>Finish node, manhole, reference: S215</td><td>00:02:35</td><td>3</td></tr></table>								MH	Start node, manhole, reference: 330	00:00:00	1	WL	Water level, 0% of the vertical dimension			REM	General remark: overlap	00:00:08	2	CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:52		CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:54		CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:56		LD	Line deviates down	00:01:24		CN	Connection other than junction at 12 o'clock, 100mm dia	00:01:34		CN	Connection other than junction at 1 o'clock, 100mm dia	00:01:53		MHF	Finish node, manhole, reference: S215	00:02:35	3
MH	Start node, manhole, reference: 330	00:00:00	1																																												
WL	Water level, 0% of the vertical dimension																																														
REM	General remark: overlap	00:00:08	2																																												
CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:52																																													
CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:54																																													
CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:56																																													
LD	Line deviates down	00:01:24																																													
CN	Connection other than junction at 12 o'clock, 100mm dia	00:01:34																																													
CN	Connection other than junction at 1 o'clock, 100mm dia	00:01:53																																													
MHF	Finish node, manhole, reference: S215	00:02:35	3																																												

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 11/11/2025 - 330X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
56	Downstream	330X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 330

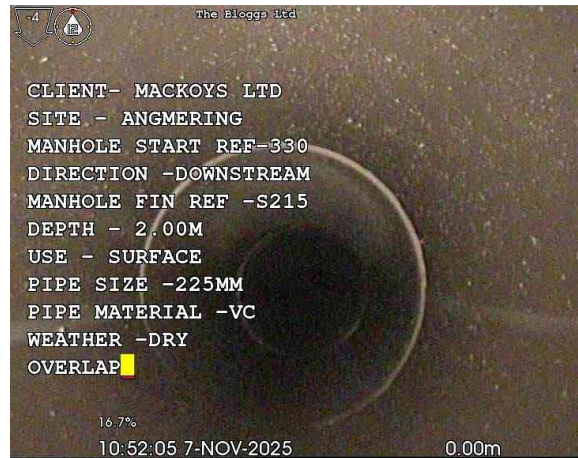

2, 00:00:08, 0.00 m
General remark, overlap



3, 00:02:35, 26.06 m
Finish node, manhole, reference: S215



Section Inspection - 11/11/2025 - 332BX

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
57	1	11/11/25	9:18	Not Specified	No Rain Or Snow	Yes	332BX
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	332B
Road:	Langmead Place	Inspected Length:	18.10 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	18.10 m	Downstream Node:	330
Surface Type:		Joint Length:		Downstream Pipe Depth:	2.000 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:157	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 330	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		3.92	CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:27		
		18.10	MHF	Finish node, manhole, reference: 332B	00:01:22	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 11/11/2025 - 332BX


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
57	Upstream	332BX		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 330

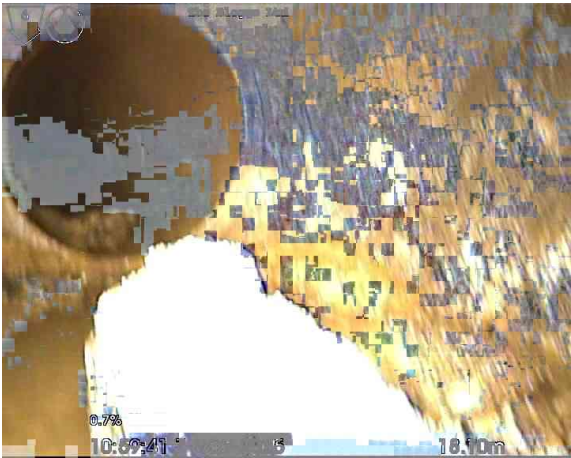

2, 00:01:22, 18.10 m
Finish node, manhole, reference: 332B




Section Inspection - 11/11/2025 - FW348X

Item No. 58	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR FW348X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	FW348
Road:	Langmead Place	Inspected Length:	2.40 m	Upstream Pipe Depth:	1.000 m
Location:	Road	Total Length:	2.40 m	Downstream Node:	F41
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

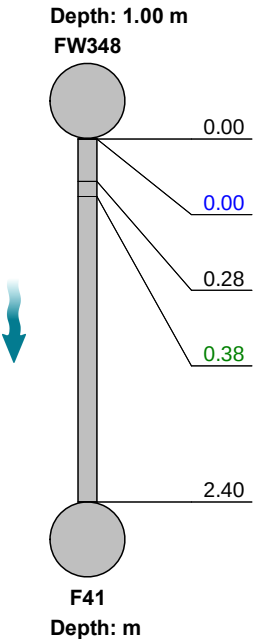Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
							
		0.00	MH	Start node, manhole, reference: FW348	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.28	JN	Junction at 6 o'clock, 100mm dia: BACKDROP	00:00:30		
		0.38	LL	Line deviates left	00:00:11		
		2.40	MHF	Finish node, manhole, reference: F41	00:00:41	2	

Construction Features

Miscellaneous Features

Structural Defects


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW348X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
58	Downstream	FW348X		

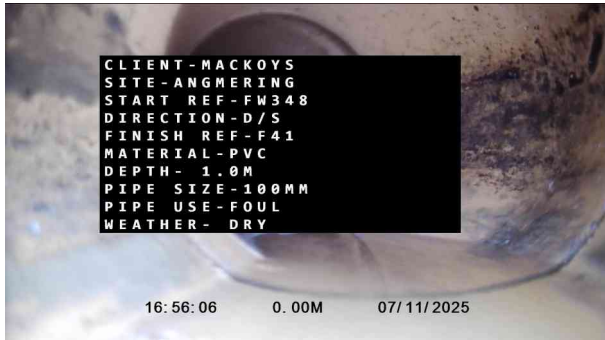

1, 00:00:00, 0.00 m
Start node, manhole, reference: FW348



2, 00:00:41, 2.40 m
Finish node, manhole, reference: F41



Section Inspection - 11/11/2025 - FW332X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
59	1	11/11/25	9:18	Not Specified	No Rain Or Snow	Yes	FW332X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	FW332
Road:	Langmead Place	Inspected Length:	5.95 m	Upstream Pipe Depth:	1.000 m
Location:	Road	Total Length:	5.95 m	Downstream Node:	F41
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:


Scale:	1:52	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.00 m FW332							
	0.00	MH	Start node, manhole, reference: FW332	00:00:00	1		
	0.00	WL	Water level, 0% of the vertical dimension				
	1.53	LR	Line deviates right	00:00:10			
	3.45	JN	Junction at 6 o'clock, 100mm dia: BACKDROP	00:00:19			
	5.95	MHF	Finish node, manhole, reference: F41	00:00:25	2		
F41 Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW332X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
59	Downstream	FW332X		

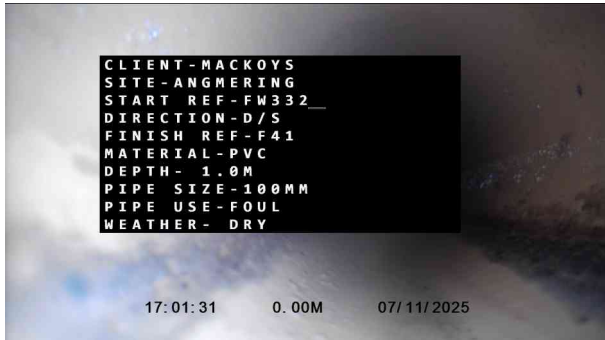

1, 00:00:00, 0.00 m
Start node, manhole, reference: FW332



2, 00:00:25, 5.95 m
Finish node, manhole, reference: F41



Section Inspection - 11/11/2025 - FW355X

Item No. 60	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR FW355X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	FW355
Road:	Langmead Place	Inspected Length:	2.11 m	Upstream Pipe Depth:	1.800 m
Location:	Road	Total Length:	2.20 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.80 m FW355							
	0.00	MH	Start node, manhole, reference: FW355		00:00:00	1	
	0.00	WL	Water level, 0% of the vertical dimension				
	2.10	LR	Line deviates right		00:00:13		
	2.10	LD	Line deviates down		00:00:13		
	2.11	BRF	Finish node, major connection without manhole, reference: MAIN		00:00:15	2	
MAIN							
Depth: m							

Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW355X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
60	Downstream	FW355X		

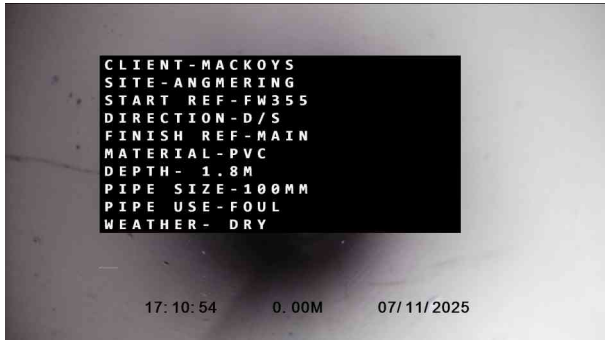

1, 00:00:00, 0.00 m
Start node, manhole, reference: FW355



2, 00:00:15, 2.11 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 11/11/2025 - RWPX

Item No. 61	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RWPX
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RWP
Road:	Langmead Place	Inspected Length:	25.49 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	25.49 m	Downstream Node:	330
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.800 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:


Scale: 1:221	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.80 m 330						
0.00	MH	Start node, manhole, reference: 330	00:00:00	1		
0.00	WL	Water level, 0% of the vertical dimension	00:00:10			
0.28	LD	Line deviates down	00:00:10			
0.28	LU	Line deviates up	00:00:16			
1.92	LD	Line deviates left	00:00:17			
2.40	WL	Water level, 20% of the vertical dimension	00:00:42			
9.89	WL	Water level, 35% of the vertical dimension	00:00:51			
13.74						
25.49	MHF	Finish node, manhole, reference: RWP	00:01:23	2		
RWP Depth: m						

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	80.0	3.1	80.0	4.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - RWPX


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
61	Upstream	RWPX		

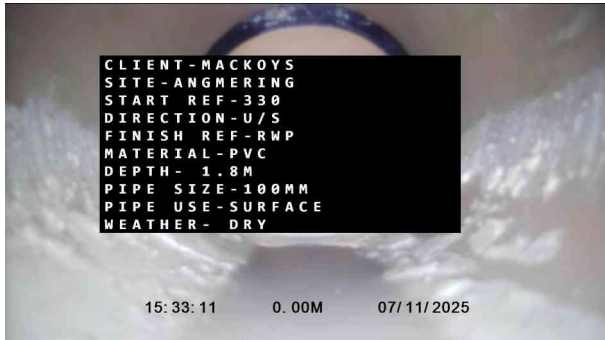

1, 00:00:00, 0.00 m
Start node, manhole, reference: 330



2, 00:01:23, 25.49 m
Finish node, manhole, reference: RWP



Section Inspection - 11/11/2025 - FW230X

Item No. 62	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR FW230X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	FW230
Road:	Langmead Place	Inspected Length:	3.07 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	3.07 m	Downstream Node:	F18
Surface Type:		Joint Length:		Downstream Pipe Depth:	0.800 m
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:


Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: F18	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		1.53	JN	Junction at 6 o'clock, 150mm dia: BACKDROP	00:00:14		
		2.20	CN	Connection other than junction at 2 o'clock, 150mm dia	00:00:28		
		2.40	SC	Pipe size changes, new size(s), 100mm high	00:00:28	2	
		3.07	MHF	Finish node, manhole, reference: FW230	00:01:02	3	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW230X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
62	Upstream	FW230X		

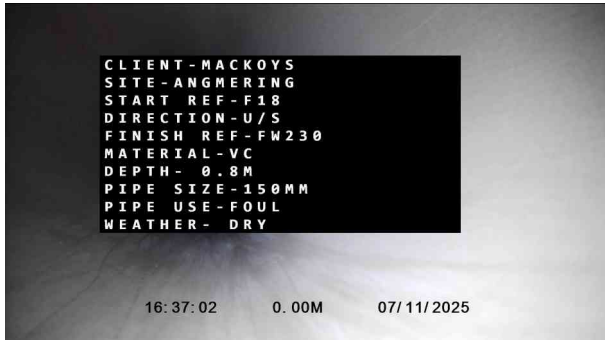

1, 00:00:00, 0.00 m
Start node, manhole, reference: F18



2, 00:00:28, 2.40 m
Pipe size changes, new size(s), 100mm high



3, 00:01:02, 3.07 m
Finish node, manhole, reference: FW230



Section Inspection - 11/11/2025 - FW230X

Item No. 63	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR FW230X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	FW230
Road:	Langmead Place	Inspected Length:	5.66 m	Upstream Pipe Depth:	0.800 m
Location:	Road	Total Length:	5.66 m	Downstream Node:	F18
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.80 m FW230							
		0.00	MH	Start node, manhole, reference: FW230	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LL	Line deviates left	00:00:10		
		2.49	LR	Line deviates right	00:00:20		
		2.49	CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:21		
		4.12	JN	Junction at 6 o'clock, 100mm dia: BACKDROP	00:00:25		
		5.66	MHF	Finish node, manhole, reference: F18	00:00:36	2	
F18 Depth: m							

Construction Features

Miscellaneous Features

Structural Defects


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW230X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
63	Downstream	FW230X		

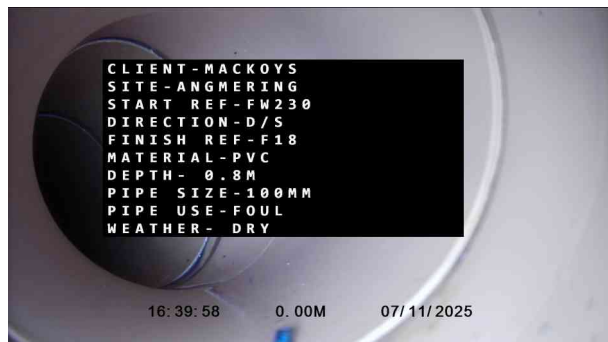

1, 00:00:00, 0.00 m
Start node, manhole, reference: FW230



2, 00:00:36, 5.66 m
Finish node, manhole, reference: F18



Section Inspection - 11/11/2025 - FW209X

Item No. 64	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR FW209X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	FW209
Road:	Langmead Place	Inspected Length:	4.99 m	Upstream Pipe Depth:	1.200 m
Location:	Road	Total Length:	4.99 m	Downstream Node:	F39
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:


Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.20 m FW209							
		0.00	MH	Start node, manhole, reference: FW209	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.09	LL	Line deviates left	00:00:07		
		1.72	LD	Line deviates down	00:00:13		
		2.49	LD	Line deviates down	00:00:16		
		4.70	JN	Junction at 6 o'clock, 100mm dia: BACKDROP	00:00:28		
		4.99	MHF	Finish node, manhole, reference: F39	00:00:31	2	
F39 Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW209X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
64	Downstream	FW209X		

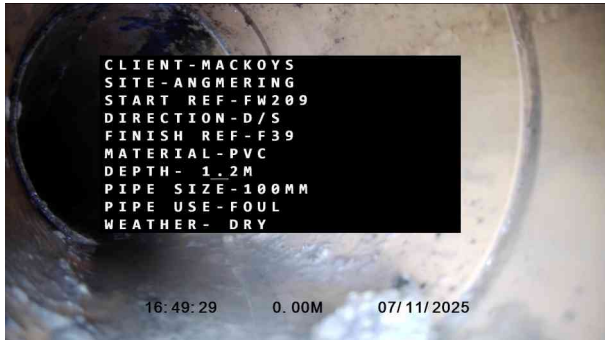

1, 00:00:00, 0.00 m
Start node, manhole, reference: FW209



2, 00:00:31, 4.99 m
Finish node, manhole, reference: F39



Item No. 65	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG69X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG69
Road:	Langmead Place	Inspected Length:	11.84 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	11.84 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:	
Recommendations:	

Scale:	1:103	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG69							
		0.00	GY	Start node, gully, reference: RG69	00:00:00	1	
		0.00	WL	Water level, 100% of the vertical dimension			
		2.49	WL	Water level, 30% of the vertical dimension	00:00:19		
		11.44	LL	Line deviates left	00:00:51		
		11.84	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:56	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG69X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
65	Downstream	RG69X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG69



2, 00:00:56, 11.84 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 17/11/2025 - RG70X


Item No. 66	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG70X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG70
Road:	Langmead Place	Inspected Length:	2.20 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	2.20 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG70	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		1.29	LU	Line deviates up	00:00:11		
		1.92	LR	Line deviates right	00:00:10		
		2.20	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:13	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG70X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
66	Downstream	RG70X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG70



2, 00:00:13, 2.20 m
Finish node, major connection without manhole, reference:
MAIN




Section Inspection - 17/11/2025 - RG68X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
67	1	17/11/25	8:19	Not Specified	No Rain Or Snow	Yes	RG68X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG68
Road:	Langmead Place	Inspected Length:	7.01 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	7.01 m	Downstream Node:	323A
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

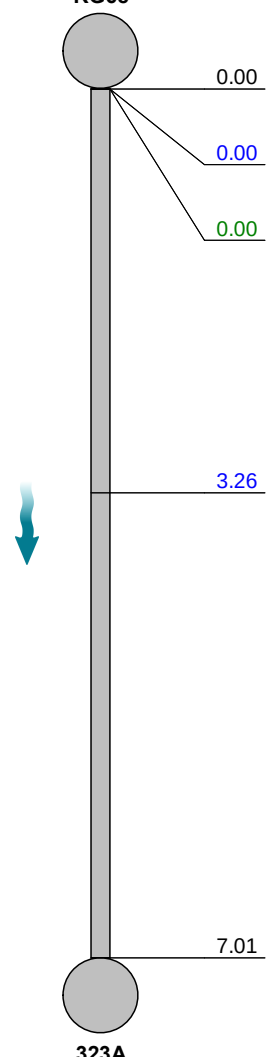
Scale:	1:61	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG68							
							
	0.00	GY	Start node, gully, reference: RG68		00:00:00	1	
	0.00	WL	Water level, 0% of the vertical dimension				
	0.00	LD	Line deviates down		00:00:06		
	3.26	WL	Water level, 20% of the vertical dimension		00:00:16		
	7.01	MHF	Finish node, manhole, reference: 323A		00:00:27	2	
323A Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG68X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
67	Downstream	RG68X		

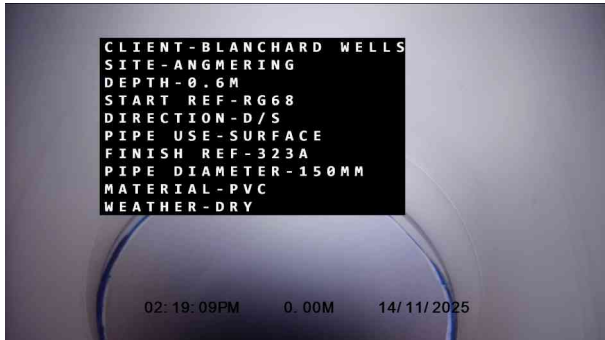

1, 00:00:00, 0.00 m
Start node, gully, reference: RG68



2, 00:00:27, 7.01 m
Finish node, manhole, reference: 323A



Item No. 68	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG53X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Comments:
Recommendations:

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG53X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
68	Upstream	RG53X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 337



2, 00:01:04, 15.56 m
Finish node, gully, reference: RG53



Section Inspection - 17/11/2025 - RG52X

Item No. 69	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG52X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RG52
Road:	Langmead Place	Inspected Length:	8.70 m	Upstream Pipe Depth:	1.600 m
Location:	Road	Total Length:	8.70 m	Downstream Node:	338
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:76	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m 338 0.00 0.00 7.71 8.70 RG52 Depth: 1.60 m							
		0.00	GY	Start node, gully, reference: 338	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		7.71	LU	Line deviates up	00:00:59		
		8.70	GYF	Finish node, gully, reference: RG52	00:01:07	2	

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG52X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
69	Upstream	RG52X		



1, 00:00:00, 0.00 m
Start node, gully, reference: 338



2, 00:01:07, 8.70 m
Finish node, gully, reference: RG52




Section Inspection - 17/11/2025 - RG51X

Item No. 70	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG51X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RG51
Road:	Langmead Place	Inspected Length:	6.72 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	6.72 m	Downstream Node:	338
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.800 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

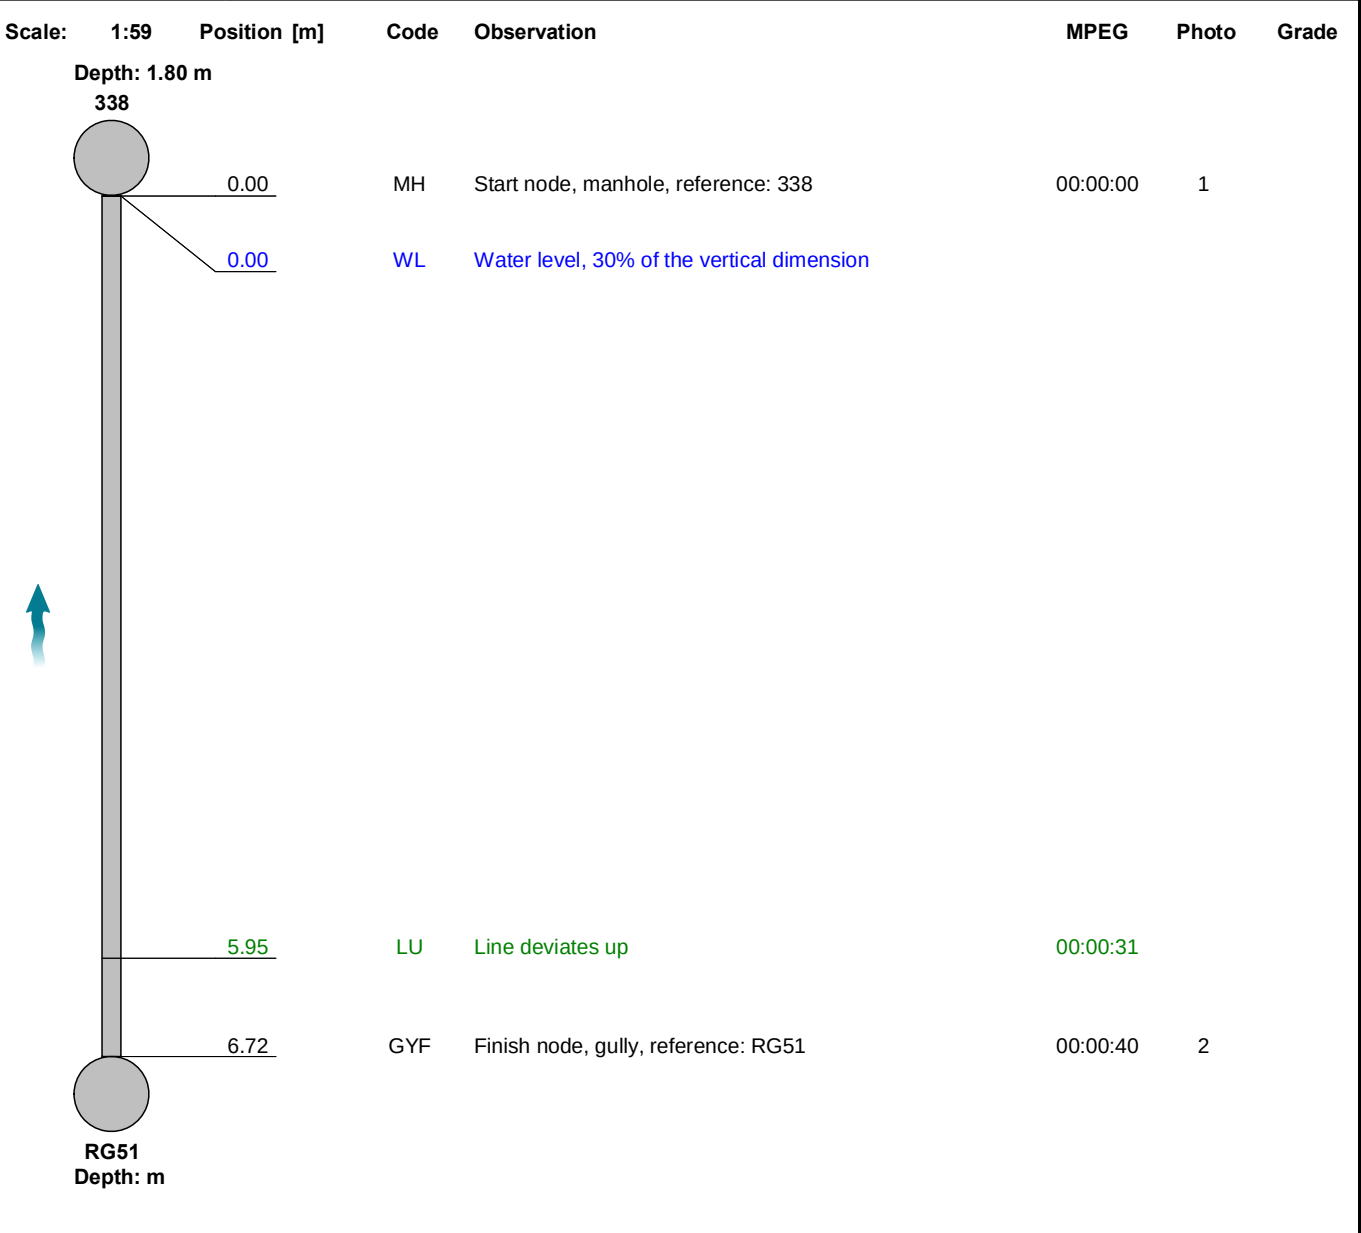

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG51X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
70	Upstream	RG51X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 338



2, 00:00:40, 6.72 m
Finish node, gully, reference: RG51



Section Inspection - 17/11/2025 - RG65X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
71	1	17/11/25	8:19	Not Specified	No Rain Or Snow	Yes	RG65X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg		CV13 BYP		Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG65
Road:	Langmead Place	Inspected Length:	8.54 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	8.54 m	Downstream Node:	261
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

Scale:	1:74	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG65							
	0.00	GY		Start node, gully, reference: RG65	00:00:00	1	
	0.00	WL		Water level, 0% of the vertical dimension			
	0.00	LD		Line deviates down	00:00:07		
	1.53	S01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:10	2	
	2.59	F01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:12		
	8.54	MHF		Finish node, manhole, reference: 261	00:00:23	3	
261 Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG65X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
71	Downstream	RG65X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG65



2, 00:00:10, 1.53 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:00:23, 8.54 m
Finish node, manhole, reference: 261

Section Inspection - 17/11/2025 - RG54X

Item No. 72	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG54X
Operator C.Blogg		Vehicle CV13 BYP		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Upstream	Upstream Node:	RG54
Road:	Langmead Place	Inspected Length:	11.47 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	11.47 m	Downstream Node:	337
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.600 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:100 Position [m] Code Observation MPEG Photo Grade

Depth: 1.60 m

337

0.00

0.00

GY Start node, gully, reference: 337 00:00:00 1

WL Water level, 25% of the vertical dimension

10.97

11.47

RG54

Depth: m

LU Line deviates up 00:00:43

GYF Finish node, gully, reference: RG54 00:00:49 2

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG54X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
72	Upstream	RG54X		



1, 00:00:00, 0.00 m
Start node, gully, reference: 337



2, 00:00:49, 11.47 m
Finish node, gully, reference: RG54
