

Project

Project Name: Mackoy Ltd - Langmead Place Angmering

Project Date: 04/11/2025

Inspection Standard: MSCC5 Sewers & Drainage GB (SRM5 Scoring)





Table of Contents

Project Name	Project Number	Project Date
Mackoy Ltd - Langmead Place Angmering		04/11/2025

Project Information	P-1
Scoring Summary	P-2
Section Item 1: RG55 > MAIN (RG55X)	1
Section Item 2: RG50 > MAIN (RG50X)	3
Section Item 3: RG49 > 340 (RG49X)	5
Section Item 4: RG46 > MAIN (RG46X)	7
Section Item 5: RG44 > MAIN (RG44X)	9
Section Item 6: RG45 > MAIN (RG45X)	11
Section Item 7: RG59 > MAIN (RG59X)	13
Section Item 8: RG60 > MAIN (RG60X)	16
Section Item 9: RG58 > MAIN (RG58X)	18
Section Item 10: RG57 > MAIN (RG57X)	20
Section Item 11: RG56 > MAIN (RG56X)	22
Section Item 12: RG72 > 262 (RG72X)	24
Section Item 13: RG66 > 261 (RG66X)	26
Section Item 14: RG63 > MAIN (RG63X)	28
Section Item 15: RG61 > 264 (RG61X)	30
Section Item 16: RG62 > 264 (RG62X)	32
Section Item 17: RG77 > MAIN (RG77X)	34
Section Item 18: RG78 > MAIN (RG78X)	36
Section Item 19: RG80 > MAIN (RG80X)	38
Section Item 20: RG79 > MAIN (RG79X)	40
Section Item 21: RG73 > MAIN (RG73X)	42
Section Item 22: RG74 > MAIN (RG74X)	44
Section Item 23: RG75 > MAIN (RG75X)	46
Section Item 24: RE373 > 341 (RE373X)	48
Section Item 25: RE363 > 341 (RE363X)	50
Section Item 26: 224 > 225 (224X)	52
Section Item 27: 337 > 338 (337X)	54




Table of Contents

Project Name	Project Number	Project Date
Mackoy Ltd - Langmead Place Angmering		04/11/2025
Section Item 28: 338 > 340 (338X)		56
Section Item 29: 342 > S217 (342X)		58
Section Item 30: 321 > 322 (321X)		60
Section Item 31: 322 > 324 (322X)		62
Section Item 32: 324 > 326 (324X)		64
Section Item 33: 262 > 263 (262X)		66
Section Item 34: 263 > 264 (263X)		68
Section Item 35: 340 > 342 (340X)		70
Section Item 36: 341 > 342 (341X)		72
Section Item 37: 223 > 222 (223X)		74
Section Item 38: 223 > 225 (223X)		76
Section Item 39: 225 > S2706 (225X)		78
Section Item 40: 261 > 262 (261X)		80
Section Item 41: F7 > F8 (F7X)		82
Section Item 42: F22 > F23 (F22X)		84
Section Item 43: F23 > F24 (F23X)		86
Section Item 44: F42 > F43 (F42X)		88
Section Item 45: F43 > F47 (F43X)		90
Section Item 46: F18 > F19 (F18X)		92
Section Item 47: F19 > F20 (F19X)		94
Section Item 48: F20 > F21 (F20X)		96
Section Item 49: F39 > F40 (F39X)		98
Section Item 50: F40 > F41 (F40X)		100
Section Item 51: F41 > F42 (F41X)		102
Section Item 52: 32A > 32B (32AX)		104
Section Item 53: 325 > 326 (325X)		106
Section Item 54: 323 > 323A (323X)		108
Section Item 55: 330 > S215 (330X)		110
Section Item 56: 330 > S215 (330X)		112





Table of Contents		
Project Name	Project Number	Project Date
Mackoy Ltd - Langmead Place Angmering		04/11/2025

Section Item 57: 332B > 330 (332BX)	114
Section Item 58: FW348 > F41 (FW348X)	116
Section Item 59: FW332 > F41 (FW332X)	118
Section Item 60: FW355 > MAIN (FW355X)	120
Section Item 61: RWP > 330 (RWPX)	122
Section Item 62: FW230 > F18 (FW230X)	124
Section Item 63: FW230 > F18 (FW230X)	126
Section Item 64: FW209 > F39 (FW209X)	128
Section Item 65: RG69 > MAIN (RG69X)	130
Section Item 66: RG70 > MAIN (RG70X)	132
Section Item 67: RG68 > 323A (RG68X)	134
Section Item 68: RG53 > 337 (RG53X)	136
Section Item 69: RG52 > 338 (RG52X)	138
Section Item 70: RG51 > 338 (RG51X)	140
Section Item 71: RG65 > 261 (RG65X)	142
Section Item 72: RG54 > 337 (RG54X)	144



Project Information

Project Name	Project Number	Project Date
Mackoy Ltd - Langmead Place Angmering		04/11/2025

Client

Company: Mackoy Ltd
Department: Monks Brook Ind Park
Street: 10 School Close
Town or City: Chandlers Ford
County: Hampshire
Post Code: SO53 4RA




Site


Company: Mackoy Ltd
Street: Langmead Place
Town or City: Angmering
County: West Sussex



Contractor

Company: The Bloggs Ltd
Contact: Chris Blogg
Street: 144 Oak Road
Town or City: Bishops Waltham
County: Hampshire
Post Code: SO32 1EQ
Phone: 
Mobile: 
Email: 





Scoring Summary

Project Name	Project Number	Project Date
Mackoy Ltd - Langmead Place Angmering		04/11/2025

Structural Defects

Item No.	PLR	Grade	Description
All inspected pipes are in an acceptable structural condition (< grade 3).			

Service / Operational Condition


Item No.	PLR	Grade	Description
All inspected pipes are in an acceptable service condition (< grade 3).			

Abandoned Surveys

Item No.	PLR	Description
All inspections complete, none are abandoned.		

Information

These scoring summaries are based on the SRM grading from the WRc.




Section Inspection - 04/11/2025 - RG55X

Item No. 1	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG55X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG55
Road:	Langmead Place	Inspected Length:	8.54 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	8.54 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

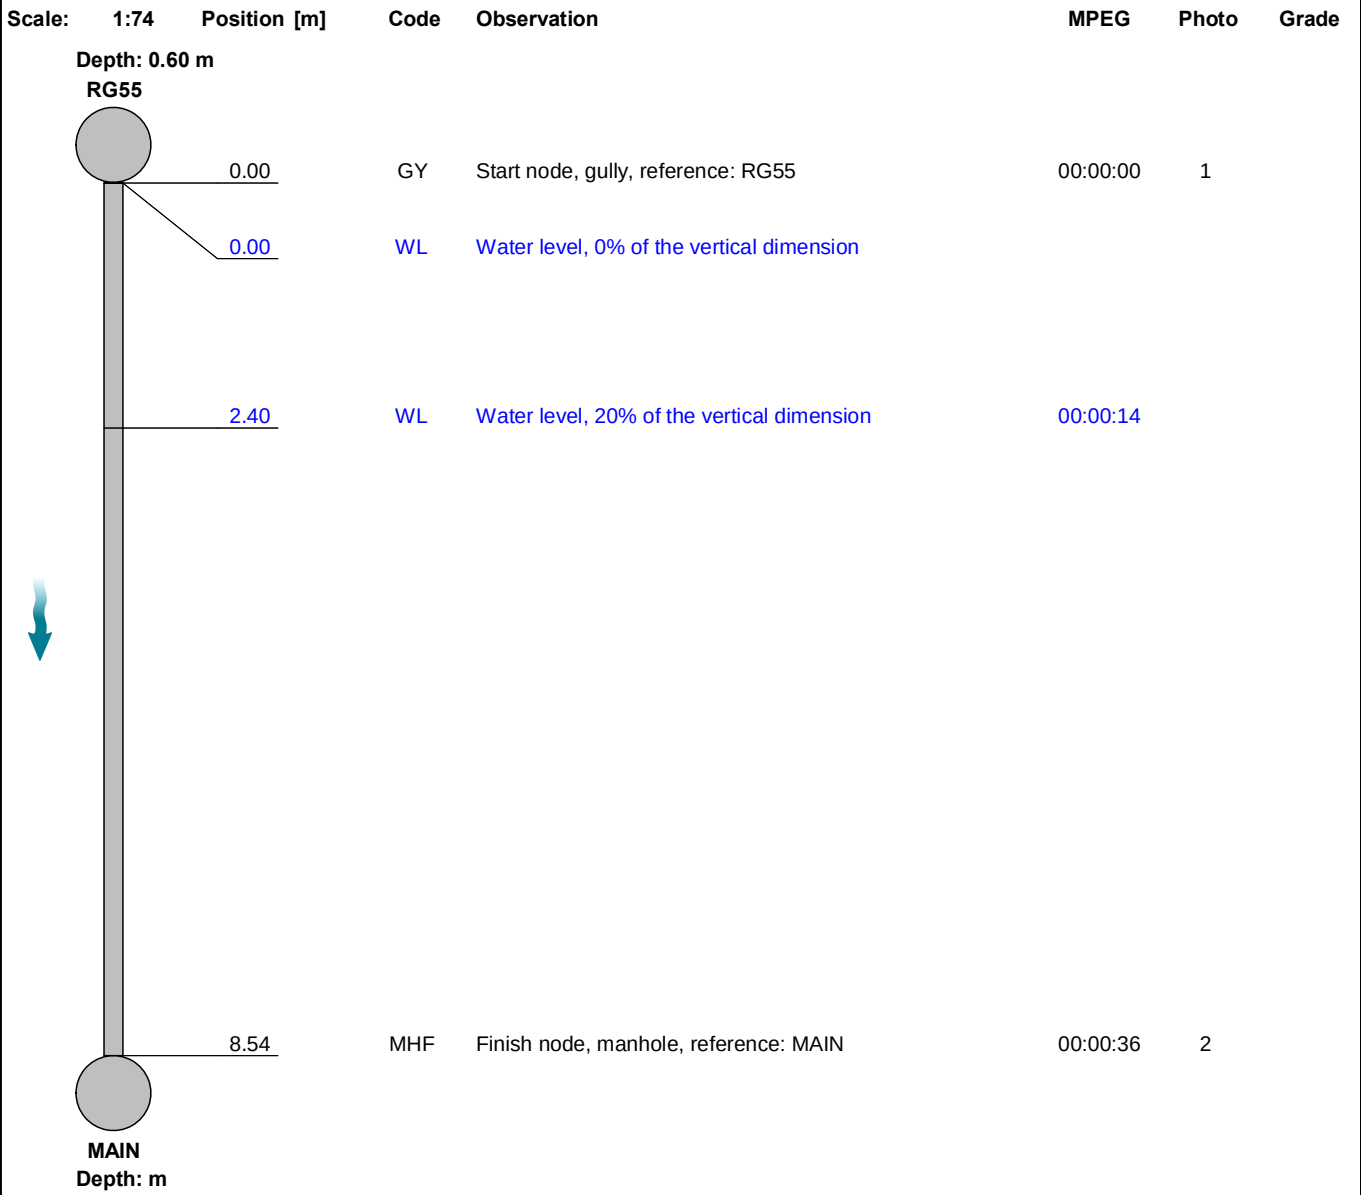


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
2	40.0	4.8	41.0	3.0	1	1.0	0.1	1.0	2.0



Section Pictures - 04/11/2025 - RG55X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
1	Downstream	RG55X		

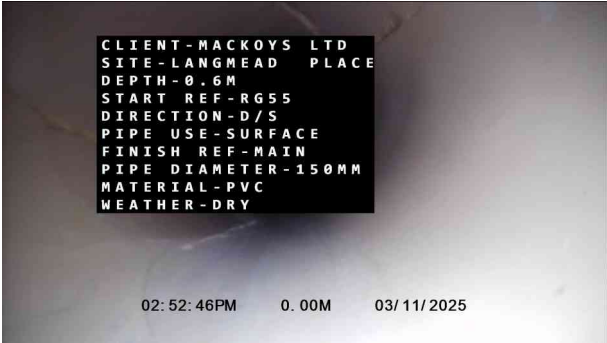

1, 00:00:00, 0.00 m
Start node, gully, reference: RG55



2, 00:00:36, 8.54 m
Finish node, manhole, reference: MAIN



Section Inspection - 04/11/2025 - RG50X

Item No. 2	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG50X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG50
Road:	Langmead Place	Inspected Length:	2.30 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	2.30 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG50	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		1.82	LR	Line deviates right	00:00:33		
		2.30	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:37	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
6	131.0	57.8	133.0	4.0	2	2.0	0.9	2.0	3.0



Section Pictures - 04/11/2025 - RG50X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
2	Downstream	RG50X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG50



2, 00:00:37, 2.30 m
Finish node, major connection without manhole, reference: MAIN



Section Inspection - 04/11/2025 - RG49X

Item No. 3	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG49X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG49
Road:	Langmead Place	Inspected Length:	1.82 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.82 m	Downstream Node:	340
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG49	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:03		
		1.82	MHF	Finish node, manhole, reference: 340	00:00:15	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.5	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG49X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
3	Downstream	RG49X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG49



2, 00:00:15, 1.82 m
Finish node, manhole, reference: 340



Section Inspection - 04/11/2025 - RG46X


Item No. 4	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG46X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG46
Road:	Langmead Place	Inspected Length:	2.40 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	2.40 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation MPEG Photo Grade

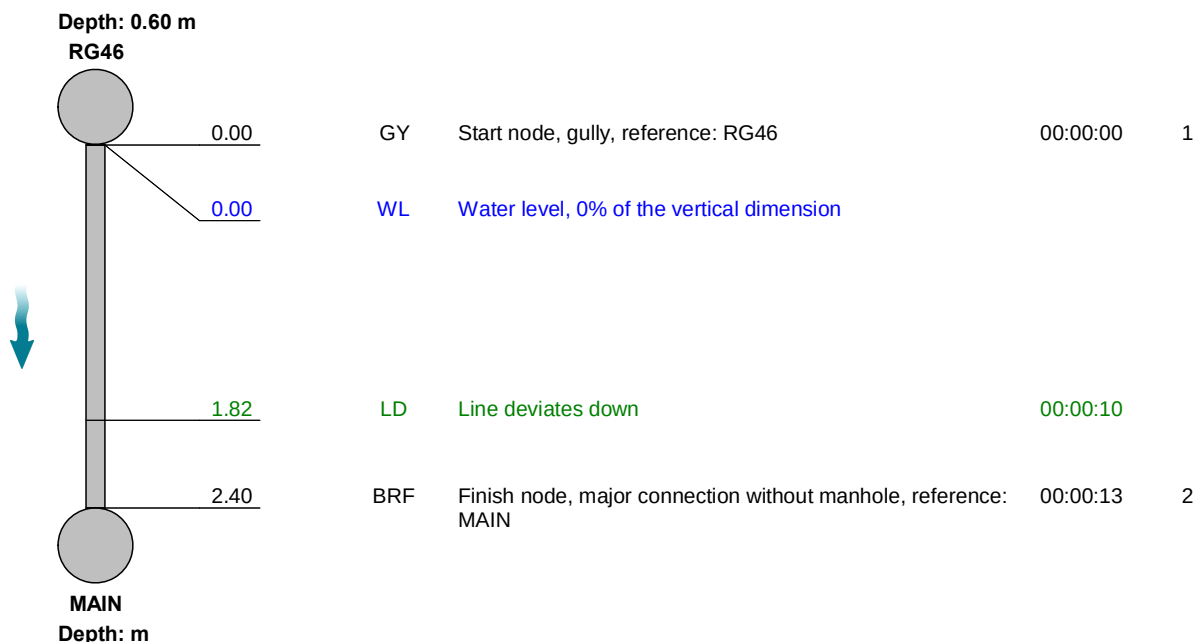


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.4	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG46X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
4	Downstream	RG46X		

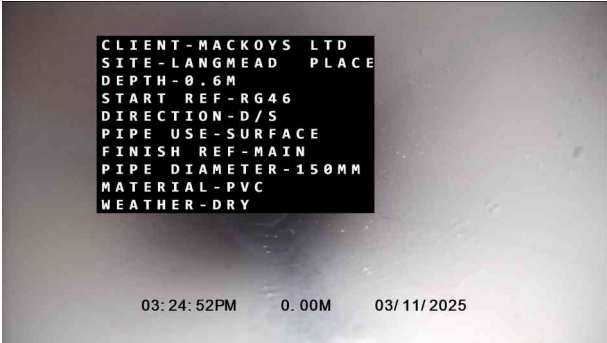

1, 00:00:00, 0.00 m
Start node, gully, reference: RG46



2, 00:00:13, 2.40 m
Finish node, major connection without manhole, reference: MAIN



Item No. 5	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG44X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG44X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
5	Downstream	RG44X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG44



2, 00:00:18, 2.88 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG45X

Item No. 6	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG45X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG45
Road:	Langmead Place	Inspected Length:	4.60 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	4.60 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG45							
0.00	GY			Start node, gully, reference: RG45	00:00:00	1	
0.00	WL			Water level, 0% of the vertical dimension			
0.00	LD			Line deviates down	00:00:07		
3.84	LL			Line deviates left	00:00:19		
4.60	BRF			Finish node, major connection without manhole, reference: MAIN	00:00:22	2	
MAIN Depth: m							

Construction Features

Miscellaneous Features

Structural Defects

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
3	1.0	0.7	3.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG45X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
6	Downstream	RG45X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG45



2, 00:00:22, 4.60 m
Finish node, major connection without manhole, reference:
MAIN




Section Inspection - 04/11/2025 - RG59X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
7	1	04/11/25	10:19	Not Specified	No Rain Or Snow	Yes	RG59X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg				Vivax Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG59
Road:	Langmead Place	Inspected Length:	10.90 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	10.90 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:95	Position [m]	Code	Observation	MPEG	Photo	Grade																																																						
Depth: 0.60 m RG59  <table><tr><td>0.00</td><td>GY</td><td>Start node, gully, reference: RG59</td><td>00:00:00</td><td>1</td></tr><tr><td>0.00</td><td>WL</td><td>Water level, 0% of the vertical dimension</td><td></td><td></td></tr><tr><td>1.53</td><td>S01</td><td>RPL</td><td>Point repair, localised lining from 12 o'clock to 11 o'clock, start</td><td>00:00:18</td><td>2</td></tr><tr><td>3.36</td><td>F01</td><td>RPL</td><td>Point repair, localised lining from 12 o'clock to 11 o'clock, finish</td><td>00:00:21</td><td></td></tr><tr><td>8.45</td><td>S02</td><td>RPL</td><td>Point repair, localised lining from 12 o'clock to 11 o'clock, start</td><td>00:00:29</td><td>3</td></tr><tr><td>9.41</td><td>F02</td><td>RPL</td><td>Point repair, localised lining from 12 o'clock to 11 o'clock, finish</td><td>00:00:32</td><td></td></tr><tr><td>9.41</td><td>WL</td><td>Water level, 30% of the vertical dimension</td><td>00:00:32</td><td></td></tr><tr><td>9.41</td><td>CN</td><td>Connection other than junction at 2 o'clock, 100mm dia</td><td>00:00:32</td><td></td></tr><tr><td>10.60</td><td>RPL</td><td>Point repair, localised lining from 12 o'clock to 11 o'clock</td><td>00:00:35</td><td>4</td></tr><tr><td>10.90</td><td>BRF</td><td>Finish node, major connection without manhole, reference: MAIN</td><td>00:00:39</td><td>5</td></tr></table>								0.00	GY	Start node, gully, reference: RG59	00:00:00	1	0.00	WL	Water level, 0% of the vertical dimension			1.53	S01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:18	2	3.36	F01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:21		8.45	S02	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:29	3	9.41	F02	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:32		9.41	WL	Water level, 30% of the vertical dimension	00:00:32		9.41	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:32		10.60	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock	00:00:35	4	10.90	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:39	5
0.00	GY	Start node, gully, reference: RG59	00:00:00	1																																																									
0.00	WL	Water level, 0% of the vertical dimension																																																											
1.53	S01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:18	2																																																								
3.36	F01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:21																																																									
8.45	S02	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:29	3																																																								
9.41	F02	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:32																																																									
9.41	WL	Water level, 30% of the vertical dimension	00:00:32																																																										
9.41	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:32																																																										
10.60	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock	00:00:35	4																																																									
10.90	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:39	5																																																									

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG59X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
7	Downstream	RG59X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG59



2, 00:00:18, 1.53 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:00:29, 8.45 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



4, 00:00:35, 10.60 m
Point repair, localised lining from 12 o'clock to 11 o'clock



Section Pictures - 04/11/2025 - RG59X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
7	Downstream	RG59X		



5, 00:00:39, 10.90 m
Finish node, major connection without manhole, reference:
MAIN



Item No. 8	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG60X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 04/11/2025 - RG60X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
8	Downstream	RG60X		




1, 00:00:00, 0.00 m
Start node, gully, reference: RG60

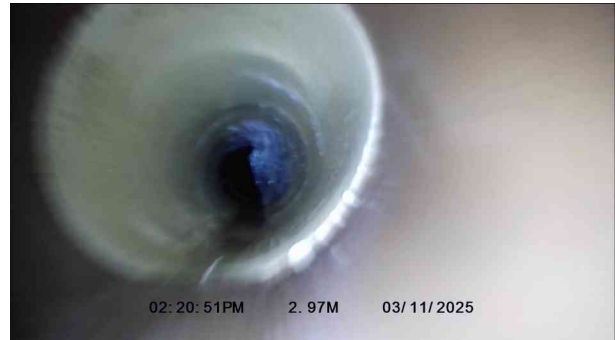

2, 00:00:11, 2.97 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:00:23, 10.11 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG58X

Item No. 9	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG58X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG58
Road:	Langmead Place	Inspected Length:	2.78 m	Upstream Pipe Depth:	0.630 m
Location:	Road	Total Length:	2.78 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.63 m RG58							
	0.00	GY	Start node, gully, reference: RG58		00:00:00	1	
	0.00	WL	Water level, 0% of the vertical dimension				
	0.00	LD	Line deviates down		00:00:09		
	1.44	WL	Water level, 20% of the vertical dimension		00:00:13		
	2.78	BRF	Finish node, major connection without manhole, reference: MAIN		00:00:18	2	
MAIN Depth: m							


Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.4	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG58X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
9	Downstream	RG58X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG58



2, 00:00:18, 2.78 m
Finish node, major connection without manhole, reference:
MAIN



Item No. 10	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG57X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Scale: 1:50 Position [m] Code Observation MPEG Photo Grade

Depth: 0.60 m
RG57

0.00

0.00

0.00

GY Start node, gully, reference: RG57 00:00:00 1

WL Water level, 0% of the vertical dimension

LD Line deviates down 00:00:07

3.07

LL Line deviates left 00:00:15

3.64

BRF Finish node, major connection without manhole, reference: MAIN 00:00:18 2


MAIN
Depth: m

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
2	1.0	0.5	2.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG57X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
10	Downstream	RG57X		

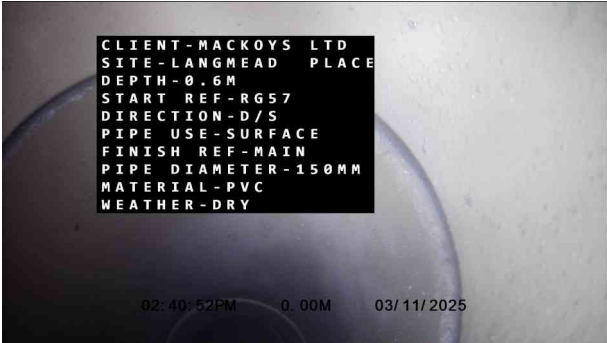

1, 00:00:00, 0.00 m
Start node, gully, reference: RG57



2, 00:00:18, 3.64 m
Finish node, major connection without manhole, reference:
MAIN



Item No. 11	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG56X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
4	206.0	68.1	451.0	5.0	1	1.0	0.2	1.0	2.0



Section Pictures - 04/11/2025 - RG56X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
11	Downstream	RG56X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG56



2, 00:00:52, 6.62 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG72X

Item No. 12	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG72X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG72
Road:	Langmead Place	Inspected Length:	8.85 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	8.85 m	Downstream Node:	262
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:77	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG72							
		0.00	GY	Start node, gully, reference: RG72	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		7.77	WL	Water level, 20% of the vertical dimension	00:00:30		
		8.85	MHF	Finish node, manhole, reference: 262	00:00:34	2	
262 Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG72X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
12	Downstream	RG72X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG72



2, 00:00:34, 8.85 m
Finish node, manhole, reference: 262



Section Inspection - 04/11/2025 - RG66X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
13	1	04/11/25	10:19	Not Specified	No Rain Or Snow	Yes	RG66X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg				Vivax Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG66
Road:	Langmead Place	Inspected Length:	8.73 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	8.73 m	Downstream Node:	261
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:76	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG66							
		0.00	GY	Start node, gully, reference: RG66	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:07		
		0.76	S01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:15	2
		2.30	F01	RPL	Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:19	
		7.20	WL	Water level, 20% of the vertical dimension	00:00:29		
		8.73	MHF	Finish node, manhole, reference: 261	00:00:42	3	
261 Depth: m							

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG66X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
13	Downstream	RG66X		




1, 00:00:00, 0.00 m
Start node, gully, reference: RG66



2, 00:00:15, 0.76 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:00:42, 8.73 m
Finish node, manhole, reference: 261




Section Inspection - 04/11/2025 - RG63X

Item No. 14	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG63X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG63
Road:	Langmead Place	Inspected Length:	4.03 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	4.03 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

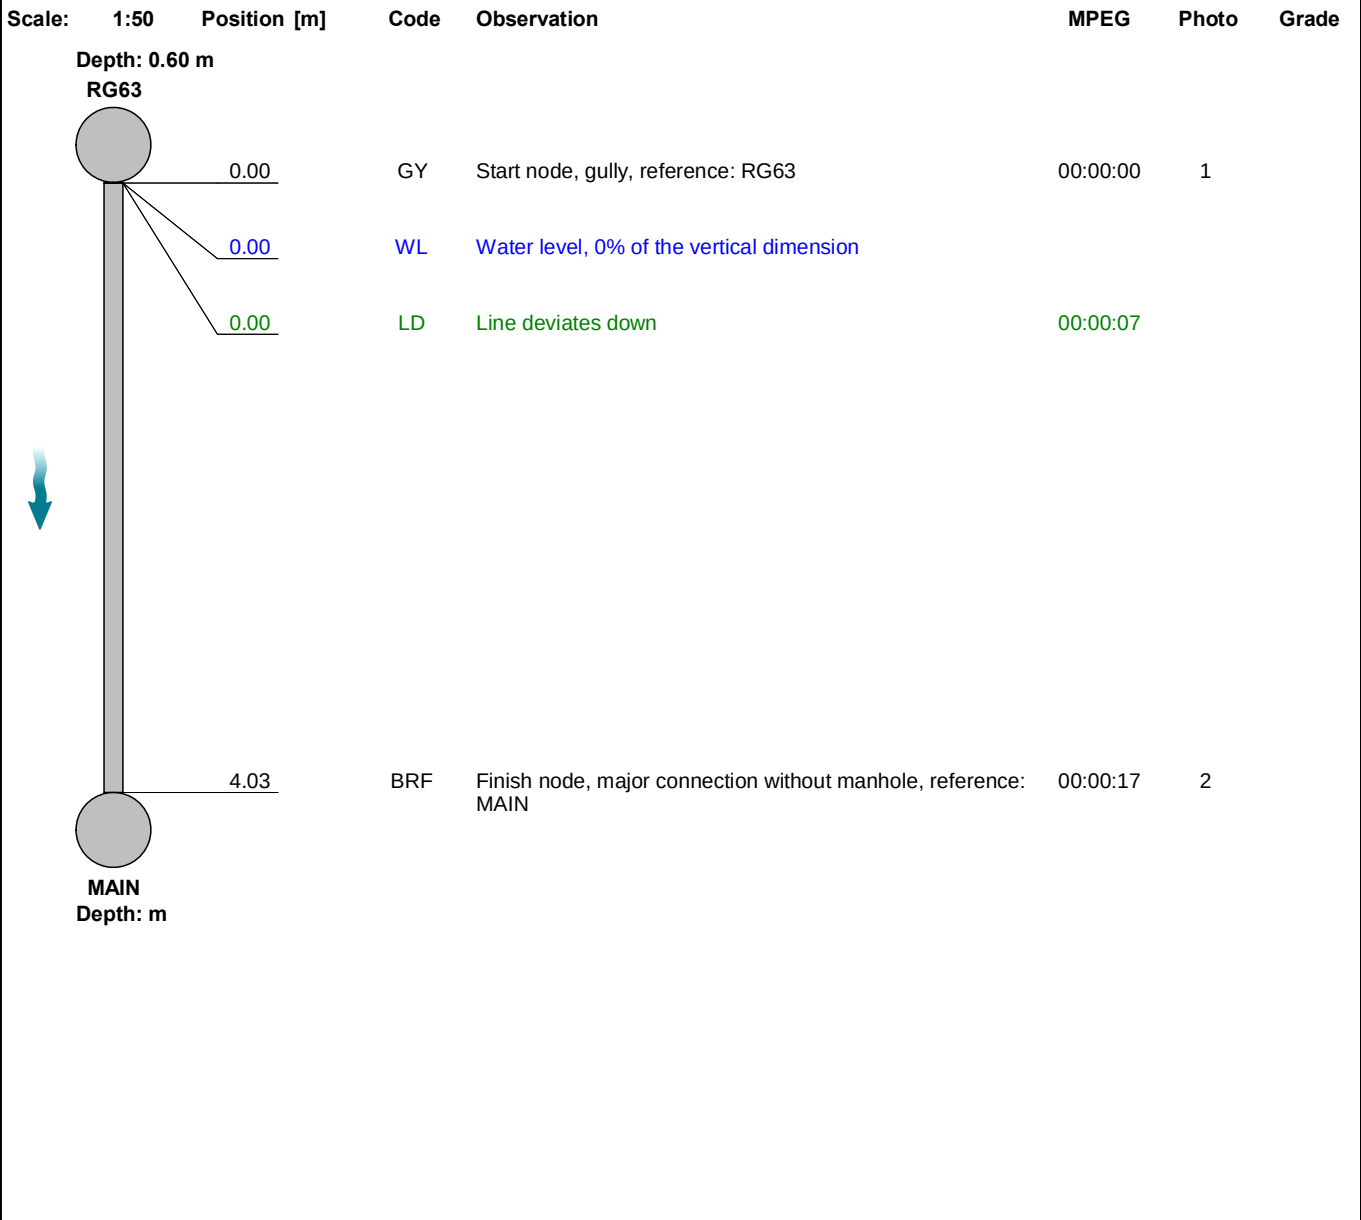

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.2	1.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 04/11/2025 - RG63X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
14	Downstream	RG63X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG63

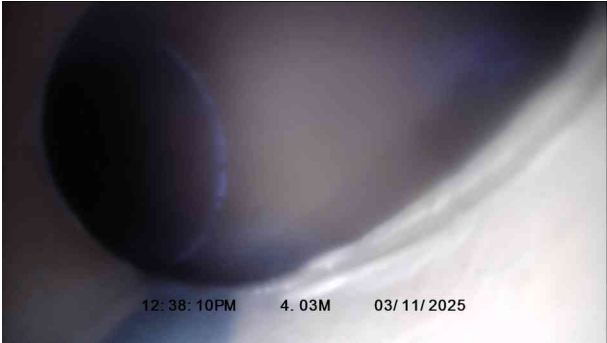

2, 00:00:17, 4.03 m
Finish node, major connection without manhole, reference: MAIN




Section Inspection - 04/11/2025 - RG61X


Item No. 15	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG61X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG61
Road:	Langmead Place	Inspected Length:	1.72 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.72 m	Downstream Node:	264
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

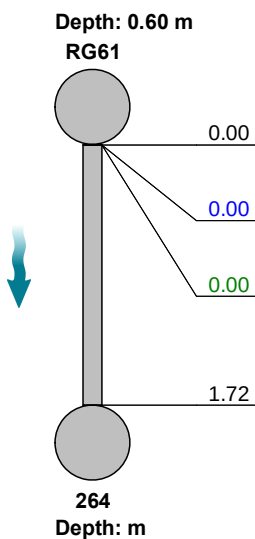Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
							
		0.00	GY	Start node, gully, reference: RG61	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:07		
		1.72	BRF	Finish node, major connection without manhole, reference: 264	00:00:35	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG61X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
15	Downstream	RG61X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG61



2, 00:00:35, 1.72 m
Finish node, major connection without manhole, reference:
264



Section Inspection - 04/11/2025 - RG62X

Item No. 16	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG62X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG62
Road:	Langmead Place	Inspected Length:	1.72 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.72 m	Downstream Node:	264
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:


Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG62	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.09	LD	Line deviates down	00:00:07		
		1.24	LD	Line deviates down	00:00:13		
		1.72	WL	Water level, 30% of the vertical dimension	00:00:15		
		1.72	BRF	Finish node, major connection without manhole, reference: 264	00:00:21	2	
Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.6	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG62X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
16	Downstream	RG62X		

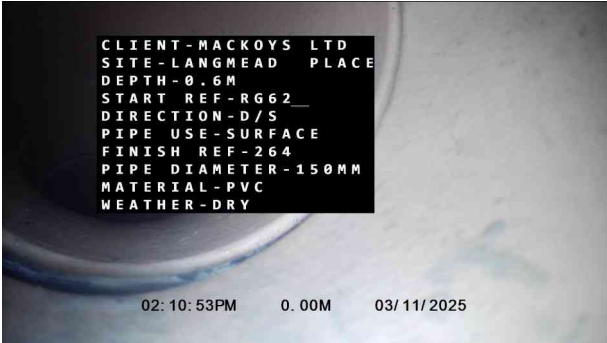

1, 00:00:00, 0.00 m
Start node, gully, reference: RG62



2, 00:00:21, 1.72 m
Finish node, major connection without manhole, reference:
264



Item No. 17	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG77X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG77
Road:	Langmead Place	Inspected Length:	4.03 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	4.03 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water		Pipe Shape:	Circular	
Type of Pipe:	Gravity drain/sewer		Dia/Height:	150 mm	
Flow Control:	No flow control		Material:	Polyvinyl chloride	
Year Constructed:	Not Specified		Lining Type:	No Lining	
Inspection Purpose:	Routine inspection		Lining Material:	No Lining	

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation MPEG Photo Grade

Code	Observation	MPEG	Photo	Grade
GY	Start node, gully, reference: RG77	00:00:00	1	
WL	Water level, 0% of the vertical dimension			
LD	Line deviates down	00:00:07		
LD	Line deviates down	00:00:11		
LR	Line deviates right	00:00:15		
LD	Line deviates down	00:00:19		
BRF	Finish node, major connection without manhole, reference: MAIN	00:00:21	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
2	1.0	0.5	2.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG77X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
17	Downstream	RG77X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG77



2, 00:00:21, 4.03 m
Finish node, major connection without manhole, reference:
MAIN

Section Inspection - 04/11/2025 - RG78X

Item No. 18	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG78X
Operator C. Bloor		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG78
Road:	Langmead Place	Inspected Length:	1.35 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.35 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
			GY	Start node, gully, reference: RG78	00:00:00	1	
			WL	Water level, 0% of the vertical dimension			
			LD	Line deviates down	00:00:06		
			BRF	Finish node, major connection without manhole, reference: MAIN	00:00:12	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.7	1.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 04/11/2025 - RG78X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
18	Downstream	RG78X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG78

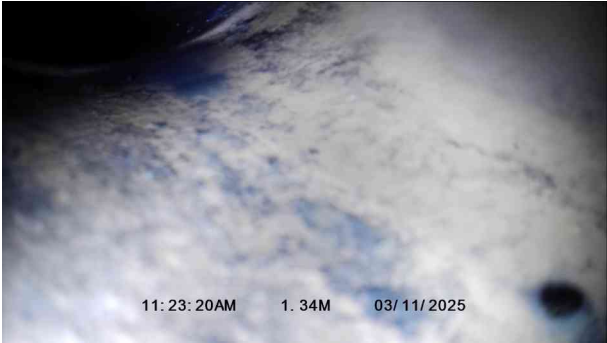

2, 00:00:12, 1.35 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG80X

Item No. 19	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG80X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG80
Road:	Langmead Place	Inspected Length:	1.53 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.53 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG80	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:06		
		1.44	JN	Junction at 2 o'clock, 150mm dia	00:00:19		
		1.53	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:31	2	

Construction Features

Miscellaneous Features

Structural Defects

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG80X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
19	Downstream	RG80X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG80



2, 00:00:31, 1.53 m
Finish node, major connection without manhole, reference: MAIN



Section Inspection - 04/11/2025 - RG79X

Item No. 20	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG79X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG79
Road:	Langmead Place	Inspected Length:	1.15 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.15 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:


Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG79	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:06		
		1.15	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:21	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.9	1.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 04/11/2025 - RG79X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
20	Downstream	RG79X		

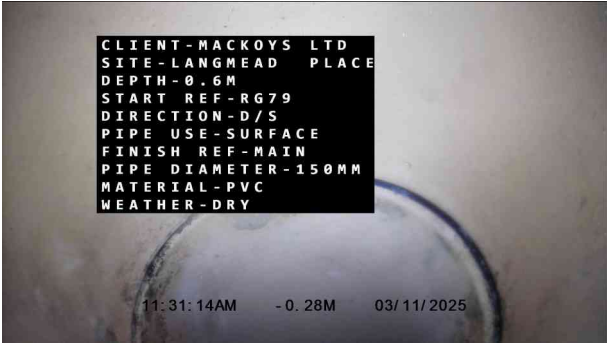

1, 00:00:00, 0.00 m
Start node, gully, reference: RG79

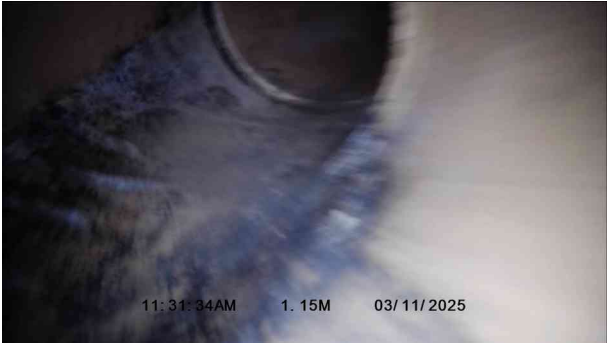

2, 00:00:21, 1.15 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG73X

Item No. 21	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG73X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG73
Road:	Langmead Place	Inspected Length:	7.20 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	7.20 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:63	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG73							
	0.00	GY		Start node, gully, reference: RG73	00:00:00	1	
	0.00	WL		Water level, 0% of the vertical dimension			
	6.81	WL		Water level, 20% of the vertical dimension	00:00:25		
	7.20	MHF		Finish node, manhole, reference: MAIN	00:00:29	2	
MAIN Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.1	1.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG73X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
21	Downstream	RG73X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG73



2, 00:00:29, 7.20 m
Finish node, manhole, reference: MAIN



Section Inspection - 04/11/2025 - RG74X

Item No. 22	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG74X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG74
Road:	Langmead Place	Inspected Length:	0.67 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	0.67 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	GY	Start node, gully, reference: RG74	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:12		
		0.38	LL	Line deviates left	00:00:13		
		0.67	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:14	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 04/11/2025 - RG74X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
22	Downstream	RG74X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG74



2, 00:00:14, 0.67 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 04/11/2025 - RG75X

Item No. 23	Insp. No. 1	Date 04/11/25	Time 10:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG75X
Operator C.Blogg		Vehicle [REDACTED]		Camera Vivax Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG75
Road:	Langmead Place	Inspected Length:	1.30 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	1.30 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	

Use:	Surface water	Pipe Shape:	Circular
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm
Flow Control:	No flow control	Material:	Polyvinyl chloride
Year Constructed:	Not Specified	Lining Type:	No Lining
Inspection Purpose:	Routine inspection	Lining Material:	No Lining

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG75		0.00	GY	Start node, gully, reference: RG75	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.00	LD	Line deviates down	00:00:05		
		1.30	BRF	Finish node, major connection without manhole, reference: MAIN			
MAIN Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 04/11/2025 - RG75X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
23	Downstream	RG75X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG75



Section Inspection - 06/11/2025 - RE373X

Item No. 24	Insp. No. 1	Date 06/11/25	Time 13:50	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RE373X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Upstream	Upstream Node:	RE373
Road:	Langmead Place	Inspected Length:	9.20 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	9.20 m	Downstream Node:	341
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.000 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:80	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.00 m	341						
0.00		MH		Start node, manhole, reference: 341	00:00:00	1	
0.00		WL		Water level, 0% of the vertical dimension			
0.00	S01	RPL		Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:07	2	
0.86	F01	RPL		Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:14		
0.86		WL		Water level, 20% of the vertical dimension	00:00:14		
6.14		CN		Connection other than junction at 10 o'clock, 100mm dia	00:00:27		
7.01		JN		Junction at 10 o'clock, 150mm dia	00:00:29		
7.21		SC		Pipe size changes, new size(s), 100mm high	00:00:30	3	
8.40		LU		Line deviates up	00:00:39		
9.20		REF		Finish node, rodding eye, reference: RE373	00:00:55	4	
RE373							
Depth: m							

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - RE373X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
24	Upstream	RE373X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 341




2, 00:00:07, 0.00 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:00:30, 7.21 m
Pipe size changes, new size(s), 100mm high



4, 00:00:55, 9.20 m
Finish node, rodding eye, reference: RE373



Section Inspection - 06/11/2025 - RE363X

Item No. 25	Insp. No. 1	Date 06/11/25	Time 13:50	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RE363X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RE363
Road:	Langmead Place	Inspected Length:	7.19 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	7.19 m	Downstream Node:	341
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.000 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:63	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.00 m 341							
0.00	MH			Start node, manhole, reference: 341	00:00:00	1	
0.00	WL			Water level, 20% of the vertical dimension			
0.00	S01	RPL		Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:08	2	
0.19	S02	CUW		Loss of vision, camera under water, start	00:00:10		
0.32	F01	RPL		Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:45		
6.10	F02	CUW		Loss of vision, camera under water, finish	00:00:45		
6.49	LU			Line deviates up	00:00:48		
7.19	REF			Finish node, rodding eye, reference: RE363	00:00:51	3	
RE363 Depth: m							

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - RE363X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
25	Upstream	RE363X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 341



2, 00:00:08, 0.00 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start

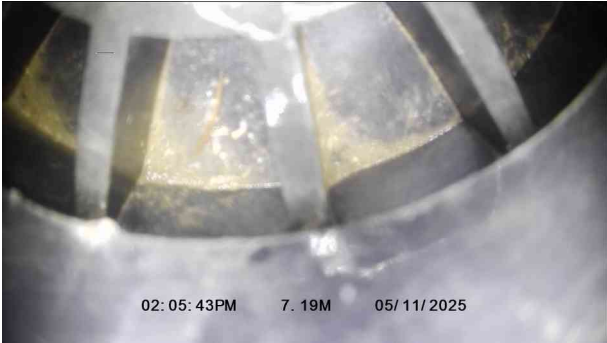

3, 00:00:51, 7.19 m
Finish node, rodding eye, reference: RE363



Item No. 26	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 224X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Scale:	1:108	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.10 m 224 MH Start node, manhole, reference: 224 00:00:00 1 WL Water level, 0% of the vertical dimension LD Line deviates down 00:01:57 MHF Finish node, manhole, reference: 225 00:02:01 225 Depth: m							


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	1.0	0.1	1.0	1.0	1	5.0	0.4	5.0	4.0



Section Pictures - 06/11/2025 - 224X				
Item No. 26	Inspection Direction Downstream	PLR 224X	Client's Job Ref	Contractor's Job Ref



1, 00:00:00, 0.00 m
Start node, manhole, reference: 224




Section Inspection - 06/11/2025 - 337X

Item No. 27	Insp. No. 1	Date 06/11/25	Time 13:50	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 337X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	337
Road:	Langmead Place	Inspected Length:	10.44 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	10.44 m	Downstream Node:	338
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.400 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

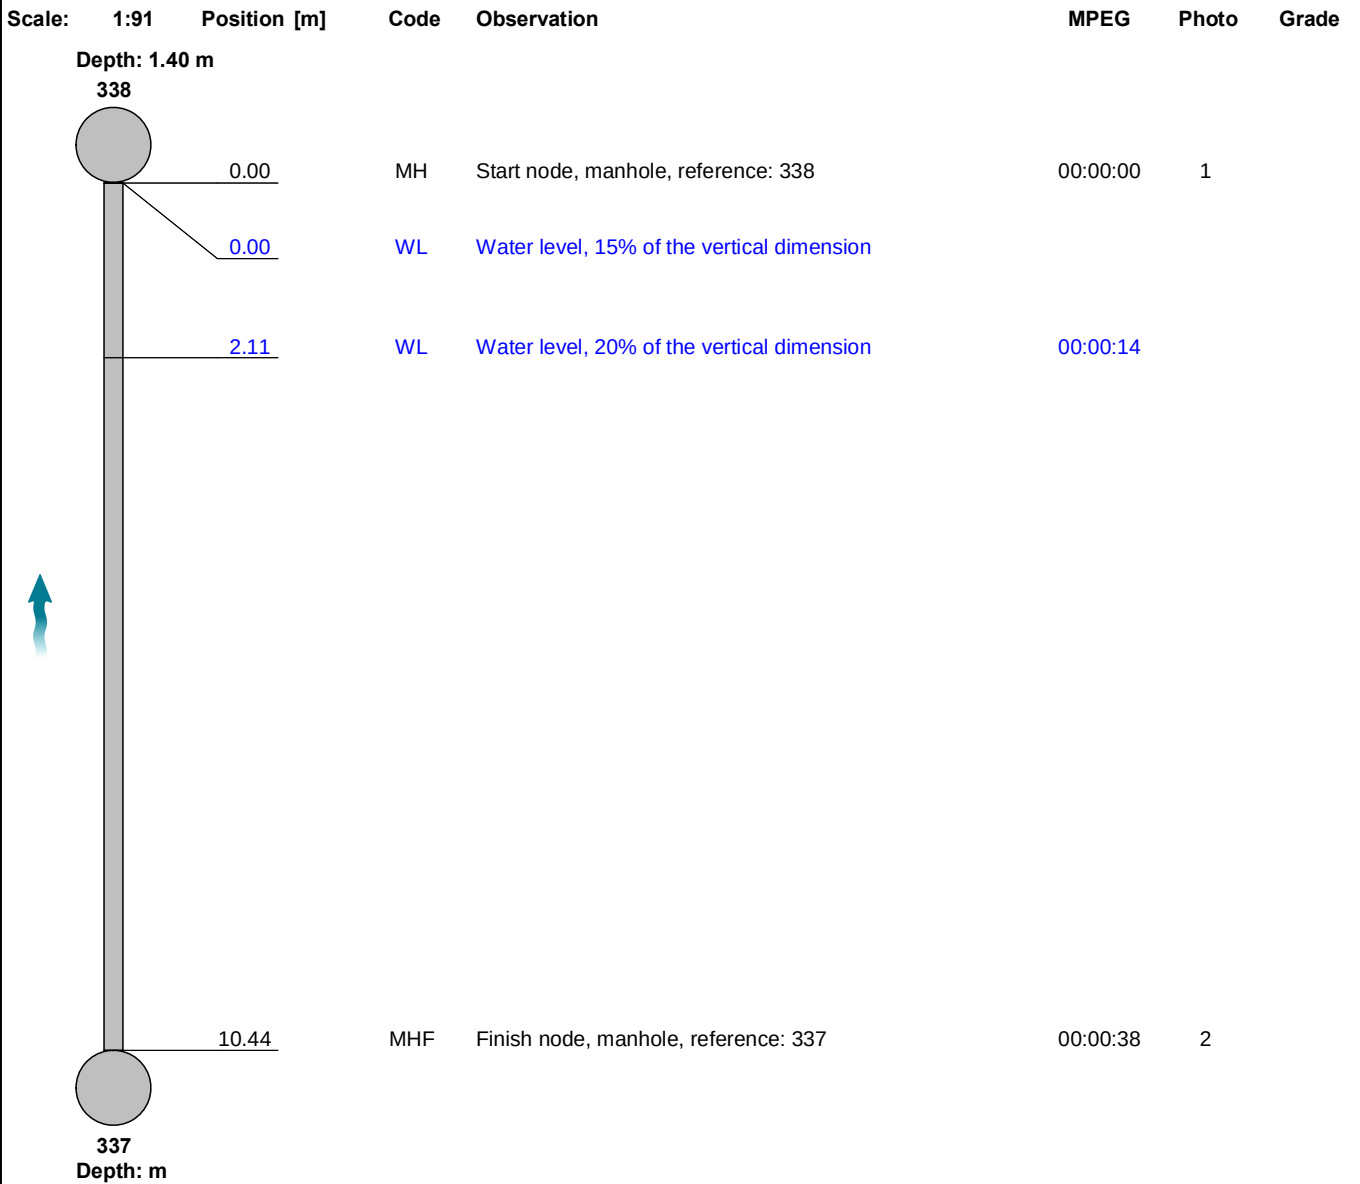

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 337X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
27	Upstream	337X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 338



2, 00:00:38, 10.44 m
Finish node, manhole, reference: 337




Section Inspection - 06/11/2025 - 338X

Item No. 28	Insp. No. 1	Date 06/11/25	Time 13:50	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 338X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	338
Road:	Langmead Place	Inspected Length:	17.60 m	Upstream Pipe Depth:	1.400 m
Location:	Road	Total Length:	17.60 m	Downstream Node:	340
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

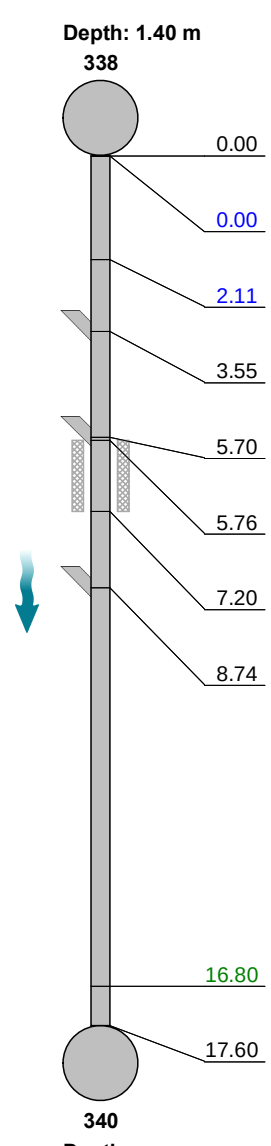
Scale:	1:153	Position [m]	Code	Observation	MPEG	Photo	Grade
							
		0.00	MH	Start node, manhole, reference: 338	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		2.11	WL	Water level, 15% of the vertical dimension	00:00:11		
		3.55	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:14		
		5.70	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:19		
		5.76	S01	RPL Point repair, localised lining from 12 o'clock to 11 o'clock, start	00:00:19	2	
		7.20	F01	RPL Point repair, localised lining from 12 o'clock to 11 o'clock, finish	00:00:22		
		8.74	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:27		
		16.80	LR	Line deviates right	00:00:57		
		17.60	MHF	Finish node, manhole, reference: 340	00:01:01	3	
Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
2	1.0	0.1	2.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 338X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
28	Downstream	338X		

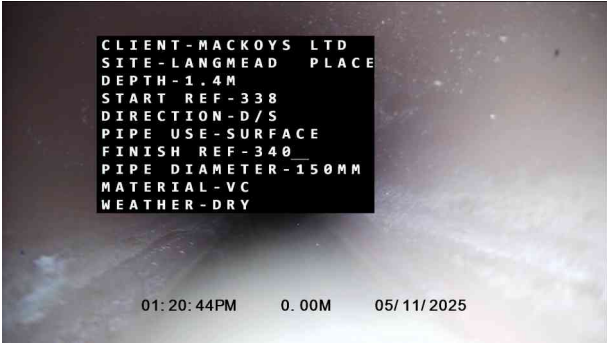


1, 00:00:00, 0.00 m
Start node, manhole, reference: 338



2, 00:00:19, 5.76 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:01:01, 17.60 m
Finish node, manhole, reference: 340



Section Inspection - 06/11/2025 - 342X

Item No. 29	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 342X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	342
Road:	Langmead Place	Inspected Length:	33.39 m	Upstream Pipe Depth:	1.900 m
Location:	Road	Total Length:	33.39 m	Downstream Node:	S217
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	300 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:290	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 342	00:00:00		
		0.00	WL	Water level, 0% of the vertical dimension			
		2.28	CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:23		
		18.71	CN	Connection other than junction at 2 o'clock, 150mm dia	00:01:51		
		30.57	CN	Connection other than junction at 10 o'clock, 150mm dia	00:03:01		
		31.10	CN	Connection other than junction at 2 o'clock, 150mm dia	00:03:04		
		31.12	WL	Water level, 20% of the vertical dimension	00:03:08		
		33.39	MHF	Finish node, manhole, reference: S217	00:03:39	1	


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	1	5.0	0.1	5.0	4.0



Section Pictures - 06/11/2025 - 342X				
Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
29	Downstream	342X		



1, 00:03:39, 33.39 m
Finish node, manhole, reference: S217



Section Inspection - 06/11/2025 - 321X

Item No. 30	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 321X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	321
Road:	Langmead Place	Inspected Length:	8.27 m	Upstream Pipe Depth:	1.600 m
Location:	Road	Total Length:	8.27 m	Downstream Node:	322
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:72	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.60 m 321 0.00 0.00 4.42 8.27 322 Depth: m							
		0.00	MH	Start node, manhole, reference: 321	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		4.42	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:38		
		8.27	MHF	Finish node, manhole, reference: 322	00:00:59	2	

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 06/11/2025 - 321X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
30	Downstream	321X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 321

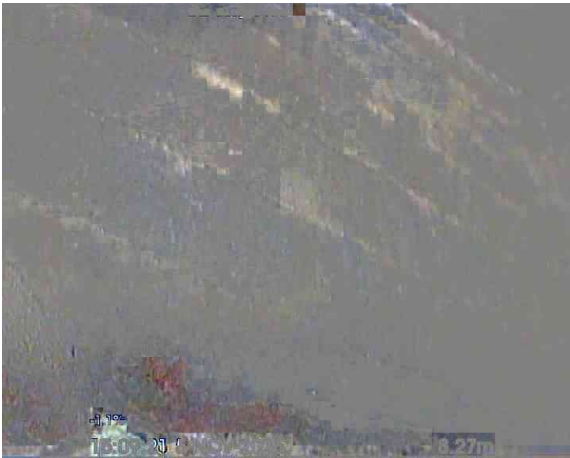

2, 00:00:59, 8.27 m
Finish node, manhole, reference: 322



Item No. 31	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 322X
Operator C. Bloor		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 06/11/2025 - 322X				
Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
31	Downstream	322X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 322



2, 00:02:13, 28.19 m
Finish node, manhole, reference: 324



Section Inspection - 06/11/2025 - 324X

Item No. 32	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 324X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	324
Road:	Langmead Place	Inspected Length:	45.97 m	Upstream Pipe Depth:	1.800 m
Location:	Road	Total Length:	45.97 m	Downstream Node:	326
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	300 mm		
Flow Control:	No flow control	Material:	Concrete		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:399	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 324	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		4.97	CN	Connection other than junction at 2 o'clock, 150mm dia	00:00:41		
		15.88	CN	Connection other than junction at 2 o'clock, 150mm dia	00:01:52		
		19.27	CN	Connection other than junction at 2 o'clock, 150mm dia	00:02:12		
		27.47	CN	Connection other than junction at 2 o'clock, 150mm dia	00:03:08		
		38.32	CN	Connection other than junction at 2 o'clock, 150mm dia	00:04:22		
		39.07	CN	Connection other than junction at 2 o'clock, 150mm dia	00:04:27		
		45.97	MHF	Finish node, manhole, reference: 326	00:05:30	2	


Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 324X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
32	Downstream	324X		

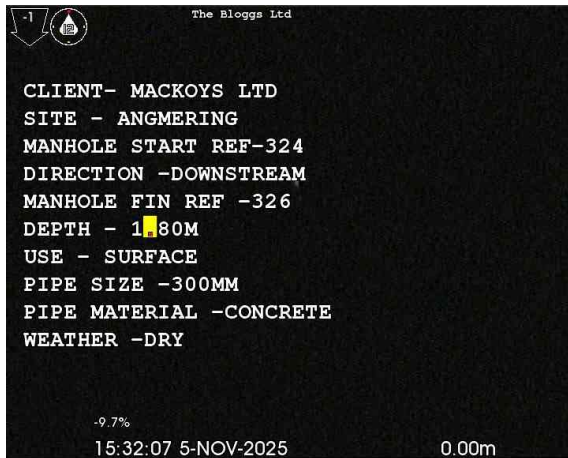

1, 00:00:00, 0.00 m
Start node, manhole, reference: 324



2, 00:05:30, 45.97 m
Finish node, manhole, reference: 326



Item No. 33	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 262X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Scale: 1:97 Position [m] Code Observation MPEG Photo Grade


Code	Observation	MPEG	Photo	Grade
MH	Start node, manhole, reference: 262	00:00:00	1	
WL	Water level, 0% of the vertical dimension			
MHF	Finish node, manhole, reference: 263	00:01:29	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 262X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
33	Downstream	262X		

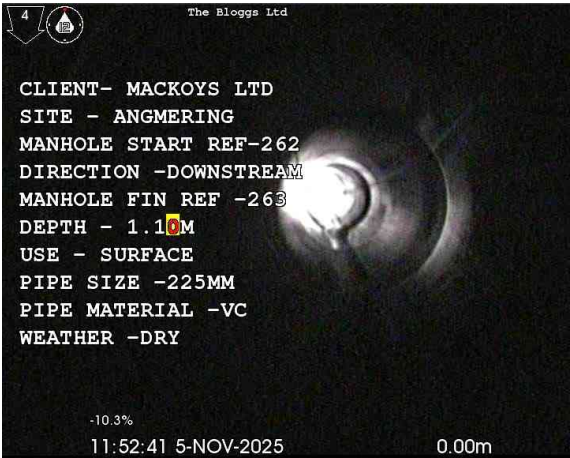

1, 00:00:00, 0.00 m
Start node, manhole, reference: 262




2, 00:01:29, 11.09 m
Finish node, manhole, reference: 263



Item No. 34	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 263X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified


Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 263X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
34	Downstream	263X		

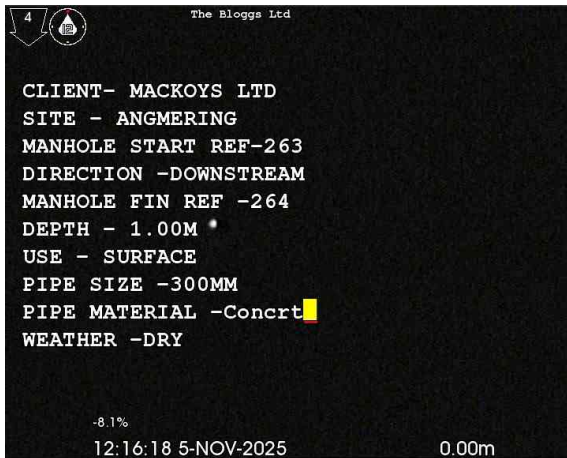

1, 00:00:00, 0.00 m
Start node, manhole, reference: 263



2, 00:06:21, 57.18 m
Finish node, manhole, reference: 264




Section Inspection - 06/11/2025 - 340X

Item No. 35	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 340X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified


Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	340
Road:	Langmead Place	Inspected Length:	13.90 m	Upstream Pipe Depth:	1.700 m
Location:	Road	Total Length:	13.90 m	Downstream Node:	342
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

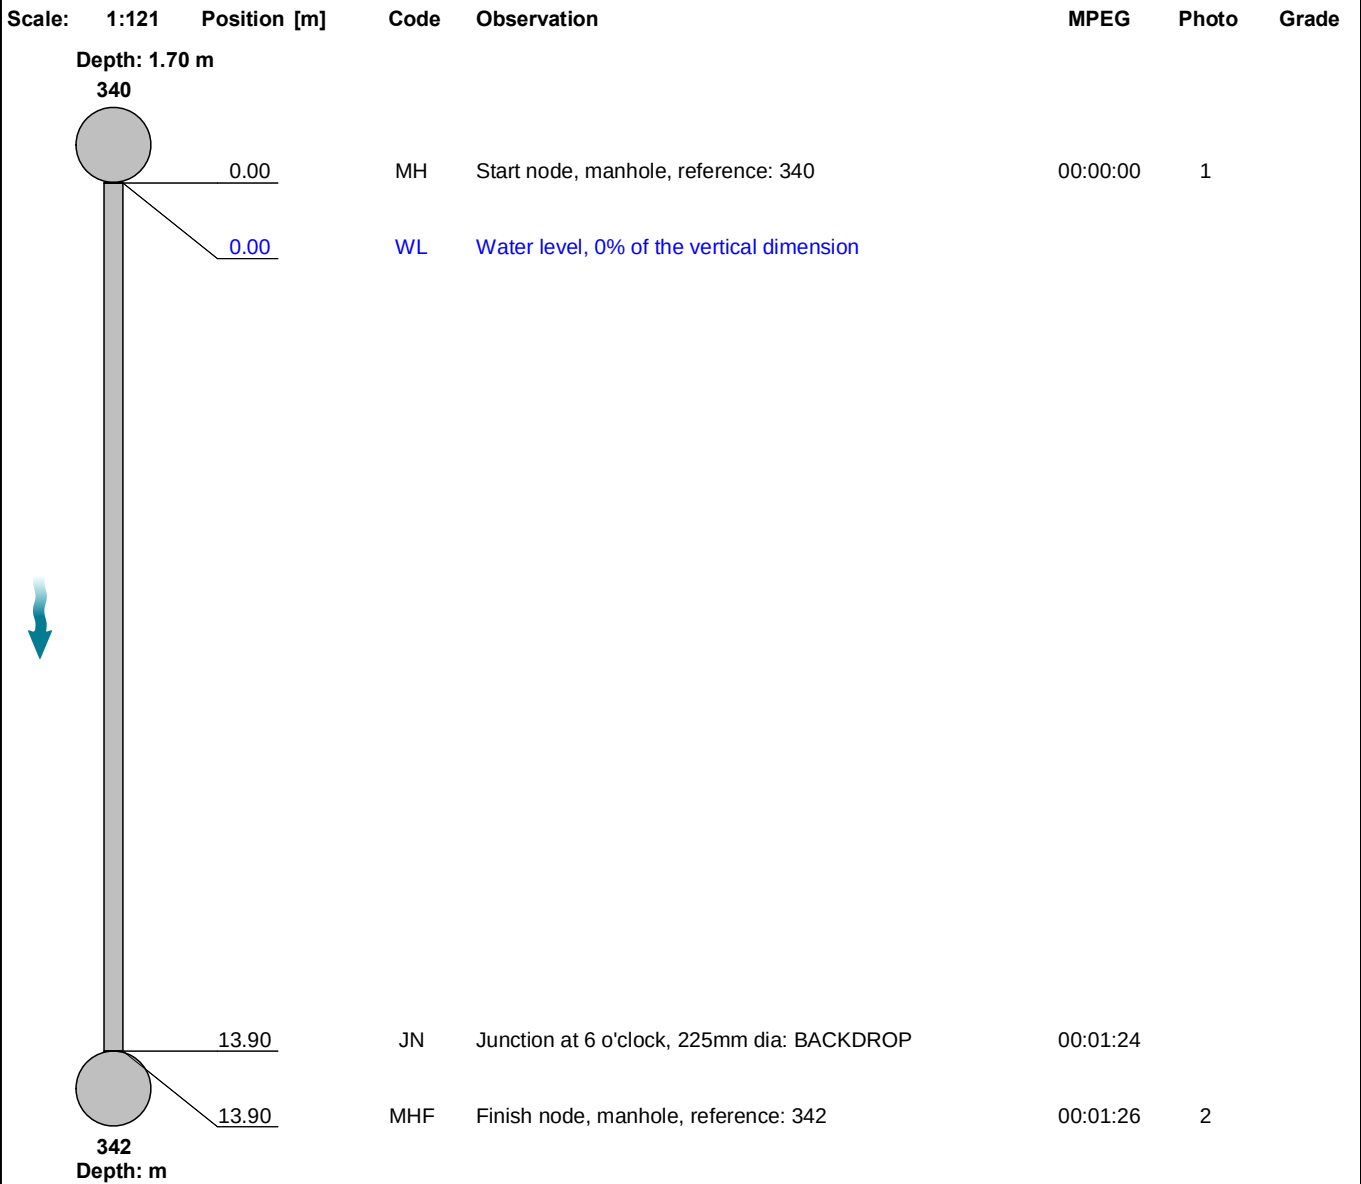


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 340X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
35	Downstream	340X		

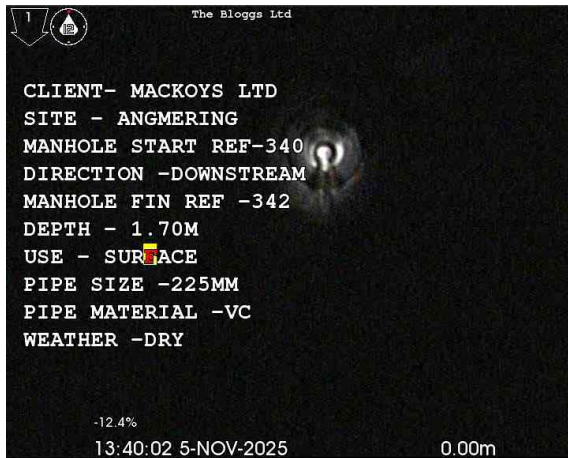

1, 00:00:00, 0.00 m
Start node, manhole, reference: 340



2, 00:01:26, 13.90 m
Finish node, manhole, reference: 342



Section Inspection - 06/11/2025 - 341X

Item No. 36	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 341X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	341
Road:	Langmead Place	Inspected Length:	24.61 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	24.67 m	Downstream Node:	342
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.800 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:214	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 342	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		4.61	CN	Connection other than junction at 10 o'clock, 150mm dia	00:00:43		
		5.41	WL	Water level, 15% of the vertical dimension	00:00:48		
		15.34	CN	Connection other than junction at 10 o'clock, 150mm dia	00:01:53		
		16.09	CN	Connection other than junction at 2 o'clock, 150mm dia	00:01:57		
		24.61	MHF	Finish node, manhole, reference: 341	00:03:17	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	1	0.0	0.2	5.0	1.0



Section Pictures - 06/11/2025 - 341X				
Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
36	Upstream	341X		

12

The Bloggs Ltd

CLIENT- MACKOYS LTD

SITE - ANGMERING

MANHOLE START REF-342

DIRECTION -UPSTREAM

MANHOLE FIN REF -341

DEPTH - 1.80M

USE - SURFACE

PIPE SIZE -225MM

PIPE MATERIAL -VC

WEATHER -DRY

-21.6%

13:51:21 5-NOV-2025

0.00m

1, 00:00:00, 0.00 m
Start node, manhole, reference: 342

77


The Bloggs Ltd

1.1%

13:54:38 5-NOV-2025

24.61m

2, 00:03:17, 24.61 m
Finish node, manhole, reference: 341



Section Inspection - 06/11/2025 - 223X

Item No. 37	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 223X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	223
Road:	Langmead Place	Inspected Length:	46.87 m	Upstream Pipe Depth:	1.300 m
Location:	Road	Total Length:	46.87 m	Downstream Node:	222
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	450 mm		
Flow Control:	No flow control	Material:	Concrete		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale: 1:406	Position [m]	Code	Observation	MPEG	Photo	Grade
	0.00	MH	Start node, manhole, reference: 223	00:00:00	1	
	0.00	WL	Water level, 0% of the vertical dimension			
	8.79	CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:58		
	11.46	CN	Connection other than junction at 2 o'clock, 100mm dia	00:01:12		
	14.16	CN	Connection other than junction at 2 o'clock, 100mm dia	00:01:26		
	17.21	CN	Connection other than junction at 2 o'clock, 100mm dia	00:01:41		
	30.22	CN	Connection other than junction at 2 o'clock, 100mm dia	00:02:47		
	32.36	CN	Connection other than junction at 10 o'clock, 100mm dia	00:02:58		
	46.87	MHF	Finish node, manhole, reference: 222	00:04:15	2	

Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 223X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
37	Downstream	223X		

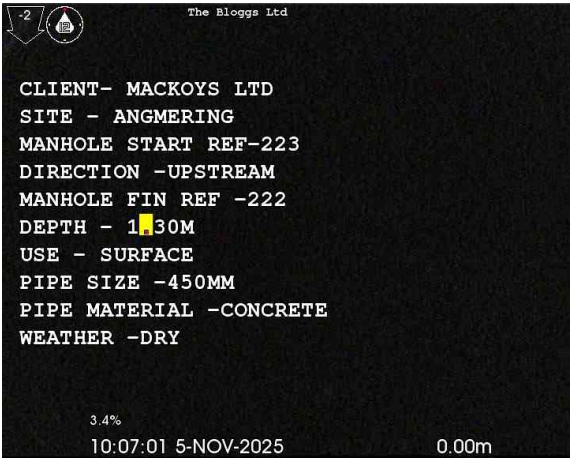

1, 00:00:00, 0.00 m
Start node, manhole, reference: 223



2, 00:04:15, 46.87 m
Finish node, manhole, reference: 222



Section Inspection - 06/11/2025 - 223X

Item No. 38	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 223X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	223
Road:	Langmead Place	Inspected Length:	25.13 m	Upstream Pipe Depth:	1.300 m
Location:	Road	Total Length:	25.13 m	Downstream Node:	225
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	450 mm		
Flow Control:	No flow control	Material:	Concrete		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:218	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.30 m							
223							
	0.00	MH	Start node, manhole, reference: 223	00:00:00	1		
	0.00	WL	Water level, 0% of the vertical dimension				
	5.61	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:35			
	5.81	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:36			
	8.92	CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:47			
	25.13	MHF	Finish node, manhole, reference: 225	00:01:52	2		
225							
Depth: m							

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 223X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
38	Downstream	223X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 223



2, 00:01:52, 25.13 m
Finish node, manhole, reference: 225



Section Inspection - 06/11/2025 - 225X

Item No. 39	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 225X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	225
Road:	Langmead Place	Inspected Length:	30.88 m	Upstream Pipe Depth:	2.000 m
Location:	Road	Total Length:	30.88 m	Downstream Node:	S2706
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	450 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:268	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 2.00 m 225 0.00 0.00 27.55 30.88 S2706 Depth: m							
		0.00	MH	Start node, manhole, reference: 225	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		27.55	CN	Connection other than junction at 10 o'clock, 100mm dia	00:02:50		
		30.88	MHF	Finish node, manhole, reference: S2706	00:03:04	2	

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 225X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
39	Downstream	225X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 225



2, 00:03:04, 30.88 m
Finish node, manhole, reference: S2706



Section Inspection - 06/11/2025 - 261X

Item No. 40	Insp. No. 1	Date 06/11/25	Time 13:55	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 261X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	261
Road:	Langmead Place	Inspected Length:	27.70 m	Upstream Pipe Depth:	1.050 m
Location:	Road	Total Length:	27.70 m	Downstream Node:	262
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:240	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 261	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		2.69	CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:25		
		10.73	CN	Connection other than junction at 10 o'clock, 150mm dia	00:01:01		
		19.19	CN	Connection other than junction at 10 o'clock, 150mm dia	00:01:40		
		27.70	MHF	Finish node, manhole, reference: 262	00:02:21	2	


Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 06/11/2025 - 261X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
40	Downstream	261X		

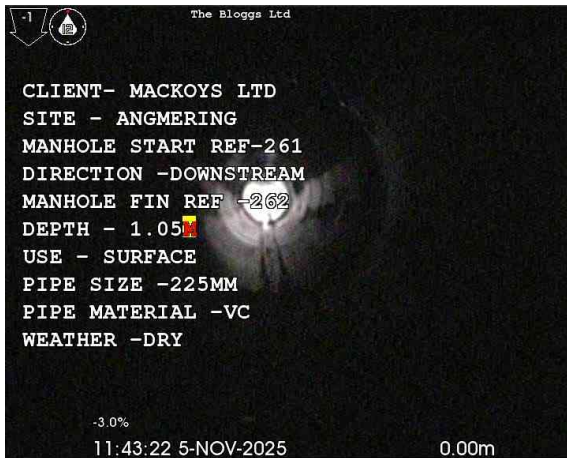

1, 00:00:00, 0.00 m
Start node, manhole, reference: 261



2, 00:02:21, 27.70 m
Finish node, manhole, reference: 262




Section Inspection - 11/11/2025 - F7X

Item No. 41	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F7X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F7
Road:	Langmead Place	Inspected Length:	13.98 m	Upstream Pipe Depth:	1.600 m
Location:	Road	Total Length:	13.98 m	Downstream Node:	F8
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

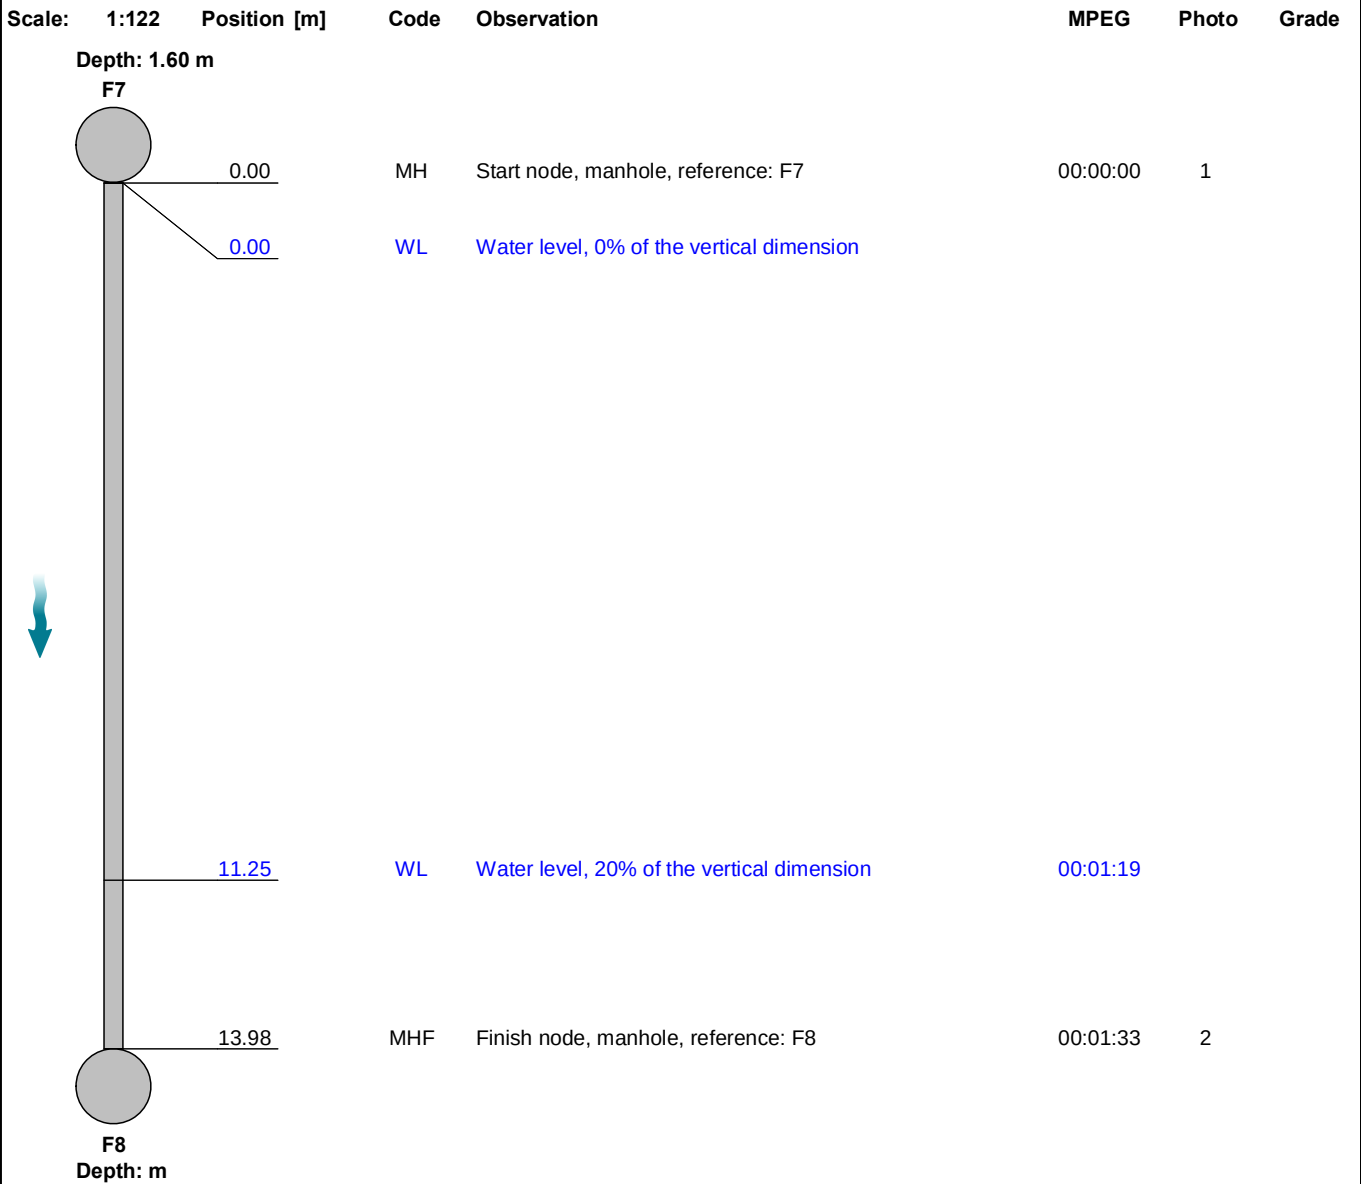

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F7X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
41	Downstream	F7X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F7



2, 00:01:33, 13.98 m
Finish node, manhole, reference: F8




Section Inspection - 11/11/2025 - F22X

Item No. 42	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F22X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified


Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	F22
Road:	Langmead Place	Inspected Length:	14.01 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	14.01 m	Downstream Node:	F23
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.400 m
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

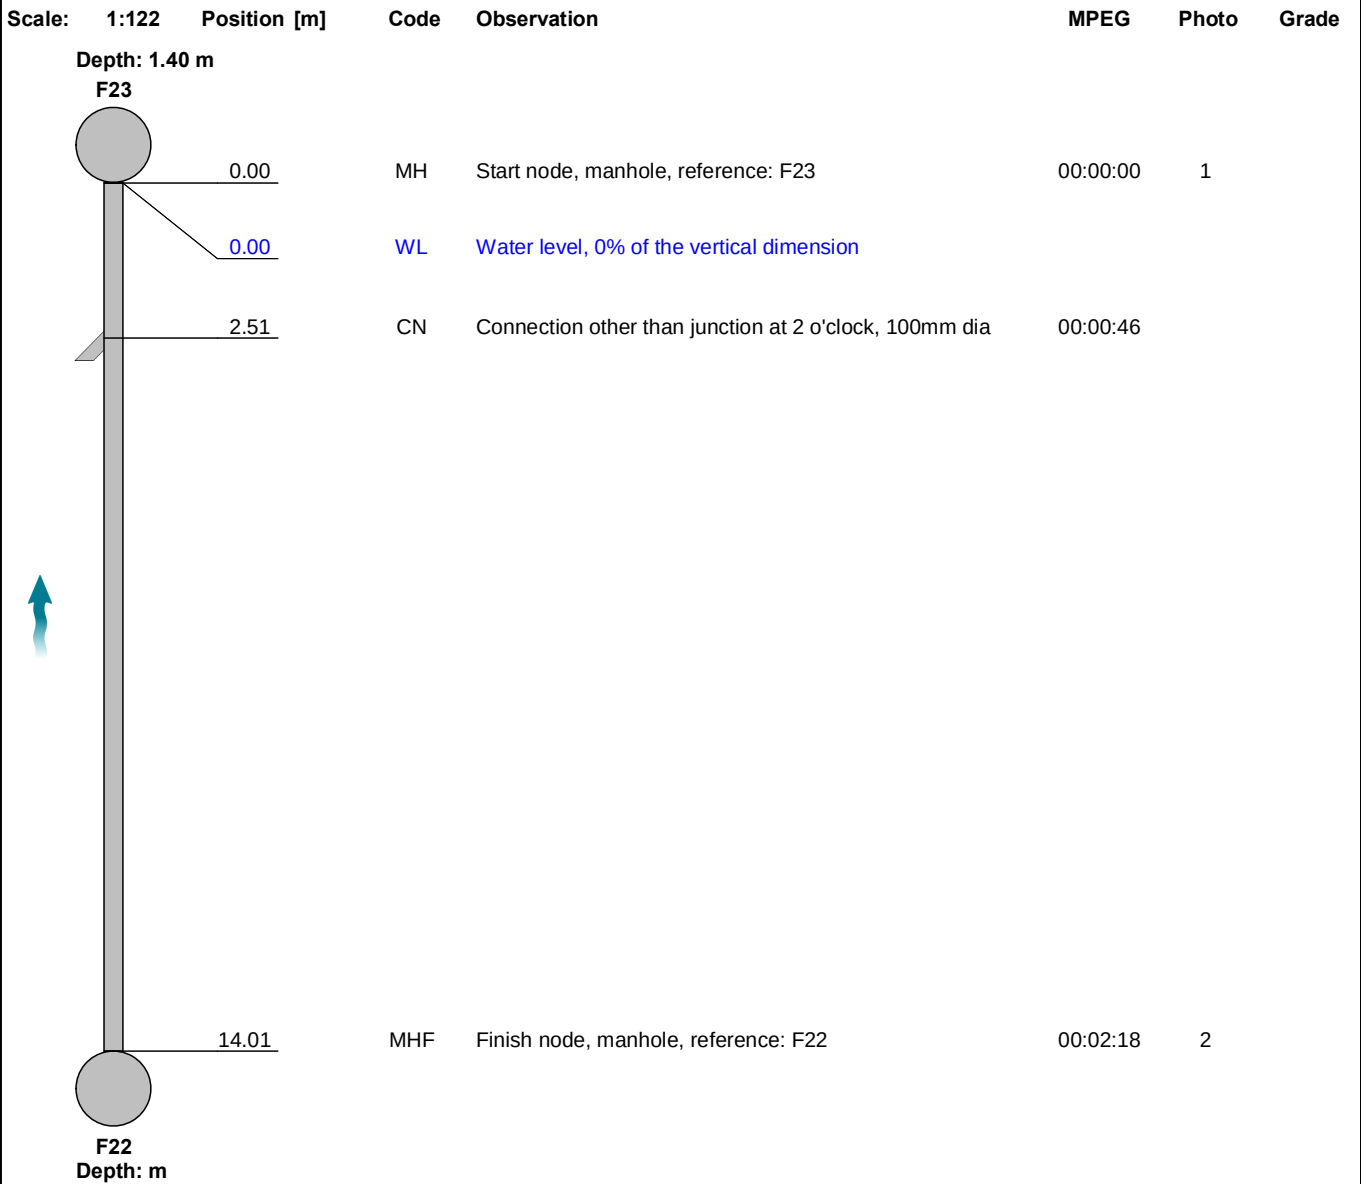


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 11/11/2025 - F22X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
42	Upstream	F22X		

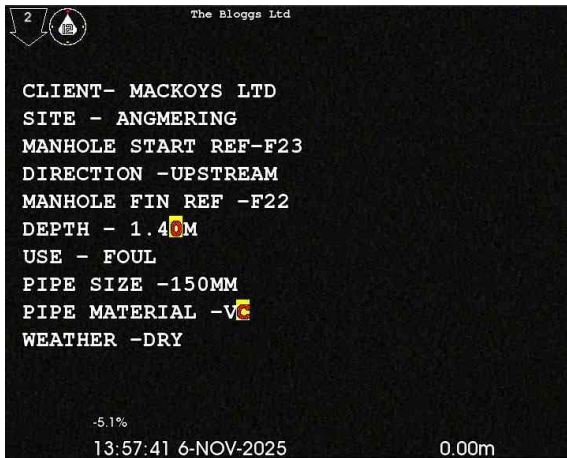

1, 00:00:00, 0.00 m
Start node, manhole, reference: F23

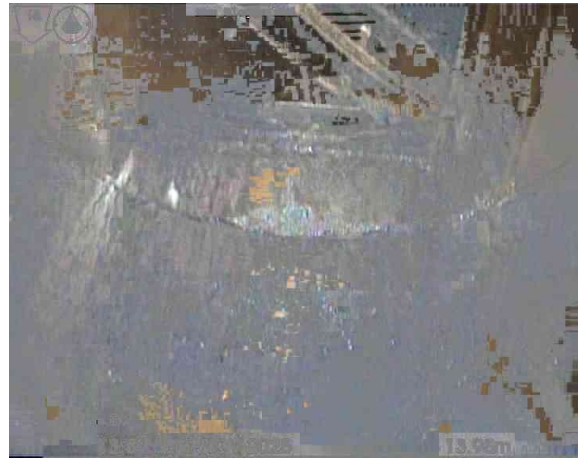


2, 00:02:18, 14.01 m
Finish node, manhole, reference: F22



Item No. 43	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F23X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified


Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 11/11/2025 - F23X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
43	Downstream	F23X		

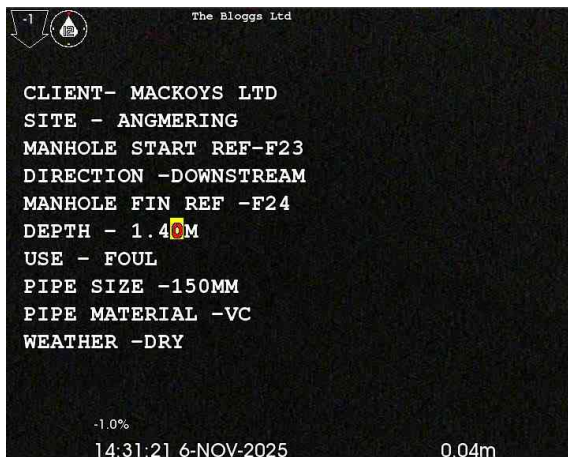

1, 00:00:00, 0.00 m
Start node, manhole, reference: F23

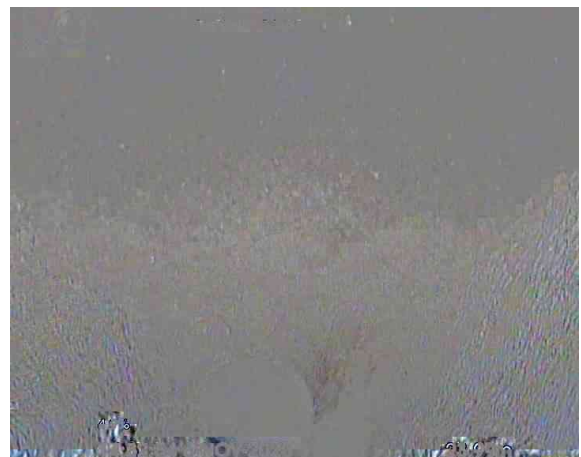

2, 00:01:32, 24.05 m
Finish node, manhole, reference: F24




Section Inspection - 11/11/2025 - F42X

Item No. 44	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F42X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F42
Road:	Langmead Place	Inspected Length:	14.70 m	Upstream Pipe Depth:	1.400 m
Location:	Road	Total Length:	14.70 m	Downstream Node:	F43
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

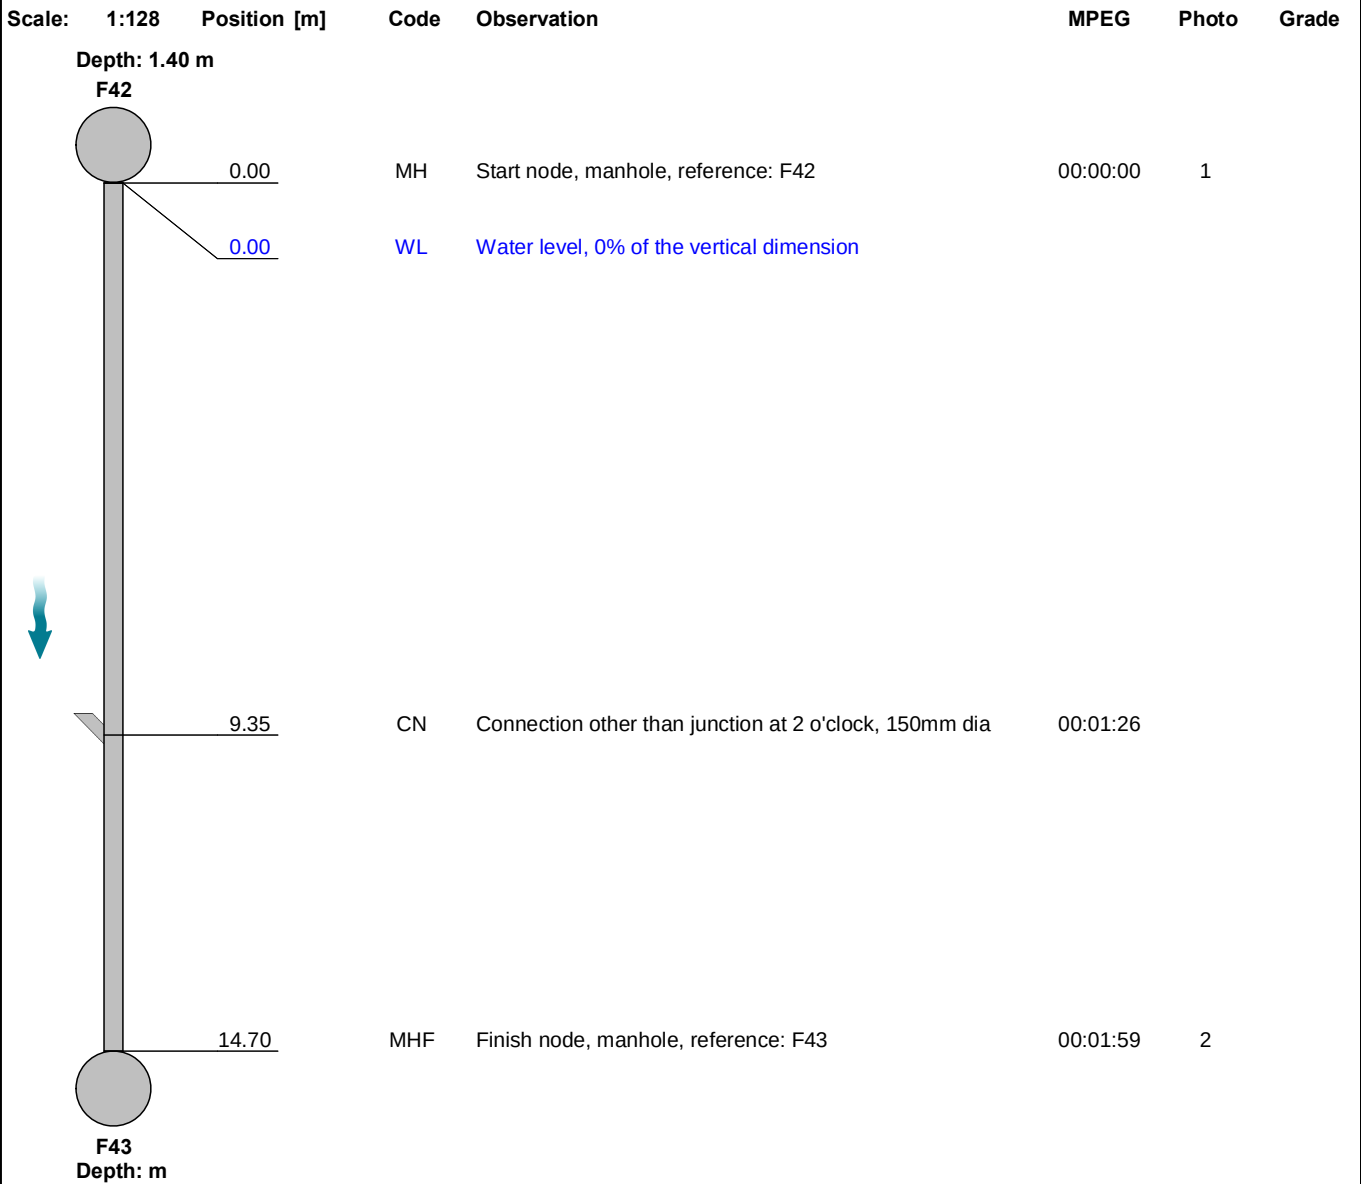

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 11/11/2025 - F42X				
Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
44	Downstream	F42X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F42



2, 00:01:59, 14.70 m
Finish node, manhole, reference: F43



Section Inspection - 11/11/2025 - F43X

Item No. 45	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F43X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F43
Road:	Langmead Place	Inspected Length:	20.42 m	Upstream Pipe Depth:	1.400 m
Location:	Road	Total Length:	20.42 m	Downstream Node:	F47
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:177	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.40 m F43 0.00 MH Start node, manhole, reference: F43 00:00:00 1 0.00 WL Water level, 0% of the vertical dimension 20.42 MHF Finish node, manhole, reference: F47 00:02:25 2 F47 Depth: m							


Construction Features

Miscellaneous Features

Structural Defects

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F43X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
45	Downstream	F43X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F43



2, 00:02:25, 20.42 m
Finish node, manhole, reference: F47




Section Inspection - 11/11/2025 - F18X

Item No. 46	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F18X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified


Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	F18
Road:	Langmead Place	Inspected Length:	7.41 m	Upstream Pipe Depth:	1.400 m
Location:	Road	Total Length:	7.41 m	Downstream Node:	F19
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

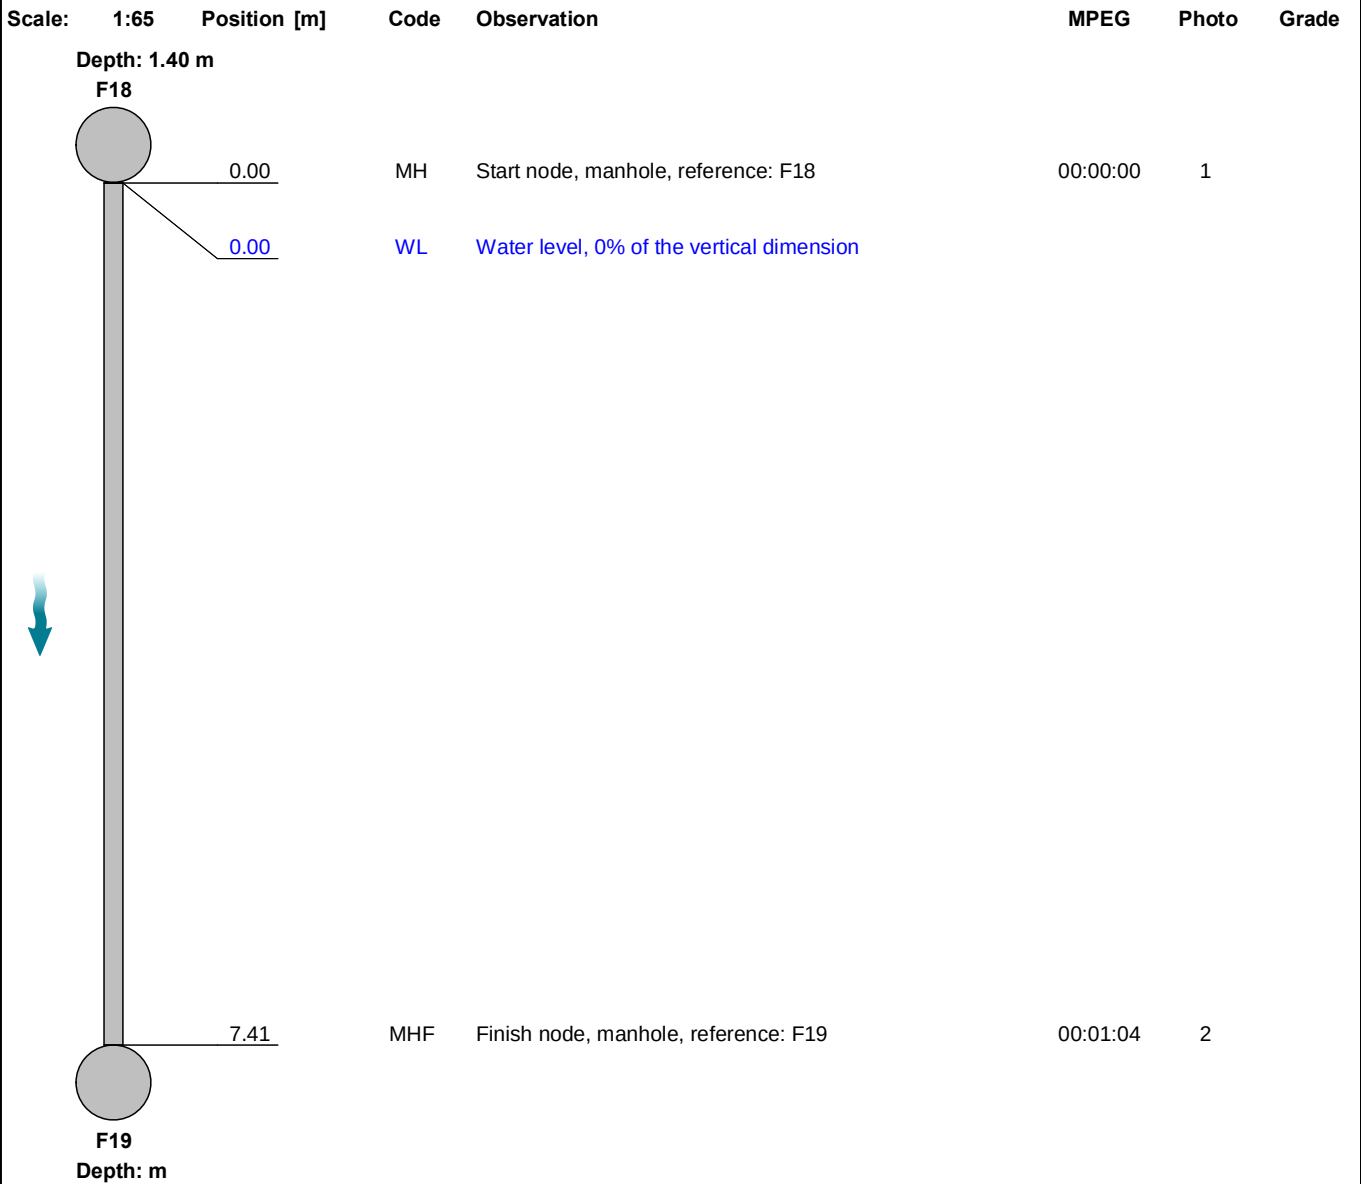


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F18X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
46	Downstream	F18X		

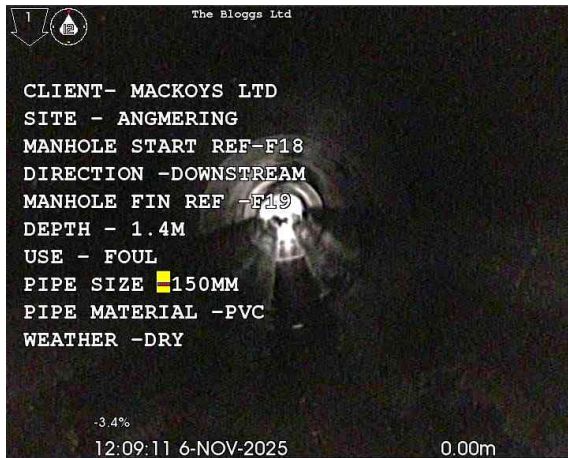

1, 00:00:00, 0.00 m
Start node, manhole, reference: F18




2, 00:01:04, 7.41 m
Finish node, manhole, reference: F19



Item No. 47	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F19X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F19X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
47	Downstream	F19X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F19




2, 00:02:49, 25.24 m
Finish node, manhole, reference: F20



Item No. 48	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F20X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F20X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
48	Downstream	F20X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F20



2, 00:04:51, 40.24 m
Finish node, manhole, reference: F21



Item No. 49	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F39X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Scale: 1:147 Position [m] Code Observation MPEG Photo Grade

Depth: 1.75 m
F39


Code	Observation	MPEG	Photo	Grade
MH	Start node, manhole, reference: F39	00:00:00	1	
WL	Water level, 0% of the vertical dimension			
WL	Water level, 20% of the vertical dimension	00:01:59		
MHF	Finish node, manhole, reference: F40	00:02:03	2	

Depth: m


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - F39X				
Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
49	Downstream	F39X		

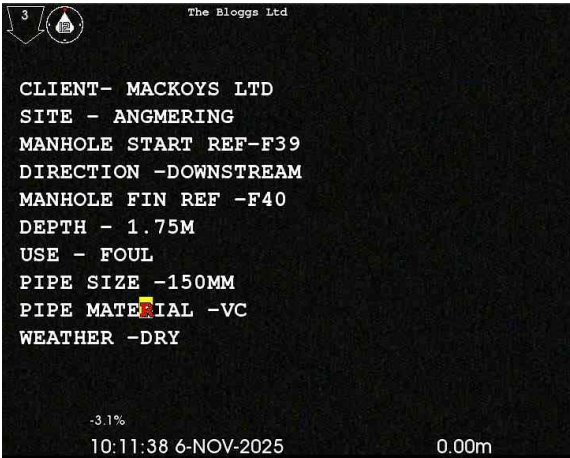


1, 00:00:00, 0.00 m
Start node, manhole, reference: F39

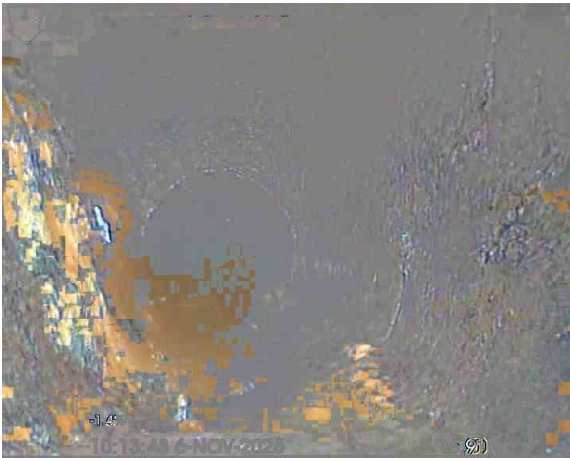

2, 00:02:03, 16.91 m
Finish node, manhole, reference: F40



Item No. 50	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F40X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Scale:	1:294	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.60 m F40  0.00 0.00 33.81 33.89 MH Start node, manhole, reference: F40 00:00:00 1 WL Water level, 0% of the vertical dimension JN Junction at 6 o'clock, 150mm dia: BACKDROP 00:03:45 MHF Finish node, manhole, reference: F41 00:03:48 2							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	2	5.0	0.3	10.0	4.0



Section Pictures - 11/11/2025 - F40X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
50	Downstream	F40X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: F40



2, 00:03:48, 33.89 m
Finish node, manhole, reference: F41



Item No. 51	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR F41X
Operator C. Bloor		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 11/11/2025 - F41X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
51	Downstream	F41X		




1, 00:00:00, 0.00 m
Start node, manhole, reference: F41

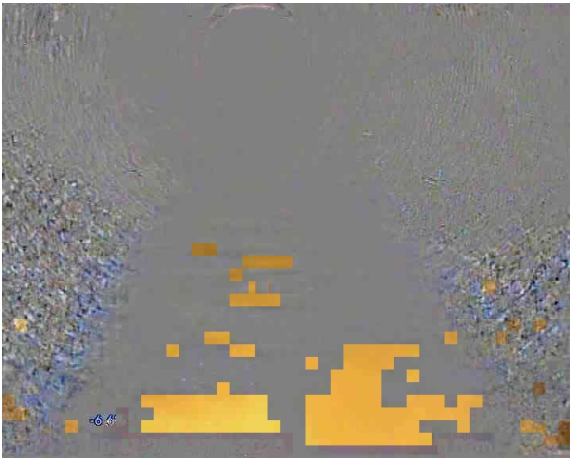

2, 00:00:08, 0.00 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:02:33, 20.32 m
Finish node, manhole, reference: F42




Section Inspection - 11/11/2025 - 32AX

Item No. 52	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 32AX
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	32A
Road:	Langmead Place	Inspected Length:	8.03 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	8.03 m	Downstream Node:	32B
Surface Type:		Joint Length:		Downstream Pipe Depth:	2.200 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

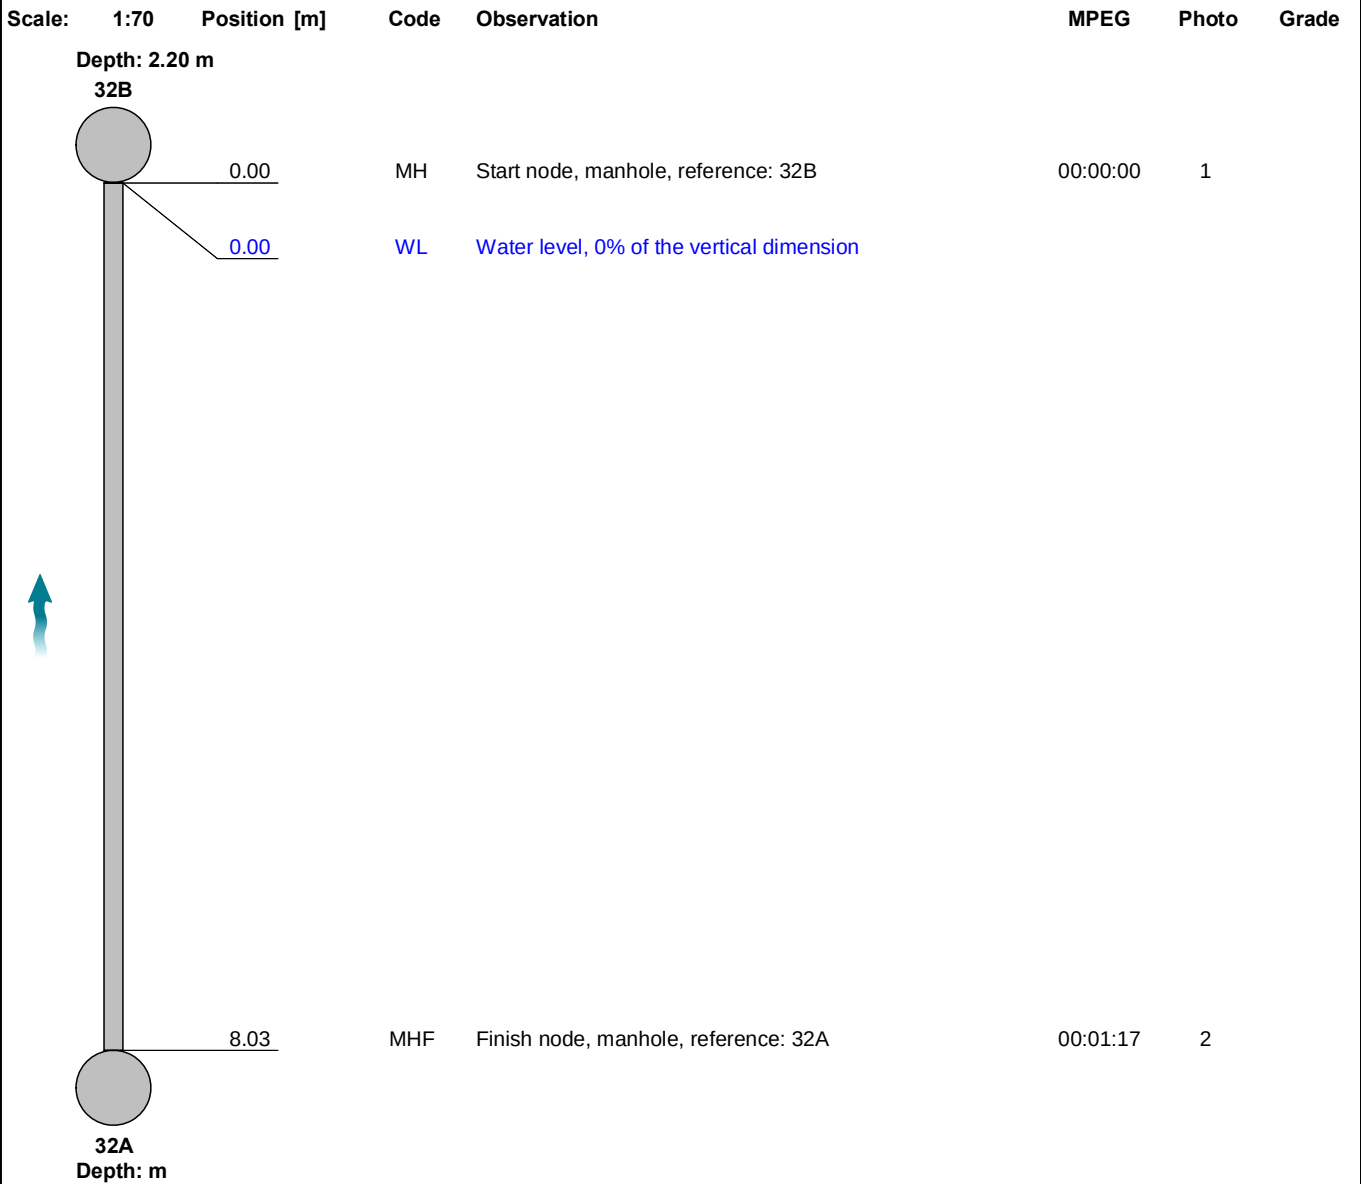

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - 32AX


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
52	Upstream	32AX		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 32B



2, 00:01:17, 8.03 m
Finish node, manhole, reference: 32A



Section Inspection - 11/11/2025 - 325X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
53	1	11/11/25	9:18	Not Specified	No Rain Or Snow	Yes	325X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg				Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	325
Road:	Langmead Place	Inspected Length:	29.80 m	Upstream Pipe Depth:	1.200 m
Location:	Road	Total Length:	29.80 m	Downstream Node:	326
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:259	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.20 m							
325							
	0.00	MH	Start node, manhole, reference: 325	00:00:00	1		
	0.00	WL	Water level, 0% of the vertical dimension				
	2.23	CN	Connection other than junction at 2 o'clock, 100mm dia	00:00:34			
	21.11	CN	Connection other than junction at 10 o'clock, 100mm dia	00:01:45			
	25.87	CN	Connection other than junction at 2 o'clock, 150mm dia	00:02:03			
	26.12	CN	Connection other than junction at 2 o'clock, 150mm dia	00:02:05			
	29.80	MHF	Finish node, manhole, reference: 326	00:02:20	2		
326							
Depth: m							


Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
2	1.0	0.1	2.0	1.0	1	2.0	0.1	2.0	3.0



Section Pictures - 11/11/2025 - 325X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
53	Downstream	325X		

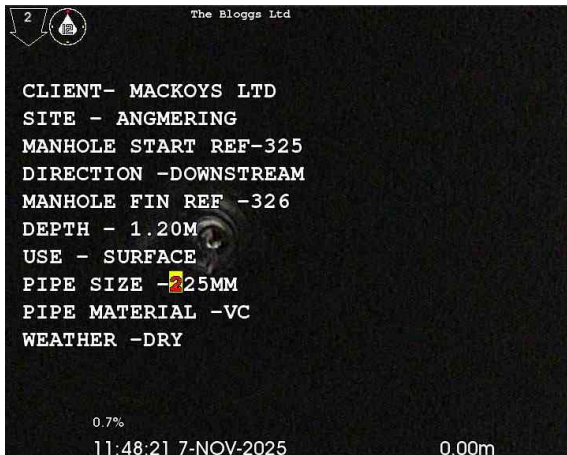

1, 00:00:00, 0.00 m
Start node, manhole, reference: 325




2, 00:02:20, 29.80 m
Finish node, manhole, reference: 326



Section Pictures - 11/11/2025 - 323X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
54	Downstream	323X		

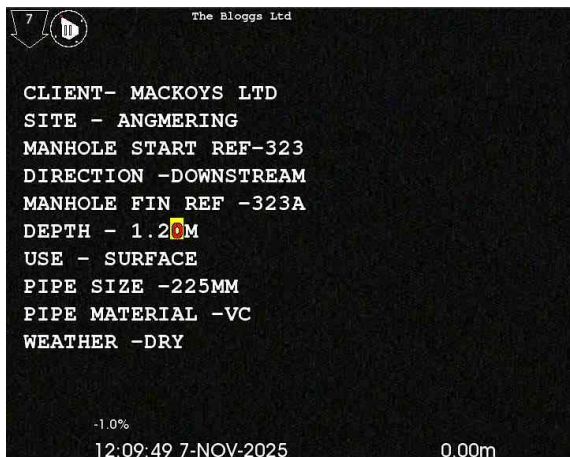

1, 00:00:00, 0.00 m
Start node, manhole, reference: 323



2, 00:01:28, 17.48 m
Finish node, manhole, reference: 323A




Section Inspection - 11/11/2025 - 330X

Item No. 55	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 330X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified


Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	330
Road:	Langmead Place	Inspected Length:	7.38 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	7.38 m	Downstream Node:	S215
Surface Type:		Joint Length:		Downstream Pipe Depth:	2.000 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

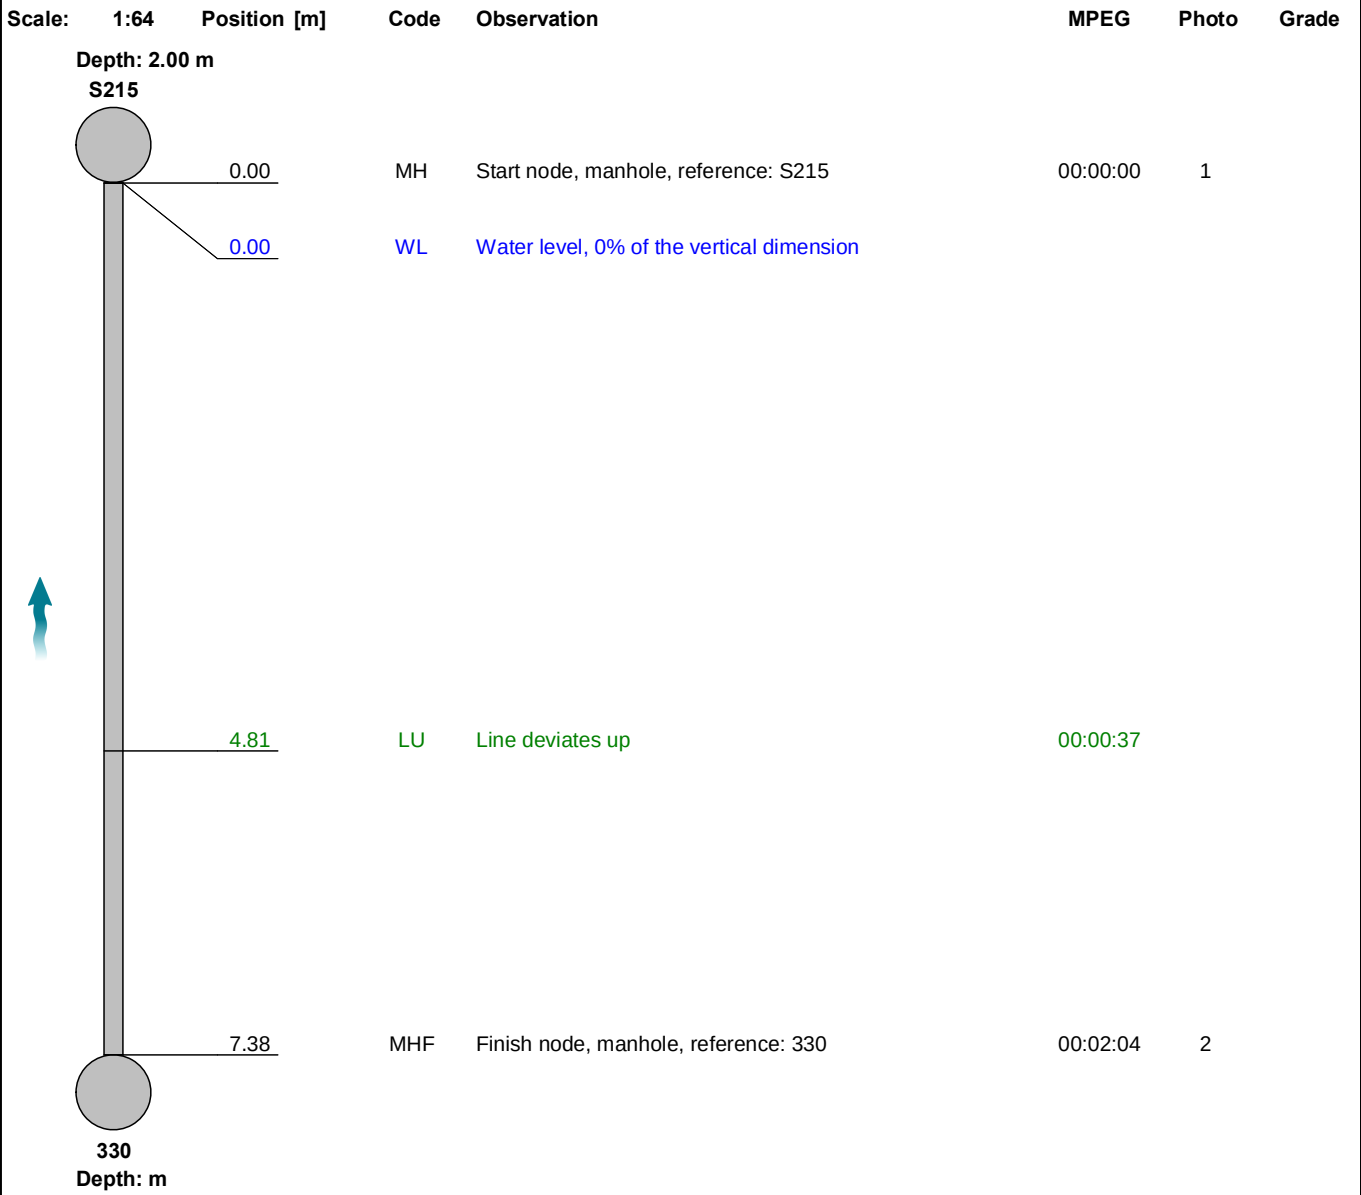

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - 330X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
55	Upstream	330X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: S215



2, 00:02:04, 7.38 m
Finish node, manhole, reference: 330



Section Inspection - 11/11/2025 - 330X

Item No. 56	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 330X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	330
Road:	Langmead Place	Inspected Length:	26.06 m	Upstream Pipe Depth:	2.000 m
Location:	Road	Total Length:	26.06 m	Downstream Node:	S215
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:226	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 2.00 m 330							
	0.00	MH	Start node, manhole, reference: 330		00:00:00	1	
	0.00	WL	Water level, 0% of the vertical dimension				
	0.00	REM	General remark: overlap		00:00:08	2	
	5.11	CN	Connection other than junction at 10 o'clock, 100mm dia		00:00:52		
	5.72	CN	Connection other than junction at 2 o'clock, 100mm dia		00:00:54		
	6.13	CN	Connection other than junction at 2 o'clock, 100mm dia		00:00:56		
	9.60	LD	Line deviates down		00:01:24		
	11.87	CN	Connection other than junction at 12 o'clock, 100mm dia		00:01:34		
	16.80	CN	Connection other than junction at 1 o'clock, 100mm dia		00:01:53		
	26.06	MHF	Finish node, manhole, reference: S215		00:02:35	3	
S215 Depth: m							


Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 11/11/2025 - 330X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
56	Downstream	330X		




1, 00:00:00, 0.00 m
Start node, manhole, reference: 330

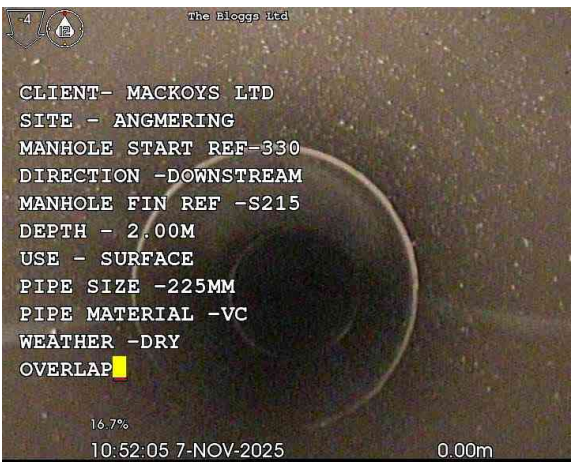

2, 00:00:08, 0.00 m
General remark, overlap



3, 00:02:35, 26.06 m
Finish node, manhole, reference: S215




Section Inspection - 11/11/2025 - 332BX

Item No. 57	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR 332BX
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	332B
Road:	Langmead Place	Inspected Length:	18.10 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	18.10 m	Downstream Node:	330
Surface Type:		Joint Length:		Downstream Pipe Depth:	2.000 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	225 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

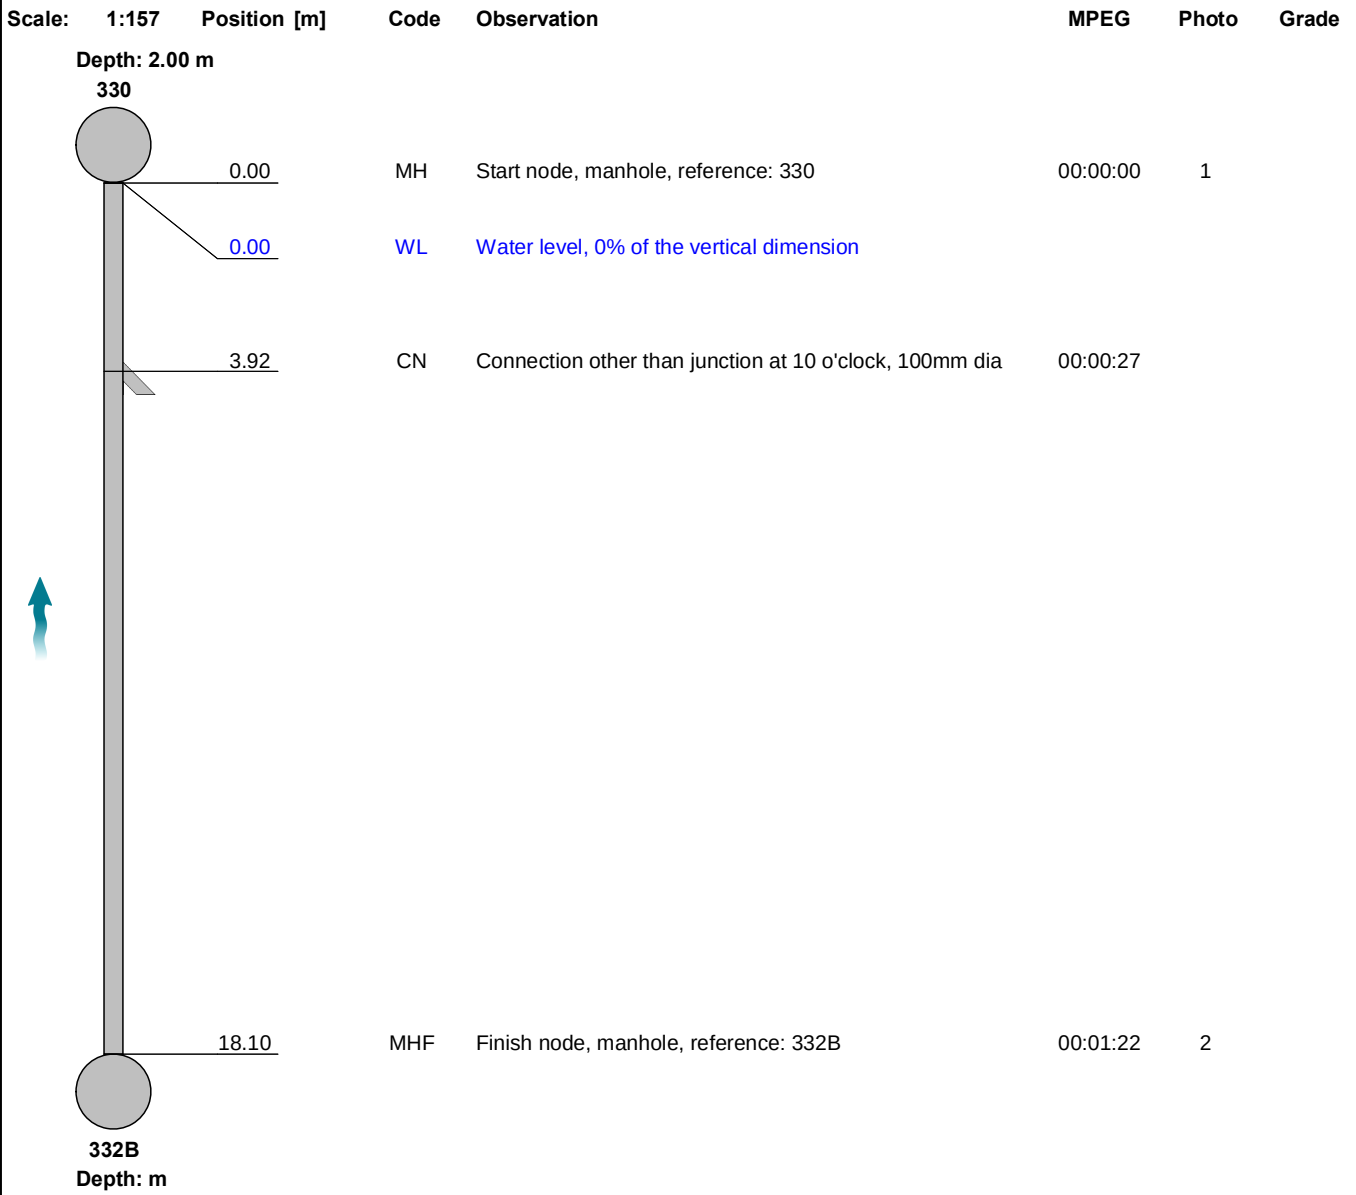

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Pictures - 11/11/2025 - 332BX


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
57	Upstream	332BX		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 330

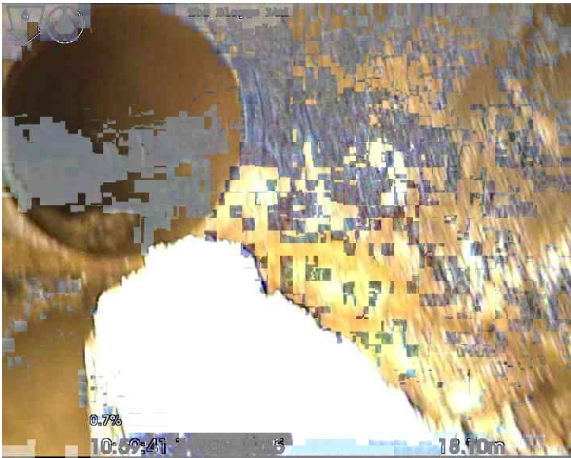

2, 00:01:22, 18.10 m
Finish node, manhole, reference: 332B




Section Inspection - 11/11/2025 - FW348X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
58	1	11/11/25	9:18	Not Specified	No Rain Or Snow	Yes	FW348X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
C.Blogg				Pushrod	Not Specified	Highways Drainage	Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	FW348
Road:	Langmead Place	Inspected Length:	2.40 m	Upstream Pipe Depth:	1.000 m
Location:	Road	Total Length:	2.40 m	Downstream Node:	F41
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

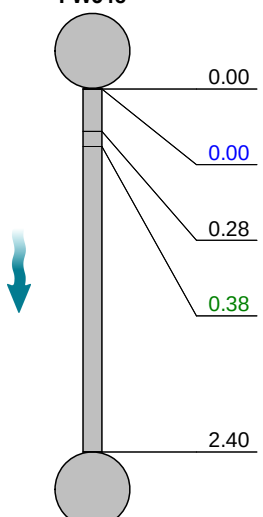Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.00 m FW348							
							
	0.00	MH		Start node, manhole, reference: FW348	00:00:00	1	
	0.00	WL		Water level, 0% of the vertical dimension			
	0.28	JN		Junction at 6 o'clock, 100mm dia: BACKDROP	00:00:30		
	0.38	LL		Line deviates left	00:00:11		
	2.40	MHF		Finish node, manhole, reference: F41	00:00:41	2	
F41 Depth: m							

Construction Features

Miscellaneous Features

Structural Defects


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW348X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
58	Downstream	FW348X		

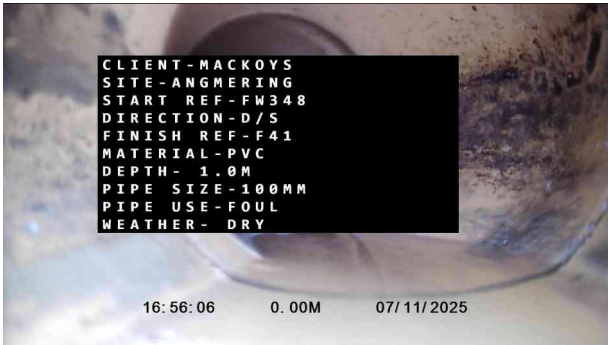

1, 00:00:00, 0.00 m
Start node, manhole, reference: FW348



2, 00:00:41, 2.40 m
Finish node, manhole, reference: F41



Section Inspection - 11/11/2025 - FW332X

Item No. 59	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR FW332X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	FW332
Road:	Langmead Place	Inspected Length:	5.95 m	Upstream Pipe Depth:	1.000 m
Location:	Road	Total Length:	5.95 m	Downstream Node:	F41
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:


Scale:	1:52	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.00 m FW332							
	0.00	MH	Start node, manhole, reference: FW332	00:00:00	1		
	0.00	WL	Water level, 0% of the vertical dimension				
	1.53	LR	Line deviates right	00:00:10			
	3.45	JN	Junction at 6 o'clock, 100mm dia: BACKDROP	00:00:19			
	5.95	MHF	Finish node, manhole, reference: F41	00:00:25	2		
F41 Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW332X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
59	Downstream	FW332X		

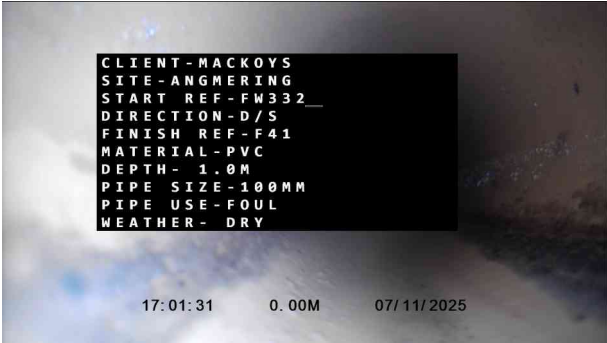

1, 00:00:00, 0.00 m
Start node, manhole, reference: FW332



2, 00:00:25, 5.95 m
Finish node, manhole, reference: F41



Section Inspection - 11/11/2025 - FW355X

Item No. 60	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR FW355X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	FW355
Road:	Langmead Place	Inspected Length:	2.11 m	Upstream Pipe Depth:	1.800 m
Location:	Road	Total Length:	2.20 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.80 m FW355							
	0.00	MH	Start node, manhole, reference: FW355		00:00:00	1	
	0.00	WL	Water level, 0% of the vertical dimension				
	2.10	LR	Line deviates right		00:00:13		
	2.10	LD	Line deviates down		00:00:13		
	2.11	BRF	Finish node, major connection without manhole, reference: MAIN		00:00:15	2	
MAIN							
Depth: m							

Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW355X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
60	Downstream	FW355X		

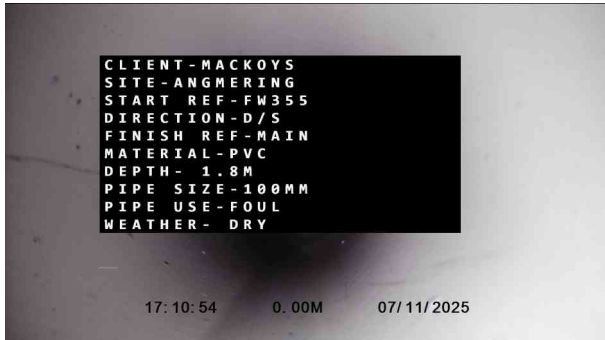

1, 00:00:00, 0.00 m
Start node, manhole, reference: FW355



2, 00:00:15, 2.11 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 11/11/2025 - RWPX

Item No. 61	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RWPX
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RWP
Road:	Langmead Place	Inspected Length:	25.49 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	25.49 m	Downstream Node:	330
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.800 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:


Scale:	1:221	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: 330	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.28	LD	Line deviates down	00:00:10		
		0.28	LU	Line deviates up	00:00:10		
		1.92	LL	Line deviates left	00:00:16		
		2.40	LD	Line deviates down	00:00:17		
		9.89	WL	Water level, 20% of the vertical dimension	00:00:42		
		13.74	WL	Water level, 35% of the vertical dimension	00:00:51		
		25.49	MHF	Finish node, manhole, reference: RWP	00:01:23	2	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	80.0	3.1	80.0	4.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - RWPX


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
61	Upstream	RWPX		

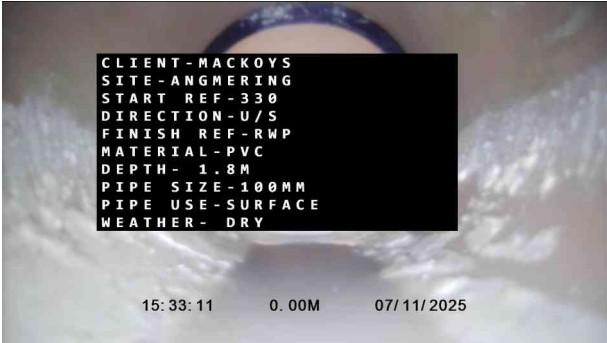

1, 00:00:00, 0.00 m
Start node, manhole, reference: 330



2, 00:01:23, 25.49 m
Finish node, manhole, reference: RWP



Section Inspection - 11/11/2025 - FW230X

Item No. 62	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR FW230X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	FW230
Road:	Langmead Place	Inspected Length:	3.07 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	3.07 m	Downstream Node:	F18
Surface Type:		Joint Length:		Downstream Pipe Depth:	0.800 m
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Vitrified clay		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.80 m F18							
	0.00	MH	Start node, manhole, reference: F18		00:00:00	1	
	0.00	WL	Water level, 0% of the vertical dimension				
	1.53	JN	Junction at 6 o'clock, 150mm dia: BACKDROP		00:00:14		
	2.20	CN	Connection other than junction at 2 o'clock, 150mm dia		00:00:28		
	2.40	SC	Pipe size changes, new size(s), 100mm high		00:00:28	2	
	3.07	MHF	Finish node, manhole, reference: FW230		00:01:02	3	
FW230 Depth: m							

Construction Features

Structural Defects

Miscellaneous Features


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW230X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
62	Upstream	FW230X		

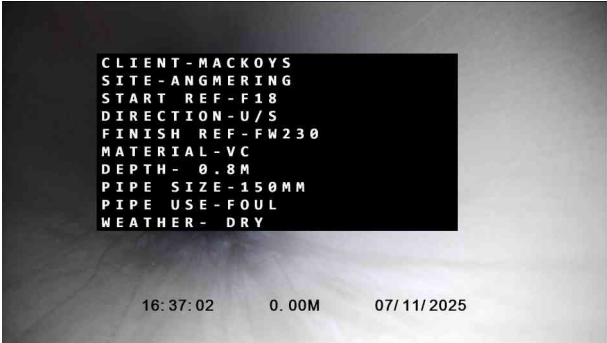

1, 00:00:00, 0.00 m
Start node, manhole, reference: F18



2, 00:00:28, 2.40 m
Pipe size changes, new size(s), 100mm high




3, 00:01:02, 3.07 m
Finish node, manhole, reference: FW230



Item No. 63	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR FW230X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified


Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade																																								
Depth: 0.80 m FW230 0.00 0.00 0.00 2.49 2.49 4.12 5.66 F18 Depth: m <table><tr><th>Code</th><th>Observation</th><th>MPEG</th><th>Photo</th><th>Grade</th></tr><tr><td>MH</td><td>Start node, manhole, reference: FW230</td><td>00:00:00</td><td>1</td><td></td></tr><tr><td>WL</td><td>Water level, 0% of the vertical dimension</td><td></td><td></td><td></td></tr><tr><td>LL</td><td>Line deviates left</td><td>00:00:10</td><td></td><td></td></tr><tr><td>LR</td><td>Line deviates right</td><td>00:00:20</td><td></td><td></td></tr><tr><td>CN</td><td>Connection other than junction at 10 o'clock, 100mm dia</td><td>00:00:21</td><td></td><td></td></tr><tr><td>JN</td><td>Junction at 6 o'clock, 100mm dia: BACKDROP</td><td>00:00:25</td><td></td><td></td></tr><tr><td>MHF</td><td>Finish node, manhole, reference: F18</td><td>00:00:36</td><td>2</td><td></td></tr></table>								Code	Observation	MPEG	Photo	Grade	MH	Start node, manhole, reference: FW230	00:00:00	1		WL	Water level, 0% of the vertical dimension				LL	Line deviates left	00:00:10			LR	Line deviates right	00:00:20			CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:21			JN	Junction at 6 o'clock, 100mm dia: BACKDROP	00:00:25			MHF	Finish node, manhole, reference: F18	00:00:36	2	
Code	Observation	MPEG	Photo	Grade																																											
MH	Start node, manhole, reference: FW230	00:00:00	1																																												
WL	Water level, 0% of the vertical dimension																																														
LL	Line deviates left	00:00:10																																													
LR	Line deviates right	00:00:20																																													
CN	Connection other than junction at 10 o'clock, 100mm dia	00:00:21																																													
JN	Junction at 6 o'clock, 100mm dia: BACKDROP	00:00:25																																													
MHF	Finish node, manhole, reference: F18	00:00:36	2																																												

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW230X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
63	Downstream	FW230X		

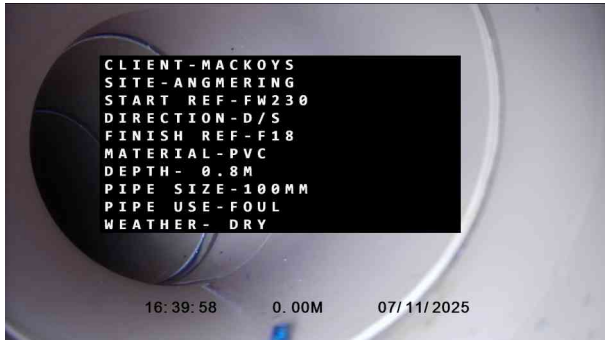

1, 00:00:00, 0.00 m
Start node, manhole, reference: FW230



2, 00:00:36, 5.66 m
Finish node, manhole, reference: F18



Section Inspection - 11/11/2025 - FW209X

Item No. 64	Insp. No. 1	Date 11/11/25	Time 9:18	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR FW209X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	FW209
Road:	Langmead Place	Inspected Length:	4.99 m	Upstream Pipe Depth:	1.200 m
Location:	Road	Total Length:	4.99 m	Downstream Node:	F39
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Foul	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	100 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.20 m FW209							
		0.00	MH	Start node, manhole, reference: FW209	00:00:00	1	
		0.00	WL	Water level, 0% of the vertical dimension			
		0.09	LL	Line deviates left	00:00:07		
		1.72	LD	Line deviates down	00:00:13		
		2.49	LD	Line deviates down	00:00:16		
		4.70	JN	Junction at 6 o'clock, 100mm dia: BACKDROP	00:00:28		
		4.99	MHF	Finish node, manhole, reference: F39	00:00:31	2	
F39 Depth: m							

Construction Features

Miscellaneous Features

Structural Defects


Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 11/11/2025 - FW209X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
64	Downstream	FW209X		

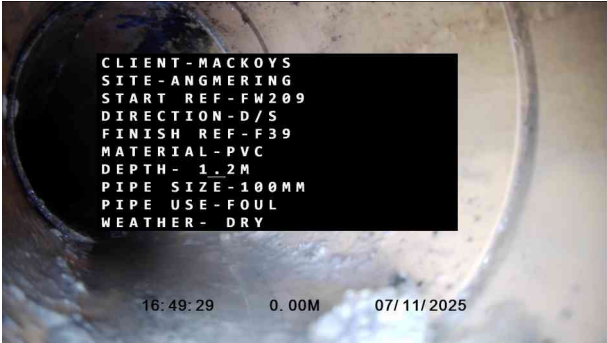

1, 00:00:00, 0.00 m
Start node, manhole, reference: FW209



2, 00:00:31, 4.99 m
Finish node, manhole, reference: F39



Section Inspection - 17/11/2025 - RG69X

Item No. 65	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG69X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified


Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG69
Road:	Langmead Place	Inspected Length:	11.84 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	11.84 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:103	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m RG69							
		0.00	GY	Start node, gully, reference: RG69	00:00:00	1	
		0.00	WL	Water level, 100% of the vertical dimension			
		2.49	WL	Water level, 30% of the vertical dimension	00:00:19		
		11.44	LL	Line deviates left	00:00:51		
		11.84	BRF	Finish node, major connection without manhole, reference: MAIN	00:00:56	2	
		MAIN					
		Depth: m					

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG69X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
65	Downstream	RG69X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG69



2, 00:00:56, 11.84 m
Finish node, major connection without manhole, reference:
MAIN



Section Inspection - 17/11/2025 - RG70X

Item No. 66	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG70X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angerming	Inspection Direction:	Downstream	Upstream Node:	RG70
Road:	Langmead Place	Inspected Length:	2.20 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	2.20 m	Downstream Node:	MAIN
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 0.60 m							
RG70							
0.00		GY	Start node, gully, reference: RG70	00:00:00	1		
0.00		WL	Water level, 0% of the vertical dimension				
1.29		LU	Line deviates up	00:00:11			
1.92		LR	Line deviates right	00:00:10			
2.20		BRF	Finish node, major connection without manhole, reference: MAIN	00:00:13	2		
MAIN							
Depth: m							

Construction Features

Miscellaneous Features

Structural Defects

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG70X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
66	Downstream	RG70X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG70



2, 00:00:13, 2.20 m
Finish node, major connection without manhole, reference: MAIN




Section Inspection - 17/11/2025 - RG68X

Item No. 67	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG68X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Downstream	Upstream Node:	RG68
Road:	Langmead Place	Inspected Length:	7.01 m	Upstream Pipe Depth:	0.600 m
Location:	Road	Total Length:	7.01 m	Downstream Node:	323A
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:
Recommendations:

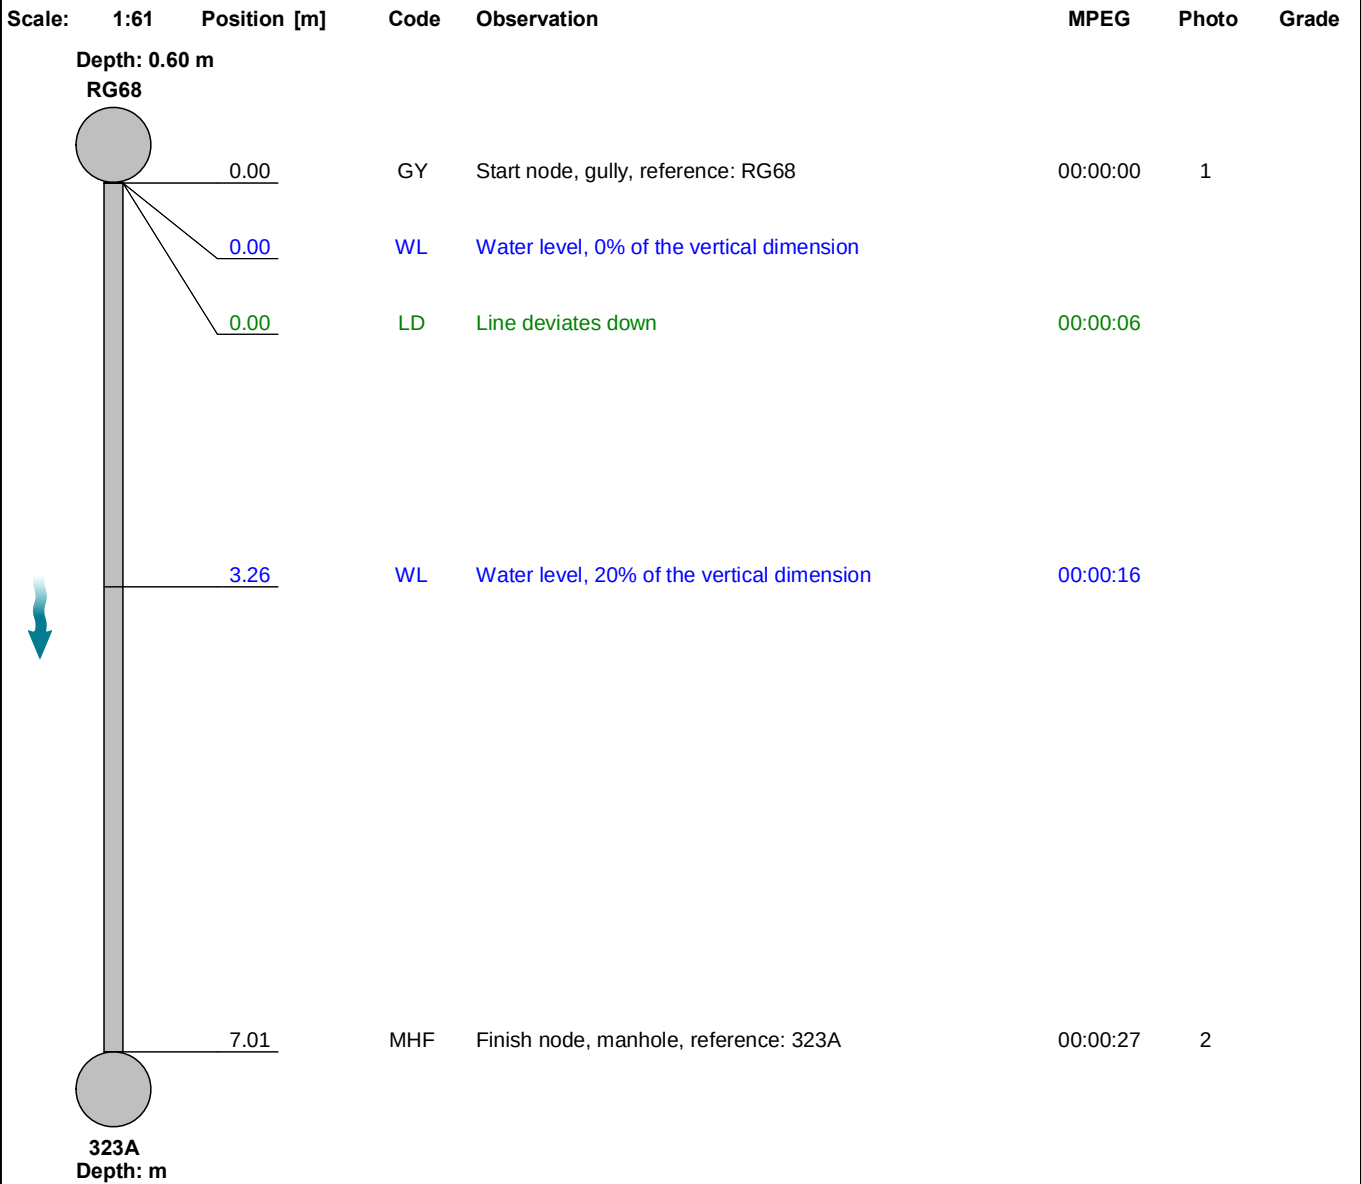

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG68X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
67	Downstream	RG68X		



1, 00:00:00, 0.00 m
Start node, gully, reference: RG68



2, 00:00:27, 7.01 m
Finish node, manhole, reference: 323A




Section Inspection - 17/11/2025 - RG53X

Item No. 68	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG53X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RG53
Road:	Langmead Place	Inspected Length:	15.56 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	15.56 m	Downstream Node:	337
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.600 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

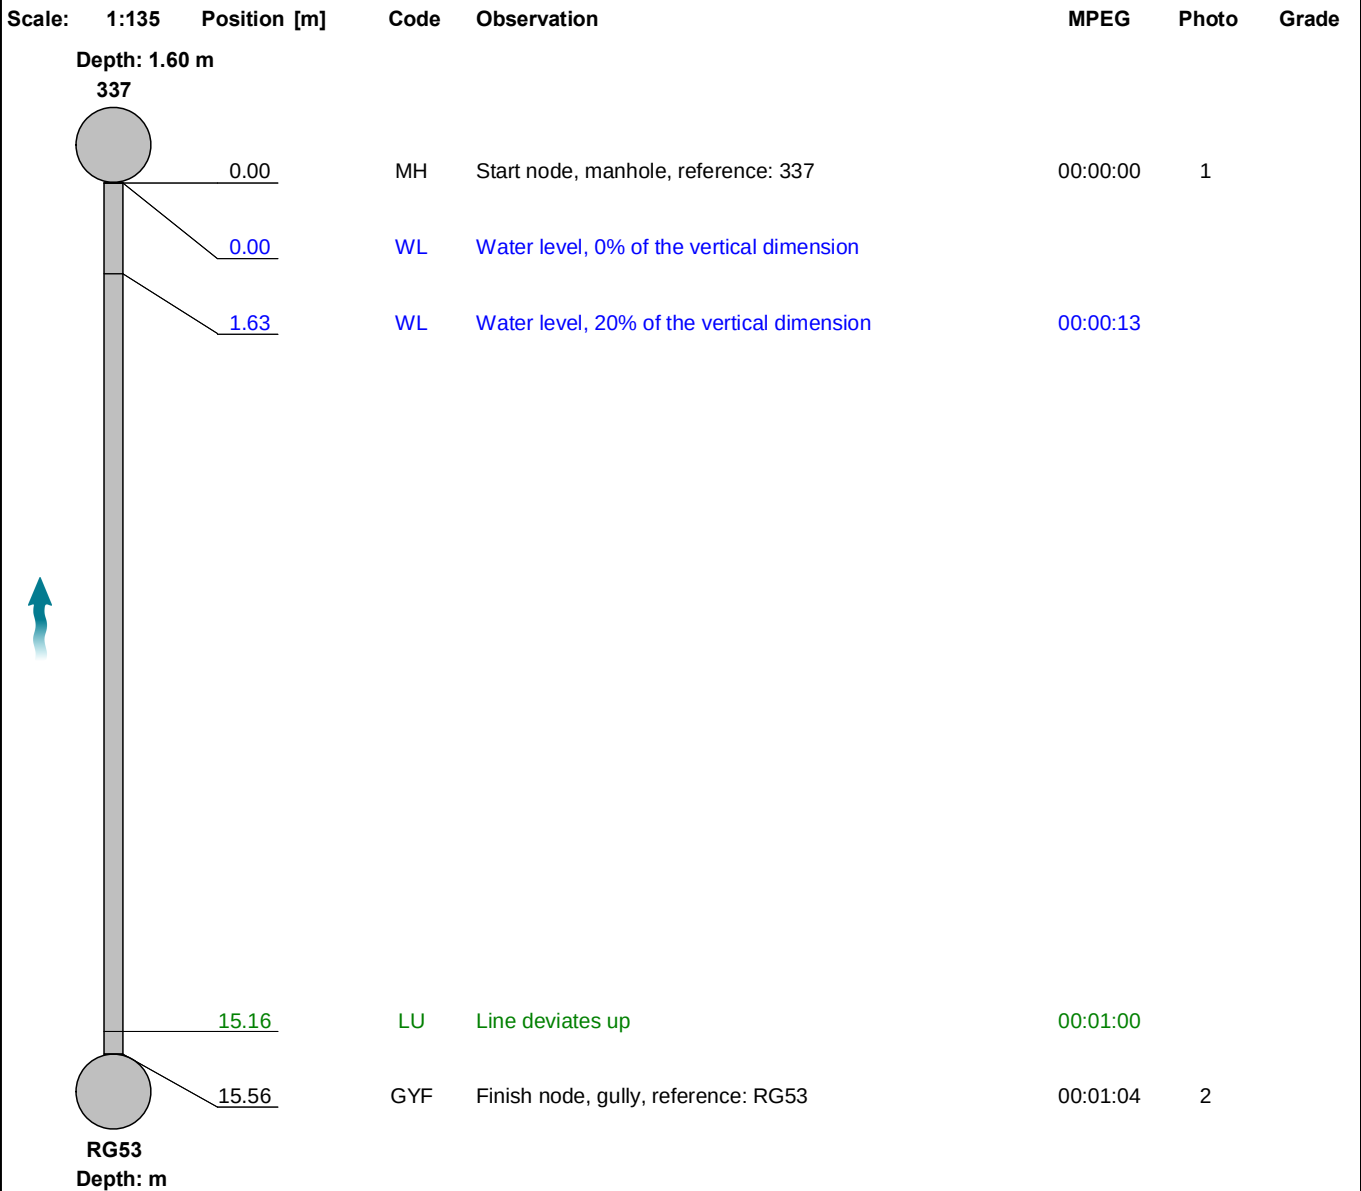

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG53X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
68	Upstream	RG53X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 337



2, 00:01:04, 15.56 m
Finish node, gully, reference: RG53




Section Inspection - 17/11/2025 - RG52X

Item No. 69	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG52X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RG52
Road:	Langmead Place	Inspected Length:	8.70 m	Upstream Pipe Depth:	1.600 m
Location:	Road	Total Length:	8.70 m	Downstream Node:	338
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

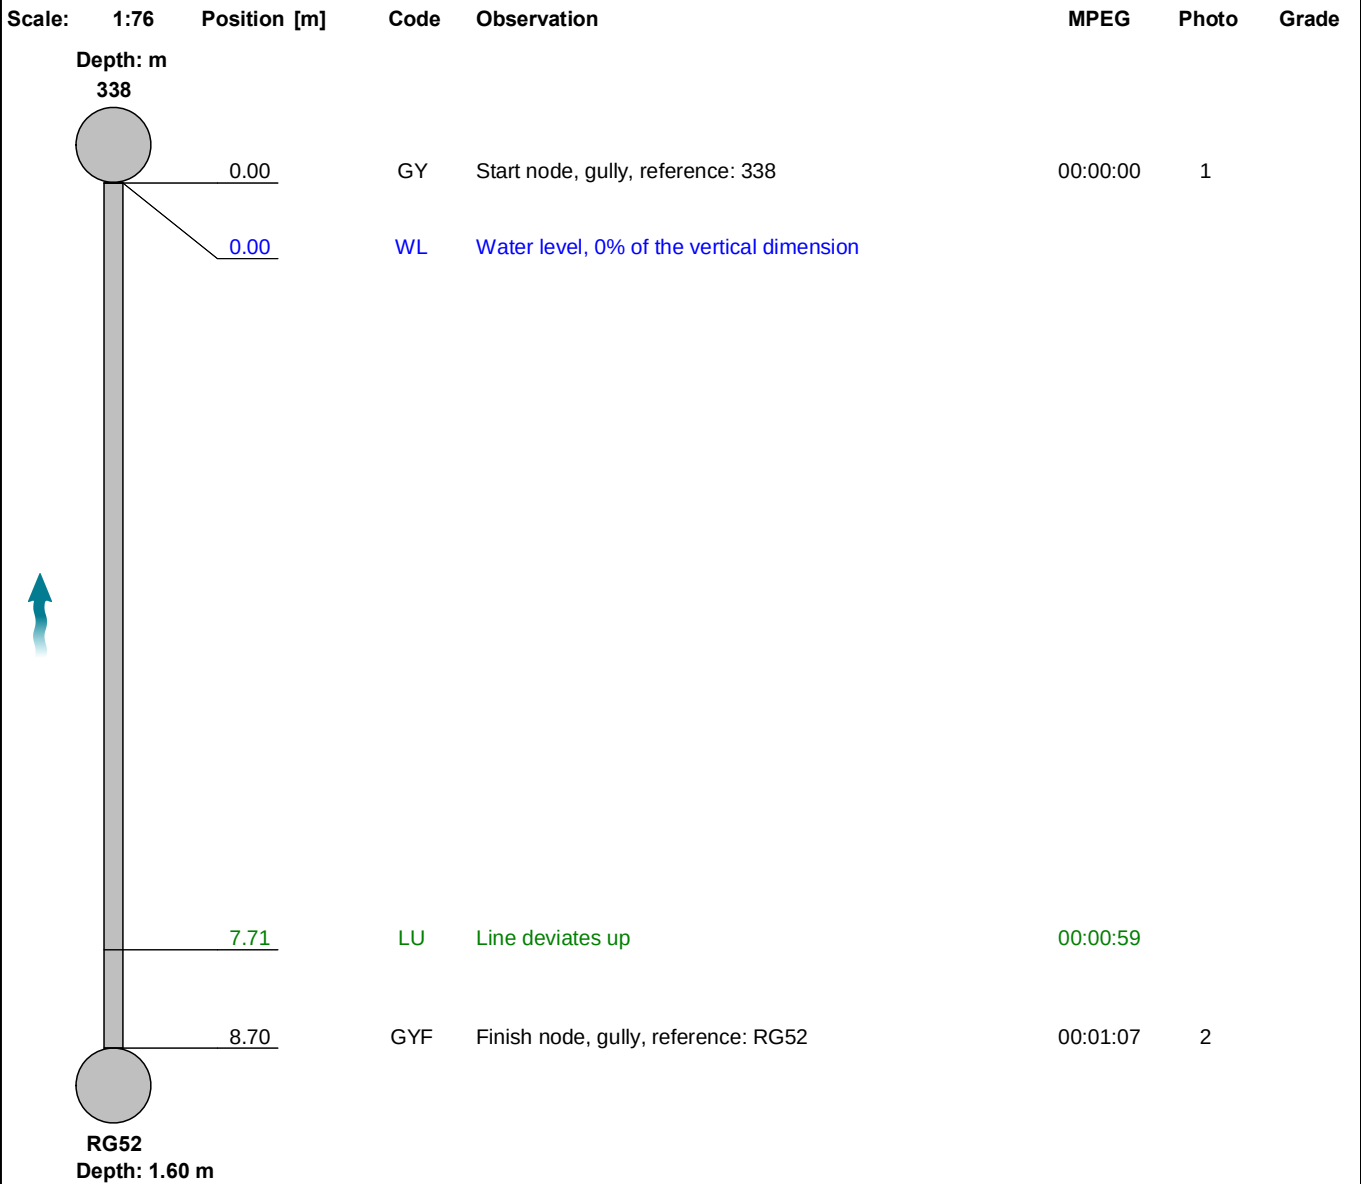

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG52X


Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
69	Upstream	RG52X		



1, 00:00:00, 0.00 m
Start node, gully, reference: 338



2, 00:01:07, 8.70 m
Finish node, gully, reference: RG52



Section Inspection - 17/11/2025 - RG51X

Item No. 70	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG51X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RG51
Road:	Langmead Place	Inspected Length:	6.72 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	6.72 m	Downstream Node:	338
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.800 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

Scale:	1:59	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: 1.80 m 338 0.00 0.00 5.95 6.72 RG51 Depth: m							
		0.00	MH	Start node, manhole, reference: 338	00:00:00	1	
		0.00	WL	Water level, 30% of the vertical dimension			
		5.95	LU	Line deviates up	00:00:31		
		6.72	GYF	Finish node, gully, reference: RG51	00:00:40	2	

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG51X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
70	Upstream	RG51X		



1, 00:00:00, 0.00 m
Start node, manhole, reference: 338



2, 00:00:40, 6.72 m
Finish node, gully, reference: RG51



Item No. 71	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG65X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Comments:	
Recommendations:	

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG65X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
71	Downstream	RG65X		




1, 00:00:00, 0.00 m
Start node, gully, reference: RG65



2, 00:00:10, 1.53 m
Point repair, localised lining from 12 o'clock to 11 o'clock, start



3, 00:00:23, 8.54 m
Finish node, manhole, reference: 261




Section Inspection - 17/11/2025 - RG54X

Item No. 72	Insp. No. 1	Date 17/11/25	Time 8:19	Client's Job Ref Not Specified	Weather No Rain Or Snow	Pre Cleaned Yes	PLR RG54X
Operator C.Blogg		Vehicle [REDACTED]		Camera Pushrod	Preset Length Not Specified	Legal Status Highways Drainage	Alternative ID Not Specified

Town or Village:	Angmering	Inspection Direction:	Upstream	Upstream Node:	RG54
Road:	Langmead Place	Inspected Length:	11.47 m	Upstream Pipe Depth:	
Location:	Road	Total Length:	11.47 m	Downstream Node:	337
Surface Type:		Joint Length:		Downstream Pipe Depth:	1.600 m
Use:	Surface water	Pipe Shape:	Circular		
Type of Pipe:	Gravity drain/sewer	Dia/Height:	150 mm		
Flow Control:	No flow control	Material:	Polyvinyl chloride		
Year Constructed:	Not Specified	Lining Type:	No Lining		
Inspection Purpose:	Routine inspection	Lining Material:	No Lining		

Comments:

Recommendations:

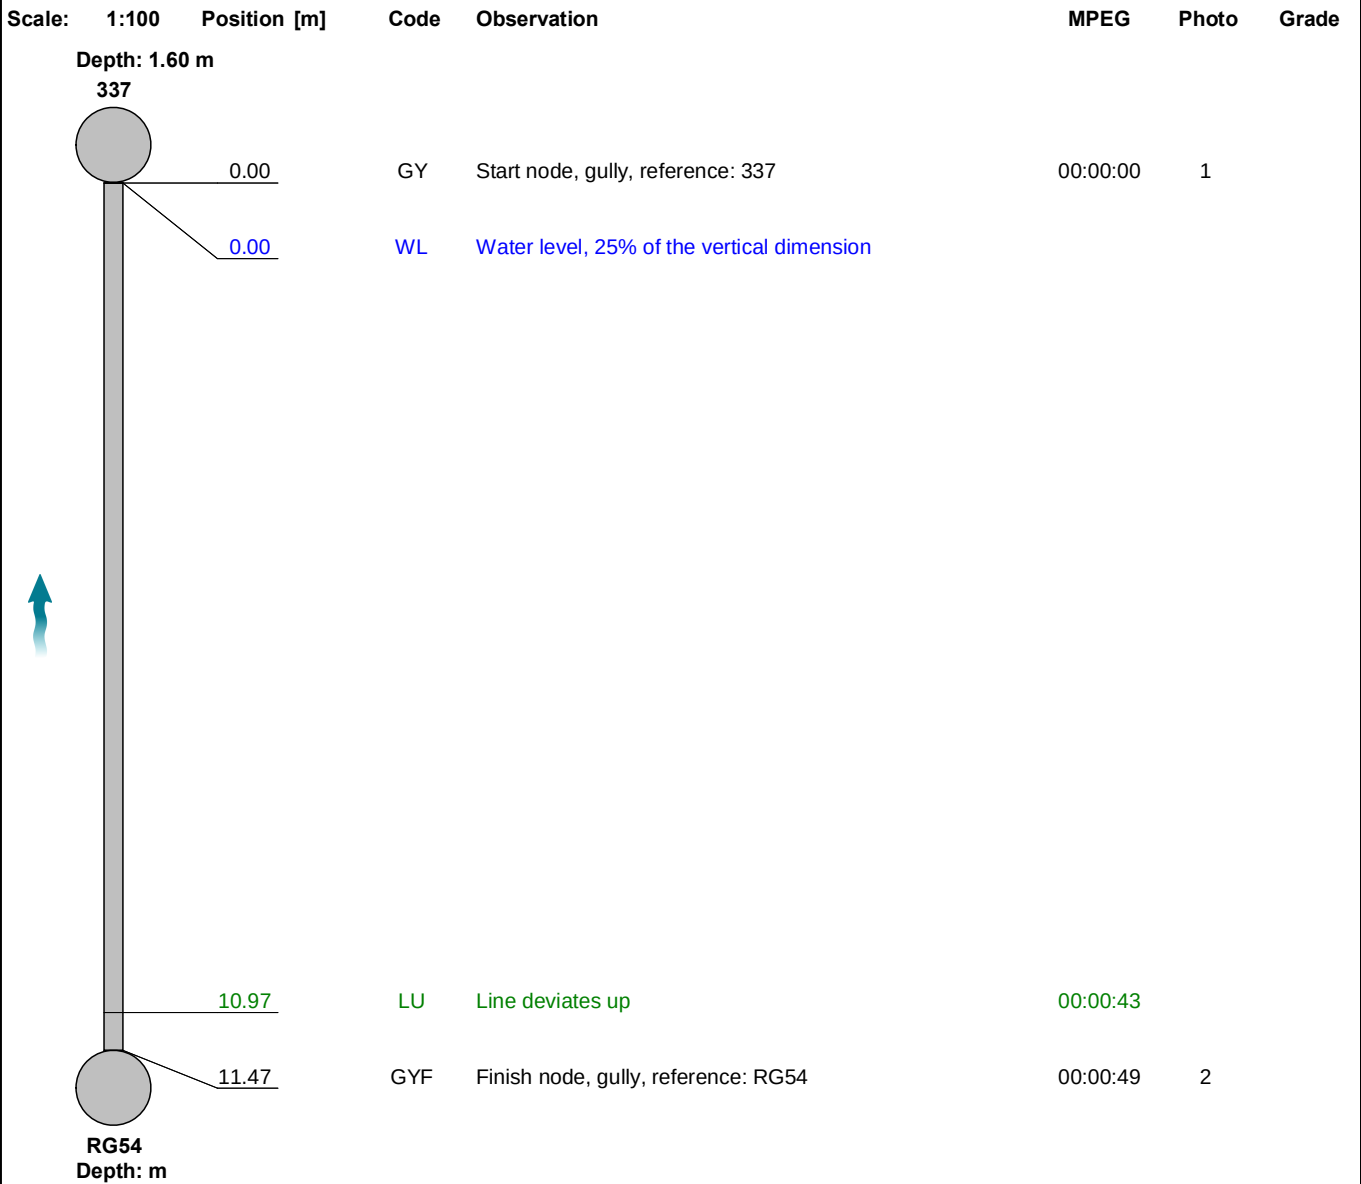

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Pictures - 17/11/2025 - RG54X

Item No.	Inspection Direction	PLR	Client's Job Ref	Contractor's Job Ref
72	Upstream	RG54X		



1, 00:00:00, 0.00 m
Start node, gully, reference: 337



2, 00:00:49, 11.47 m
Finish node, gully, reference: RG54
