




Advice taken from a TPO-Registered Tree Surgeon 13/12/14:

A	Holly – No action necessary	E	Corsican Pine - Reduction removing 1.2metres and a branch overhanging the road. Height after pruning 4.5metres, spread 4.5metres
B	Cherry – Remove one branch to balance it. Non-TPO tree*	F	Holm Oak – No action necessary
C	Horse Chestnut – No action necessary. Non-TPO tree*	G	a) Willow – Non-TPO*. Remove and replace with liquid amber maple** b) Willow – Reduction by 1.2metres. After pruning height 5.5metres, spread 9.1metres. If neighbouring willow (a) is removed, willow (b) will have a better shape
D	Corsican Pine – Reduction removing 1.2metres and a branch overhanging the road. Height after pruning 7.6metres, spread 7.6metres	H	Pine – No action necessary

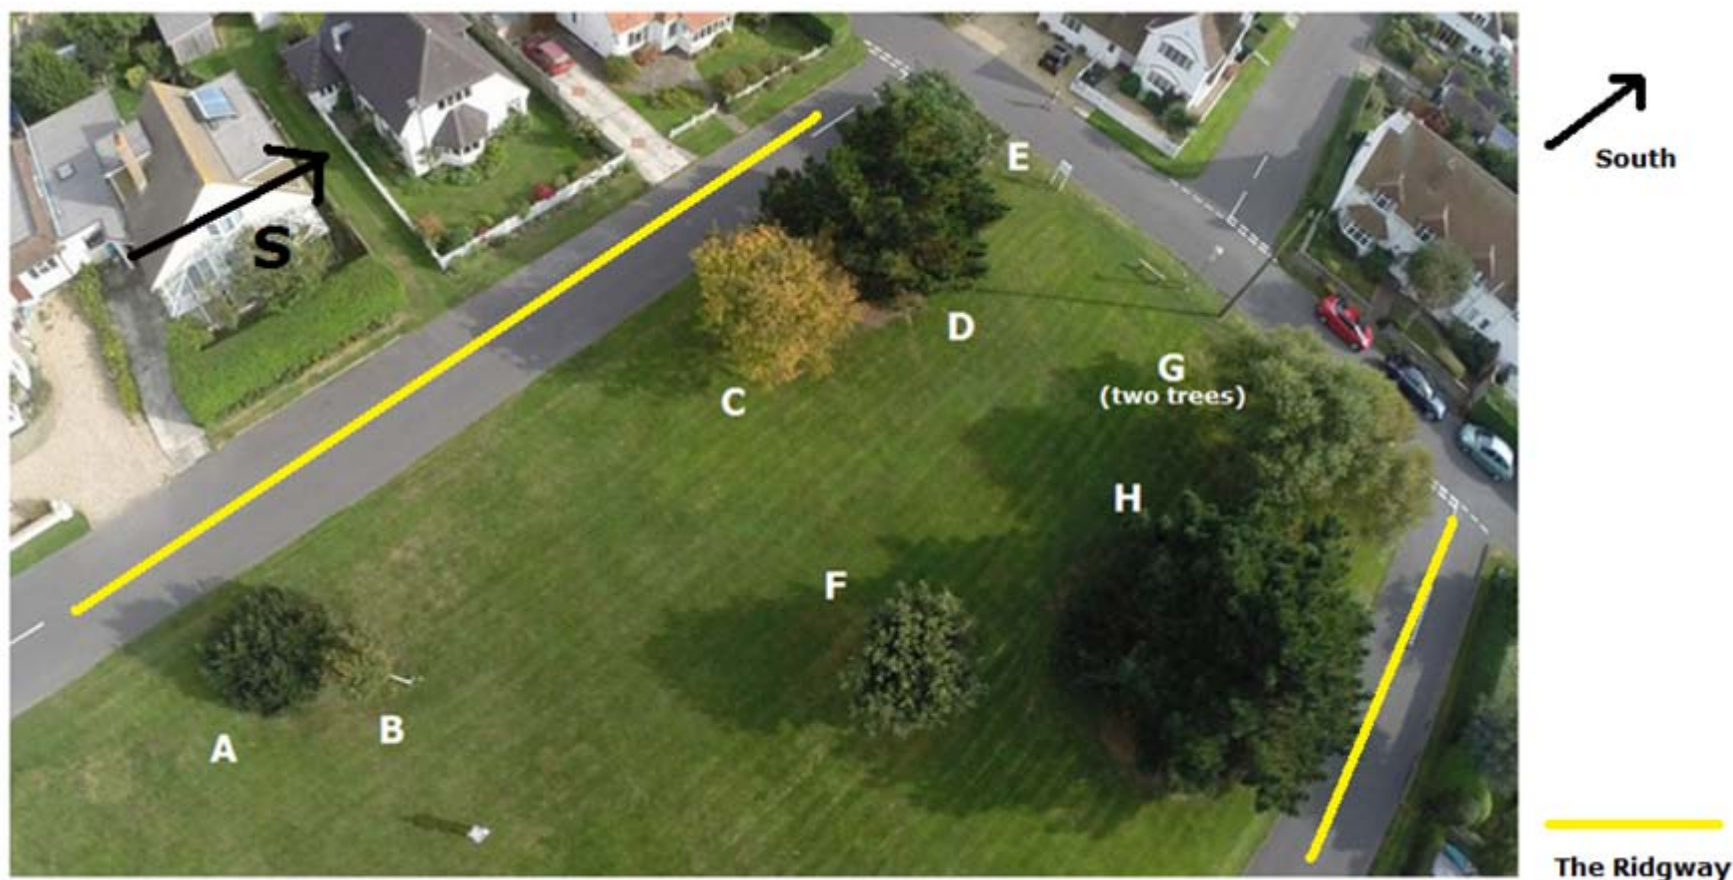

I	Hawthorne – Non-TPO*. Crown lift 2metres and reduction. Height after pruning 3.6metres, spread 3metres. Risk of eye damage to pedestrians
J	Holm Oak – Crown lift by 2metres and reduction 25%. Height after pruning 4.5metres, spread 9.1metres. Phone line entangled with branches
K	Corsican pine – Reduction by 2metres on road side. Height after pruning 3.6metres, spread 9.1metres
L	White poplar – Remove one branch overhanging road by 1.5metres

* Please confirm these trees are non-TPO ** Or similar (to be agreed by residents)
