

Location of trees, categorisation & protection/management proposals

Ford Airfield, Yapton Road, Ford, Yapton,
West Sussex



Barrell Plan Ref: 24053-15-RM1

Client Plan Refs:
Topo (May-01-2024) 32809 R1.dwg
Layout (2024-12-13) 180641_TOR-RMN1-MP-P004 Rev A



Permission is granted to scale from this drawing for Local Authority Planning Approval purposes relating to tree protection measures only. Where applicable this drawing is to be read in conjunction with the arboricultural report. This drawing is the copyright of Barrell Tree Consultancy 2024 ©

This drawing to be reproduced in colour only.
www.barrelltreecare.co.uk

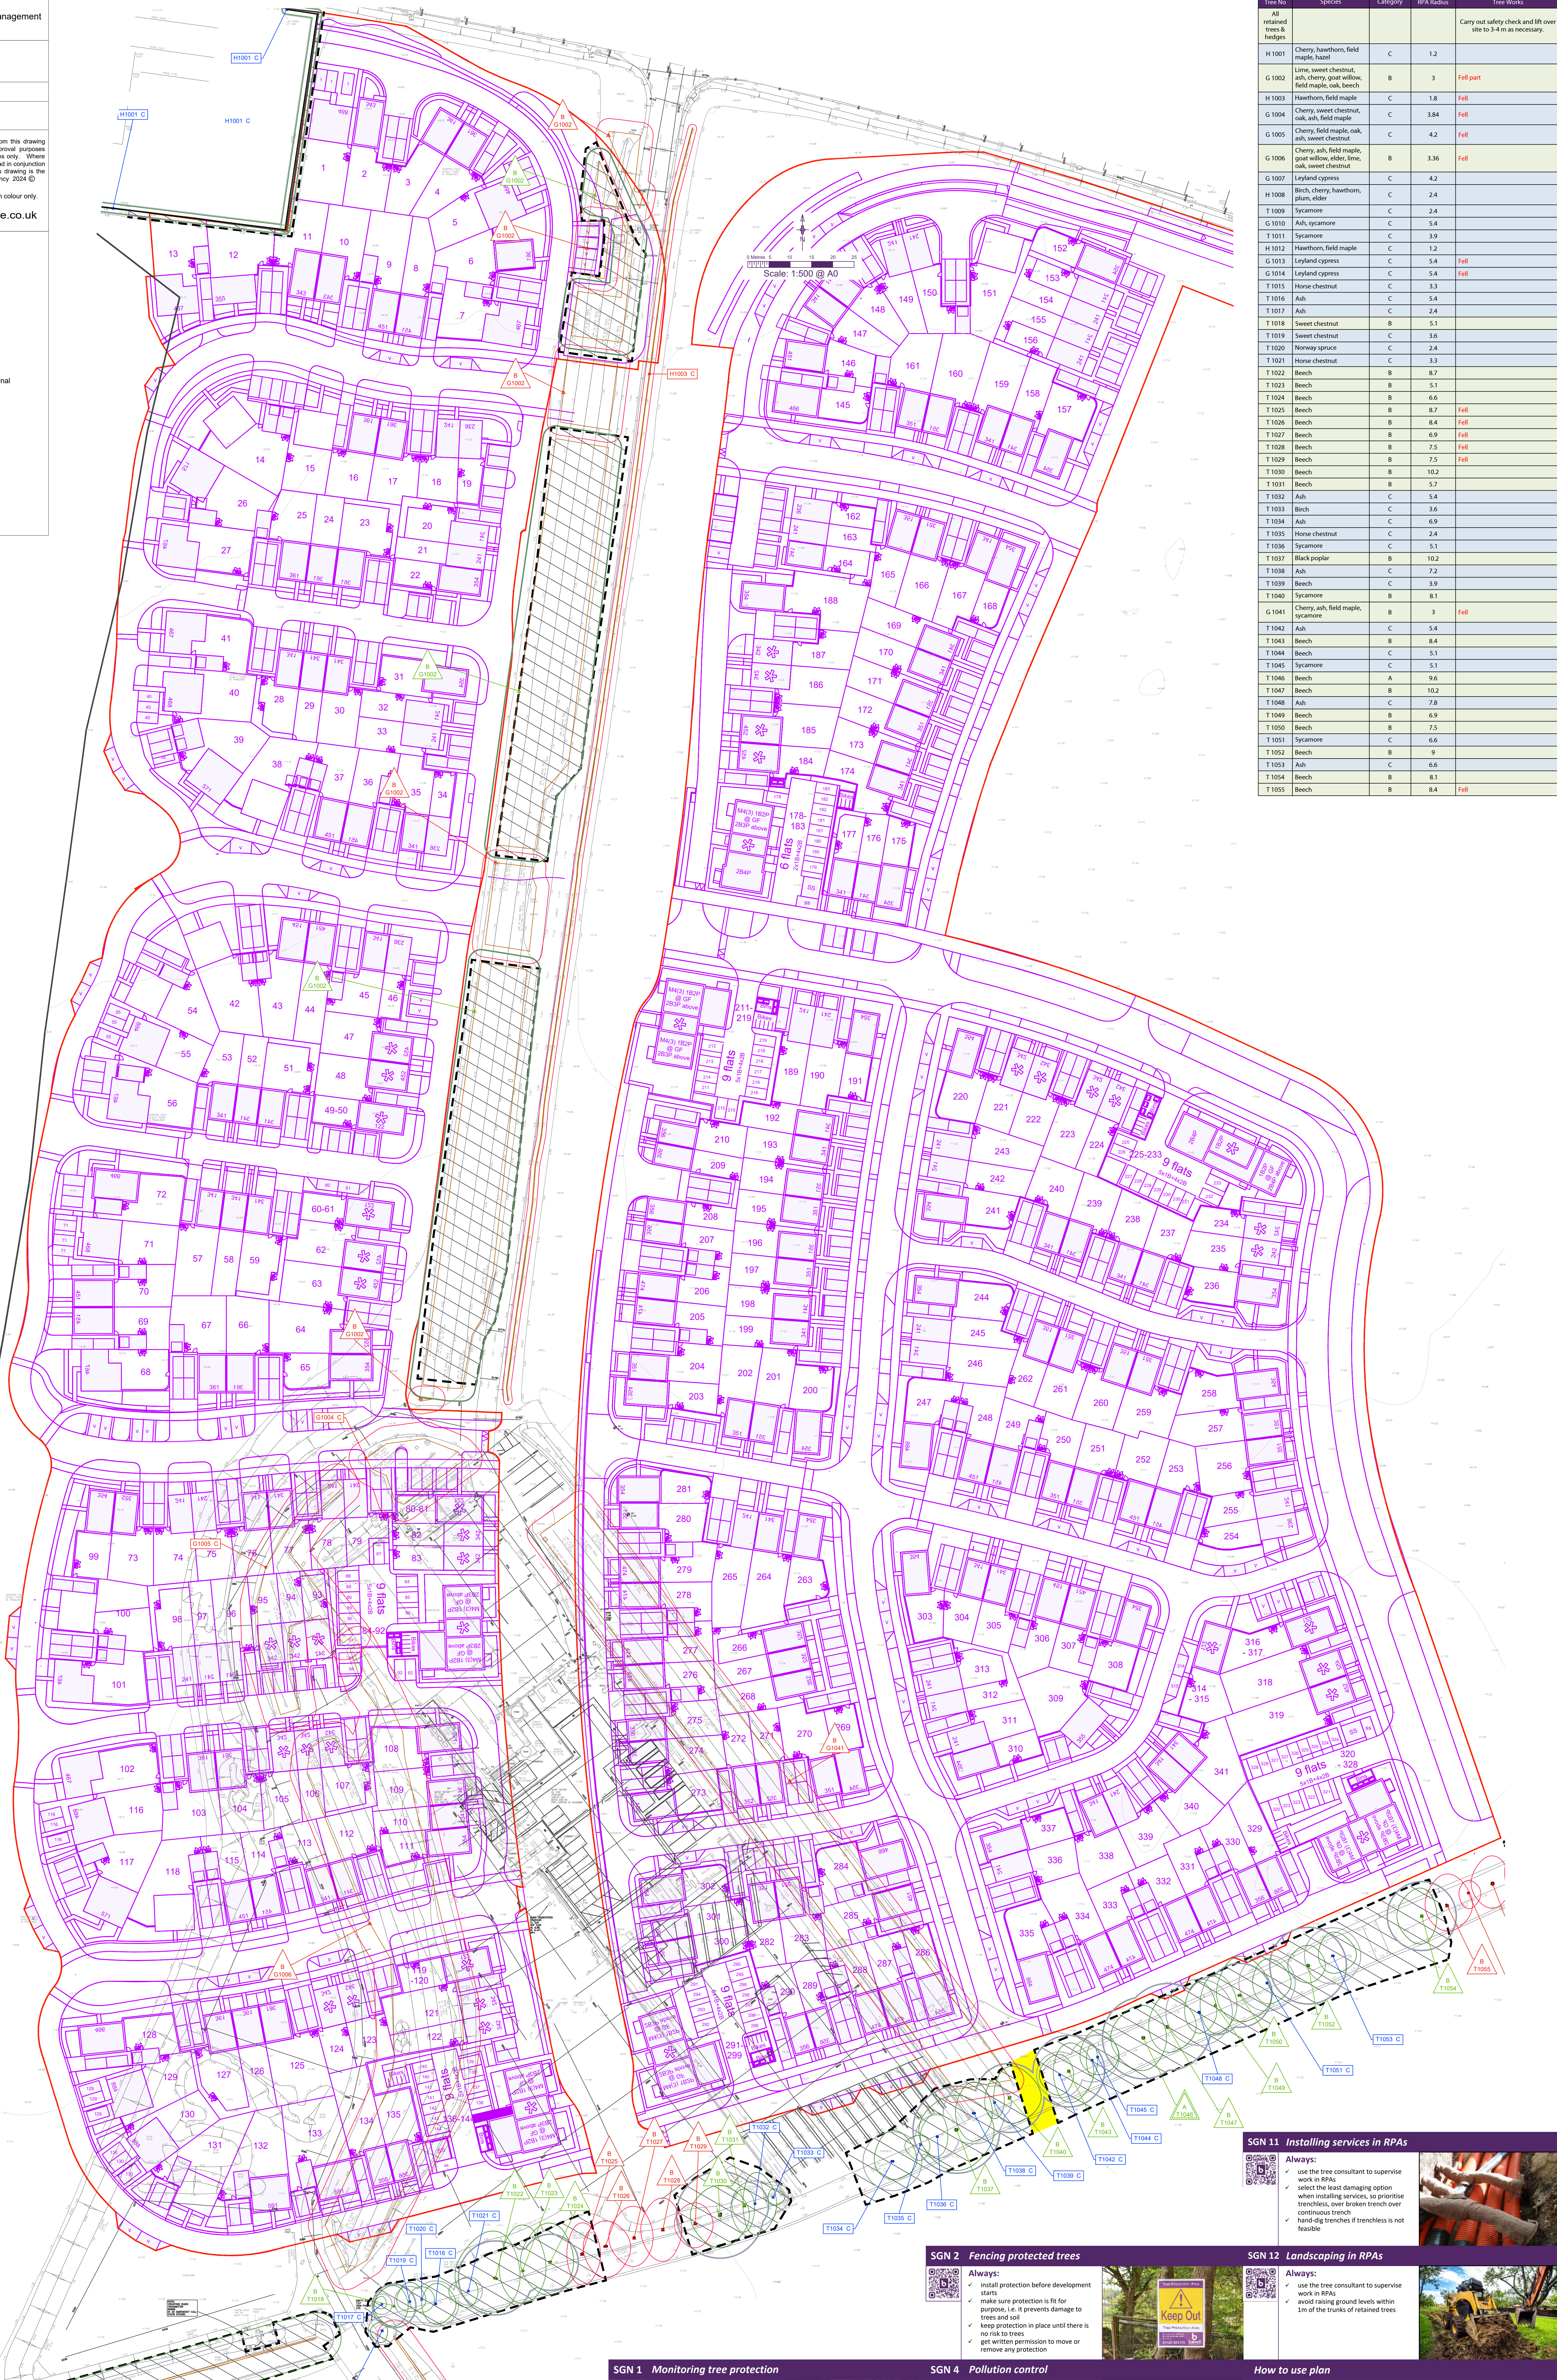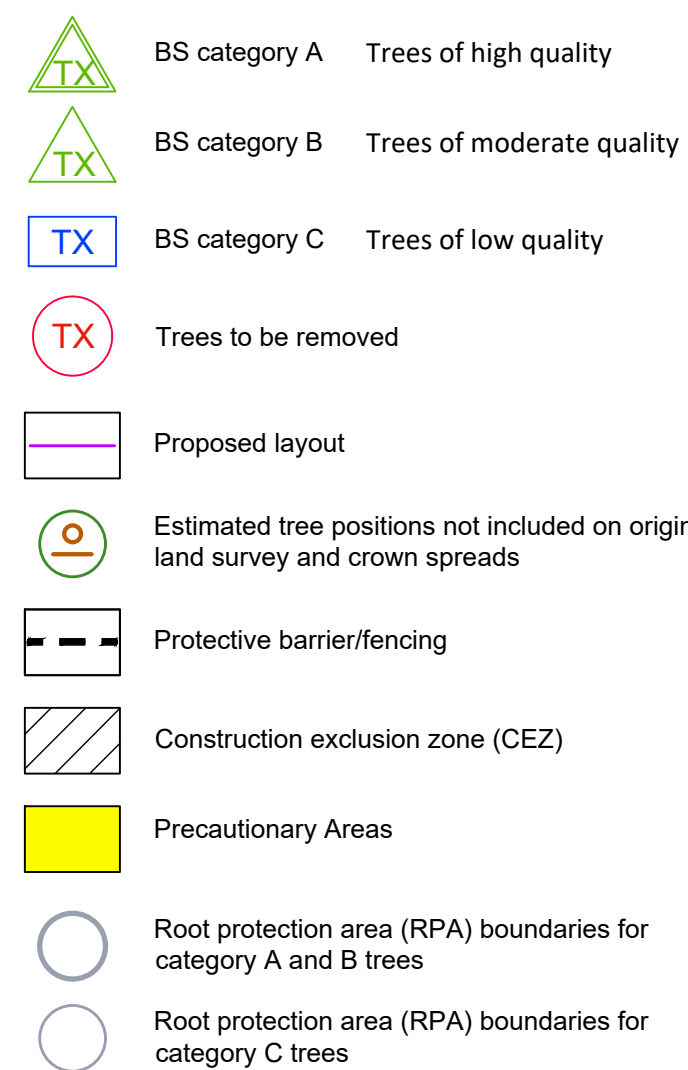

Tree No	Species	Category	BP/Radius	Tree Works
All retained trees & hedgins				Carry out safety check and lift over site to 3-4 m in an necessary
H 1001	Cherry, hawthorn, field maple, hazel	C	1.2	
G 1002	Lime, sweet chestnut, ash, cherry, goat willow, field maple, oak, beech	B	3	Fell part
H 1003	Hawthorn, field maple	C	1.8	Fell
G 1004	Cherry, sweet chestnut, oak, ash, field maple	C	3.84	Fell
G 1005	Cherry, field maple, oak, ash, sweet chestnut	C	4.2	Fell
G 1006	Cherry, ash, field maple, goat willow, elder, lime, oak, sweet chestnut	B	3.36	Fell
G 1007	Lyland cypress	C	4.2	
H 1008	Birch, cherry, hawthorn, plum, elder	C	2.4	
T 1009	Sycamore	C	2.4	
G 1010	Ash, sycamore	C	5.4	
T 1011	Hawthorn	C	3.9	
H 1012	Sycamore, field maple	C	1.2	
G 1013	Lyland cypress	C	5.4	Fell
G 1014	Lyland cypress	C	5.4	Fell
T 1015	Horse chestnut	C	3.3	
T 1016	Ash	C	5.4	
T 1017	Ash	C	2.4	
T 1018	Sweet chestnut	B	5.1	
T 1019	Sweet chestnut	C	3.6	
T 1020	Norway spruce	C	2.4	
T 1021	Horse chestnut	C	3.3	
T 1022	Beech	B	8.7	
T 1023	Beech	B	5.1	
T 1024	Beech	B	6.6	
T 1025	Beech	B	8.7	Fell
T 1026	Beech	B	8.4	Fell
T 1027	Beech	B	6.9	Fell
T 1028	Beech	B	7.5	Fell
T 1029	Beech	B	7.5	Fell
T 1030	Beech	B	10.2	
T 1031	Beech	B	5.7	
T 1032	Ash	C	5.4	
T 1033	Beech	C	3.6	
T 1034	Ash	C	6.9	
T 1035	Horse chestnut	C	2.4	
T 1036	Sycamore	C	5.1	
T 1037	Black poplar	B	10.2	
T 1038	Ash	C	7.2	
T 1039	Beech	C	3.9	
T 1040	Sycamore	B	8.1	
G 1041	Cherry, ash, field maple, sycamore	B	3	Fell
T 1042	Ash	C	5.4	
T 1043	Beech	B	8.4	
T 1044	Beech	C	5.1	
T 1045	Sycamore	C	5.1	
T 1046	Beech	A	9.6	
T 1047	Beech	B	10.2	
T 1048	Ash	C	7.8	
T 1049	Beech	B	6.9	
T 1050	Beech	B	7.5	
T 1051	Sycamore	C	6.6	
T 1052	Beech	B	9	
T 1053	Ash	C	6.6	
T 1054	Beech	B	8.1	
T 1055	Beech	B	8.4	Fell

SGN 1 *Monitoring tree protection*



Always:

- ✓ have a pre-commencement meeting with the tree consultant before development starts
- ✓ use the tree consultant to regularly check that protection remains fit for purpose
- ✓ use the tree consultant to supervise work in RPAs
- ✓ keep a written record of supervision



SGN 4 Pollution control



Always:

- ✓ keep toxic products away from RPAs



SGN 12 Landscaping in RPAs



Always:

- ✓ use the tree consultant to supervise work in RPAs
- ✓ avoid raising ground levels within 1m of the trunks of retained trees



SGN 11 *Installing services in RPAs*



Always:

- ✓ use the tree consultant to supervise work in RPAs
- ✓ select the least damaging option when installing services, so prioritise trenchless, over broken trench over continuous trench
- ✓ hand-dig trenches if trenchless is not feasible



How to use plan

More detailed guidance on each Site Guidance Note (SGN) can be found in a printed hard copy compilation of all the SGNs, **Manual for Managing Trees On Development Sites version 3.0**, issued to the project manager at the pre-commencement site meeting. (This should be retained on site throughout the duration of works). Additionally, an electronic pdf compilation of all the SGNs, was submitted with this drawing to the local planning authority and the client. Alternatively, a pdf of each SGN can be downloaded by:

1. clicking the image links in the electronic pdf version of this plan;
2. clicking a mobile phone QR (Quick Response) code reader over the QR code in the paper version of this plan; or,
3. visiting our website at www.borrelltreecare.co.uk/resources/technical-guidance
