

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
1	1	50	100
1	2	50	150
0	2	50	200
1	3	50	250
0	3	50	300
2	5	50	350
7	12	50	400
9	21	50	450
9	30	50	500
6	36	50	550
6	42	50	600
5	47	50	650
4	51	50	700
6	57	50	750
5	62	50	800
7	69	50	850
9	78	50	900


North Littlehampton Test Reference: - DCP10

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	300	0	3	83.3	2.8	1.5	1.5
300	350	3	5	25.0	10.1	7.0	7.0
350	500	5	30	6.0	45.4	43.2	43.2
500	700	30	51	9.5	27.9	23.9	23.9
700	900	51	78	7.4	36.4	33.0	33.0

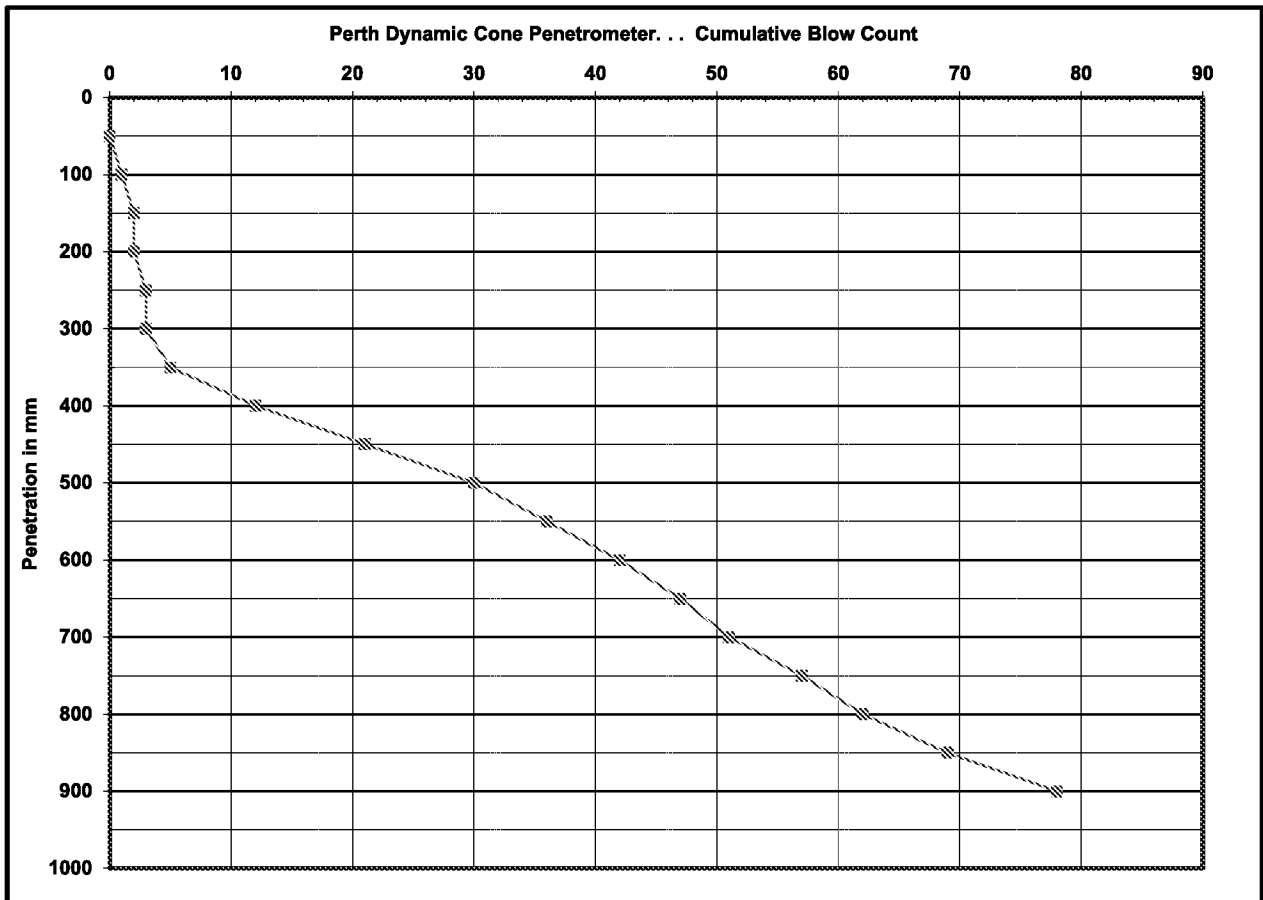

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP10

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
1	1	50	100
0	1	50	150
1	2	50	200
2	4	50	250
6	10	50	300
6	16	50	350
7	23	50	400
5	28	50	450
9	37	50	500
7	44	50	550
11	55	50	600
9	64	50	650
9	73	50	700
5	78	50	750
11	89	50	800
12	101	50	850
13	114	50	900


North Littlehampton Test Reference: - DCPI I

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	250	0	4	50.0	4.8	2.9	2.9
250	700	4	73	6.5	41.6	38.9	38.9
700	750	73	78	10.0	26.5	22.5	22.5
750	900	78	114	4.2	66.8	69.0	66.8

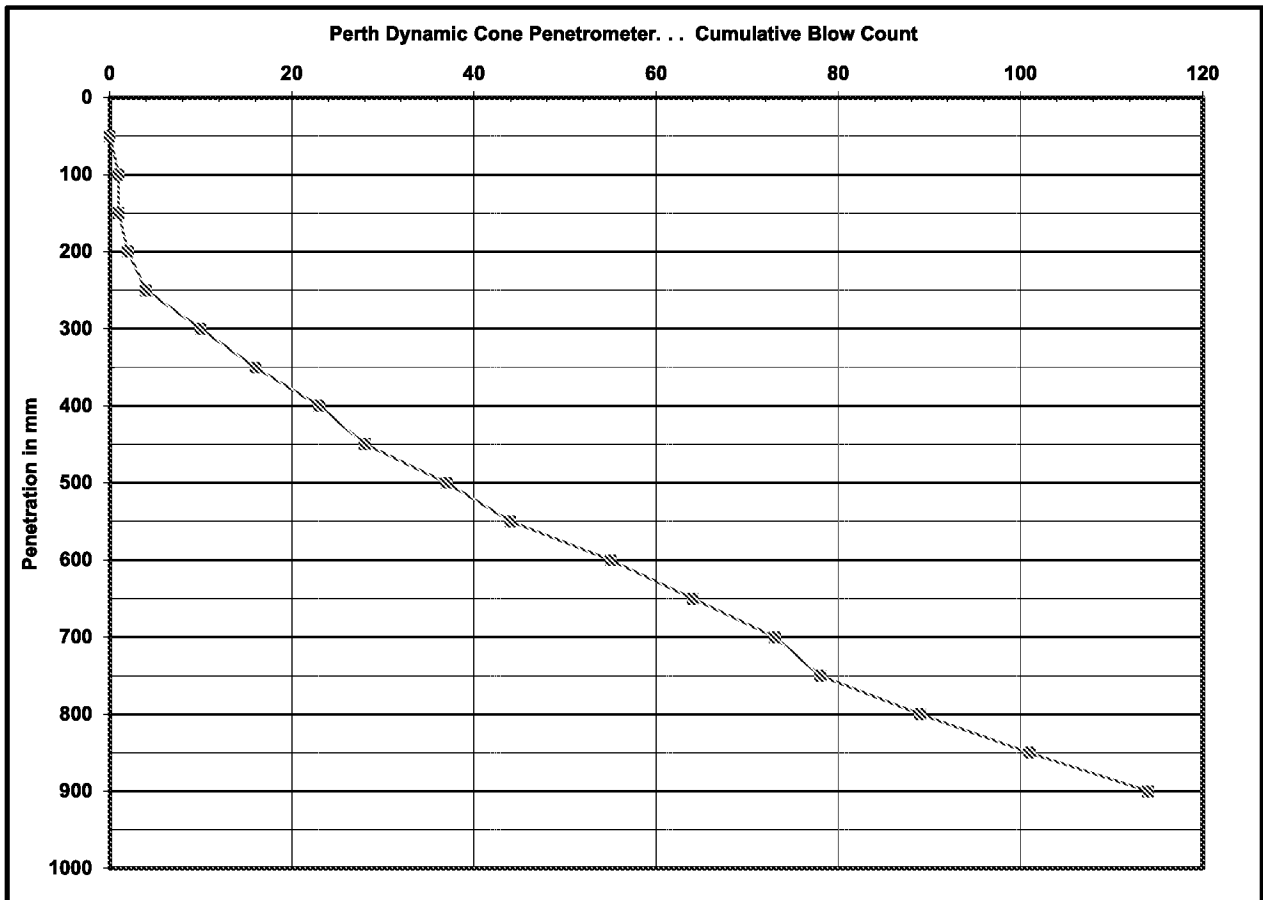

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCPI I

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
1	1	50	100
2	3	50	150
1	4	50	200
1	5	50	250
1	6	50	300
1	7	50	350
2	9	50	400
5	14	50	450
6	20	50	500
8	28	50	550
8	36	50	600
8	44	50	650
13	57	50	700
8	65	50	750
7	72	50	800
7	79	50	850
6	85	50	900


North Littlehampton Test Reference: - DCPI2

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	150	0	3	33.3	7.4	4.8	4.8
150	400	3	9	41.7	5.9	3.6	3.6
400	650	9	44	7.1	37.8	34.6	34.6
650	700	44	57	3.8	72.7	76.4	72.7
700	900	57	85	7.1	37.8	34.6	34.6

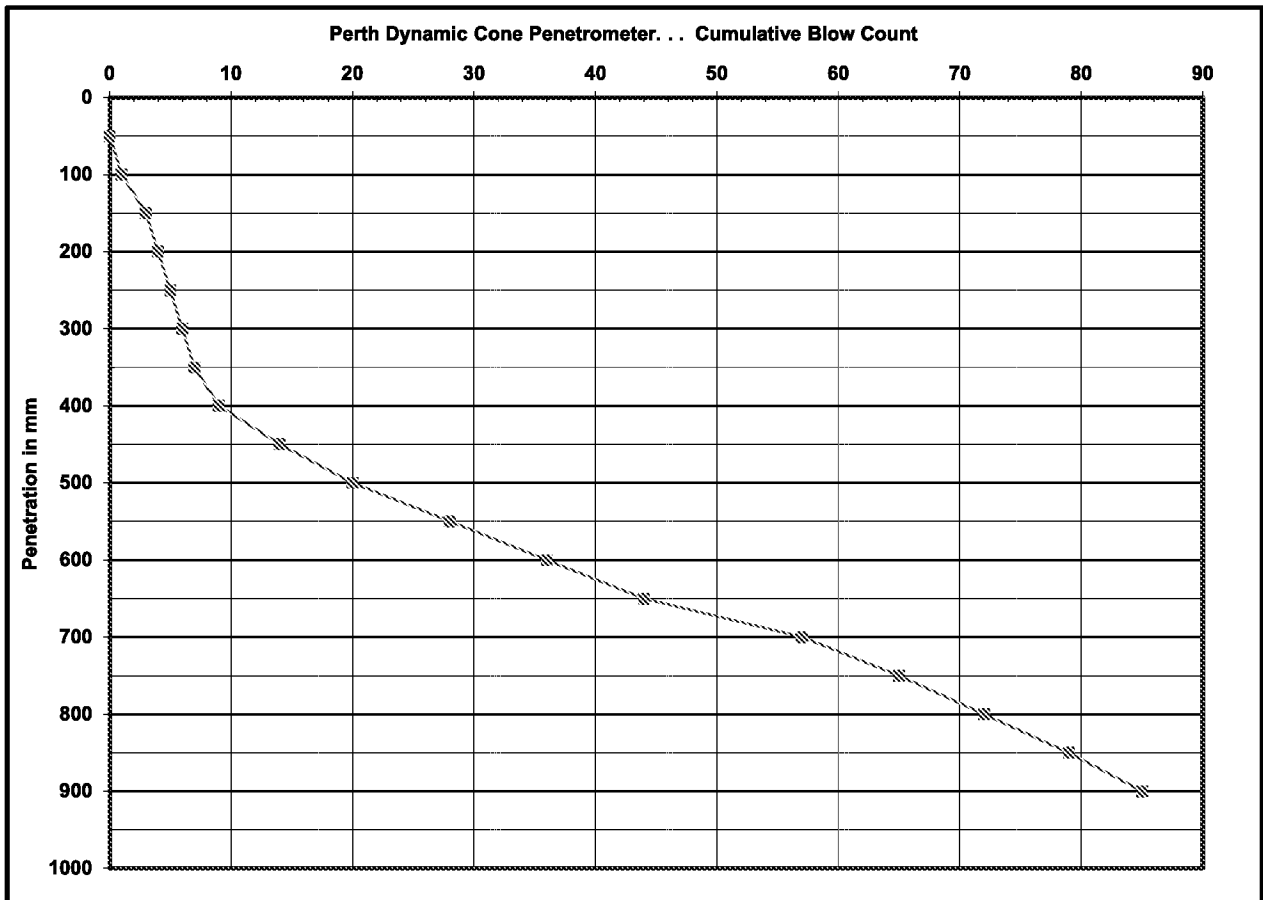

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCPI2

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
1	1	50	100
1	2	50	150
1	3	50	200
1	4	50	250
1	5	50	300
1	6	50	350
3	9	50	400
11	20	50	450
16	36	50	500
15	51	50	550
14	65	50	600
11	76	50	650
10	86	50	700
9	95	50	750
9	104	50	800
8	112	50	850
8	120	50	900


North Littlehampton Test Reference: - DCPI3

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	350	0	6	50.0	4.8	2.9	2.9
350	400	6	9	16.7	15.4	11.7	11.7
400	600	9	65	3.6	78.6	84.0	78.6
600	900	65	120	5.5	50.3	48.9	48.9

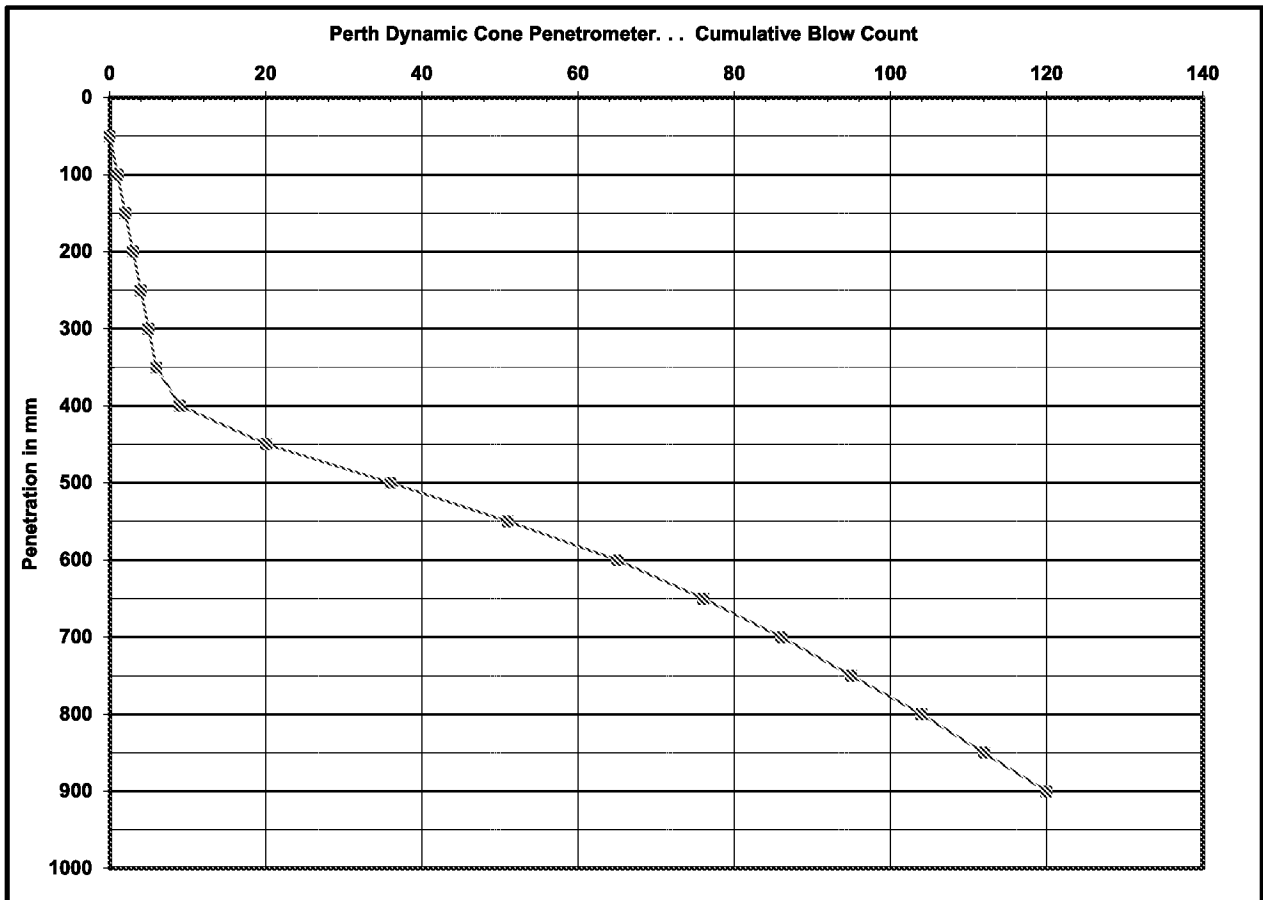

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCPI3

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
1	1	50	100
1	2	50	150
2	4	50	200
1	5	50	250
1	6	50	300
1	7	50	350
6	13	50	400
10	23	50	450
11	34	50	500
10	44	50	550
9	53	50	600
9	62	50	650
7	69	50	700
9	78	50	750
9	87	50	800
8	95	50	850
7	102	50	900


North Littlehampton Test Reference: - DCPI4

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	350	0	7	42.9	5.7	3.5	3.5
350	400	7	13	8.3	32.1	28.4	28.4
400	650	13	62	5.1	53.9	53.2	53.2
650	900	62	102	6.3	43.5	41.0	41.0

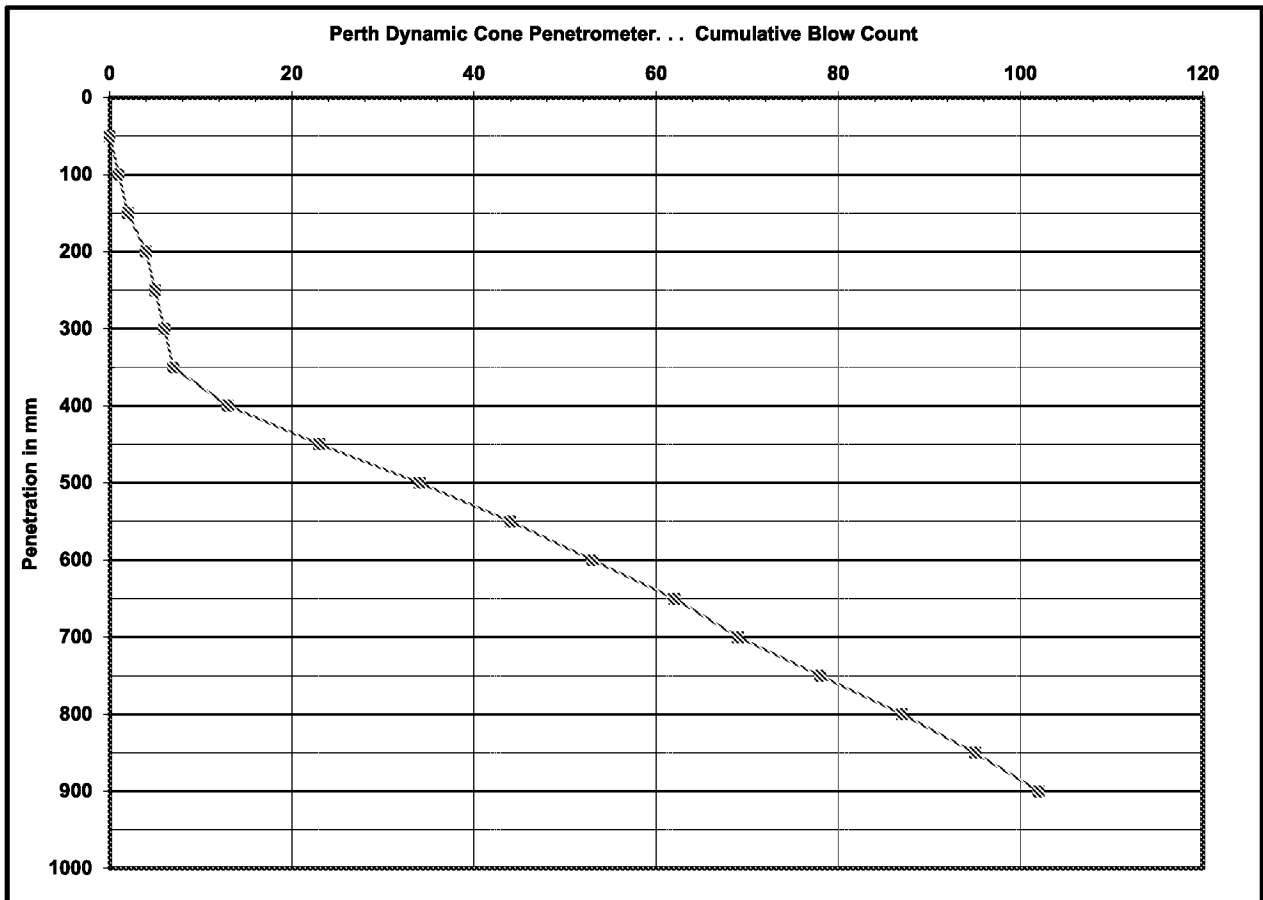

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCPI4

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
1	1	50	100
1	2	50	150
1	3	50	200
1	4	50	250
1	5	50	300
1	6	50	350
1	7	50	400
2	9	50	450
3	12	50	500
3	15	50	550
5	20	50	600
5	25	50	650
4	29	50	700
4	33	50	750
2	35	50	800
1	36	50	850
1	37	50	900


North Littlehampton Test Reference: - DCP15

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	400	0	7	50.0	4.8	2.9	2.9
400	550	7	15	18.8	13.6	10.1	10.1
550	750	15	33	11.1	23.7	19.7	19.7
750	800	33	35	25.0	10.1	7.0	7.0
800	900	35	37	50.0	4.8	2.9	2.9

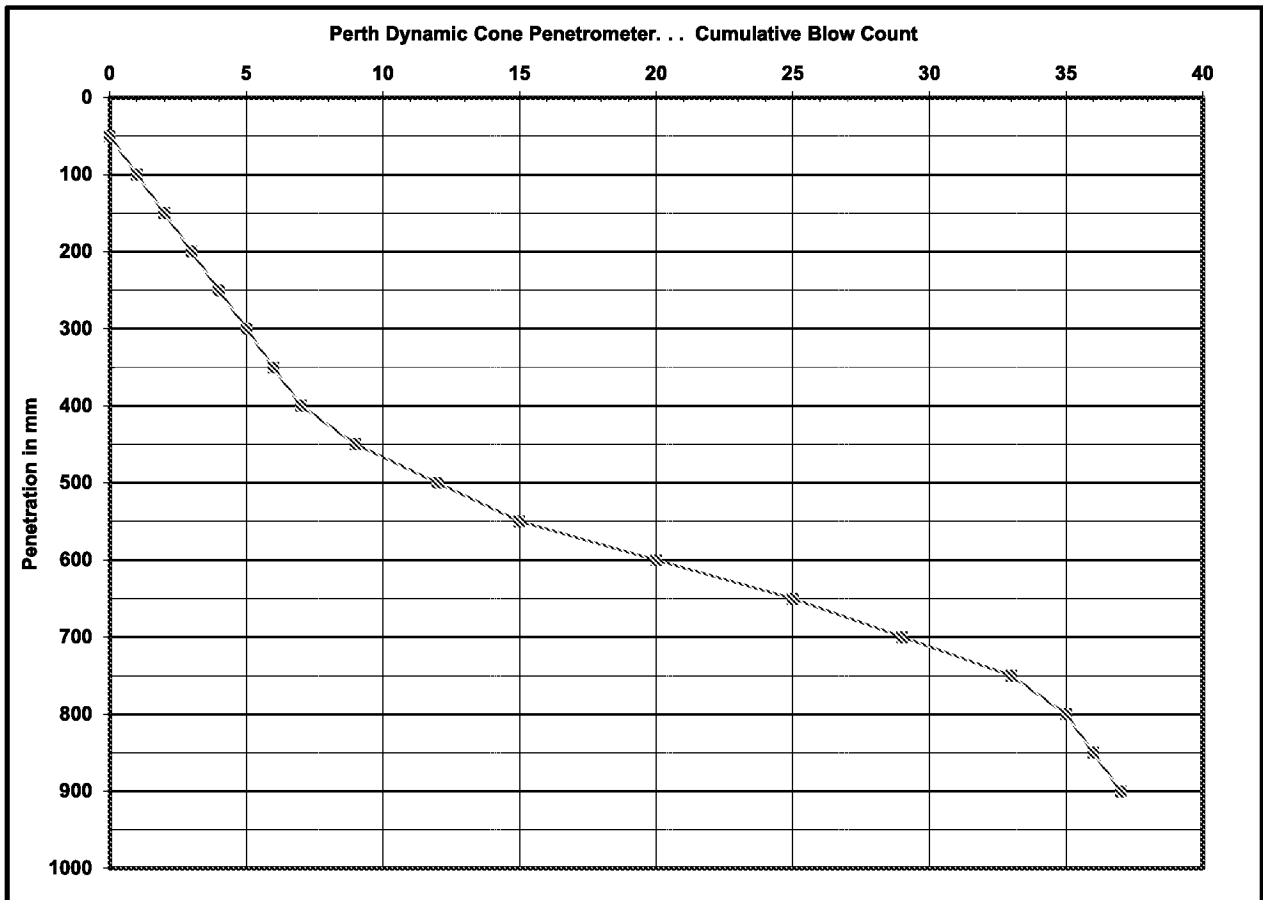

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP15

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
2	2	50	100
1	3	50	150
1	4	50	200
2	6	50	250
1	7	50	300
1	8	50	350
2	10	50	400
1	11	50	450
0	11	50	500
1	12	50	550
0	12	50	600
0	12	50	650
1	13	50	700
4	17	50	750
1	18	50	800
2	20	50	850
2	22	50	900


North Littlehampton Test Reference: - DCPI6

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	100	0	2	25.0	10.1	7.0	7.0
100	200	2	4	50.0	4.8	2.9	2.9
200	250	4	6	25.0	10.1	7.0	7.0
250	450	6	11	40.0	6.1	3.8	3.8
500	550	11	12	50.0	4.8	2.9	2.9
650	700	12	13	50	4.8	2.9	2.9
700	900	13	22	22.2	11.4	8.1	8.1

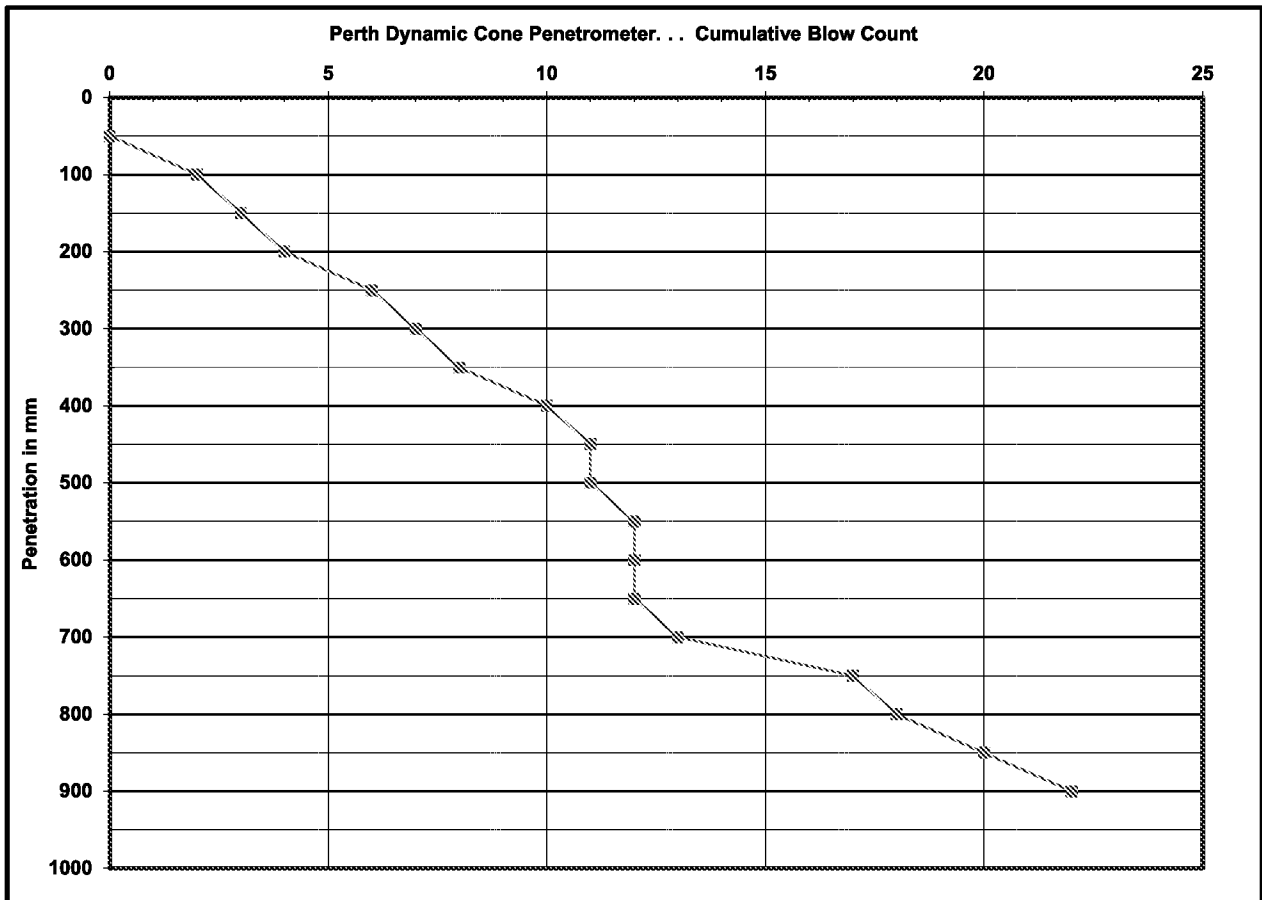

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCPI6

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
1	1	50	100
1	2	50	150
0	2	50	200
0	2	50	250
1	3	50	300
1	4	50	350
7	11	50	400
9	20	50	450
10	30	50	500
7	37	50	550
8	45	50	600
6	51	50	650
8	59	50	700
11	70	50	750
11	81	50	800
12	93	50	850
8	101	50	900


North Littlehampton Test Reference: - DCPI7

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	150	0	2	50.0	4.8	2.9	2.9
250	350	2	4	50.0	4.8	2.9	2.9
350	600	4	45	6.1	44.7	42.4	42.4
600	650	45	51	8.3	32.1	28.4	28.4
650	900	51	101	5.0	55.1	54.6	54.6

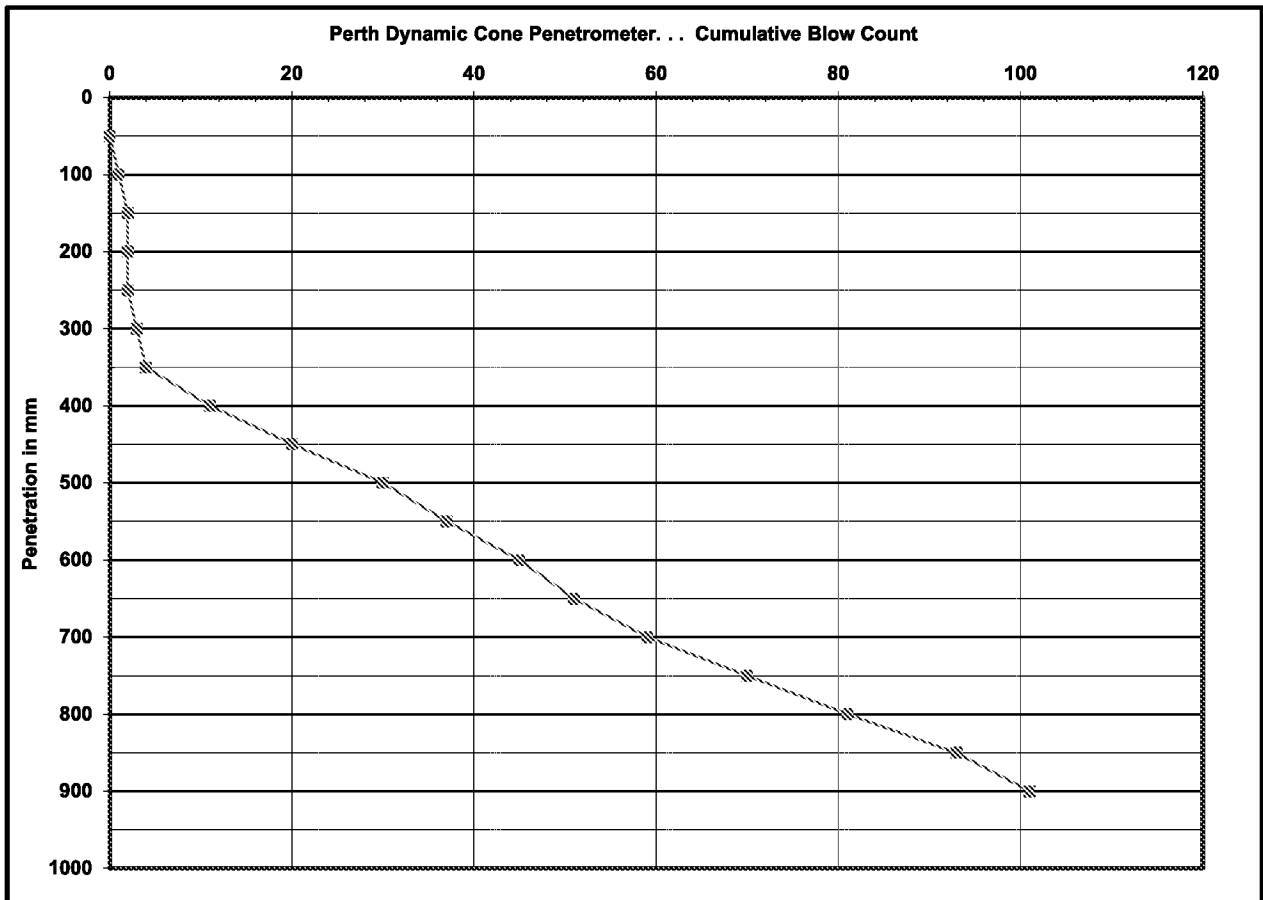

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCPI7

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
1	1	50	100
1	2	50	150
1	3	50	200
0	3	50	250
1	4	50	300
1	5	50	350
2	7	50	400
3	10	50	450
2	12	50	500
1	13	50	550
3	16	50	600
3	19	50	650
2	21	50	700
3	24	50	750
5	29	50	800
4	33	50	850
3	36	50	900


North Littlehampton Test Reference: - DCPI8

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	200	0	3	50.0	4.8	2.9	2.9
250	350	3	5	50.0	4.8	2.9	2.9
350	500	5	12	21.4	11.8	8.5	8.5
500	550	12	13	50.0	4.8	2.9	2.9
550	900	13	36	15.2	17.0	13.1	13.1

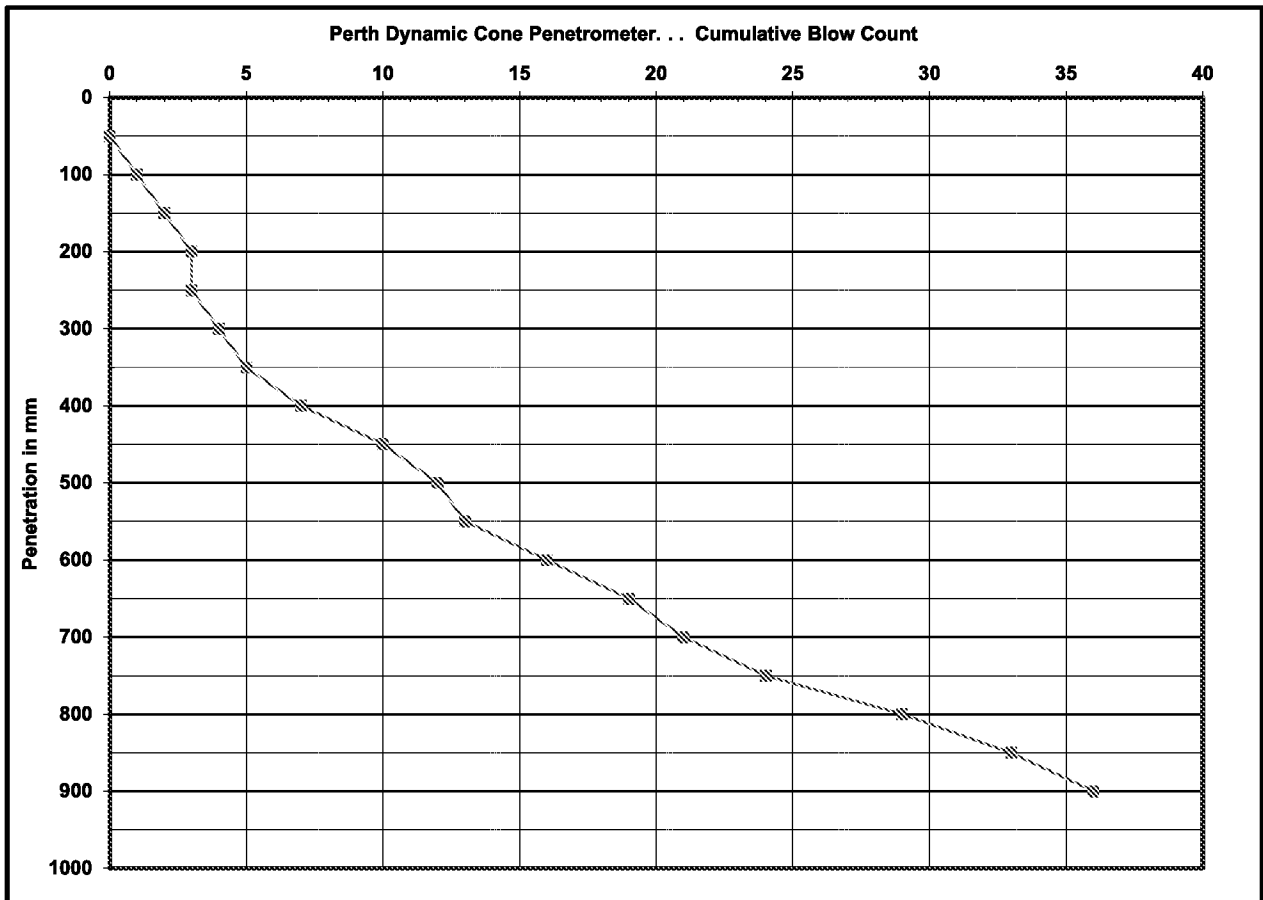

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCPI8

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
1	1	50	100
2	3	50	150
2	5	50	200
1	6	50	250
1	7	50	300
1	8	50	350
1	9	50	400
3	12	50	450
3	15	50	500
3	18	50	550
2	20	50	600
1	21	50	650
1	22	50	700
2	24	50	750
1	25	50	800
2	27	50	850
9	36	50	900


North Littlehampton Test Reference: - DCPI9

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	100	0	1	50.0	4.8	2.9	2.9
100	200	1	5	25.0	10.1	7.0	7.0
200	400	5	9	50.0	4.8	2.9	2.9
400	550	9	18	16.7	15.4	11.7	11.7
550	700	18	22	37.5	6.6	4.1	4.1
700	850	22	27	30	8.3	5.5	5.5
850	900	27	36	5.6	49.3	47.7	47.7

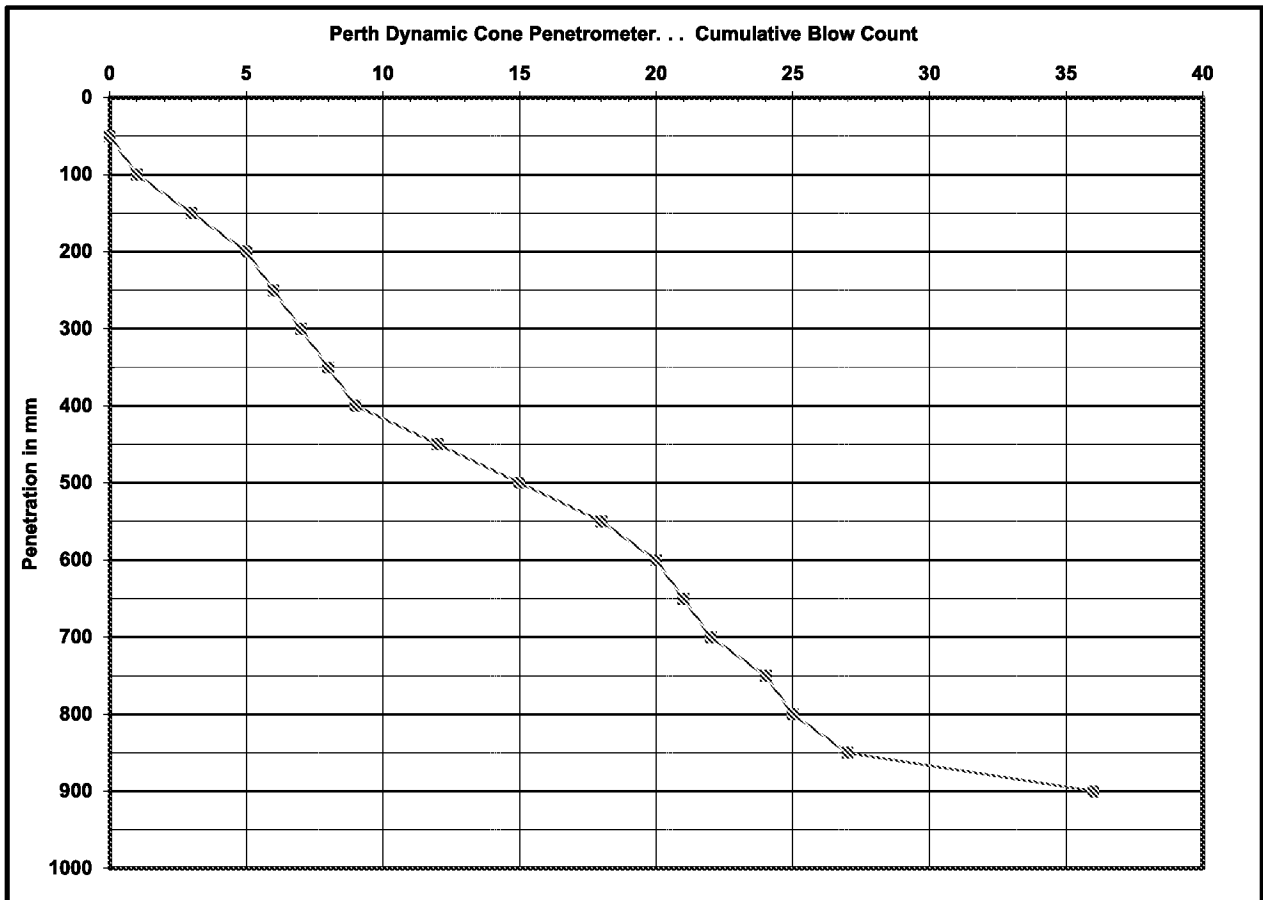

Tested by	OA	Checked	Approved
-----------	----	---------	----------

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCPI9

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
0	0	50	100
1	1	50	150
0	1	50	200
2	3	50	250
1	4	50	300
1	5	50	350
1	6	50	400
0	6	50	450
0	6	50	500
1	7	50	550
1	8	50	600
1	9	50	650
1	10	50	700
2	12	50	750
1	13	50	800
1	14	50	850
2	16	50	900


North Littlehampton Test Reference: - DCP20

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
100	150	0	1	50.0	4.8	2.9	2.9
200	250	1	3	25.0	10.1	7.0	7.0
250	400	3	6	50.0	4.8	2.9	2.9
500	700	6	10	50.0	4.8	2.9	2.9
700	750	10	12	25.0	10.1	7.0	7.0
750	900	12	16	37.5	6.6	4.1	4.1

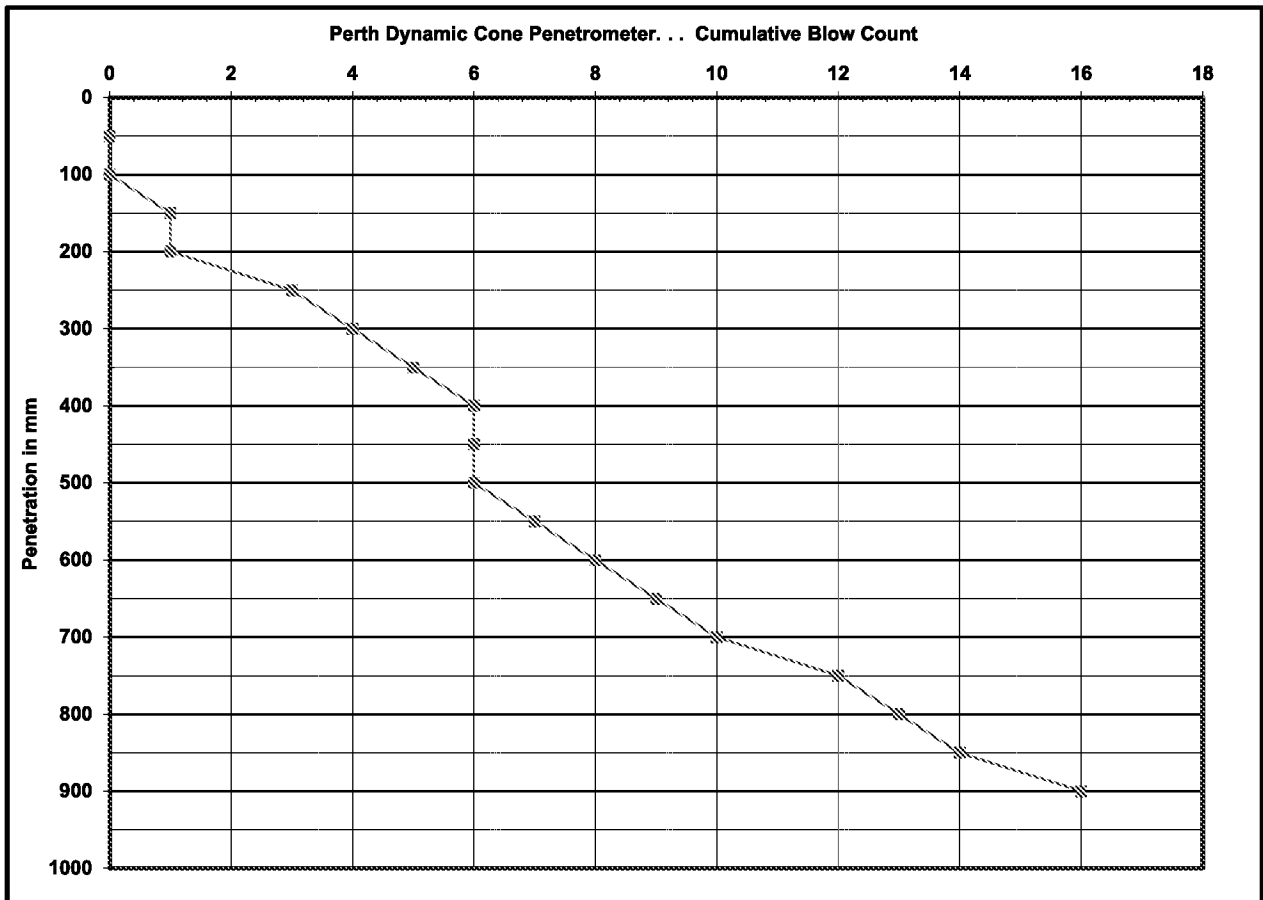

Tested by	OA	Checked	Approved
-----------	----	---------	----------

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP20

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
0	0	50	100
0	0	50	150
0	0	50	200
1	1	50	250
0	1	50	300
0	1	50	350
0	1	50	400
1	2	50	450
1	3	50	500
0	3	50	550
1	4	50	600
1	5	50	650
0	5	50	700
1	6	50	750
1	7	50	800
1	8	50	850
1	9	50	900


North Littlehampton Test Reference: - DCP21

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
200	250	0	1	50.0	4.8	2.9	2.9
400	500	1	3	50.0	4.8	2.9	2.9
550	650	3	5	50.0	4.8	2.9	2.9
700	900	5	9	50.0	4.8	2.9	2.9

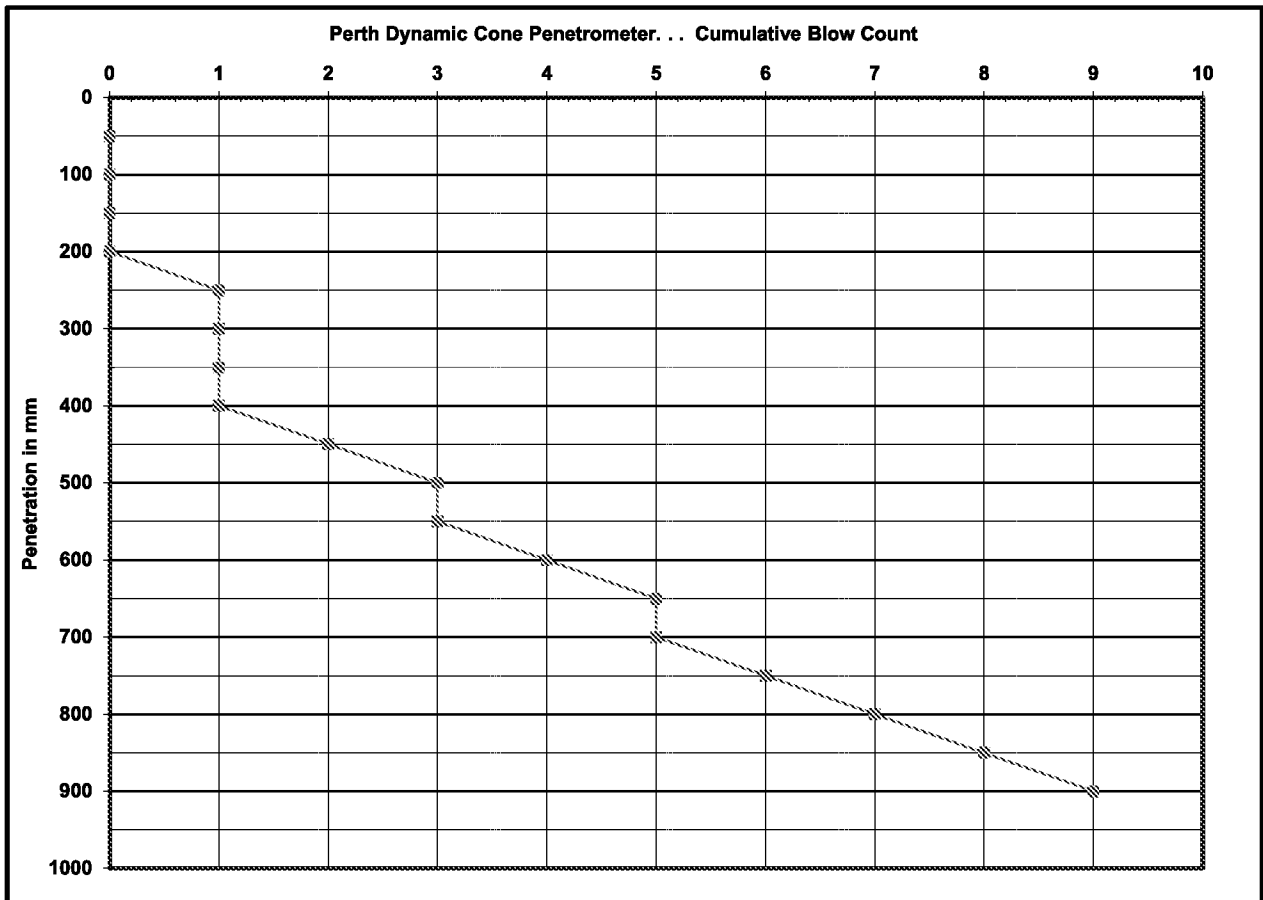

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP21

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
0	0	50	100
1	1	50	150
0	1	50	200
0	1	50	250
1	2	50	300
0	2	50	350
1	3	50	400
1	4	50	450
1	5	50	500
0	5	50	550
1	6	50	600
2	8	50	650
0	8	50	700
1	9	50	750
2	11	50	800
1	12	50	850
2	14	50	900


North Littlehampton Test Reference: - DCP22

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
100	150	0	1	50.0	4.8	2.9	2.9
250	300	1	2	50.0	4.8	2.9	2.9
350	500	2	5	50.0	4.8	2.9	2.9
550	650	5	8	33.3	7.4	4.8	4.8
700	900	8	14	33.3	7.4	4.8	4.8

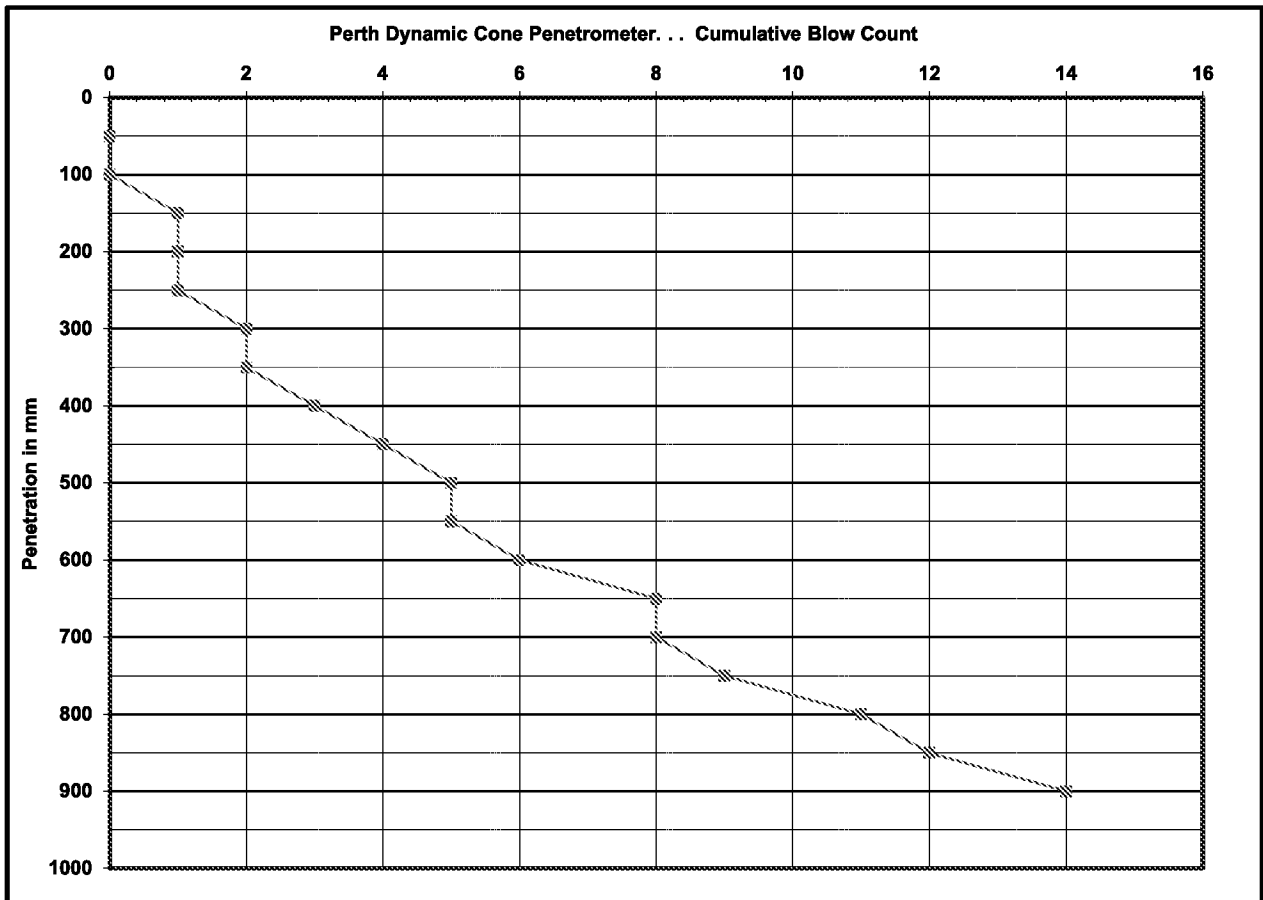

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP22

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
0	0	50	100
0	0	50	150
1	1	50	200
0	1	50	250
1	2	50	300
1	3	50	350
1	4	50	400
1	5	50	450
1	6	50	500
1	7	50	550
2	9	50	600
2	11	50	650
2	13	50	700
1	14	50	750
1	15	50	800
1	16	50	850
1	17	50	900


North Littlehampton Test Reference: - DCP23

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
150	200	0	1	50.0	4.8	2.9	2.9
250	550	1	7	50.0	4.8	2.9	2.9
550	700	7	13	25.0	10.1	7.0	7.0
700	900	13	17	50.0	4.8	2.9	2.9

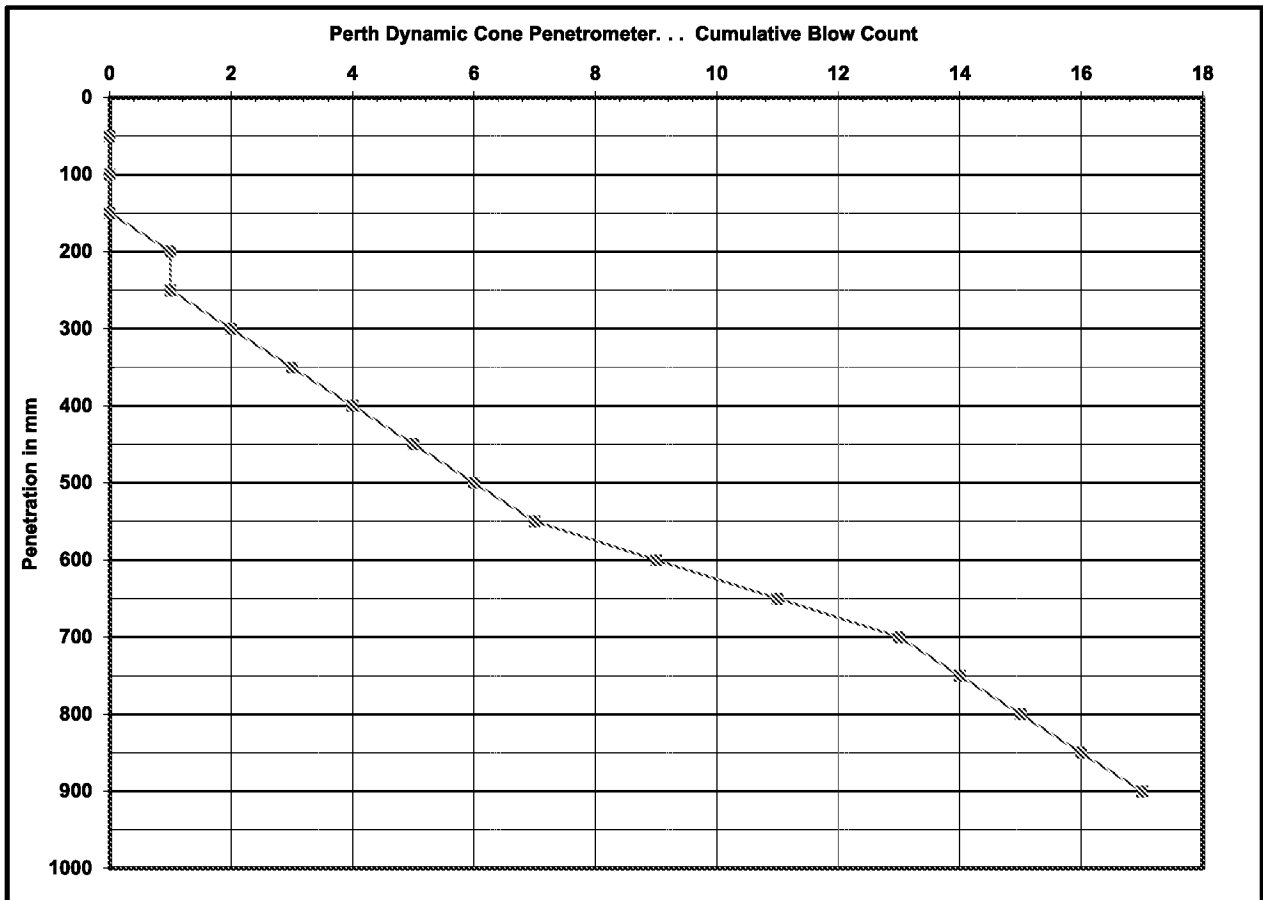

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP23

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
0	0	50	100
1	1	50	150
0	1	50	200
0	1	50	250
1	2	50	300
0	2	50	350
1	3	50	400
1	4	50	450
2	6	50	500
0	6	50	550
1	7	50	600
1	8	50	650
1	9	50	700
1	10	50	750
2	12	50	800
2	14	50	850
1	15	50	900


North Littlehampton Test Reference: - DCP24

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
100	150	0	1	50.0	4.8	2.9	2.9
250	300	1	2	50.0	4.8	2.9	2.9
350	500	2	6	37.5	6.6	4.1	4.1
550	750	6	10	50.0	4.8	2.9	2.9
750	850	10	14	25.0	10.1	7.0	7.0
850	900	14	15	50	4.8	2.9	2.9

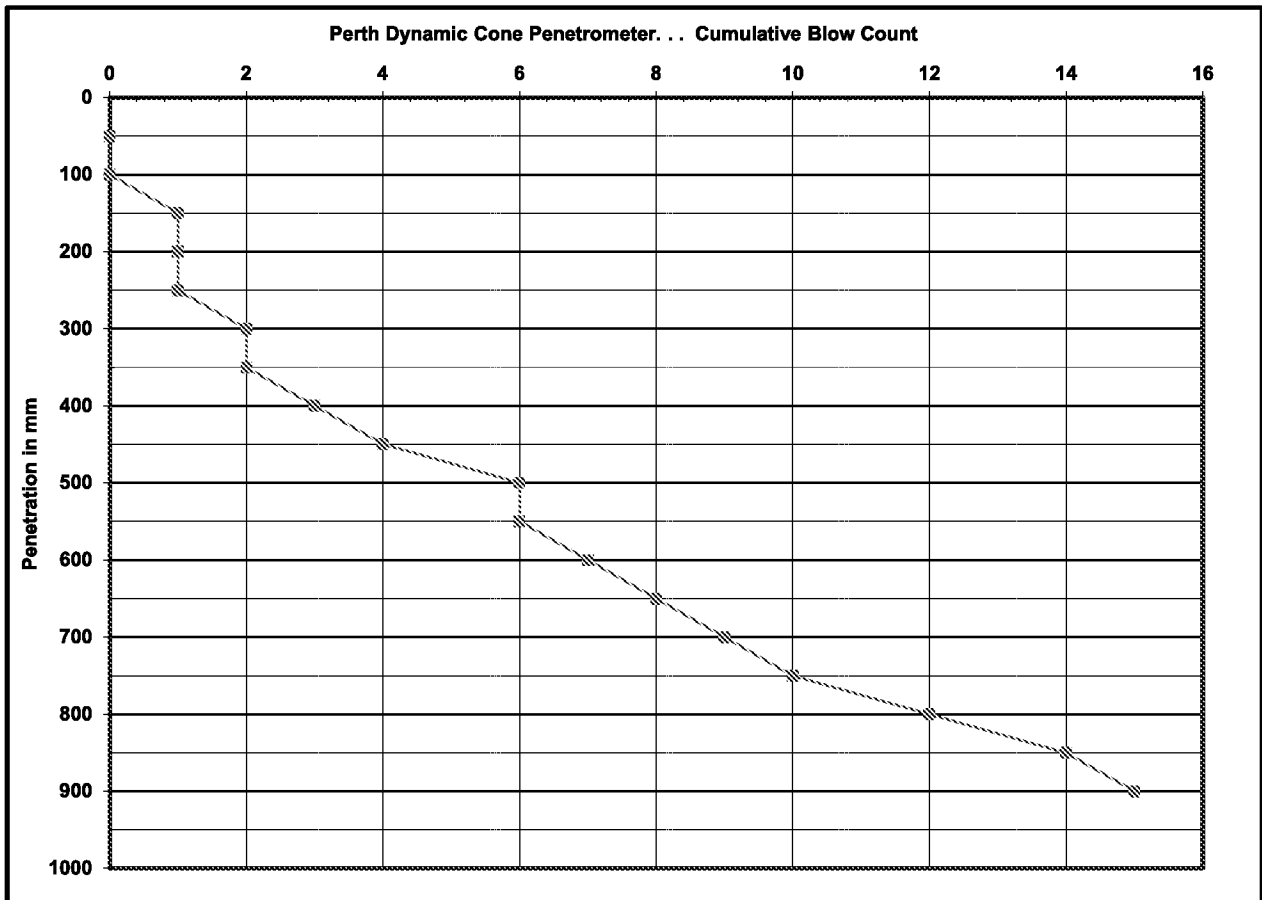

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP24

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
1	1	50	100
1	2	50	150
3	5	50	200
1	6	50	250
1	7	50	300
4	11	50	350
4	15	50	400
2	17	50	450
1	18	50	500
1	19	50	550
2	21	50	600
1	22	50	650
2	24	50	700
2	26	50	750
1	27	50	800
0	27	50	850
1	28	50	900


North Littlehampton Test Reference: - DCP25

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	150	0	2	50.0	4.8	2.9	2.9
150	200	2	5	16.7	15.4	11.7	11.7
200	300	5	7	50.0	4.8	2.9	2.9
300	450	7	17	15.0	17.3	13.4	13.4
450	650	17	22	40.0	6.1	3.8	3.8
650	800	22	27	30	8.3	5.5	5.5
850	900	27	28	50.0	4.8	2.9	2.9

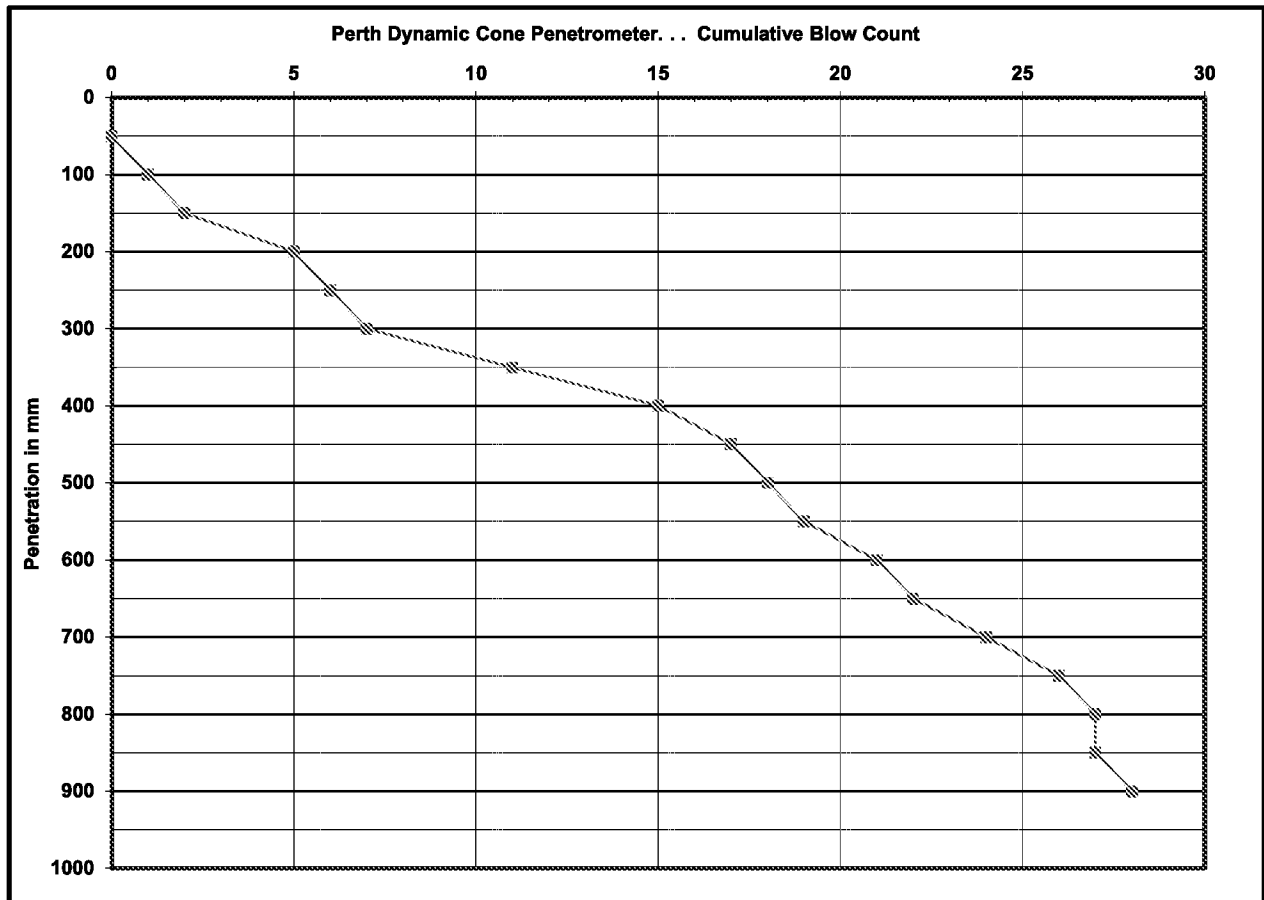

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP25

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
2	2	50	100
1	3	50	150
3	6	50	200
2	8	50	250
2	10	50	300
1	11	50	350
2	13	50	400
1	14	50	450
1	15	50	500
1	16	50	550
1	17	50	600
1	18	50	650
1	19	50	700
1	20	50	750
0	20	50	800
1	21	50	850
1	22	50	900


North Littlehampton Test Reference: - DCP26

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	150	0	3	33.3	7.4	4.8	4.8
150	300	3	10	21.4	11.8	8.5	8.5
300	750	10	20	45.0	5.4	3.3	3.3
800	900	20	22	50.0	4.8	2.9	2.9

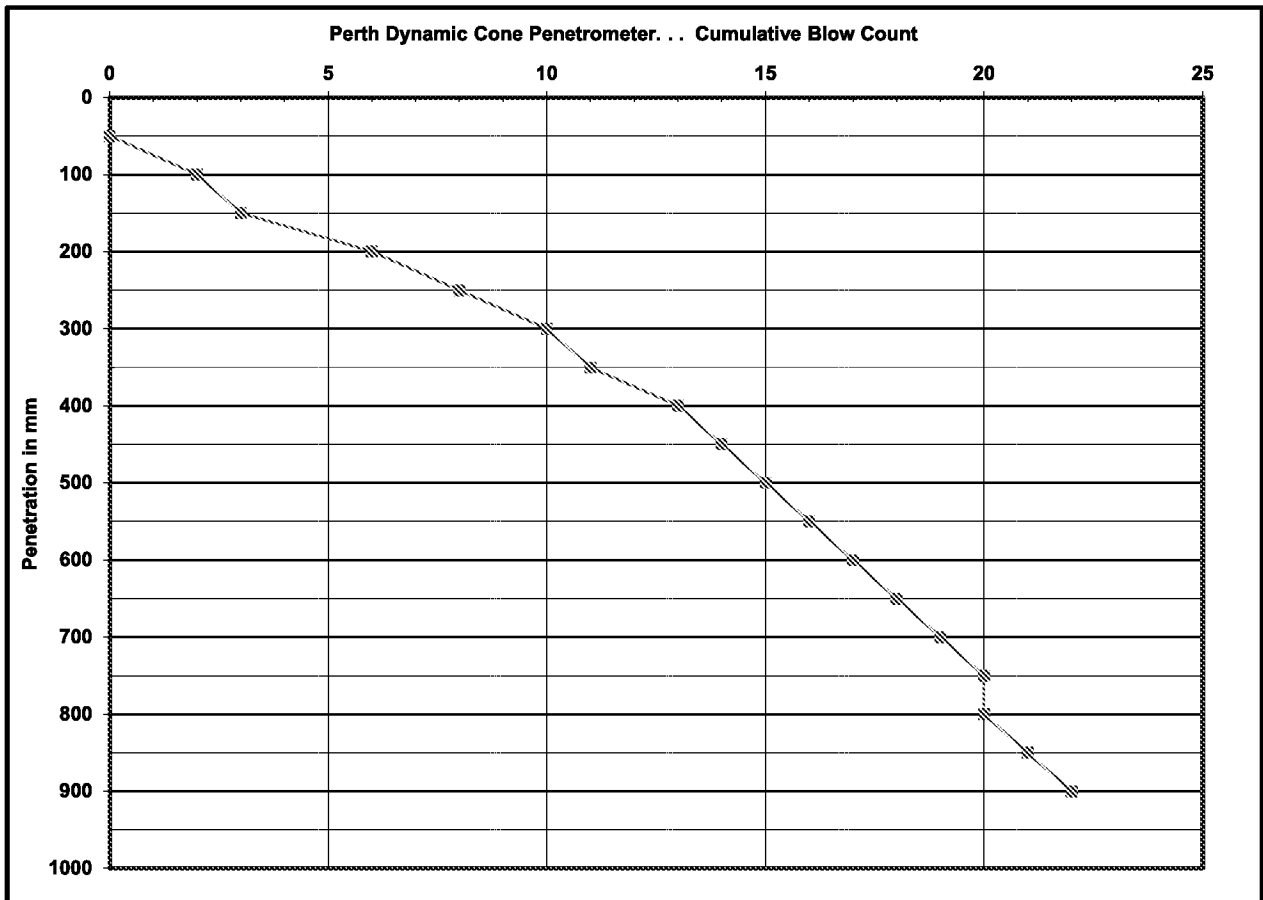

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP26

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
1	1	50	50
1	2	50	100
1	3	50	150
2	5	50	200
1	6	50	250
1	7	50	300
1	8	50	350
0	8	50	400
1	9	50	450
1	10	50	500
0	10	50	550
1	11	50	600
0	11	50	650
1	12	50	700
1	13	50	750
2	15	50	800
1	16	50	850
1	17	50	900


North Littlehampton Test Reference: - DCP27

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	200	1	5	37.5	6.6	4.1	4.1
200	350	5	8	50.0	4.8	2.9	2.9
400	500	8	10	50.0	4.8	2.9	2.9
550	600	10	11	50.0	4.8	2.9	2.9
650	900	11	17	41.7	5.9	3.6	3.6

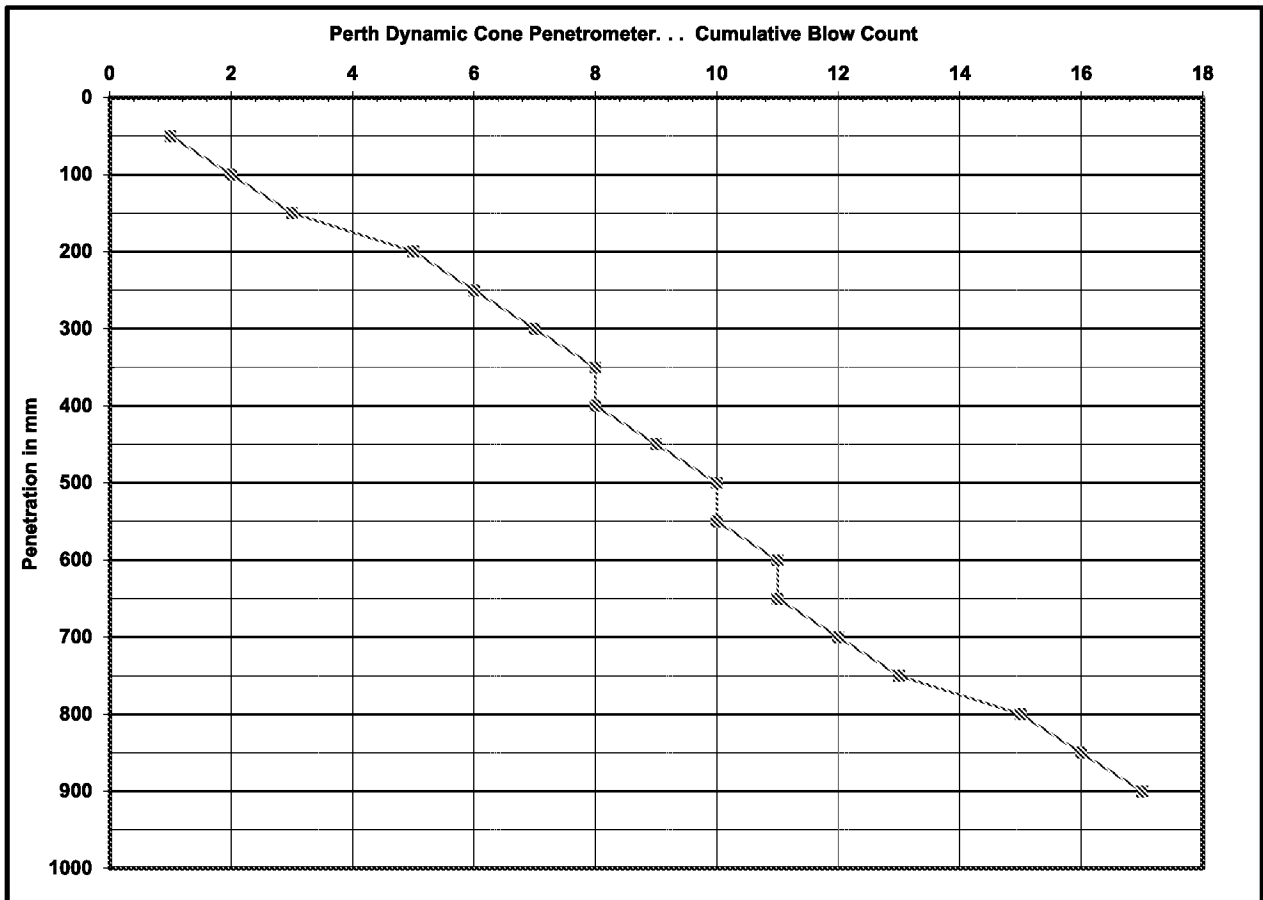

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP27

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
2	2	50	100
1	3	50	150
1	4	50	200
0	4	50	250
1	5	50	300
2	7	50	350
2	9	50	400
1	10	50	450
1	11	50	500
1	12	50	550
1	13	50	600
2	15	50	650
1	16	50	700
3	19	50	750
2	21	50	800
2	23	50	850
1	24	50	900


North Littlehampton Test Reference: - DCP28

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	200	0	4	37.5	6.6	4.1	4.1
250	400	4	9	30.0	8.3	5.5	5.5
400	600	9	13	50.0	4.8	2.9	2.9
600	700	13	16	33.3	7.4	4.8	4.8
700	850	16	23	21.4	11.8	8.5	8.5
850	900	23	24	50	4.8	2.9	2.9

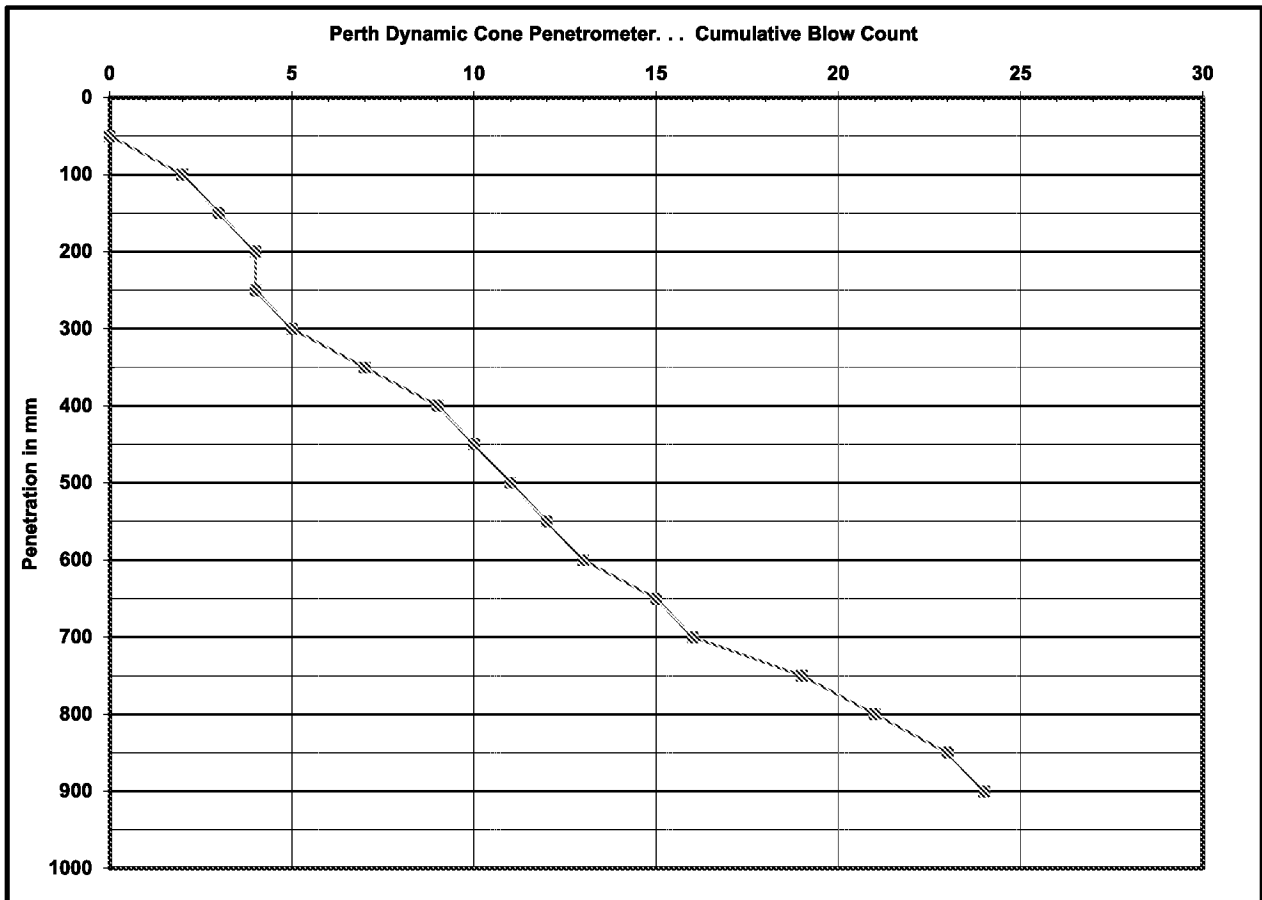

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP28

Dynamic Cone CBR Test

Nr Blows	S Blows	Penetration mm	S Pen. mm
0	0	50	50
2	2	50	100
3	5	50	150
3	8	50	200
2	10	50	250
2	12	50	300
3	15	50	350
2	17	50	400
2	19	50	450
3	22	50	500
2	24	50	550
2	26	50	600
2	28	50	650
1	29	50	700
2	31	50	750
1	32	50	800
1	33	50	850
2	35	50	900


North Littlehampton Test Reference: - DCP29

Job Nr LP2128
0

Date 22-Jan-20

CBR VALUE CALCULATIONS

Initial S Pen mm	Final S Pen mm	Initial S Blows	Final S Blows	Pen/Blow mm	CBR TRRL	CBR KVH	CBR Value (%)
50	650	0	28	21.4	11.8	8.5	8.5
650	700	28	29	50.0	4.8	2.9	2.9
700	750	29	31	25.0	10.1	7.0	7.0
750	850	31	33	50.0	4.8	2.9	2.9
850	900	33	35	25.0	10.1	7.0	7.0

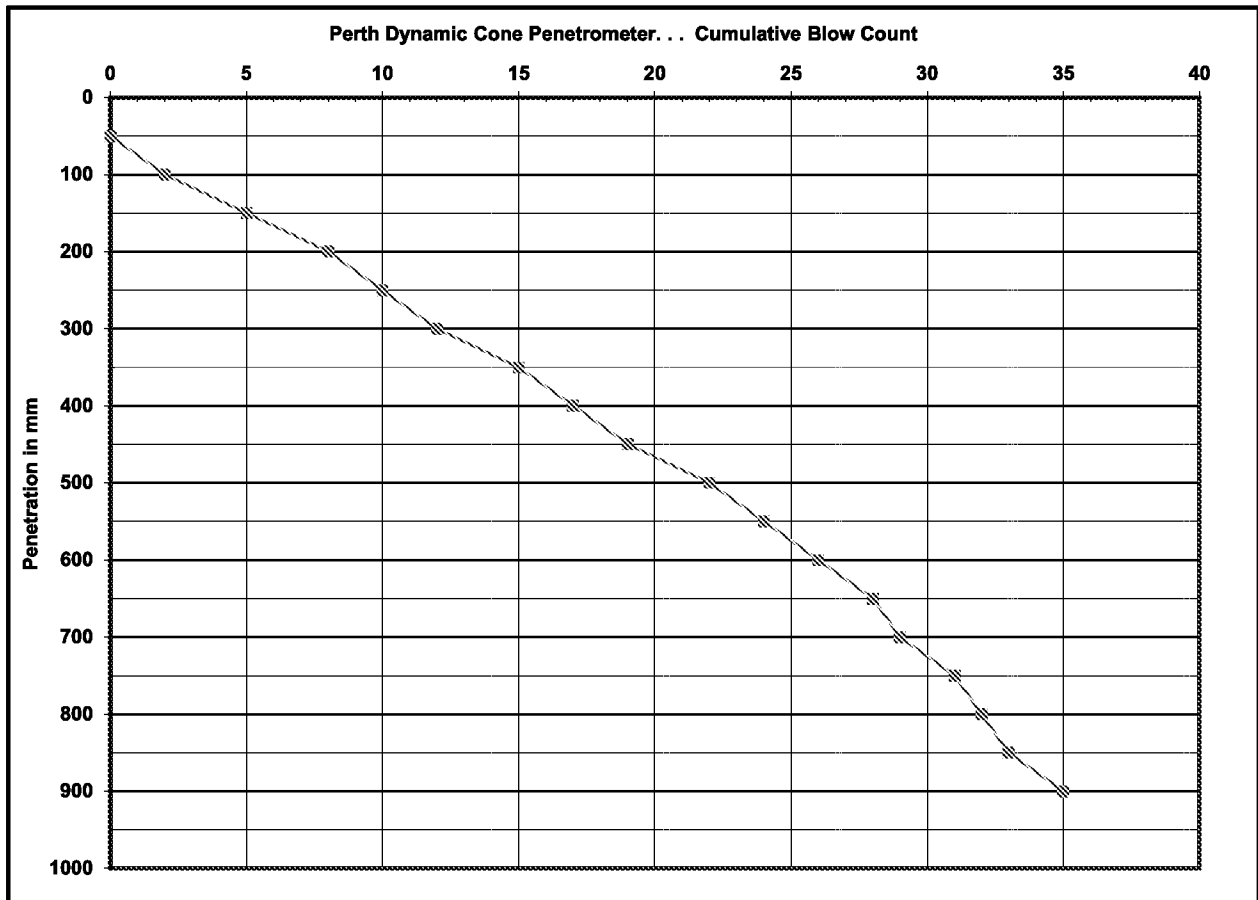

Tested by	OA	Checked		Approved	
-----------	----	---------	--	----------	--

Site: North Littlehampton

Client: Persimmon Homes

Date: 22/01/2020

Job No: LP2128

Test No: DCP29
