

QUOTATION

Our Ref:	FREE.220926.LITTLEHAMPTON	Date:	22 September 2026
Client:	Freedom Leisure 1-6 The Paddocks Carriers Way East Hoathly, East Sussex BN8 6AG	Site:	Freedom Leisure Littlehampton Wave Sea Road Littlehampton BN16 2NA
FAO:	<u>Gavin Lee</u> <u>Technical Manager</u>		
Subject:	New Container & Ground Works	Drawing Ref:	

General Notes

- All works to be carried out during normal working hours.
 - We will schedule any deliveries to accommodate the site for best practise due to public interface.
 - Access will be restricted while works undertaken.
 - We understand that our operatives must sign in first before undertaking any work.
 - They will then liaise with the person authorised by the client.
 - They are required to wear Hi-Vis and other appropriate PEP for the work to be undertaken.
 - They will then sign out once the work has been completed and notarized by the client.
 - All operatives are DBS checked.
- All prices correct at time of the quotation however suppliers have been implementing price increases without warning. Once an order is placed, we can fix costs with the suppliers.
- We have assumed free on-site parking for the duration of the contract.
- Our cost includes all redundant materials to be taken away for disposal.
- **Client to close the working area to all members of the staff for the duration of the contract.**
- We will prepare risk assessments, method statements in conjunction with works, along with details of materials used.
 - We will provide segregation barriers so works can be undertaken.
- We understand that Freedom Leisure operate on a Purchase order system only.
 - No works will be undertaken without a Purchase order and no additional works will be carried out by ourselves without a quote being submitted covering that work and its subsequent confirmation in writing.

New Container & Ground Works	
<u>Groundworks</u> <u>Single Storage base</u> To form new concrete foundation for single storage unit. • To be excavated to a depth of 500mm then filled with 350mm of type-1 compounded. • To then sit a layer of A142 Mesh Reinforcing steel and pour C25 type concrete to a depth of 150mm, brought to a scabble finish. • Make good ground to an even level surface all round. <u>Double Storage base</u> <i>To form new concrete foundation for double storage unit storage unit.</i> • <i>To be excavated to a depth of 500mm then filled with 350 mm of type-1 compounded.</i> • <i>To then sit a layer of A142 Mesh Reinforcing steel and pour C25 type concrete to a depth of 150mm, brought to a scabble finish.</i> • <i>Make good ground to and even level surface all round</i>	
<u>Electrics</u> <u>Electrical single unit</u> • To supply and fit 20 metres of 6mm 3-core SWA cable from existing distribution board to new container. • Supply and fit 1no. single-phase 4-way consumer unit inside container. • Supply and fit 1no IP-rated double socket and 1no. bulk head light with sensor. • All cables to be surfaced mounted and run in appropriate containment. • SWA cable to be suspended in mid-air from main incoming cupboard to container. <u>Electrical Double unit</u> <i>As above with extra link to adjoining unit, inclusive of supply and fit 1no IP-rated double socket and 1no bulk head light with sensor.</i>	

Supply of 20ft Container (Cost Per Container)


- Premium 20ft New One trip Container
- XL Vent System included for Anti Condensation (either Green or Blue)
- 2185kg Tare Weight
- Dimensions (approximate) Length 20ft x Width 8ft x Height 8ft 6"
- c/w
 - Lockbox included
 - Easy Open Handle
 - 28mm Polyurethane Coated Plywood or Bamboo Composite flooring

Delivery 1 x 20ft Container

- Delivery based on HIAB to crane offload and subject to suitable site for offloading.

Delivery of 2x 20ft Containers

Delivery based on ARTIC HIAB to crane offload and subject to suitable site for offloading.

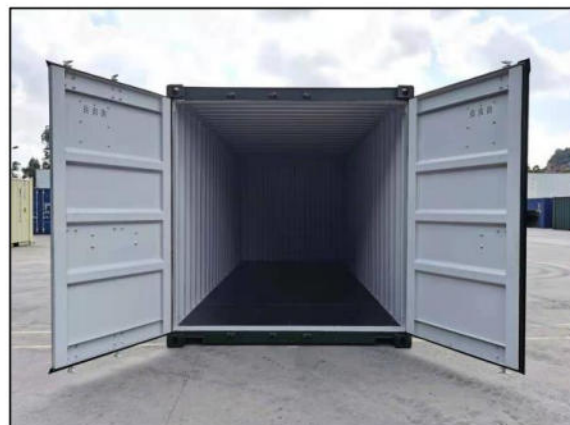

TOTAL COST for SINGLE FOUNDATION AND CONTAINER

TERMS & CONDITIONS

Terms: Nett, payable 30 days from date of invoice.

VAT to be charged in accordance with the Act.

INCLUSIONS

Our price includes for all necessary labour and materials including:

- Delivery of materials to site
- Offloading and portorage of materials to working area
- Disposal of all our redundant materials upon completion if required.
- Installation of all materials

EXCLUSIONS

Our price does not include for:

- Any works outside of the scope of this quotation.

ALL PRICES ARE CURRENT AND MAY BE LIABLE TO INCREASES AT ANY TIME BUT WILL REMAIN FIXED ONCE THE ORDER HAS BEEN PLACED.

We hope we have interpreted your requirements correctly and look forward to receiving your further instructions.

Yours faithfully



George Bertos
E &OE
