


Mate Geotechnical Services

Groundwater Monitoring at "Long Acre" the Street, Walberton

LOCATION	Pipe I.D.	Pipe Depth	Pipe Height	A.O.D. Ground Level	DATE Dry Cold Week	DATE Dry Cold Week	DATE Light Rain Thursday	DATE Light Rain in Week	DATE Dry Cold Week	DATE Rain most of Week	DATE Some Rain in Week	DATE Some Rain in Week	DATE Rain most of Week	DATE Some Slight Rain	DATE Some Rain in Week	DATE Little Rain	DATE Some Rain in Week	
"Long Acre" the Street WALBERTON Wednesday 15th February 2023				ToP BGL	Wed'sday 15-Feb	Wed'sday 15-Feb	Saturday 18-Feb	Saturday 25-Feb	Saturday 4-Mar	Saturday 11-Mar	Saturday 18-Mar	Saturday 25-Mar	Sunday 2-Apr	Saturday 8-Apr	Saturday 15-Apr	Saturday 22-Apr	Sunday 30-Apr	E N D
Maximum Depth	GWP #1	2950			2200	2592	2629	2740	2848	1889	1968	1768	1208	1751	1260	1991	2079	O f
Below Ground Level	(north)	-2232	718	14.958	-2200	-1874	-1911	-2022	-2130	-1171	-1250	-1050	-490	-1033	-542	-1273	-1361	M O N I T O R I N G
Level Above O.D.		12.008		14.240	12.040	12.366	12.329	12.218	12.110	13.069	12.990	13.190	13.750	13.207	13.698	12.967	12.879	C Y C L E
Change from Previous						326	-37	-111	-108	959	-79	200	560	-543	491	-731	-88	
Water Strike Below Ground Level		-2250																
Maximum Depth	GWP #2	2950			2450	2643	2392	2475	2571	1581	1697	1572	1074	1626	1110	1843	1908	
Below Ground Level	(centre)	-2426	524	14.432	-2450	-2119	-1868	-1951	-2047	-1057	-1173	-1048	-550	-1102	-586	-1319	-1384	
Level Above O.D.		11.482		13.908	11.458	11.789	12.040	11.957	11.861	12.851	12.735	12.860	13.358	12.806	13.322	12.589	12.524	
Change from Previous						331	251	-83	-96	990	-116	125	498	-552	516	-733	-65	
Water Strike Below Ground Level		-2470																
Maximum Depth	GWP #3	2950			2378	2912	2841	2850	2920	2158	2284	2162	1422	2254	1548	2430	2512	
Below Ground Level	(south)	-2378	572	14.357	-2378	-2340	-2269	-2278	-2348	-1586	-1712	-1590	-850	-1682	-976	-1858	-1940	
Level Above O.D.		11.407		13.785	11.407	11.445	11.516	11.507	11.437	12.199	12.073	12.195	12.935	12.103	12.809	11.927	11.845	
Change from Previous						38	71	-9	-70	762	-126	122	740	-832	706	-882	-82	
Water Strike Below Ground Level		2428 Dry			Dry													
					Water Depth on Pipe Installation	Reading on Leaving the Site				Visibly Dry into Wet Mud								

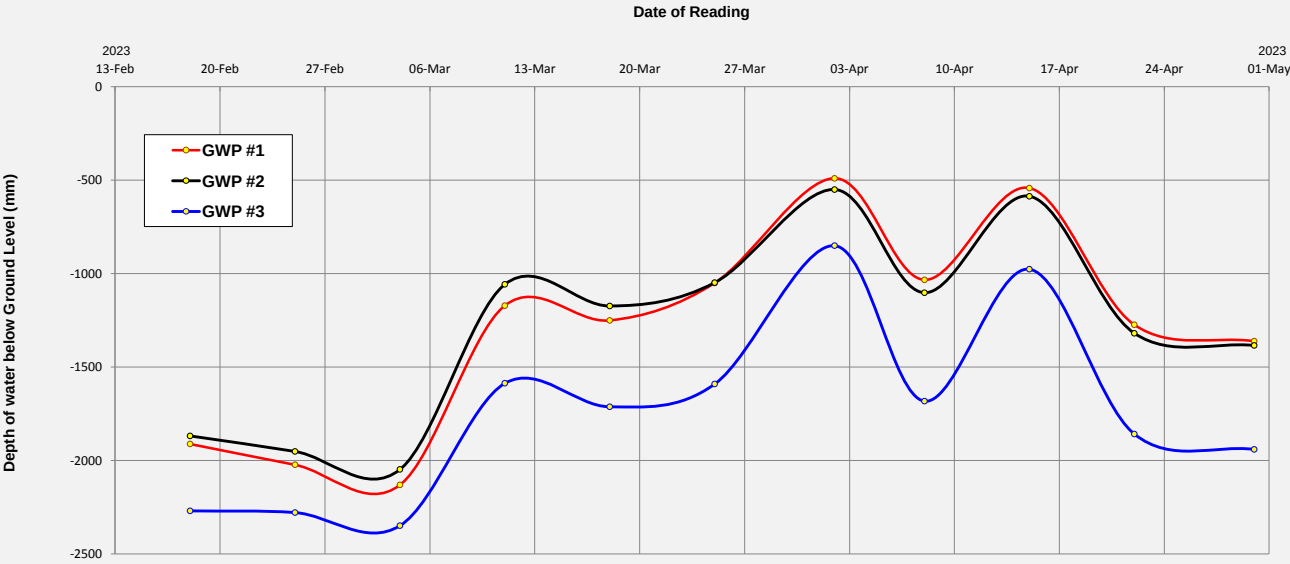

Groundwater Monitoring -- in Groundwater Points GWP#1, GWP#2 & GWP#3
