




SGN 1 Monitoring tree protection



- Always:**
- have a pre-commencement meeting with the tree consultant before development starts
 - use the tree consultant to regularly check that protection remains fit for purpose
 - use the tree consultant to supervise work in rpas
 - keep a written record of supervision

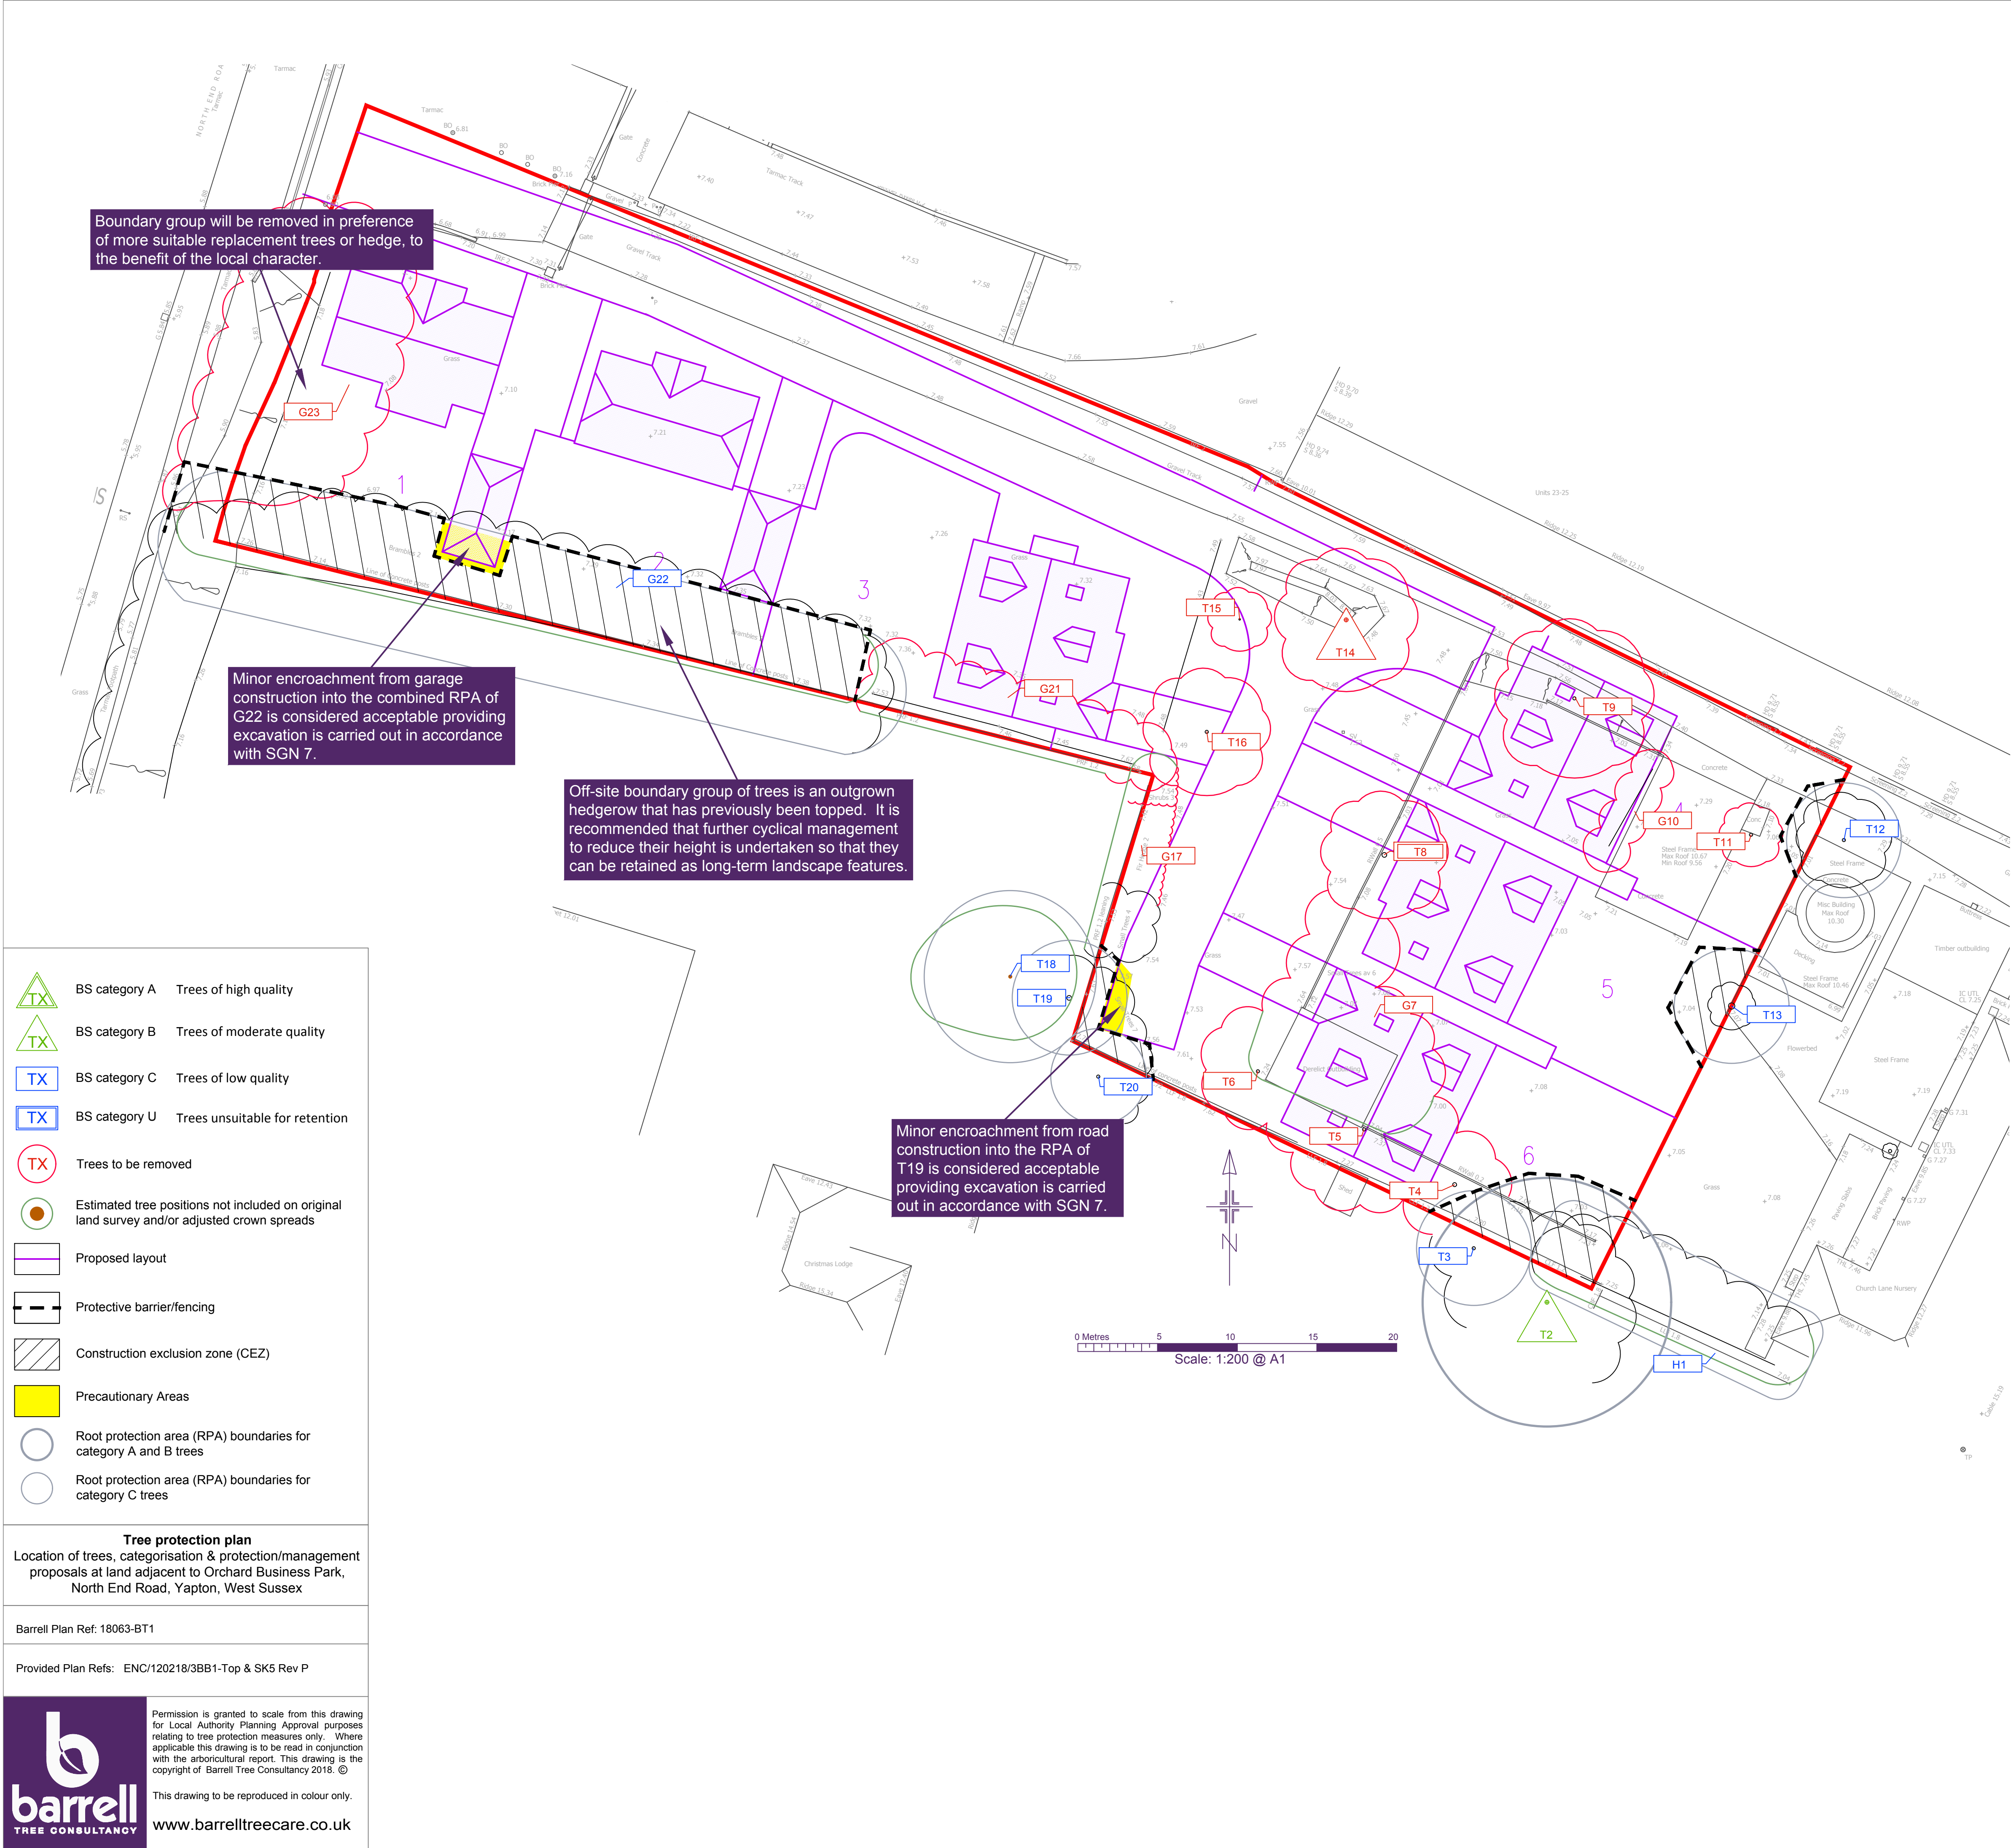

SGN 2 Fencing protected trees



- Always:**
- install protection before development starts
 - make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
 - keep protection in place until there is no risk to trees
 - get written permission to move or remove any protection



SGN 4 Pollution control



- Always:**
- keep toxic products away from RPAs



SGN 7 Excavating in RPAs



- Always:**
- use the tree consultant to supervise work in RPAs
 - use hand tools to dig in RPAs
 - protect exposed roots from sunlight and drying out



SGN 12 Landscaping in RPAs



- Always:**
- use the tree consultant to supervise work in RPAs
 - avoid raising ground levels within 1m of the trunks of retained trees



How to use plan

- More detailed guidance on each Site Guidance Note (SGN) can be found in a printed hard copy compilation of all the SGNs, issued to the Site Manager at the pre-commencement site meeting (**Note:** This should be retained on site throughout the duration of works). Additionally, an electronic pdf compilation of all the SGNs, was submitted with this drawing to the local planning authority and the client. Alternatively, a pdf of each SGN can be downloaded by:
- clicking the image links in the electronic pdf version of this plan;
 - holding a mobile phone QR (Quick Response) code reader over the QR code in the paper version of this plan; or,
 - visiting our website at <https://www.barrelltreecare.co.uk/resources/technical-guidance>

Tree No	Species	Category	RPA Radius	Tree Works
All retained trees & hedges				Carry out safety check and lift over site to 3-4m as necessary.
H1	Leyland cypress	C	3.0	-
T2	Beech	B	7.8	-
T3	Bay laurel	C	3.6	-
T4	Sycamore	C	3.0	Fell for development
T5	Sycamore	C	5.4	Fell for development
T6	Cherry	C	2.4	Fell for development
G7	Cherry, hawthorn	C	1.5	Fell for development
T8	Sycamore	U	3.0	Fell for management
T9	Birch	C	4.2	Fell for development
G10	Palm	C	2.4	Fell for development
T11	Palm	C	2.4	Fell for development
T12	Hornbeam	C	3.6	-
T13	Palm	C	3.6	-
T14	Ash	B	4.2	Fell for development
T15	Fruit	C	1.5	Fell for development
T16	Apple	C	5.1	Fell for development
G17	Cypress	C	1.5	Fell for development
T18	Birch	C	5.4	-
T19	Larch	C	3.6	-
T20	Sycamore	C	3.0	-
G21	Cypress	C	3.0	Fell for development
G22	Beech, hornbeam	C	3.0	Reduce height to just above previous pruning points at 12m to re-instate cyclical management regime.
G23	Cypress	C	5.4	Fell for development



Permission is granted to scale from this drawing for Local Authority Planning Approval purposes relating to tree protection measures only. Where applicable this drawing is to be read in conjunction with the arboricultural report. This drawing is the copyright of Barrell Tree Consultancy 2018. ©

This drawing to be reproduced in colour only.
www.barrelltreecare.co.uk
