



Aggregate Test Certificate

Client: Dudman Aggregates Ltd.
Albion Wharf, Albion Street
Southwick
Brighton BN42 4DP


Sample Reference: 21.35.4/20 (LS).01
Source of Material: Carboniferous L/stone
Torr Works

Material Description: 4/20mm Con. Graded (In-House Grading)
Visual Description: Grey/Pink Carboniferous Limestone
Test Method: Particle Size Distribution to BS EN 933-1

Sieve Size	Percentage Passing	Limits
40mm	100	100
31.5mm	100	98-100
20mm	92	90-100
10mm	40	25-60
4mm	4	0-15
2mm	3	0-5
0.063	2	0-4

Date Sampled: 30th August 2021
Date Tested: 6th September 2021

Particle Size Distribution Grading Curve

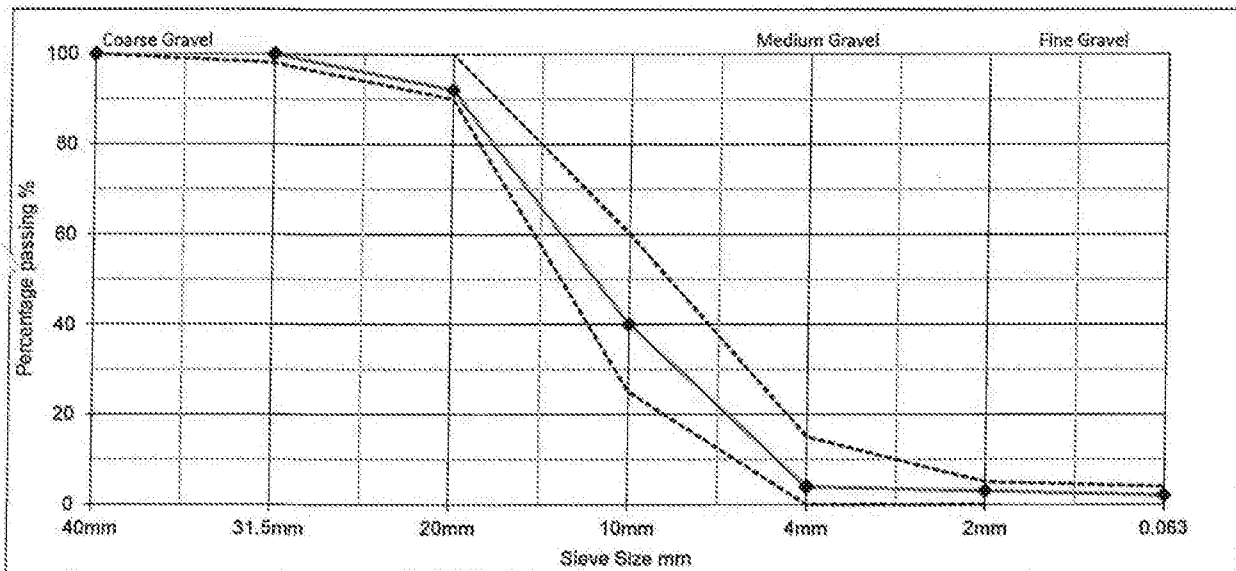


The material tested complies with the above in-house grading requirements

Signed:

Date of Issue: 20th September 2021

Neil Jay :-Group Technical Manager:-Dudman Aggregates Limited

Company registration Number : 7803522



CONVEYANCE NOTE

Invoice No. ASD/07/0107-1340

Customer Address

Purdown Greenhousham Ltd
New Down Lane
Waterlooville
Hampshire
PO17 5SE

Customer Address

Purdown Greenhousham Ltd
c/o Dudman, Parkside West North End Road
Waterlooville
Hampshire
PO17 5SE

Dudman Programme Licence
Registration Number

☐ ☐ ☐ ☐

13/07/21 14:30

Date

13/07/21

Customer Ref

0000

Product

Purdown Land Clearance
BASEMENT SEE

Unit

Yard

Unit

12.000

On

30.700

13/07/21

For Customer, GARDEN & PPA work over the morning session

Comments

Work to be done - installation of water shutters in garden

Form of Payment

Form of Payment

Web Ref No.

13/07/21/00

Delivery Name

0000

Customer Reference

£

Driver Signature

13/07/21

Customer

Unit

Unit

Date

Print

For customer use - details are as described above and begin to the customer's account

Site Name: Stakers Farm, Yaptin




Note Number: ABI418-38
Date: 15th March 2021
Subject: SuDS As Built Information Form – 38 Unit Site
Revision: A


[illegible]

Free Tickets

Site Name: Stakers Farm, Yapton

Page 1 of 20

Site Name: Stakers Farm, Yapton

[illegible]









Site Name: Stakers Farm, Yapton

[illegible]

Site Name: Stakers Farm, Yapton


[illegible]

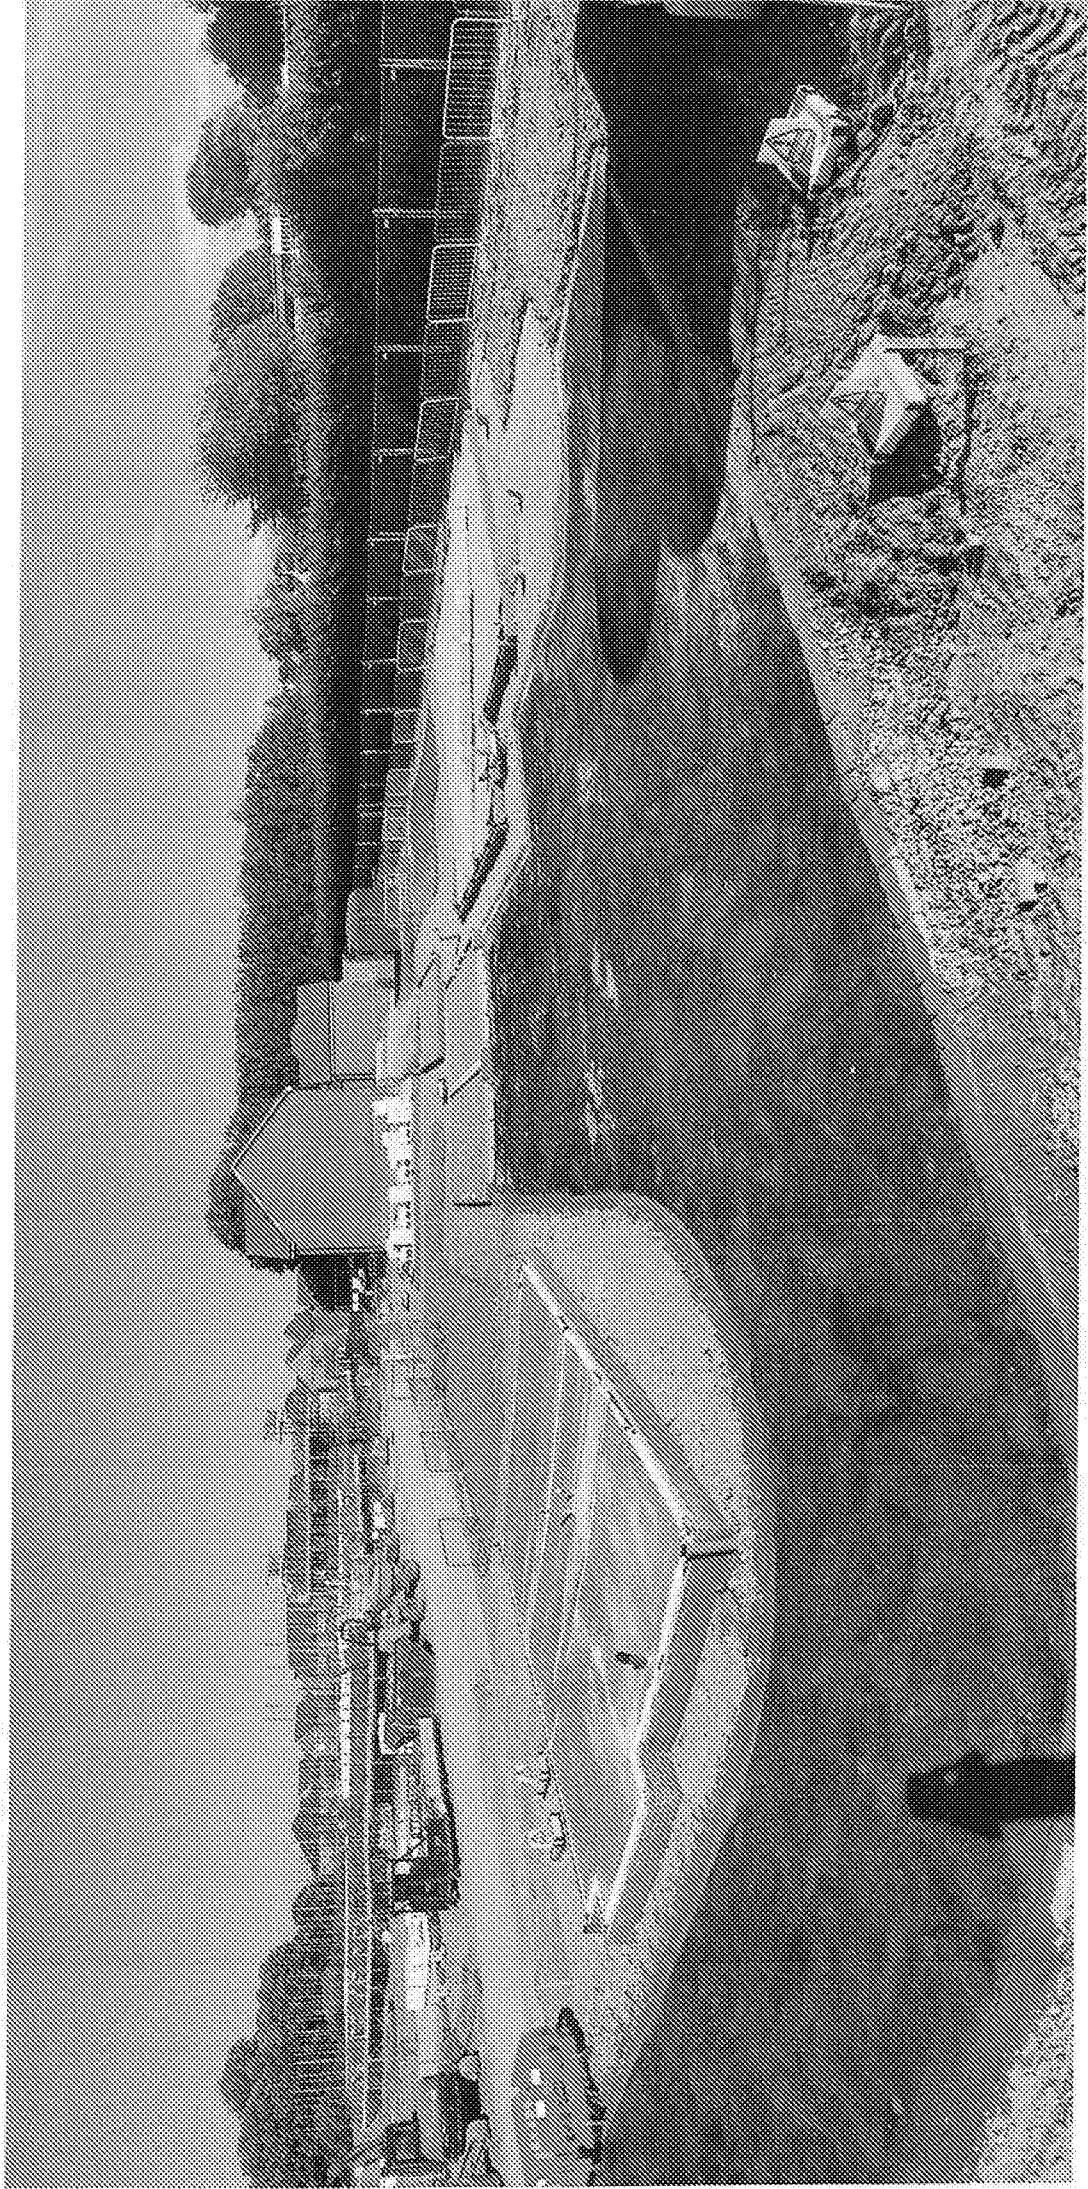






Site Name: Stakers Farm, Yapton

Page 5 of 20

Site Name: Stakers Farm, Yapton

[illegible]



OUTLOOK

Darryl Sanders

Sent from my iPhone

now




OUTLOOK

Darryl Sanders

Sent from my iPhone

now

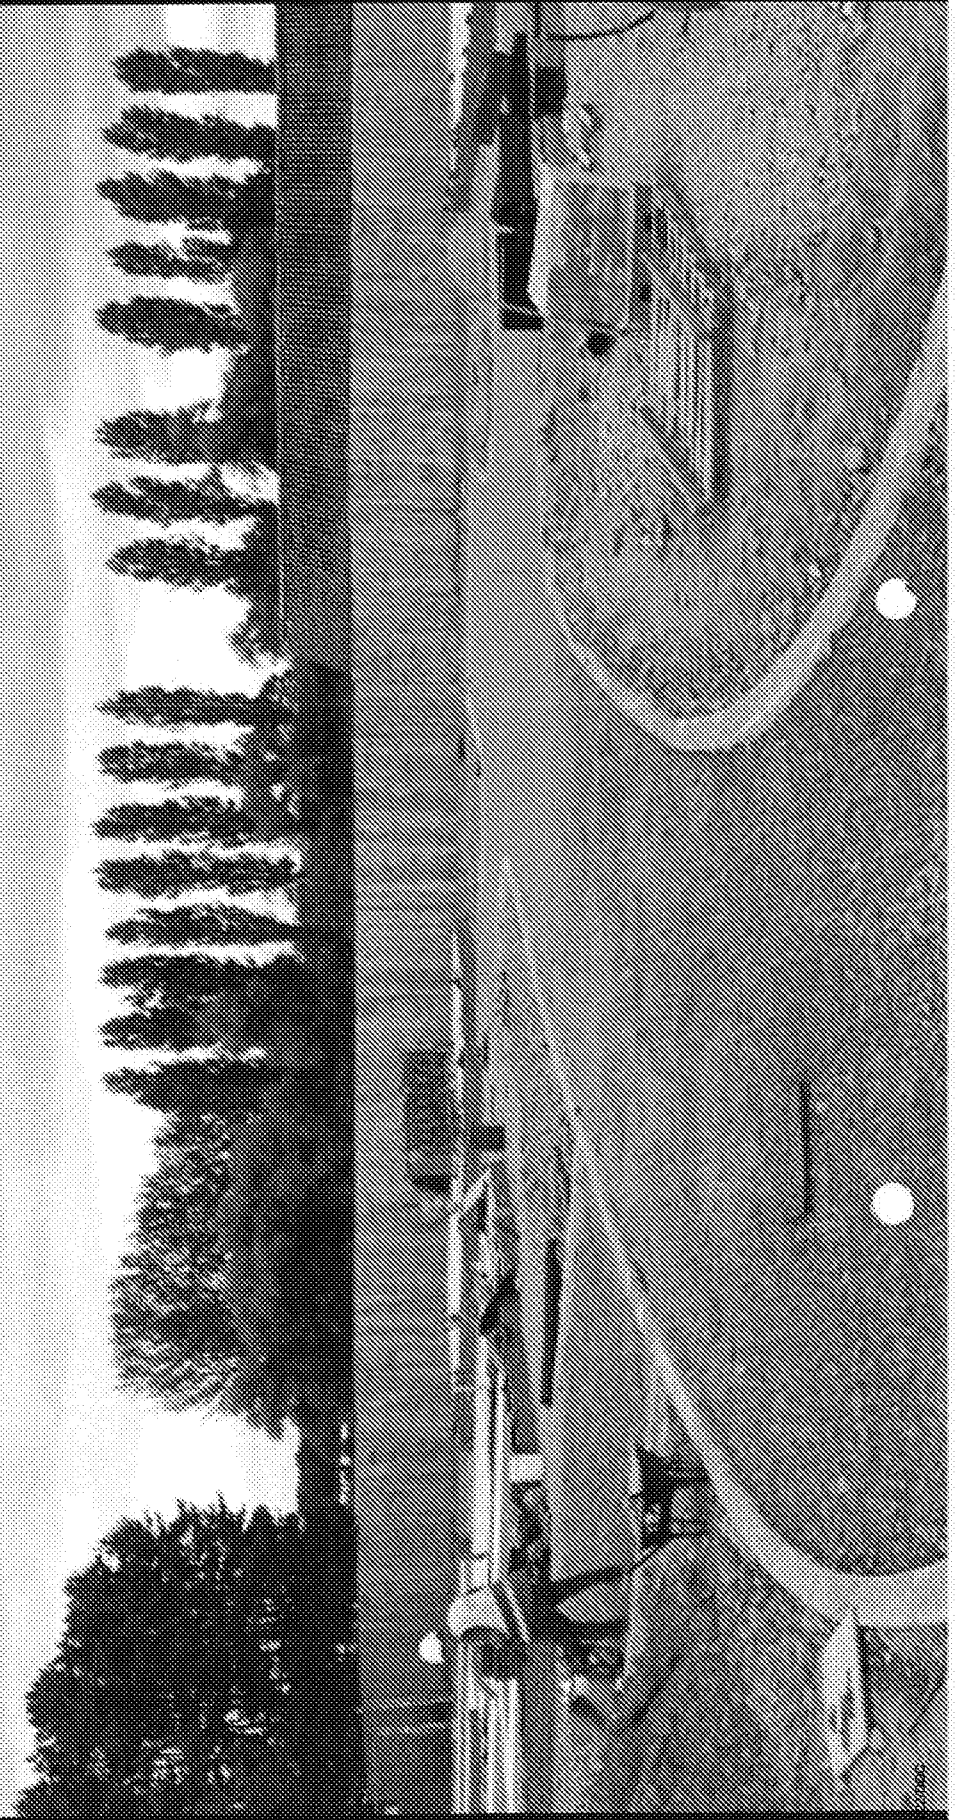


Site Name: Stakers Farm, Yapton

RUN DISTRICT COUNCIL Y/6/22/DOC

[illegible]



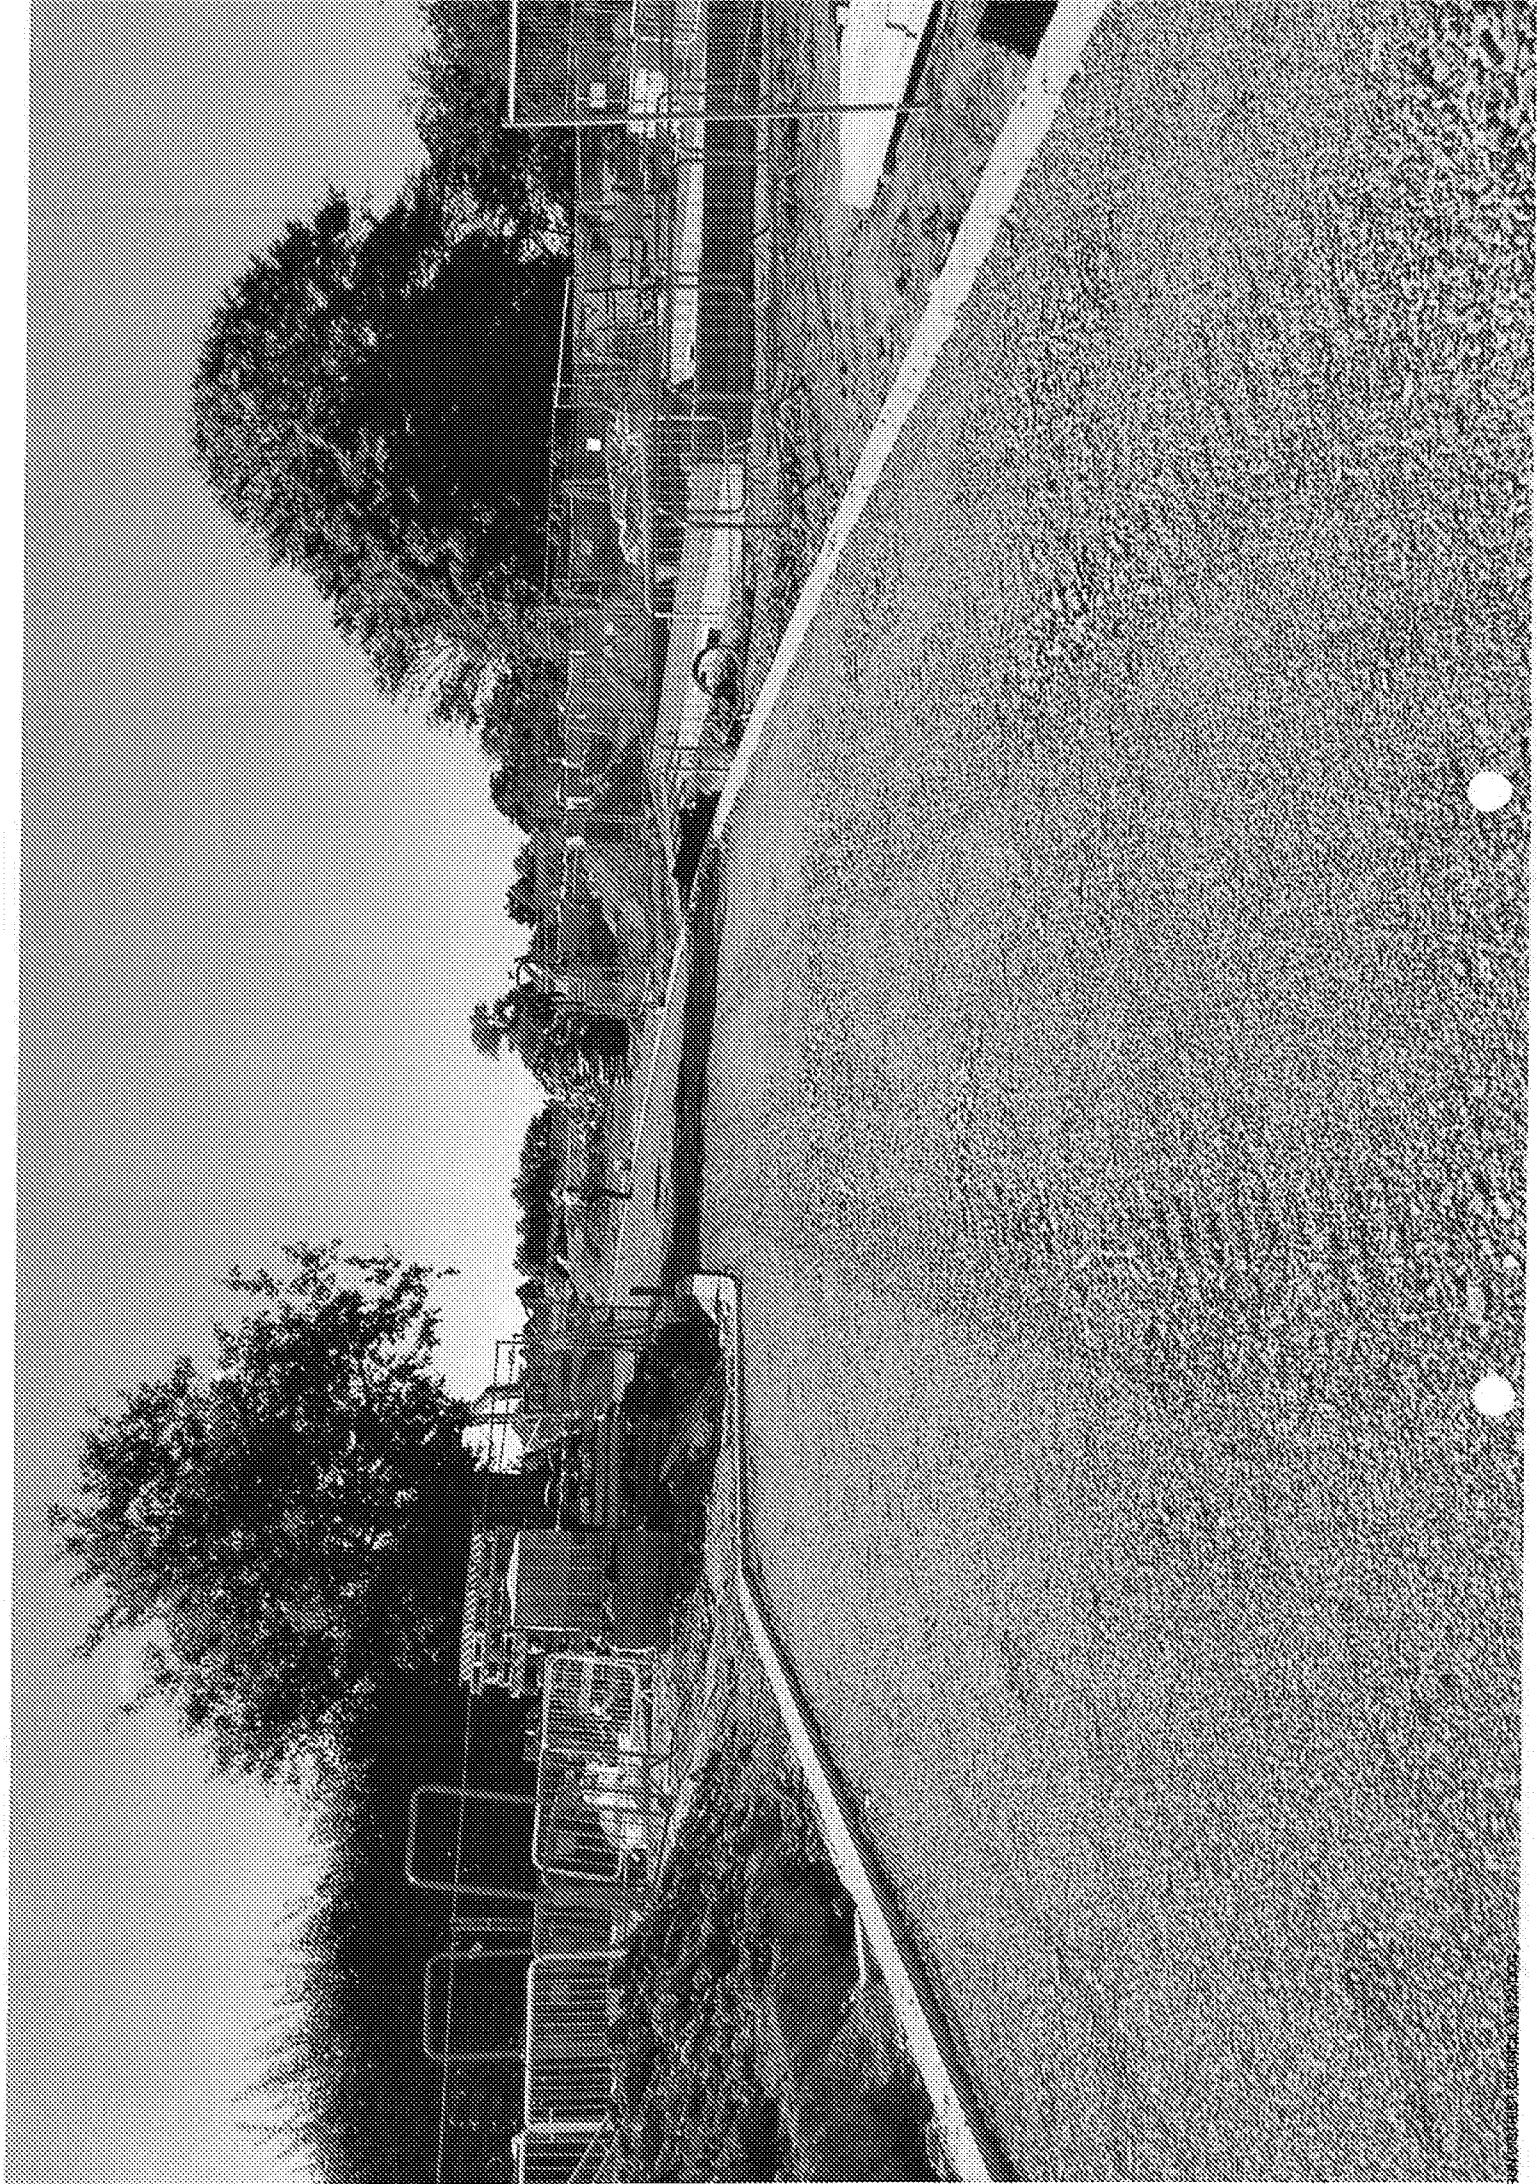

2.

Private Drives

All Private Drives are to be supported by photos at all stages of the infrastructure build and .dwg as built CAD files. Any variations to the design must be supported by demonstrable calculations and approvals from Dandara (Engineering Department only) or the Civil Engineering Designer (Odyssey).

Private Drive (Plots 1-2) – Type 5B Construction

Details	Units	As Built Recording	Notes <i>Including justifications for varying the design</i>
Has the drive been surveyed in GPS and CAD .dwg format?	N/A	Yes / No	State Drawing Number
Formation Level	mAOD		
Terram Geotextile installed?	N/A	Yes / No	Supporting Photos
Thickness of Sub-base	mm		
Sub-base material and reference to import ticket	N/A		Supplier name and details. Import Ticket Reference Number.

Private Drive (Plots 37-38) – Type 5B Construction

Details	Units	As Built Recording	Notes <i>Including justifications for varying the design</i>
Has the drive been surveyed in GPS and CAD .dwg format?	N/A	Yes / No	State Drawing Number
Formation Level	mAOD		
Terram Geotextile installed?	N/A	(Yes) / No	Supporting Photos
Thickness of Sub-base	mm	395 mm	
Sub-base material and reference to import ticket	N/A	4/20	Supplier name and details. Import Ticket Reference Number.

AS BUILT INFORMATION
Site Name: Stakers Farm, Yapton

 **dandara**

Private Drive (Plots 36) – Type 5B Construction

N/A Show home

Details	Units	As Recording	Built	Notes Including justifications for varying the design
Has the drive been surveyed in GPS and CAD .dwg format?	N/A	☒ Yes ☐ No		State Drawing Number
Formation Level	mAOD	7.038 7.038 7.031		
Terram Geotextile installed?	N/A	☒ Yes ☐ No		Supporting Photos
Thickness of Sub-base	mm	395		
Sub-base material and reference to import ticket	N/A			Supplier name and details. Import Ticket Reference Number.

Private Drive (Plots 9-10) – Type 5B Construction

Details	Units	As Recording	Built	Notes Including justifications for varying the design
Has the drive been surveyed in GPS and CAD .dwg format?	N/A	☒ Yes ☐ No		State Drawing Number
Formation Level	mAOD	7.038 7.031		
Terram Geotextile installed?	N/A	☒ Yes ☐ No		Supporting Photos
Thickness of Sub-base	mm	395.		
Sub-base material and reference to import ticket	N/A	4/20.		Supplier name and details. Import Ticket Reference Number.

AS BUILT INFORMATION
Site Name: Stakers Farm, Yapton



Private Drive (Plots 11-12) – Type 5B Construction

Details	Units	As Recording	Built	Notes <i>Including justifications for varying the design</i>
Has the drive been surveyed in GPS and CAD .dwg format?	N/A	☒ Yes / No		State Drawing Number
Formation Level	mAOD	6.981 6.871		
Terram Geotextile installed?	N/A	☒ Yes / No		Supporting Photos
Thickness of Sub-base	mm	395		
Sub-base material and reference to import ticket	N/A	4/20		Supplier name and details. Import Ticket Reference Number.

Private Drive (Plots 13-14) – Type 5B Construction

Details	Units	As Recording	Built	Notes <i>Including justifications for varying the design</i>
Has the drive been surveyed in GPS and CAD .dwg format?	N/A	☒ Yes / No		State Drawing Number
Formation Level	mAOD	6.844 6.674 6.668		
Terram Geotextile installed?	N/A	☒ Yes / No		Supporting Photos
Thickness of Sub-base	mm	395		
Sub-base material and reference to import ticket	N/A	4/20		Supplier name and details. Import Ticket Reference Number.

AS BUILT INFORMATION
Site Name: Stakers Farm, Yapton



Private Drive (Plots 20-21) – Type 5B Construction

Details	Units	As Recording	Built	Notes <i>Including justifications for varying the design</i>
Has the drive been surveyed in GPS and CAD .dwg format?	N/A	☒ Yes / No		State Drawing Number
Formation Level	mAOD	6.366 6.349		
Terram Geotextile installed?	N/A	☒ Yes / No		Supporting Photos
Thickness of Sub-base	mm	395		
Sub-base material and reference to import ticket	N/A	4/20		Supplier name and details. Import Ticket Reference Number.

Private Drive (Plots 22) – Type 5B Construction

Details	Units	As Recording	Built	Notes <i>Including justifications for varying the design</i>
Has the drive been surveyed in GPS and CAD .dwg format?	N/A	☒ Yes / No		State Drawing Number
Formation Level	mAOD	6.073 6.061		
Terram Geotextile installed?	N/A	☒ Yes / No		Supporting Photos
Thickness of Sub-base	mm	395		
Sub-base material and reference to import ticket	N/A	4/20		Supplier name and details. Import Ticket Reference Number.

Private Drive (Plots 25-26) – Type 5B Construction

Details	Units	As Recording	Built	Notes <i>Including justifications for varying the design</i>
Has the drive been surveyed in GPS and CAD .dwg format?	N/A	☒ Yes / No		State Drawing Number
Formation Level	mAOD	5876 5856		
Terram Geotextile installed?	N/A	☒ Yes / No		Supporting Photos
Thickness of Sub-base	mm	395		
Sub-base material and reference to import ticket	N/A	4/20		Supplier name and details. Import Ticket Reference Number.

Private Drive (Plots 27-28) – Type 5B Construction

Details	Units	As Recording	Built	Notes <i>Including justifications for varying the design</i>
Has the drive been surveyed in GPS and CAD .dwg format?	N/A	☒ Yes / No		State Drawing Number
Formation Level	mAOD	6.011 6.068 6.059		
Terram Geotextile installed?	N/A	☒ Yes / No		Supporting Photos
Thickness of Sub-base	mm	395		
Sub-base material and reference to import ticket	N/A	4/20		Supplier name and details. Import Ticket Reference Number.
