APPENDIX A
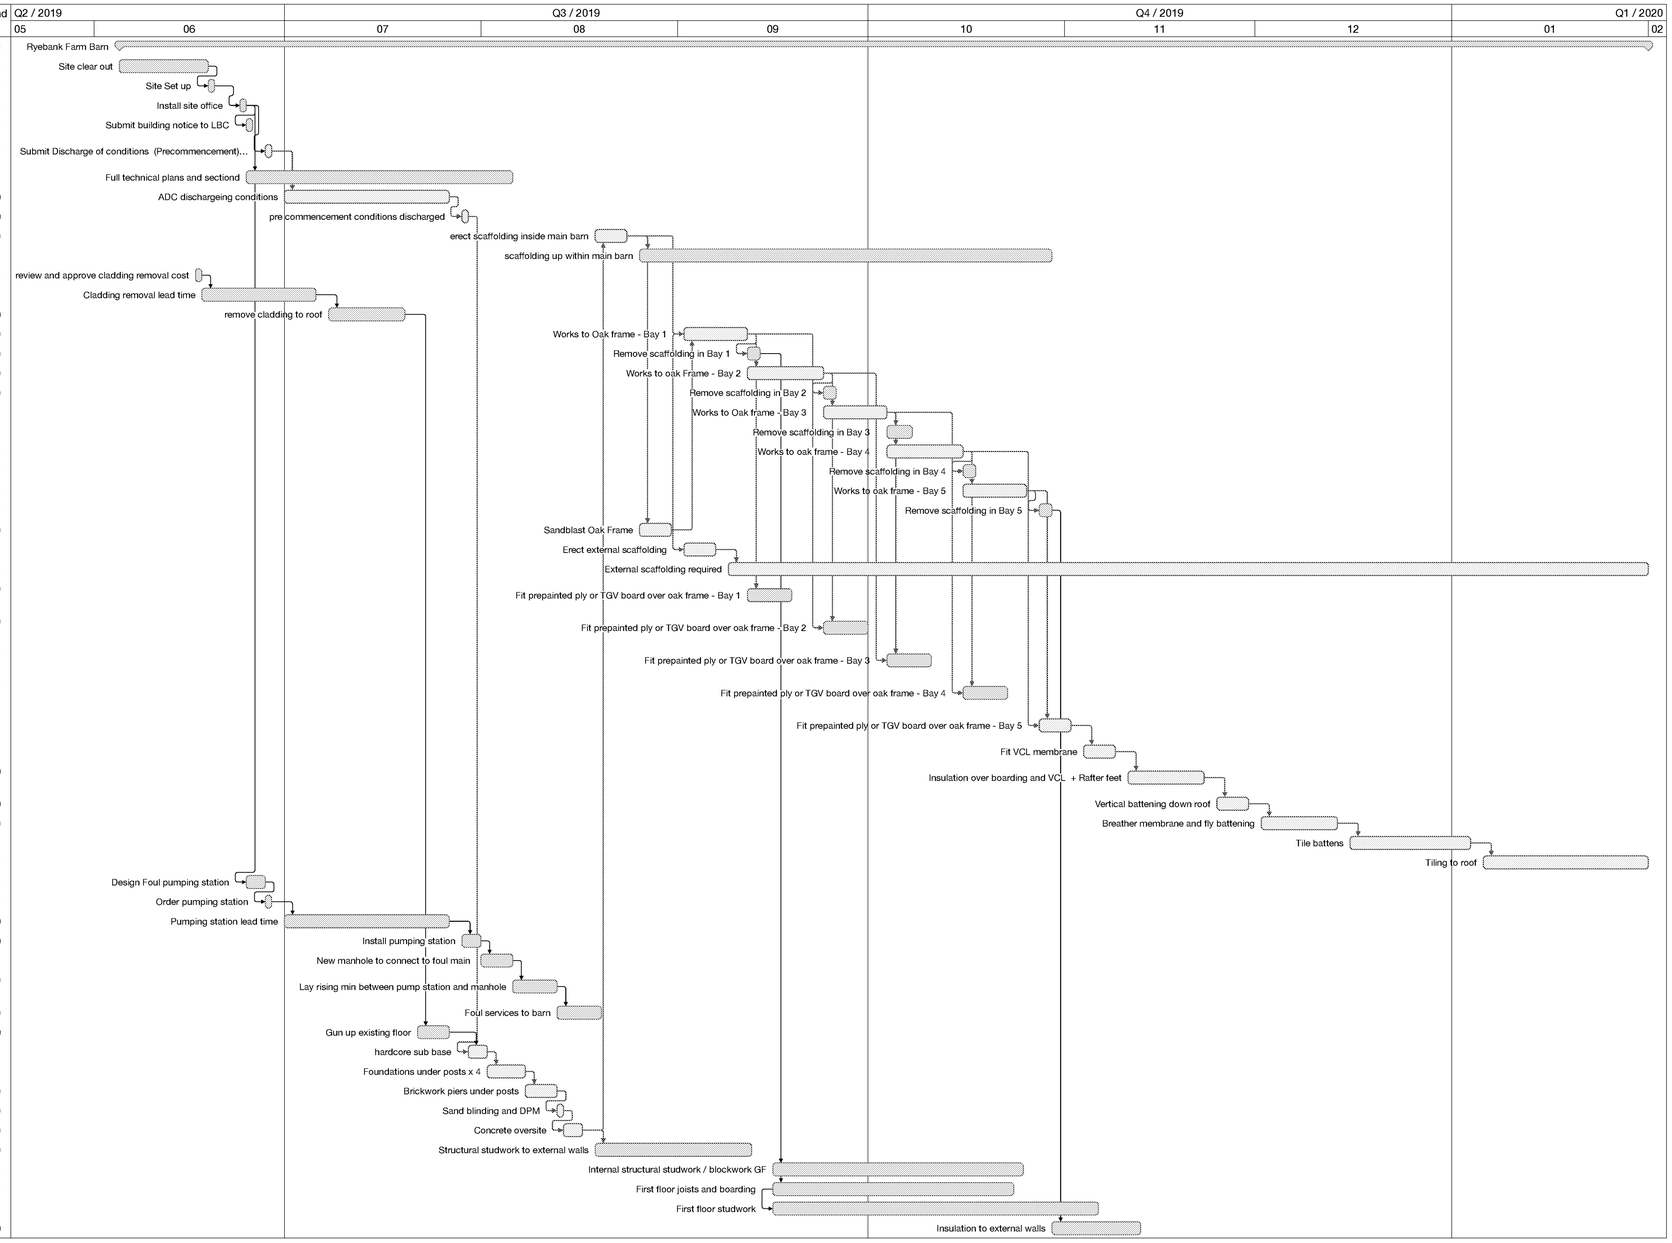
#	Traits	Title	Given Work	Predecessors	Expected Start	Expected End
0		**Ryebank Farm Barn**			**5 June 2019**	**31 Jan 2020**
1		Site clear out	2 weeks		5 June 2019	18 Jun 2019
2		Site Set up	1 day ?	1	19 Jun 2019	19 Jun 2019
3		Install site office	1 day ?	2	24 Jun 2019	24 Jun 2019
4		Submit building notice to LBC	1 day ?	3	25 Jun 2019	25 Jun 2019
5		Submit Discharge of conditions (Precommencement) to ADC	1 day ?	3	28 Jun 2019	28 Jun 2019
6		Full technical plans and sectiond	6 weeks	3	25 Jun 2019	5 Aug 2019
7		ADC dischargeing conditions	4 weeks	5	1 July 2019	26 July 2019
8		pre commencement conditions discharged	1 day ?	7	29 July 2019	29 July 2019
9		erect scaffolding inside main barn	1 week	50	19 Aug 2019	23 Aug 2019
10		scaffolding up within main barn	2.4m?	9	26 Aug 2019	29 Oct 2019
11		review and approve cladding removal cost	1 day ?		17 Jun 2019	17 Jun 2019
12		Cladding removal lead time	2.8 weeks	11	18 Jun 2019	5 July 2019
13		remove cladding to roof	2 weeks	12	8 July 2019	19 July 2019
14		Works to Oak frame - Bay 1	8 days	9; 24	2 Sep 2019	11 Sep 2019
15		Remove scaffolding in Bay 1	2 days	14	12 Sep 2019	13 Sep 2019
16		Works to oak Frame - Bay 2	8 days	14	12 Sep 2019	23 Sep 2019
17		Remove scaffolding in Bay 2	2 days	16	24 Sep 2019	25 Sep 2019
18		Works to Oak frame - Bay 3	8 days	16	24 Sep 2019	3 Oct 2019
19		Remove scaffolding in Bay 3	2 days	18	4 Oct 2019	7 Oct 2019
20		Works to oak frame - Bay 4	8 days	18	4 Oct 2019	15 Oct 2019
21		Remove scaffolding in Bay 4	2 days	20	16 Oct 2019	17 Oct 2019
22		Works to oak frame - Bay 5	8 days	20	16 Oct 2019	25 Oct 2019
23		Remove scaffolding in Bay 5	2 days	22	28 Oct 2019	29 Oct 2019
24		Sandblast Oak Frame	1 week	9	26 Aug 2019	30 Aug 2019
25		Erect external scaffolding	1 week	14SS	2 Sep 2019	6 Sep 2019
26		External scaffolding required	5.2m?	25	9 Sep 2019	31 Jan 2020
27		Fit prepainted ply or TGV board over oak frame - Bay 1	1 week	14	12 Sep 2019	18 Sep 2019
28		Fit prepainted ply or TGV board over oak frame - Bay 2	1 week	14; 16	24 Sep 2019	30 Sep 2019
29		Fit prepainted ply or TGV board over oak frame - Bay 3	1 week	16; 18	4 Oct 2019	10 Oct 2019
30		Fit prepainted ply or TGV board over oak frame - Bay 4	1 week	18; 20	16 Oct 2019	22 Oct 2019
31		Fit prepainted ply or TGV board over oak frame - Bay 5	1 week	20; 22	28 Oct 2019	1 Nov 2019
32		Fit VCL membrane	1 week	31	4 Nov 2019	8 Nov 2019
33		Insulation over boarding and VCL + Rafter feet	2 weeks	32	11 Nov 2019	22 Nov 2019
34		Vertical battening down roof	1 week	33	25 Nov 2019	29 Nov 2019
35		Breather membrane and fly battening	2 weeks	34	2 Dec 2019	13 Dec 2019
36		Tile battens	3 weeks	35	16 Dec 2019	3 Jan 2020
37		Tiling to roof	4 weeks	36	6 Jan 2020	31 Jan 2020
38		Design Foul pumping station	3 days	3	25 Jun 2019	27 Jun 2019
39		Order pumping station	1 day ?	38	28 Jun 2019	28 Jun 2019
40		Pumping station lead time	4 weeks	39	1 July 2019	26 July 2019
41		Install pumping station	3 days	40	29 July 2019	31 July 2019
42		New manhole to connect to foul main	3 days	41	1 Aug 2019	5 Aug 2019
43		Lay rising min between pump station and manhole	1 week	42	6 Aug 2019	12 Aug 2019
44		Foul services to barn	1 week	43	13 Aug 2019	19 Aug 2019
45		Gun up existing floor	1 week	13	22 July 2019	26 July 2019
46		hardcore sub base	3 days	8; 45	30 July 2019	1 Aug 2019
47		Foundations under posts x 4	4 days	46	2 Aug 2019	7 Aug 2019
48		Brickwork piers under posts	3 days	47	8 Aug 2019	12 Aug 2019
49		Sand blinding and DPM	1 day	48	13 Aug 2019	13 Aug 2019
50		Concrete oversite	3 days	49	14 Aug 2019	16 Aug 2019
51		Structural studwork to external walls	3.73 weeks	50	19 Aug 2019	12 Sep 2019
52		Internal structural studwork / blockwork GF	1.48 months	15	16 Sep 2019	25 Oct 2019
53		First floor joists and boarding	1.4 months	15	16 Sep 2019	23 Oct 2019
54		First floor studwork	1.87 months	53SS	16 Sep 2019	6 Nov 2019
55		Insulation to external walls	2 weeks	23	30 Oct 2019	12 Nov 2019
