
Lucion Environmental Ltd
Registered in England + Wales 6495874
VAT Registration Number 208156326

Asbestos Demolition Survey Report

Job Ref No: **472686**, Account Ref No: **21795**, Contract Ref No: **66629**

HMP Ford, Ford Road, Arundel, West Sussex, BN18 0BX

Title: HMP Ford - Demolition Surveys of Accommodation Buildings (Batch 3)

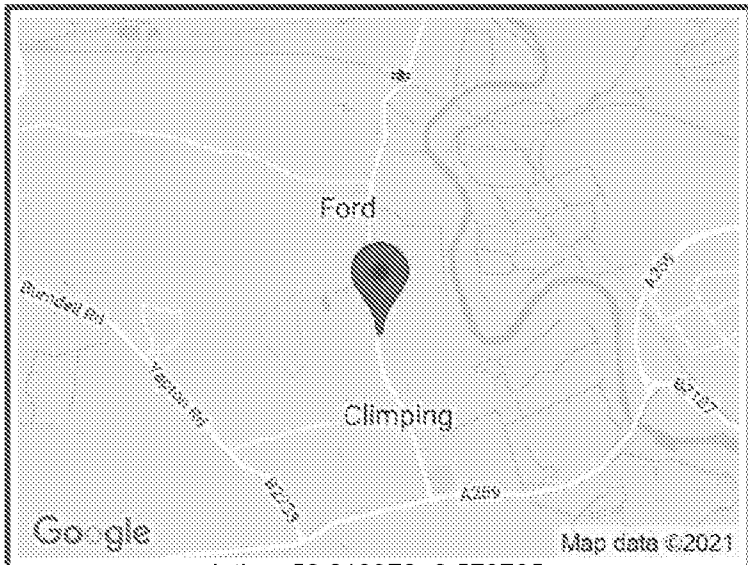

latlng: 50.816378,-0.579795



on site photo

Total Records	Analysed Records	No Asbestos Detected	R3	R2	R1
1574	543	396	137	10	0

Head Office
7 Halifax Court, Dunston,
Gateshead, NE11 9JT

Issuing Office:
South East & London
Lucion Environmental Ltd, Unit 22
Salbrook Road Industrial Estate,
Redhill, Surrey, RH1 5GJ

UKAS INSPECTION 0263

Report Summary

This certificate is for the attention of	**Terence Coston** **Gov Facility Services Limited (GFSL)** Accero 3, Concourse Way Sheaf Street Sheffield S1 2BJ United Kingdom
Contract Title	HMP Ford - Demolition Surveys of Accommodation Buildings (Batch 2)
Survey Type	Survey, Demolition
Site Address	HMP Ford, Ford Road, Arundel, West Sussex, BN18 0BX
Buildings Surveyed	Accommodation Hut G1, Accommodation Hut G2, Accommodation Hut H1, Accommodation Hut H2, Accommodation Hut I1, Accommodation Hut I2, Accommodation Hut O1, Accommodation Hut O2, Accommodation Hut P1, Accommodation Hut P2, external ducts for blocks P, G, H, O, I
Surveyor(s)	Luke Armstrong, James Timon, Doug Alexander
[redacted]	
Survey Date	Monday, 7th June, 2021 - Thursday, 10th June, 2021
Analyst(s)	Sarah Bell, Michaela White, Mark Davison, Kelly Harrison, Jennifer Hardy, Jennifer Gibson, Jarek Galik, Jake Scott
[redacted]	
Approved signatory	Joel Walker
[redacted]	
Approval date	Monday, 21st June, 2021
Report Rendered on	Mon 21 Jun 2021 @ 15:16:09

Report Contents

Asbestos Register and Executive Summary 4
Introduction 11
Buildings Included in Survey Scope 12
Site Data 13
Survey Methodology 14
HSG 264 Asbestos: The Survey Guide 14
Survey Methodology - Important Notes 15
Method of Sample analysis 17
HSG 248 Asbestos: The Analysts' Guide for Sampling, Analysis and Clearance Procedures 17
Sampling Strategy 18
Results and Findings 19
Initial Risk Level Assessment 19
Recommendations 22
Cited References and Further Reading 24
Management Recommendation Detail 25
Areas Excluded & Not Fully Accessed During Survey 74
Survey Inspection Detail, Sample Test Report and Risk Level Assessment Report 75
Annotated Plans and Other Additional Documents 263
Additional Advice and Information 263
Material Test Certificate 264
Annotated Floorplan(s) 272

Asbestos Register and Executive Summary

The current survey report is not intended to be used as a bill of quantities for asbestos removal activities. This survey can be used to compile a scope of work and technical specification. We can assist you in the preparation of these documents.

Summary of Asbestos Containing Materials

Ordered By Building, Level and Location

Building	Level	Location	Item / Product Examined	Material Description	Risk Level (Material Score)	Initial Control Recommendation
Accommodation Hut G1	0	001/corridor	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G1	0	002/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G1	0	003/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G1	0	004/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G1	0	005/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G1	0	006/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G1	0	007/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G1	0	008/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G1	0	009/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G1	0	013/kitchen	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G1	1	001/loft space	Slaters felt	Asbestos-containing bituminous product	R3 (3)	Remove
Accommodation Hut G1	9	999/externals	Wall panels with textured coating in porch	Asbestos-containing insulating board	R2 (6)	Remove
Accommodation Hut G1	9	999/externals	Ceiling panels with textured coating in porch	Asbestos-containing insulating board	R3 (6)	Remove
Accommodation Hut G2	0	001/corridor	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G2	0	002/plant room	Floor covering	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G2	0	005/kitchen	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G2	0	006/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G2	0	007/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G2	0	008/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G2	0	009/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G2	0	010/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G2	0	011/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove

table continued from previous page...

Building	Level	Location	Item / Product Examined	Material Description	Risk Level (Material Score)	Initial Control Recommendation
Accommodation Hut G2	0	012/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut G2	0	013/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	001/corridor	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	002/plant room	Lining panels to walls in electrical area	Asbestos-containing cement	R3 (4)	Remove
Accommodation Hut H1	0	002/plant room	Floor covering	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	005/kitchen	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	006/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	007/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	008/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	009/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	010/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	011/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	012/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	0	013/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H1	1	001/loft space	Slaters felt	Asbestos-containing bituminous product	R3 (3)	Remove
Accommodation Hut H2	0	001/corridor	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	0	002/plant room	Floor covering on duct cover and in electrical area	Asbestos-containing floor tile with bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	0	002/plant room	Floor covering	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	0	002/plant room	Walls	Asbestos-containing cement panels with textured coating	R3 (4)	Remove
Accommodation Hut H2	0	002/plant room	Ceiling	Asbestos-containing cement panels with textured coating	R3 (4)	Remove
Accommodation Hut H2	0	005/kitchen	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	0	006/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	0	007/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	0	008/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	0	009/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	0	010/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove

table continued from previous page...

Building	Level	Location	Item / Product Examined	Material Description	Risk Level (Material Score)	Initial Control Recommendation
Accommodation Hut H2	0	011/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	0	012/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	0	013/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut H2	1	001/loft space	Cement floor to boiler room below	Asbestos-containing cement	R3 (4)	Remove
Accommodation Hut I1	0	001/corridor	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	001/corridor	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	001/corridor	Cement debris in duct	Asbestos-containing cement	R2 (8)	Remove
Accommodation Hut I1	0	002/plant room	Cement debris in floor duct	Asbestos-containing cement	R2 (8)	Remove
Accommodation Hut I1	0	002/plant room	Lining panels to walls in electrical area	Asbestos-containing cement	R3 (4)	Remove
Accommodation Hut I1	0	002/plant room	Floor covering	Asbestos-containing floor tile with bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	005/kitchen	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	006/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	007/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	008/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	009/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	010/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	011/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	012/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I1	0	013/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	001/corridor	Cement debris in duct	Asbestos-containing cement	R2 (6)	Remove
Accommodation Hut I2	0	001/corridor	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	001/corridor	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	002/plant room	Ceiling	Asbestos-containing cement with textured coating	R3 (4)	Remove
Accommodation Hut I2	0	002/plant room	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	002/plant room	Floor covering	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	002/plant room	Walls	Asbestos-containing cement with textured coating	R3 (4)	Remove

table continued from previous page...

Building	Level	Location	Item / Product Examined	Material Description	Risk Level (Material Score)	Initial Control Recommendation
Accommodation Hut I2	0	005/kitchen	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	006/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	007/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	008/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	009/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	010/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	011/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	012/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	0	013/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut I2	1	001/loft space	Cement panels to ceiling below	Asbestos-containing cement	R3 (4)	Remove
Accommodation Hut O1	0	001/corridor	Felt debris in floor ducts	Asbestos-containing bituminous product	R2 (6)	Remove
Accommodation Hut O1	0	001/corridor	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	002/plant room	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	002/plant room	Floor covering	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	002/plant room	Floor tiles & adhesive	Asbestos-containing cement panels with textured coating	R3 (4)	Remove
Accommodation Hut O1	0	002/plant room	Cement lining to walls & ceiling	Asbestos-containing cement panels with textured coating	R3 (4)	Remove
Accommodation Hut O1	0	005/kitchen	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	006/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	007/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	008/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	009/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	010/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	011/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	012/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	0	013/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O1	1	001/loft space	Cement floor to boiler room below	Asbestos-containing cement	R3 (4)	Remove

table continued from previous page...

Building	Level	Location	Item / Product Examined	Material Description	Risk Level (Material Score)	Initial Control Recommendation
Accommodation Hut O2	0	001/corridor	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	002/plant room	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	002/plant room	Walls	Asbestos-containing cement panels with textured coating	R3 (4)	Remove
Accommodation Hut O2	0	002/plant room	Ceiling	Asbestos-containing cement panels with textured coating	R3 (4)	Remove
Accommodation Hut O2	0	002/plant room	Floor covering	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	005/kitchen	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	006/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	007/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	008/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	009/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	010/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	011/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	012/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	0	013/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut O2	1	001/loft space	Cement floor to boiler room below	Asbestos-containing cement	R3 (4)	Remove
Accommodation Hut P1	0	001/corridor	Floor tiles debris in floor ducts	Asbestos-containing floor tile with bitumen adhesive	R2 (8)	Remove
Accommodation Hut P1	0	001/corridor	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	0	002/plant room	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	0	002/plant room	Floor covering	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	0	005/kitchen	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	0	006/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	0	007/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	0	008/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	0	009/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	0	010/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove

table continued from previous page...

Building	Level	Location	Item / Product Examined	Material Description	Risk Level (Material Score)	Initial Control Recommendation
Accommodation Hut P1	0	011/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	0	012/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	0	013/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P1	9	999/externals	Wall panels with textured coating in porch	Asbestos-containing insulating board	R2 (5)	Remove
Accommodation Hut P1	9	999/externals	Ceiling panels with textured coating in porch	Asbestos-containing insulating board	R3 (5)	Remove
Accommodation Hut P2	0	001/corridor	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	002/plant room	Floor covering	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	002/plant room	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	005/kitchen	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	006/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	007/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	008/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	009/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	010/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	011/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	012/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	0	013/bedroom	Subfloor	Asbestos-containing bitumen adhesive	R3 (3)	Remove
Accommodation Hut P2	9	999/externals	Ceiling panels with textured coating in porch	Asbestos-containing insulating board	R3 (5)	Remove
Accommodation Hut P2	9	999/externals	Wall panels with textured coating in porch	Asbestos-containing insulating board	R2 (5)	Remove
external ducts for blocks P, G, H, O, I	9	999/externals ducts	Shuttering through out the ducts	Asbestos-containing cement	R3 (4)	Remove
external ducts for blocks P, G, H, O, I	9	999/externals ducts	Cement debris in ducts	Asbestos-containing cement	R2 (6)	Remove
external ducts for blocks P, G, H, O, I	9	999/externals ducts	Pipework flange gasket through out the ducts	Asbestos-containing gasket	R2 (7)	Remove

Summary of Areas Excluded & Not Fully Accessed During Survey

Building	Level	Location	Item / Product Examined	Accessibility	Access Comments
external ducts for blocks P, G, H, O, I	9	999/externals ducts	***Entire Location***	Limited Access	reasons of health and safety
				Due to services and depth of duct	

Introduction

This report aims to:

- Introduce pertinent legislation relating to the management of asbestos in non-domestic premises
- Outline the sample testing and inspection methodology employed by the surveyor
- Relate the significance of the report contents to the Control of Asbestos Regulations (2012)
- Detail survey findings compliant with HSG 264
- Serve as a reference document to assist in making further steps towards the management of any asbestos containing materials in the premises
- Provide the information necessary to compile an asbestos management plan compliant with the Control of Asbestos Regulations (2012)
- Form an asbestos register

Regulation 4 of the Control of Asbestos Regulations (2012) states the obligations that persons defined as "duty holders" have to manage asbestos containing materials in non-domestic premises. This instrument defines a duty holder as being:

> *"Every person who has, by virtue of a contract or tenancy, an obligation of any extent in relation to the maintenance or repair of non-domestic premises or any means of access thereto or egress there from; or*
>
> *In relation to any part of non-domestic premises where there is no such contract or tenancy, every person who, to any extent, has control of that part of non-domestic premises or any means of access thereto or egress there from" -* ***CAR, 2012.***

Regulation 4 also states the following:

> *"In order to enable him [sic "dutyholder"] to manage the risk from asbestos in non-domestic premises, the dutyholder shall ensure that a suitable and sufficient assessment is carried out as to whether asbestos is or is liable to be present in the premises"*

This report satisfies this requirement, unless stated otherwise, by detailing the inspection findings reporting the presence of asbestos containing materials in those areas given in the survey inspection detail.

Health and Safety Guidance - Publication "Asbestos: The Survey Guide (HSG 264)" details the material assessment that must be carried out to determine the risk posed by asbestos containing materials in buildings. This material risk assessment has been carried out on those materials strongly presumed or proven to contain asbestos. The resulting material assessment risk ratings can (in conjunction with the management recommendation made for these materials) then be used to form the basis of an asbestos management plan.

Where possible the surveyor has attempted to interpret the needs of the client in their demolition works however the reader must satisfy themselves that the report includes those areas affected by demolition works.

Buildings Included in Survey Scope

Site Address: **HMP Ford, Ford Road, Arundel, West Sussex, BN18 0BX**

Surveyed Buildings: **Accommodation Hut G1, Accommodation Hut G2, Accommodation Hut H1, Accommodation Hut H2, Accommodation Hut I1, Accommodation Hut I2, Accommodation Hut O1, Accommodation Hut O2, Accommodation Hut P1, Accommodation Hut P2, external ducts for blocks P, G, H, O, I**

Every effort has been made to identify all asbestos materials so far as was reasonably practical to do so within the scope of the survey and the attached report. Methods used to carry out the survey were agreed with the client prior to any works being commenced by way of acceptance of our contract / quotation.

This survey was conducted in accordance with Health and Safety Guidance - Publication "Asbestos: The Survey Guide (HSG 264)". Lucion Environmental Ltd cannot accept any liability for loss, injury, damage or penalty issues that arise for reasons of survey scope limitations. Lucion Environmental Ltd cannot be held responsible for any damage caused as part of this survey carried out on your behalf. Due to the nature and necessity of sampling for asbestos some damage is unavoidable and will be limited to that necessary for taking of the samples.

The "areas excluded and not fully accessed during survey" section of this report gives details of those buildings, locations and items not accessed at the time of the survey (where appropriate, and if all areas were fully accessed, no items are listed). The "included buildings" list above gives details of those buildings included in the survey scope. The inspection log should be referenced for details of specific locations inspected within these buildings.

The scope of this survey relates only to building or area(s) inspected and does not include any form of investigation of the land on which the building is situated.

Where investigation of an intrusive nature (within the scope of the survey being performed) is needed to discern the presence of a material and the property is occupied during the inspection the level of intrusion may be restricted. As far as is reasonably practicable such restrictions will be indicated within the "areas excluded & not fully accessed during survey" section of this report. Scenarios leading to intrusion restriction may [by way of example] include (but are not limited to) security integrity of the building envelope, significant damage to decorative finishes, risk to the structural integrity of the building, occupation within adjacent areas. Investigations undertaken in such situations may, through circumstantial restrictions, be incomplete. Further investigation works may be required once unrestricted access can be offered.

A report is provided electronically via the NexGen web-portal. Rendering of the report will create a unique pdf version identified in the footer of the document where date and time of rendering is recorded. Document history can be reviewed via the 'View File History' when viewing the report online. Prior to commencing any works or review of the report, the most current version should be obtained via the link to the NexGen web-portal; any local pdf copies should not be relied on as containing the most current information.

As per the client's specification, materials previously identified as containing asbestos (by other asbestos consultancies) have had this positive identification transferred to this report. Lucion Environmental Ltd cannot accept any liability for errors in this information.

Items or areas <u>not</u> covered by this survey that are scheduled to undergo demolition should be investigated prior to commencement of such activities.

Site Data

Site ID	92833
Address	HMP Ford, Ford Road, Arundel, West Sussex, BN18 0BX
Property Type	Prison

Survey Methodology

The asbestos survey findings detailed in this report were gathered using documented in house inspection (TOP01.01) and sampling procedures (TOP01.02) that implement the requirements of the Health and Safety Executive Publications HSG 264 (Asbestos: The survey guide) and HSG 248 (Asbestos: The analysts' guide for sampling, analysis and clearance procedures). All asbestos surveys aim to locate as far as is reasonable practical, the presence and extent of any ACMs in the building within the defined scope of the survey (refer HSG 264). This method complies with section 3 of Regulation 4 (CAR, 2012)

HSG 264 Asbestos: The Survey Guide

Publication HSG 264 sub-divides asbestos surveys into 2 principal types, termed: Management and Refurbishment & Demolition surveys respectively. These survey types may be summarised as follows (both have been shown to allow visualisation of the scope of the present management survey relative to the refurbishment & demolition survey specification and their suggested application/s).

Management Survey - Standard Sampling, Identification and Assessment

The underlying purpose and inspection methodology of the management survey is to locate the presence, extent and condition by way of sampling and inspection of suspect asbestos containing materials as they are encountered. Where possible, representative samples of materials suspected by the surveyor to contain asbestos are taken and analysed for the presence and type of asbestos fibre present. This survey is intended for integration into a plan for the management of asbestos containing materials under Regulation 4 of CAR (2012). The management surveys offers information allowing routine and simple maintenance works to be carried and this reflects the surveyor's level of intrusion at the time of the inspection. More extensive maintenance or repair work may require additional investigations to be undertaken; the findings of this survey should be checked with this in mind to confirm whether or not they of adequate scope.

Demolition Survey - Full Access, Sampling and Identification

The demolition survey is fully intrusive (as far as is reasonably practicable) and is aimed at locating all asbestos containing materials within the whole building if demolition is planned.

For refurbishment and demolition surveys, normally, unless otherwise specified (refer to the Method Statement as listed in Annotated Plans and Other Additional Documents section of this document), fully invasive and possibly destructive investigation of all survey areas or the whole building, in order to locate and assess all materials suspected as containing asbestos, will be undertaken. The survey records only the location and estimated extent of asbestos containing materials. A priority rating has been assigned to asbestos containing materials encountered during the course of the inspection to aid ongoing management of these materials prior to refurbishment (HSG 264 states a duration in excess of 3 months as requiring ongoing management of ACMs). Recommendations made for material management are based solely on isolated item inspection and material assessment and may be subject to change in the context of the overall refurbishment works. However, the surveyor will default to "remove" as a recommendation within a refurbishment or demolition survey. These types of survey are normally recommended prior to refurbishment work commencing in the survey area or demolition of the whole building. There is a specific requirement in CAR (2012) (Regulation 7) for all asbestos containing materials to be removed as far reasonably practicable before refurbishment or demolition.

Survey Methodology - Important Notes

Reasonable Skill and Care

Although all survey areas that have been examined are reported in accordance with HSG 264 and documented in house procedures (for the specified survey type) and all reasonable skill and care has been exercised by the surveyor in doing so, it must be realised that no survey can reasonably guarantee beyond doubt that all asbestos containing materials have been located. Reasons for this limitation may include health and safety issues, reasons of practicality, non-access to live equipment and dangerous or contaminated environments or risk of unsafe levels of damage being inflicted on the survey area amongst others, or the location of the material being outside the investigative scope of the survey type undertaken.

Please note, refurbishment and demolition asbestos surveys are used to locate and describe, as far as reasonably practicable, all asbestos containing materials in the area where the refurbishment work will take place or in the whole building if demolition or refurbishment is planned. To do this, investigations will need to be of an intrusive nature and involve destructive inspection techniques. Notwithstanding the purpose of refurbishment and demolition surveys, the practical reality is that no survey should ever be used as an absolute guarantee to have identified all asbestos containing materials. Destructive inspection points will be in locations intended to represent the structure as a whole. Therefore, there remains the potential for hidden, obscured and discrete areas within the building fabric and/or structure that may contain unlocatable asbestos containing materials that may only become apparent during demolition or refurbishment activities.

Non-asbestos Materials - A Reasoned Argument

All items examined by the surveyor at the time of the survey are listed in the inspection detail of this report. This detail includes those items believed by the surveyor not to contain asbestos and an appropriate categorisation of their material composition is given. Employing this rationale the surveyor can use experience and judgement to form a reasoned argument that there is evidence to suggest that the material may not contain asbestos. Periodically "non-asbestos" building materials may be sampled by way of a method control to further support the surveyor's argument. These materials do not bear any risk assessment detail.

Materials Presumed to Contain Asbestos

If the surveyor feels that a reasoned argument against a material containing asbestos cannot be formed, the item in question may be presumed to contain asbestos. This may include, but is not restricted to, areas where access cannot be gained. This scenario attracts the designation "P" in the sampling strategy column of the "Survey Inspection Detail, Sample Test Report and Risk Level Assessment Report" table within this report.

Materials Strongly Presumed to Contain Asbestos

In the case of a material or materials being encountered that the surveyor suspects, following visual assessment, as containing asbestos but cannot be sampled for reasons of practicality, that material is strongly presumed to contain asbestos. An assessment (where possible) of the material's extent and condition is made. Nota bene: as no definitive assessment of asbestos fibre type contained in the material may be made, this portion of the priority score is based on a strongly presumed worst-case scenario of fibre type commonly contained in the material concerned. This scenario attracts the designation "SP" in the sampling strategy column of the "Survey Inspection Detail, Sample Test Report and Risk Level Assessment Report" table within this report.

Sampling of Materials

If access to the material permits, a representative sample of the material is taken according to the "sampling strategy". An assessment (where necessary or possible) of the material's extent and condition is made. As no practical sampling strategy can be assured as being entirely representative of the circumstances encountered during surveying, care should be exercised when interpreting results. That is to say that if works are planned that may cause disturbance or require the removal of asbestos containing materials, implementation of a more intense sampling regime may be desirable.

Floor slab - The term “floor slab” can constitute a floor to any level and is not just limited to the ground floor. These areas have not been intrusively inspected to any particular depth. An inspection has been carried out as far as practicable which may have involved the scraping of any superficial top layer but this does not constitute as a full depth intrusive inspection of the slab. Should this level of inspection be required for future works then specialist heavy engineering drilling tools will be required to be used followed by a further specific survey to this area on completion.

Material Cross Referencing

In the event of a suspect material being encountered with a frequency that does not permit repeated re-sampling on the grounds of practicality, the surveyor may cross reference this item with one that has already been sampled. To do this the surveyor will ensure that the material is identical in nature (through examining visual appearance e.g. colour) to that of the material to which it is referenced. Nota bene: as no definitive assessment of asbestos fibre type contained in the material may be made, this portion of the priority score is strongly presumed as being the same as that of the material from which it is cross referenced.

Asbestos Removal

It should be noted that this report is not intended to be used as a bill of quantities for the removal of asbestos containing materials; it purely provides support. Extents and quantities recorded during the survey have been estimated to the best of the surveyor’s ability, however, these shall require verification and accurate measurement prior to removal of the asbestos containing materials through production of an appropriate Technical Specification and Scope of Works. These documents can be prepared by Lucion upon request.

Operational Buildings

The inspection and testing will be conducted to minimise any disruption to the occupiers as far as practical. To this end, the building or area undergoing survey should be unoccupied in order to minimise risk to employees or members of the public on the premises. Ideally, the building or area will not be in use and all furnishings will have been removed. It should be noted that occupied or operational buildings may place certain restrictions on the scope of the survey in respect of intrusive access and sampling strategy, for example it will not be possible to inspect behind a ceiling which is a known or suspected ACM, and that it may prove impossible to adequately investigate all areas of the property at the time of the initial survey. Where this is the case it may be required to undertake additional surveys or inspections immediately prior to the proposed refurbishment or demolition works at a time and cost agreed with the client. Aspects of these additional inspections, e.g. penetration of known ACMs, may also require the services of a Licensed Asbestos Removal Contractor and notification of the work to the Enforcing Authority. It is the client’s responsibility to ensure that the information provided in the survey is adequate and relates to their requirements.

Dust Sampling

The survey may include taking dust samples from areas where contamination is suspected to be present due to visible signs of damage to asbestos containing materials or signs of previous unsatisfactory asbestos removal works but does not include random dust sampling where there is no apparent source of asbestos.

Stored, portable and random use

Unless specifically identified within the report, no responsibility can be accepted by Lucion for non-systematic or random use of asbestos within the property or in contrast to the products and uses as detailed in HSG264 Appendix 2, for example adhoc use of packers in cavities (wall, floor, ceiling). Not only are these items small, but their occurrence is sporadic and they may only become visible once complete sections of wall, floor or ceiling are removed during demolition or refurbishment. In addition, unless specifically identified within the report, no responsibility can be accepted by Lucion, for stored or portable items of asbestos.

Method of Sample analysis

The bulk asbestos fibre identification results detailed in this report and the appended certificate of bulk analysis were obtained using a documented in house testing procedure (TOP01.03) that implements the requirements of Health and Safety Executive Publication HSG 248, Appendix 2 (Asbestos: The analysts' guide for sampling, analysis and clearance procedures). All samples collected during the course of this survey are tested in accordance with this method.

HSG 248 Asbestos: The Analysts' Guide for Sampling, Analysis and Clearance Procedures

Publication HSG 248 describes a two stage approach to the detection and subsequent identification of asbestos fibre in bulk (i.e. suspect sample) materials. Initially the microscopist will examine the material under a low power stereo light microscope. The microscopist then performs extensive optical tests using polarised light microscopy in order to confirm or refute that the material contains an asbestos mineral. This technique allows for the detection of the six common forms of asbestos fibre as follows:

Asbestos Fibre Type	Common Nomenclature
Chrysotile	White Asbestos
Amosite	Brown Asbestos
Crocidolite	Blue Asbestos
Asbestos Actinolite	N/A
Asbestos Anthophyllite	N/A
Asbestos Tremolite	N/A

The results of this test are given, where appropriate, in the inspection detail report for each sample taken and are summarised in the management recommendation report. They are also separately detailed in the bulk-analysis report appended to this report. The homogeneity of asbestos containing materials can differ depending on their type. Typically, homogeneous materials include sprayed coatings, insulating board and asbestos cement products. Other materials are typically less homogeneous including pipe lagging (due to patch repairs, hand mixing at time of application), textured coatings (due to low concentration of asbestos fibre and hand application), composites (due to low concentration of asbestos fibre and material matrix) and debris samples (due to the potentially inconsistent occurrences that have led to their presence). Whilst sampling frequencies / techniques and analysis methods attempt to address the issue of non-homogeneity it should be realised that sampling in accordance with HSG 264 and analysis in accordance with HSG 248 cannot always obviate the problems of determining asbestos fibre content in non-homogeneous materials. The results of sample analysis presented in this report therefore pertain to the samples analysed and so relate only to the time at which sampling took place and to the conditions prevailing during that time.

Sampling Strategy

Product Type	Sampling Strategy
Vinyl, composite floor coverings, surface coverings	One sample per room, or one sample per 40m^2 per product type or colour. Where large expanses of the same material have been used throughout an area, the frequency of sampling may be decreased at the discretion of the surveyor. Associated adhesives, depending on site and material conditions, will either be collected as separate samples or included with the floor covering as a single entity.
Textured Coatings	One composite sample per room or one sample per 9m^2 dependent on similarity of coating type. Where large expanses of the same material have been used throughout an area. The frequency of sampling may be increased or decreased at the discretion of the surveyor.
Gaskets, ropes, woven product, seals, mastics, papers, felts	One sample per product type, or if appropriate, per area or location.
Asbestos containing insulating board	One sample per location or per 25m^2 of continuous product run. The frequency of sampling may be increased or decreased at the discretion of the surveyor dependent on such factors as consistency of product type or occurrence of different board types. The specific nature of this material has been determined on site using the competence and experience of the surveyor. Lucion Environmental accepts no liability for any decision based on this determination and as such it should only be regarded as an opinion. Where doubt exists as to the classification of a board material HSE Approved Code of Practice L143 "Managing and working with asbestos" recommends carrying out a water absorption test. Lucion Environmental will perform this test only upon specific request.
Cement Products	One sample per product type, or if appropriate, per area or location. The specific nature of this material has been determined on site using the competence and experience of the surveyor. Lucion Environmental accepts no liability for any decision based on this determination and as such it should only be regarded as an opinion. Where doubt exists as to the classification of a board material HSE Approved Code of Practice L143 "Managing and working with asbestos" recommends carrying out a water absorption test. Lucion Environmental will perform this test only upon specific request.
Debris	One sample per location, or more at the discretion of the surveyor. Where debris exists in a location quantification can be hindered by a number of factors including paint coverings, air movement, the passage of time etc. The surveyor reports only the material discernable within the confines of the survey sufficient to show that debris exists in a location. Further focused investigation may be needed to determine the extent of debris for the purposes of decontamination.
Insulative Materials	One sample per material product type (to include change in outward appearance) and at least one sample per 10 metre pipe run. In addition, one sample per different product applied to pipe bends.
Sprayed Insulation	One sample per 20m^2 of material

Results and Findings

The item examination and inspection findings, bulk analysis results, material assessment and initial risk level assessment are reported in the form of an asbestos inspection and testing detail register. The purpose and structure of this register are explained in the proceeding sections.

Initial Risk Level Assessment

The initial risk level assessments made within this report for those items strongly presumed, or positively proven by sampling and subsequent analysis, to contain asbestos have been made on the basis of the Material Assessment Algorithm detailed within the publications HSG 264 and HSG 227.

This assessment aims to elucidate the potential for a particular material to release hazardous fibres and expose those within the specific area to asbestos dust. The following table gives the scoring strategy for the initial risk level assessment and indicates the scoring degree of those points that are considered, namely product type, condition, surface treatment and asbestos fibre type present.

	Score	Score Category
Product Type An assessment of the inherent risk a product may pose (Product debris is assessed on the product type from which it originates)	1	**Asbestos reinforced composites** - Plastics / resins / mastics / felts / vinyl tiling / semi rigid paints / decorative finishes / asbestos cement and other such similar bound materials.
	2	**Materials of a medium asbestos content including** - Asbestos insulating board / millboard / low density insulation board / textiles / gaskets / ropes / papers / debris from asbestos containing composite material and cement.
	3	**Materials of a high asbestos content including** - Thermal insulation / sprayed asbestos / loose asbestos / packing / filled padding / all other debris.
Material Condition An assessment of the damage or deterioration in condition of product	0	**Undamaged** - No visible signs of damage
	1	**Minor damage** - Light material surface abrasion / abrasion to edges
	2	**Medium damage** - Evidence of loose asbestos fibre protruding from material / poor condition of material is notable
	3	**Major damage** - Significant damage to materials often resulting in the short-term production of asbestos containing debris / delamination of sprays and thermal insulation / asbestos debris

table continued from previous page...

	Score	Score Category
Surface Treatment An assessment of the level of fibre retention the surface of a material may be capable of	0	**Composite materials** - Plastics / resins / mastics / felts / vinyl tiling / semi rigid paints / decorative finishes
	1	**Sealed and enclosed materials** - Painted asbestos insulating board (with exposed face painted or encapsulated) / enclosed asbestos lagging and sprayed asbestos (as originally installed) / unsealed asbestos cement products
	2	**Unsealed and encapsulated materials** - Unsealed asbestos insulating board / asbestos lagging, sprayed asbestos and woven material encapsulated (remedially)
	3	**Unsealed friable materials** - Unsealed asbestos lagging and sprayed asbestos
Asbestos Fibre Type An assessment of asbestos fibre types propensity to cause asbestos related diseases	1	**Serpentine Asbestos** - Chrysotile
	2	**Amphibole Asbestos** - Amosite / Anthophyllite / Tremolite / Actinolite
	3	**Amphibole Asbestos** - Crocidolite

Material / Accessibility Score

Following the rating of a material using the above criteria, the resulting aggregated additive material score may be assessed in terms of accessibility to derive an assessment of initial risk level as follows:

	Very Low Risk (2-4)	Low Risk (5-6)	Medium Risk (7-9)	High Risk (10-12)
Normally Inaccessible (1)	R3	R3	R3	R2
Periodically Accessed (2)	R3	R3	R2	R1
Frequently Accessed (3)	R3	R2	R1	R1

The level of access to the ACM determines how easily the product can be reached by the building occupants which could result in a disturbance that causes fibre release, it relates purely to access and does not consider product type.

The above is defined by the following:

1. Normally inaccessible or occasionally accessed: The ACM will not be accessed or is unlikely to be disturbed.
2. Periodically accessed: The ACM is likely to be disturbed occasionally.
3. Frequently accessed: The ACM is routinely and easily disturbed.

General Interpretation of Risk Assessment Level

>

Risk Assessment Level	Interpretation of the Recommended Control Action [1]
P1	immediate implementation
R2	as soon as practicable - *in interim period material should be regularly inspected and its management planned for*
R3	not immediately necessary - *material should be regularly inspected and its management planned for*

Recommendations

In addition to the risk assessment level assigned to strongly presumed and identified asbestos containing material, a management control action recommendation is also made. In the case of survey carried our prior to refurbishment or demolition works, the "normal" recommendation will be "remove" as the surveyor assumes that asbestos removal will take place prior to other works commencing (unless the surveyor has been advised otherwise in advance of the survey). However in certain circumstances another recommendation may be made and those commmonly used are given in the recommendations table.

The current recommendations conventionally made by the surveyor may include the following:

Recommendation	Description	Notes
Access Restriction	Restriction of access to area / location only to personnel wearing appropriate PPE / RPE.	Suitability of RPE / PPE must be carefully assessed and procedure invoked to ensure these control measures are adhered to.
Access Prohibition	Prohibition of access to area / location to all personnel.	Area should be marked clearly as being prohibited to all personnel, possibly in conjunction with asbestos warning stickers.

1. The risk level assessment is determined on the basis of information (including a subjective 'access' assessment) collated during the course of the survey. The risk assessment level needs to be reviewed periodically,(normally in line with a frequency defined in an asbestos management plan) to verify its validity and prior to any refurbishment work within the building/ site. Note: this risk level assessment is outside Lucion's scope of UKAS accreditation.

table continued from previous page...

Recommendation	Description	Notes
Environmental Clean	A cleanup of areas following disturbance of asbestos or discovery of loose asbestos dust/debris/material.	The work is not removal (i.e. requiring physical force) and consists of vacuuming, wiping, picking up and bagging of debris. The work can be either licensed or unlicensed depending on the product and whether exposure is likely to exceed the 4 hour control limit or sporadic and low intensity limit. For licensed work a 4-stage clearance by a UKAS accredited laboratory is required, whilst for non-licensed work appropriate air tests are recommended and as long as any work with insulation or insulating board materials does not take more than two hours in any seven day period, and no one person works for more than one hour in that two hour period.
Material Repair	Repair of the material in such a manner as to minimise the release of asbestos fibre.	Repair of materials is recommended by the Health and Safety Executive as an alternative to removal, where reasonably safe to so.
Material Encapsulation	Encapsulation of the material in a manner that ensures the complete enclosure of any remaining asbestos fibres.	Encapsulation of materials is a possible alternative to their removal, where reasonably safe to do so. Works should also be accompanied by appropriate air test performed by a UKAS accredited laboratory.
Material Removal	Removal of the material in instances where it is remaining in situ would lead to a high residual risk level. Or removal may be necessary to permit work within the location. Removal of materials may also be carried out on a preventive basis.	Removal works should be carried out in accordance with the relevant ACOP (approved code of practice), L143

Any recommendations made within this report are made on the basis of findings collated at the time of survey.
Recommendations should undergo careful client evaluation prior to a final management decision being made.
Lucion Environmental Ltd does not accept any responsibility for any works carried out as a result of recommendations made within this report.

Cited References and Further Reading

1. Control of Asbestos Regulations (2012) ~ The Stationery Office. **ISBN 978-0111521083**
2. Construction (Design and Management) Regulations (2015) ~ The Stationery Office. **ISBN 9780717666263**
3. The Hazardous Waste (England and Wales) Regulations (2005) ~ The Stationery Office. **ISBN 011072685-5**
4. Managing and working with asbestos Control of Asbestos Regulations 2012. Approved Code of Practice & guidance L143 (second edition, 2013) ~ HSE Books. **ISBN 978-0717666188**
5. A Comprehensive Guide to Managing Asbestos in Premises (2002) ~ HSE Books. **ISBN 978-0717623815**
6. Asbestos Essentials: A task manual for building, maintenance and allied trades of non-licensed asbestos work (third edition, 2012) ~ HSE Books. **ISBN 978-0717665037**
7. Asbestos Essentials Task Sheets [http://www.hse.gov.uk/asbestos/essentials/] ~ HSE. *electronic downloadable version of the above*
8. Asbestos: The licensed contractors' guide HSG247 (2006) ~ HSE Books. **ISBN 978-0717628742**
9. Asbestos: The analysts' guide for sampling, analysis and clearance procedures HSG248 (2005) ~ HSE Books. **ISBN 978-0717628759**
10. Asbestos: The Survey Guide HSG 264 (second edition, 2012) ~ HSE Books. **ISBN 978-0717665020**
11. The Management of Health and Safety at Work Regulations (1999) ~ The Stationery Office. **ISBN 011085625-2**
12. The Health & Safety at Work etc. Act (1974) ~ The Stationery Office.

Management Recommendation Detail

Please note, this report is not intended to be used as a bill of quantities for the removal of asbestos containing materials. The designing, planning and costing of asbestos removal requires an appropriate Technical Specification and Scope of Works. These documents can be prepared by Lucion upon request.

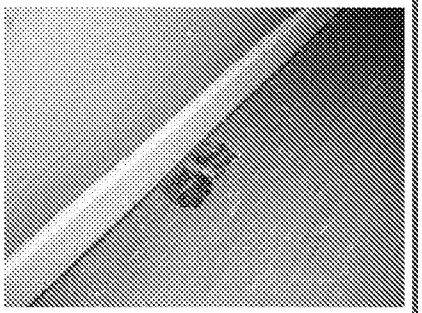
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut G1	0	001/ corridor	Subfloor	472686-3	Asbestos-containing bitumen adhesive	Chrysotile	3	24 Sqm.	R3	Remove	
Accommodation Hut G1	0	002/ bedroom	Subfloor	472686-3	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G1	0	003/ bedroom	Subfloor	472686-3	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...


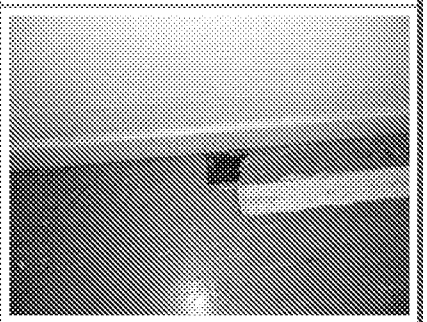
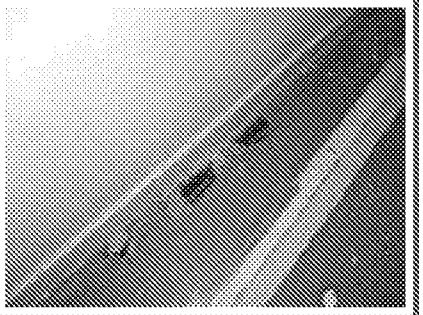
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut G1	0	004/ bedroom	Subfloor	472686-3	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G1	0	005/ bedroom	Subfloor	472686-3	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G1	0	006/ bedroom	Subfloor	472686-3	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

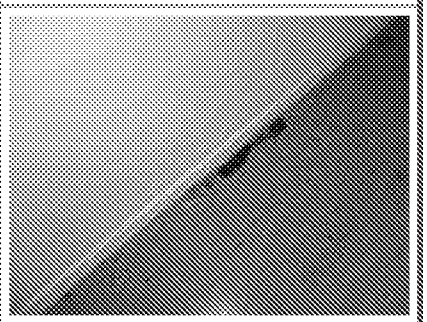
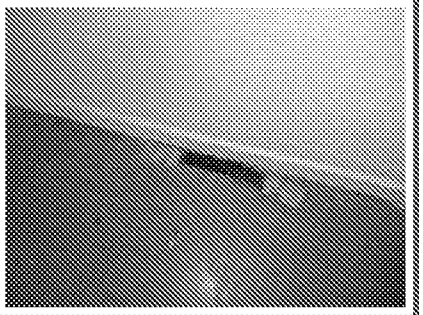
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut G1	0	007/ bedroom	Subfloor	472686-3	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G1	0	008/ bedroom	Subfloor	472686-3	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G1	0	009/ bedroom	Subfloor	472686-3	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

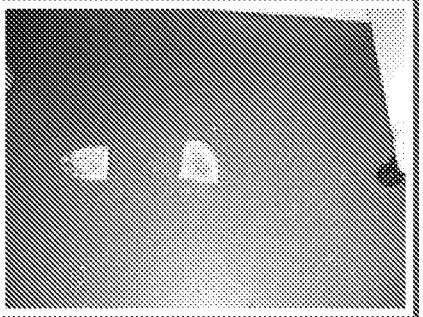
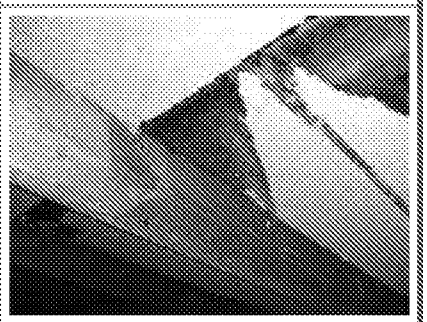
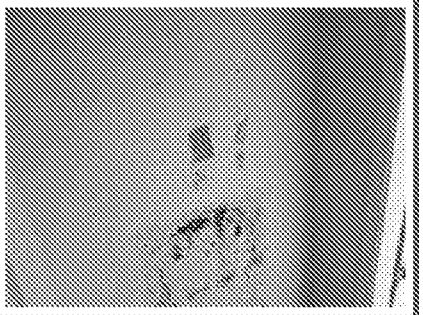
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut G1	0	013/ kitchen	Subfloor	472686-3	Asbestos-containing bitumen adhesive	Chrysotile	3	8 Sqm.	R3	Remove	
Accommodation Hut G1	1	001/loft space	Slaters felt	472686-8	Asbestos-containing bituminous product	Chrysotile	3	100 Sqm.	R3	Remove	
Accommodation Hut G1	9	999/ externals	Wall panels with textured coating in porch	472686-11	Asbestos-containing insulating board	Amosite, Chrysotile	6	6 Sqm.	R2	Remove	

table continued from previous page...


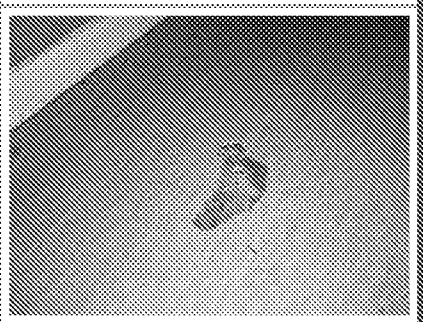
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut G1	9	999/ externals	Ceiling panels with textured coating in porch	472686-10	Asbestos-containing insulating board	Amosite, Chrysotile	6	2 Sqm.	R3	Remove	
Accommodation Hut G2	0	001/ corridor	Subfloor	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	21 Sqm.	R3	Remove	
Accommodation Hut G2	0	002/plant room	Floor covering	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	4 Sqm.	R3	Remove	

table continued from previous page...

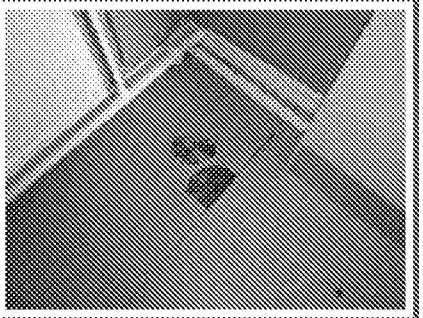

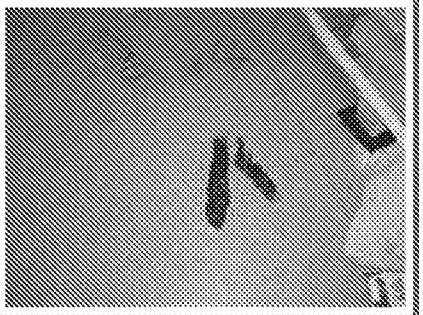
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut G2	0	005/ kitchen	Subfloor	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G2	0	006/ bedroom	Subfloor	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G2	0	007/ bedroom	Subfloor	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

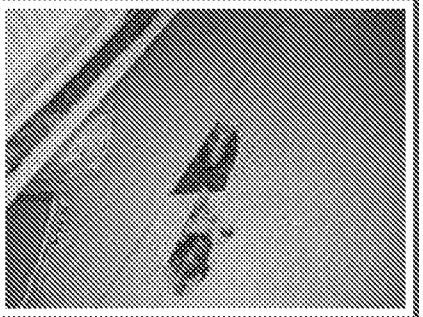
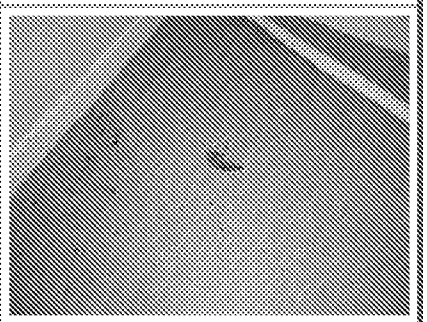
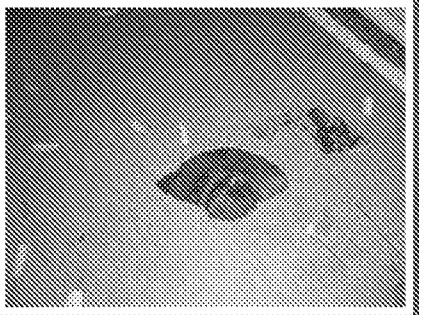
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut G2	0	008/ bedroom	Subfloor	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G2	0	009/ bedroom	Subfloor	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G2	0	010/ bedroom	Subfloor	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

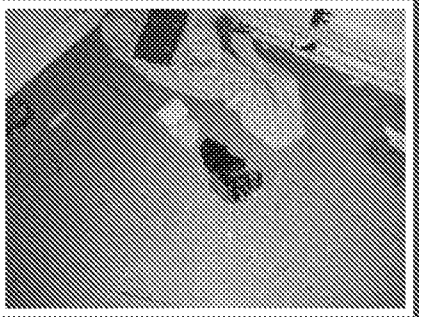
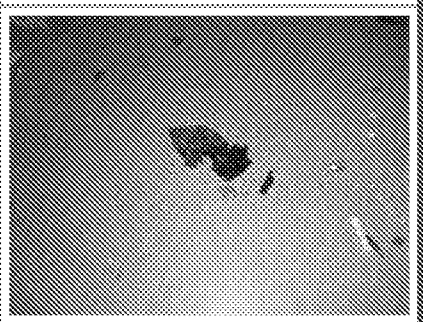
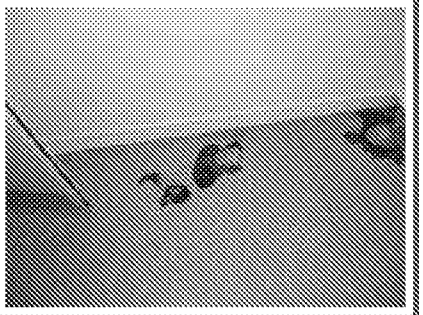
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut G2	0	011/ bedroom	Subfloor	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G2	0	012/ bedroom	Subfloor	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut G2	0	013/ bedroom	Subfloor	472686-14	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

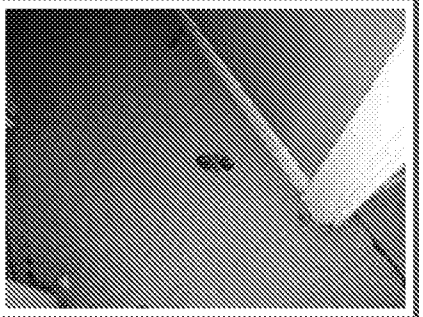
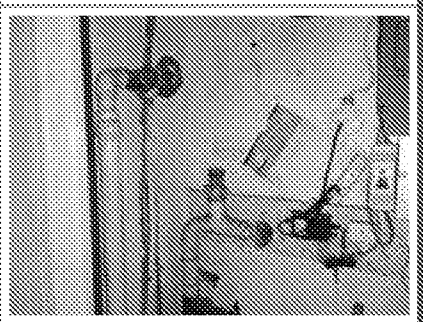
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut H1	0	001/ corridor	Subfloor	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	21 Sqm.	R3	Remove	
Accommodation Hut H1	0	002/plant room	Lining panels to walls in electrical area	472686-84	Asbestos-containing cement	Chrysotile	4	4 Sqm.	R3	Remove	
Accommodation Hut H1	0	002/plant room	Floor covering	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	4 Sqm.	R3	Remove	

table continued from previous page...

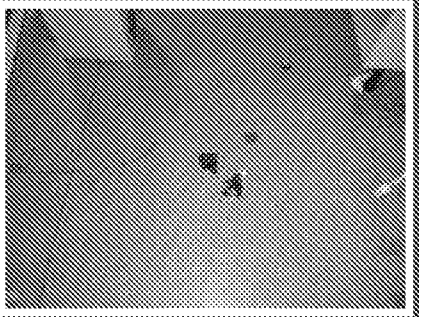
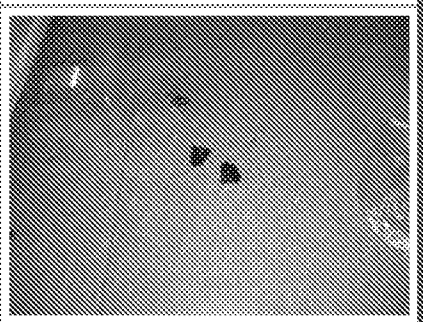
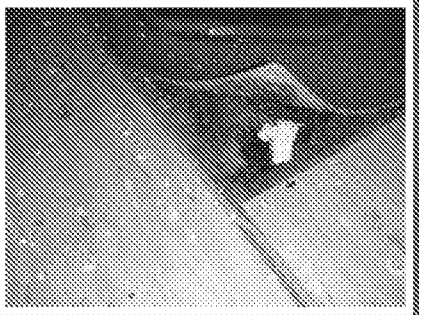
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut H1	0	005/ kitchen	Subfloor	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H1	0	006/ bedroom	Subfloor	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H1	0	007/ bedroom	Subfloor	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

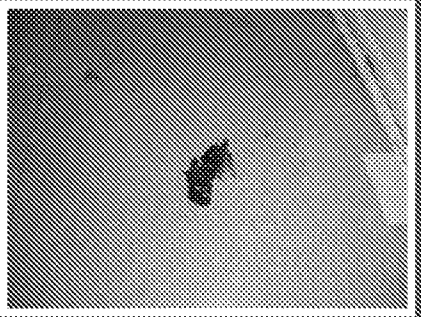
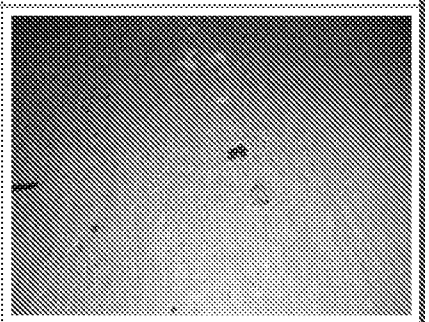
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut H1	0	008/ bedroom	Subfloor	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H1	0	009/ bedroom	Subfloor	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H1	0	010/ bedroom	Subfloor	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

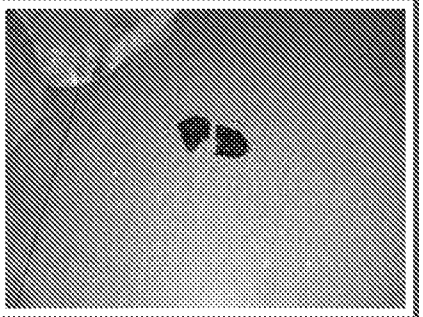
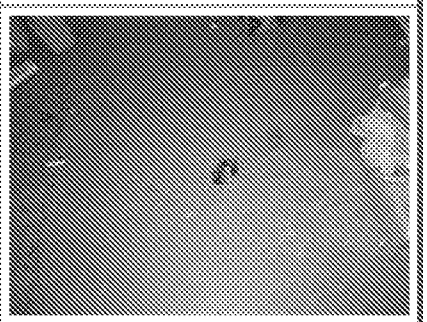
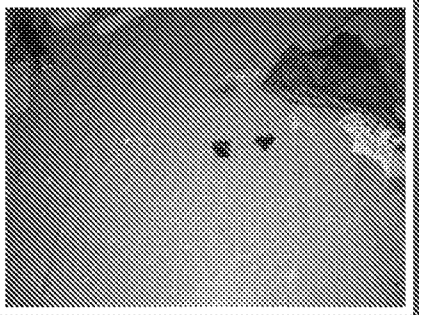
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut H1	0	011/ bedroom	Subfloor	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H1	0	012/ bedroom	Subfloor	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H1	0	013/ bedroom	Subfloor	472686-79	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

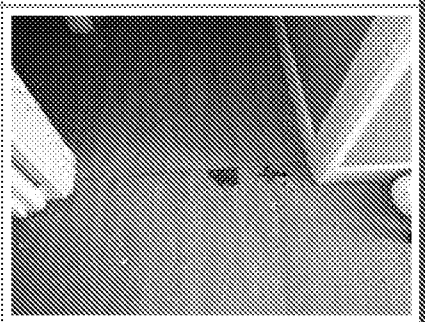
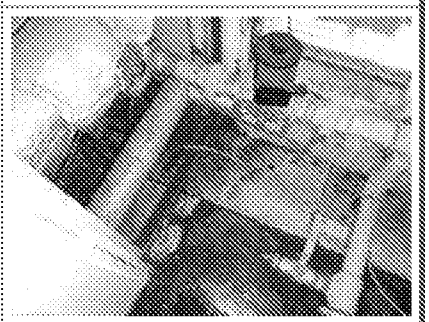
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut H1	1	001/loft space	Slaters felt	472686-86	Asbestos-containing bituminous product	Chrysotile	3	100 Sqm.	R3	Remove	
Accommodation Hut H2	0	001/ corridor	Subfloor	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	21 Sqm.	R3	Remove	
Accommodation Hut H2	0	002/plant room	Floor covering on duct cover and in electrical area	472686-96	Asbestos-containing floor tile with bitumen adhesive	Chrysotile	3	0.5 Sqm.	R3	Remove	

table continued from previous page...

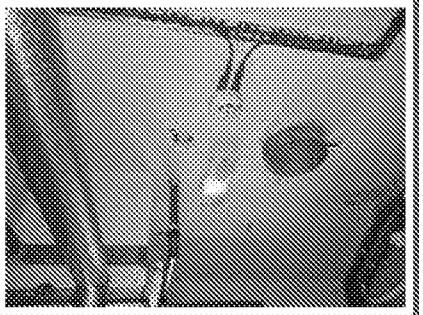
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut H2	0	002/plant room	Floor covering	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	4 Sqm.	R3	Remove	
Accommodation Hut H2	0	002/plant room	Walls	472686-93	Asbestos-containing cement panels with textured coating	Chrysotile	4	10 Sqm.	R3	Remove	
Accommodation Hut H2	0	002/plant room	Ceiling	472686-92	Asbestos-containing cement panels with textured coating	Chrysotile	4	4 Sqm.	R3	Remove	

table continued from previous page...

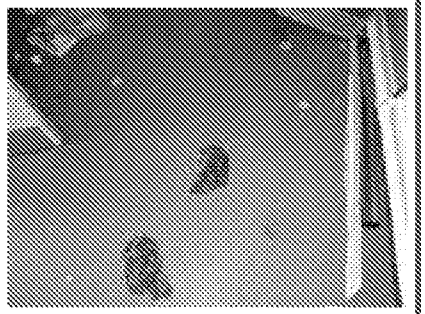
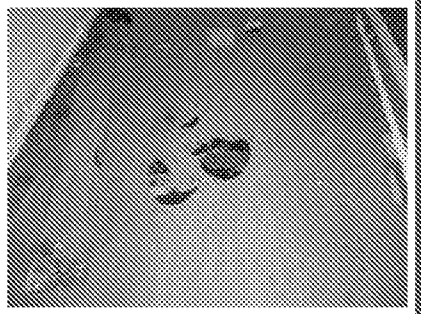
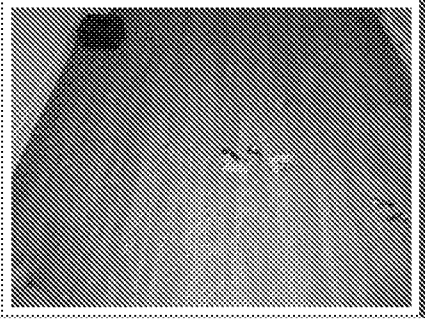
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut H2	0	005/ kitchen	Subfloor	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H2	0	006/ bedroom	Subfloor	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H2	0	007/ bedroom	Subfloor	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

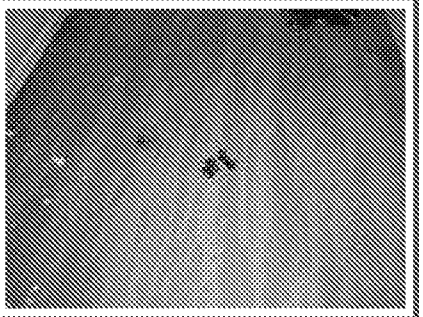
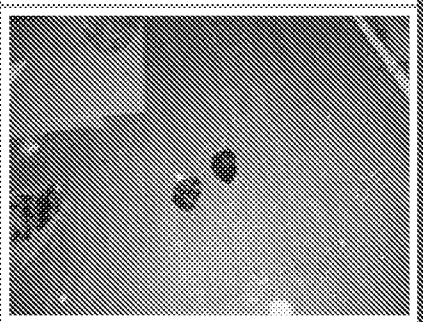
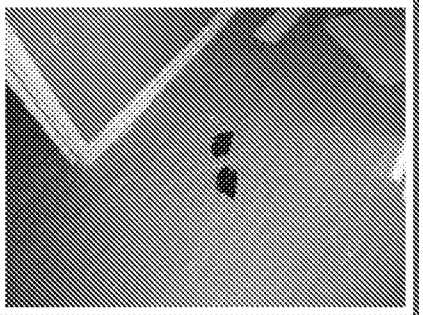
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut H2	0	008/ bedroom	Subfloor	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H2	0	009/ bedroom	Subfloor	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H2	0	010/ bedroom	Subfloor	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

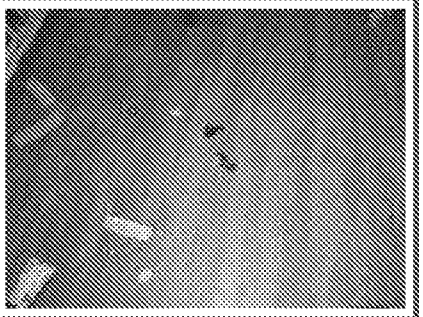
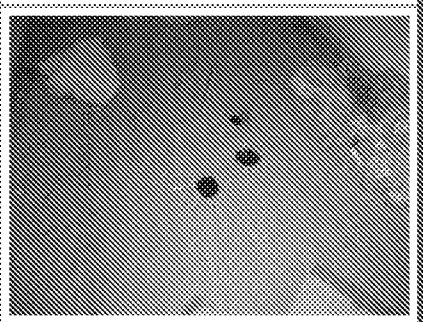
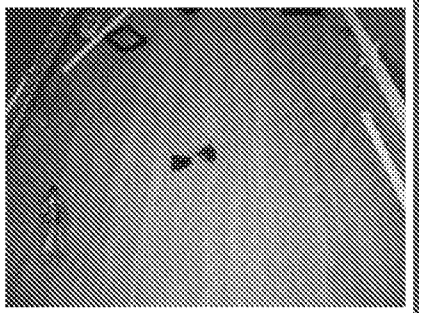
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut H2	0	011/ bedroom	Subfloor	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H2	0	012/ bedroom	Subfloor	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut H2	0	013/ bedroom	Subfloor	472686-91	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

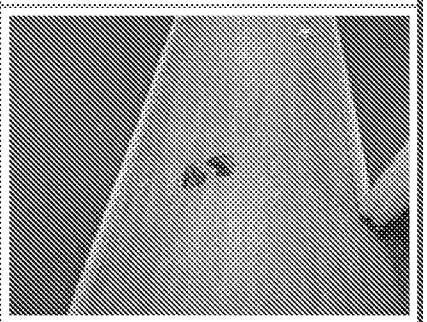
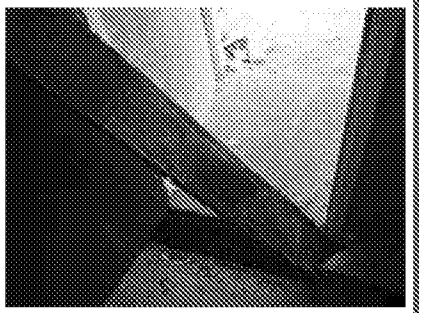
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut H2	1	001/loft space	Cement floor to boiler room below	472686-99	Asbestos-containing cement	Chrysotile	4	4 Sqm.	R3	Remove	
Accommodation Hut I1	0	001/ corridor	Subfloor	472686-104	Asbestos-containing bitumen adhesive	Chrysotile	3	21 Sqm.	R3	Remove	
Accommodation Hut I1	0	001/ corridor	Floor covering on duct cover	472686-106	Asbestos-containing floor tile with bitumen adhesive	Chrysotile	3	0.5 Sqm.	R3	Remove	

table continued from previous page...

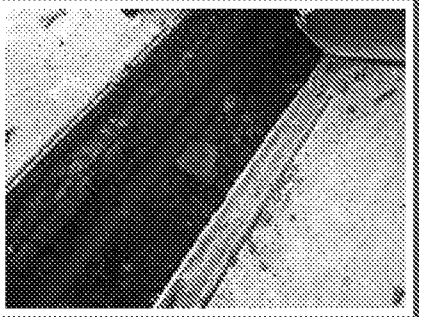
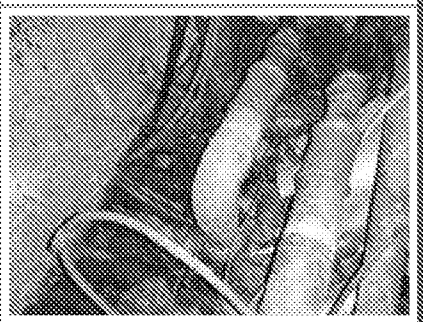
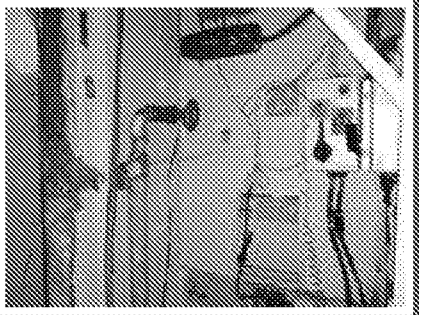
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut I1	0	001/ corridor	Cement debris in duct	472686-107	Asbestos-containing cement	Chrysotile	8	0.1 Sqm.	R2	Remove	
Accommodation Hut I1	0	002/plant room	Cement debris in floor duct	472686-107	Asbestos-containing cement	Chrysotile	8	0.1 Sqm.	R2	Remove	
Accommodation Hut I1	0	002/plant room	Lining panels to walls in electrical area	472686-112	Asbestos-containing cement	Chrysotile	4	4 Sqm.	R3	Remove	

table continued from previous page...

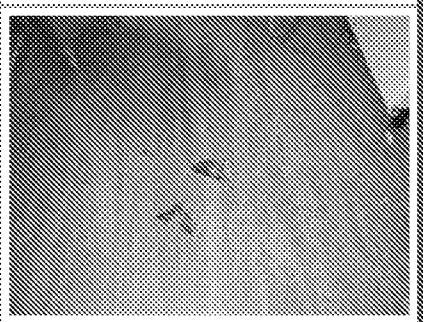

Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut I1	0	002/plant room	Floor covering	472686-109	Asbestos-containing floor tile with bitumen adhesive	Chrysotile	3	4 Sqm.	R3	Remove	
Accommodation Hut I1	0	005/ kitchen	Subfloor	472686-104	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I1	0	006/ bedroom	Subfloor	472686-104	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

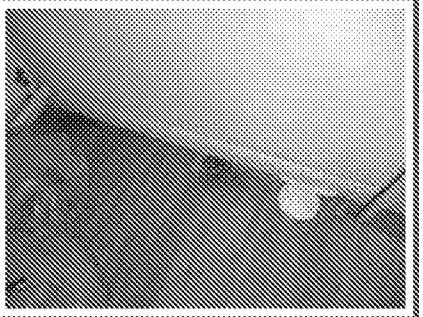
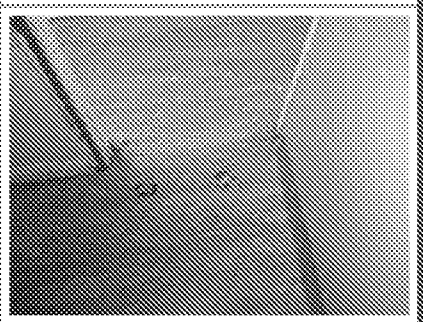
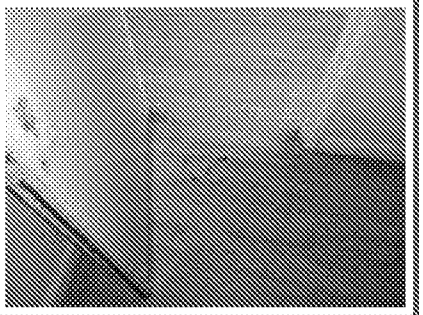
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut I1	0	007/ bedroom	Subfloor	472686-104	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I1	0	008/ bedroom	Subfloor	472686-104	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I1	0	009/ bedroom	Subfloor	472686-104	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

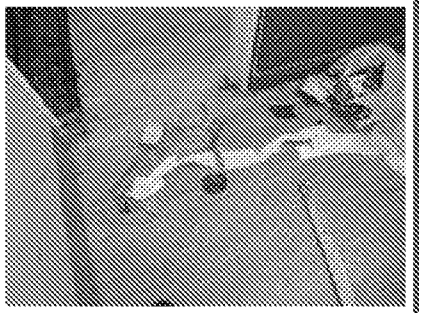
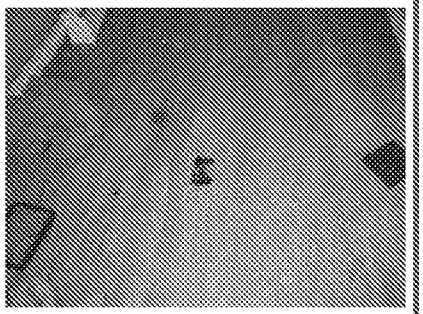
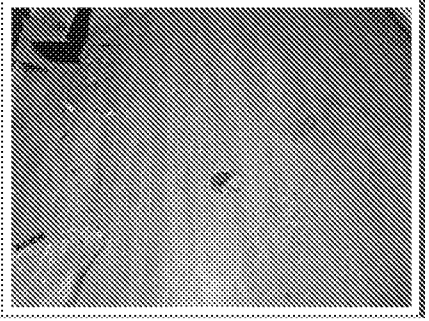
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut I1	0	010/ bedroom	Subfloor	472686-104	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I1	0	011/ bedroom	Subfloor	472686-104	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I1	0	012/ bedroom	Subfloor	472686-104	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

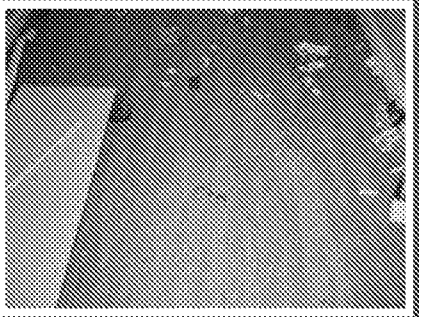
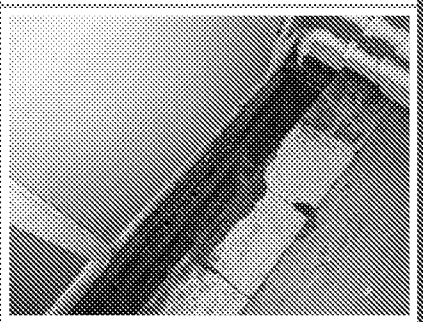
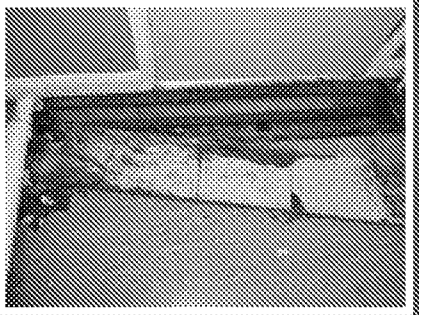
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut I1	0	013/ bedroom	Subfloor	472686-104	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I2	0	001/ corridor	Cement debris in duct	472686-121	Asbestos-containing cement	Chrysotile	6	0.1 Sqm.	R2	Remove	
Accommodation Hut I2	0	001/ corridor	Floor covering on duct cover	472686-120	Asbestos-containing floor tile with bitumen adhesive	Chrysotile	3	0.5 Sqm.	R3	Remove	

table continued from previous page...

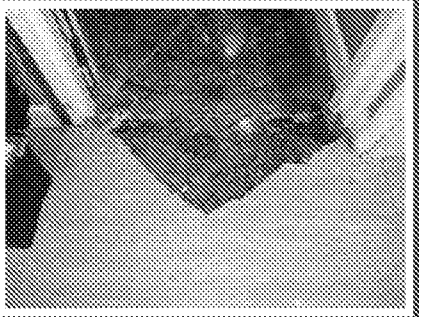
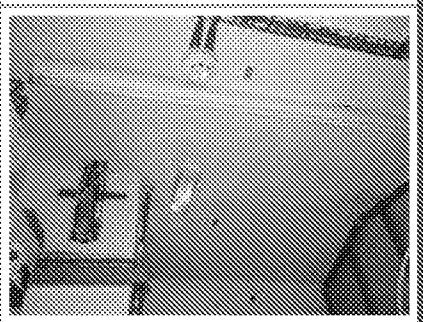
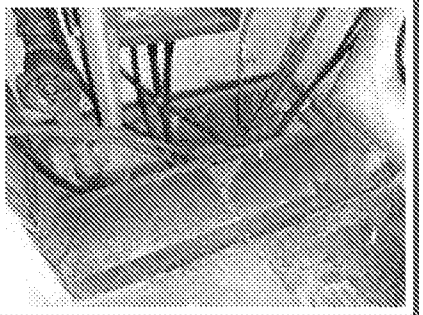
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut I2	0	001/ corridor	Subfloor	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	21 Sqm.	R3	Remove	
Accommodation Hut I2	0	002/plant room	Ceiling	472686-122	Asbestos-containing cement with textured coating	Chrysotile	4	4 Sqm.	R3	Remove	
Accommodation Hut I2	0	002/plant room	Floor covering on duct cover	472686-120	Asbestos-containing floor tile with bitumen adhesive	Chrysotile	3	0.3 Sqm.	R3	Remove	

table continued from previous page...

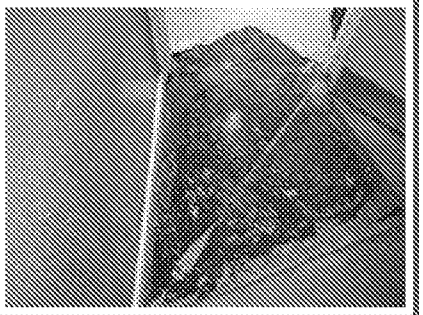
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut I2	0	002/plant room	Floor covering	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	4 Sqm.	R3	Remove	
Accommodation Hut I2	0	002/plant room	Walls	472686-123	Asbestos-containing cement with textured coating	Chrysotile	4	14 Sqm.	R3	Remove	
Accommodation Hut I2	0	005/ kitchen	Subfloor	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

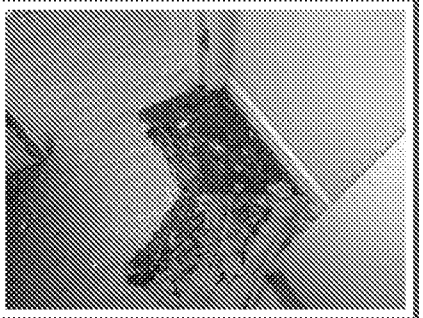
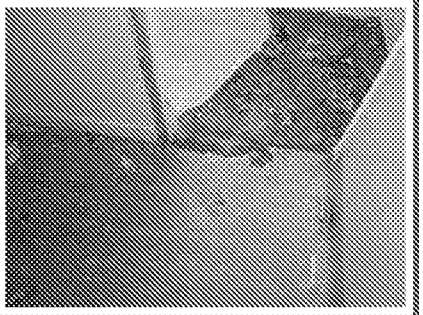
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut I2	0	006/ bedroom	Subfloor	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I2	0	007/ bedroom	Subfloor	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I2	0	008/ bedroom	Subfloor	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

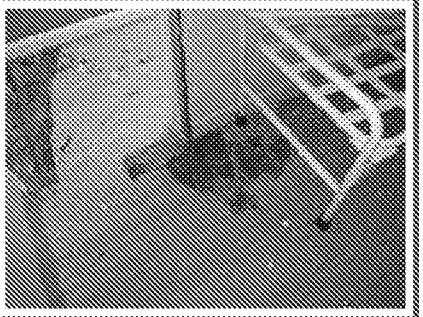
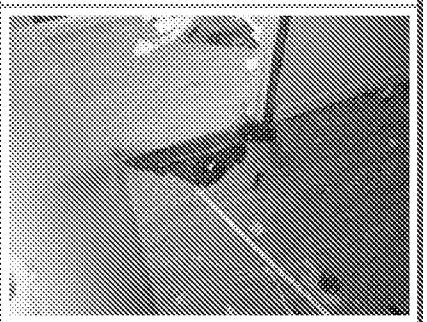
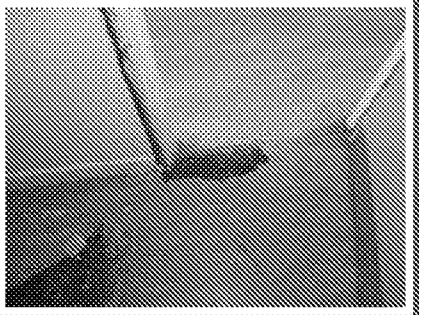
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut I2	0	009/ bedroom	Subfloor	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I2	0	010/ bedroom	Subfloor	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I2	0	011/ bedroom	Subfloor	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

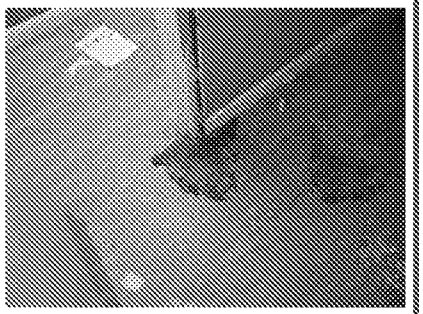
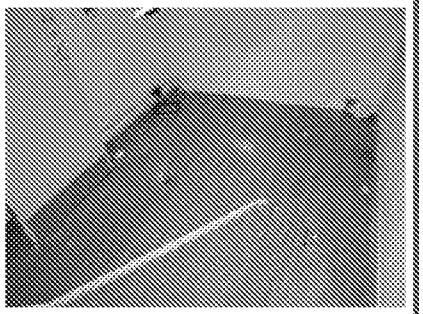
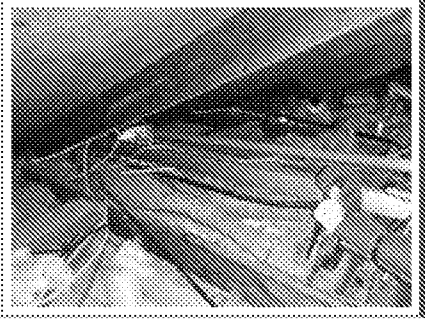
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut I2	0	012/ bedroom	Subfloor	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I2	0	013/ bedroom	Subfloor	472686-118	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut I2	1	001/loft space	Cement panels to ceiling below	472686-128	Asbestos-containing cement	Chrysotile	4	4 Sqm.	R3	Remove	

table continued from previous page...

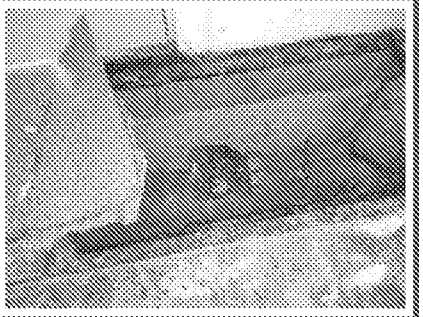
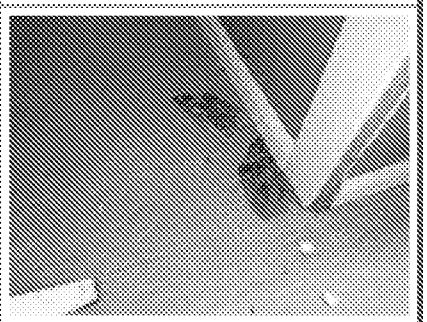
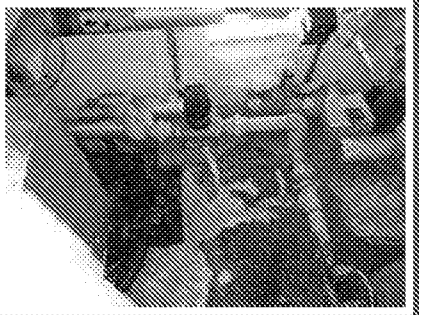
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O1	0	001/ corridor	Felt debris in floor ducts	472686-50	Asbestos-containing bituminous product	Chrysotile	8	0.1 Sqm.	R2	Remove	
Accommodation Hut O1	0	001/ corridor	Subfloor	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	21 Sqm.	R3	Remove	
Accommodation Hut O1	0	002/plant room	Floor covering on duct cover	472686-55	Asbestos-containing floor tile with bitumen adhesive	Chrysotile	3	0.5 Sqm.	R3	Remove	

table continued from previous page...

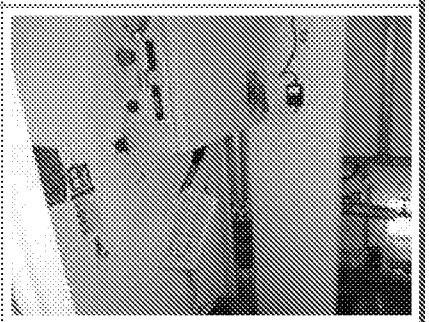
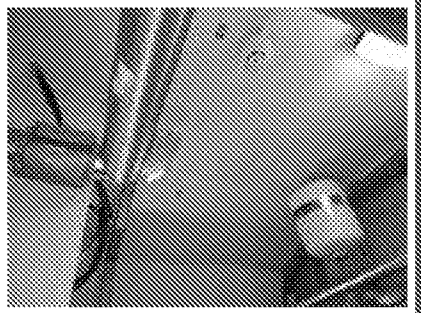
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O1	0	002/plant room	Floor covering	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	4 Sqm.	R3	Remove	
Accommodation Hut O1	0	002/plant room	Floor tiles & adhesive	472686-52	Asbestos-containing cement panels with textured coating	Chrysotile	4	10 Sqm.	R3	Remove	
Accommodation Hut O1	0	002/plant room	Cement lining to walls & ceiling	472686-51	Asbestos-containing cement panels with textured coating	Chrysotile	4	4 Sqm.	R3	Remove	

table continued from previous page...

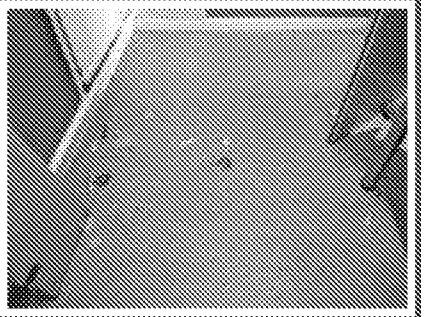
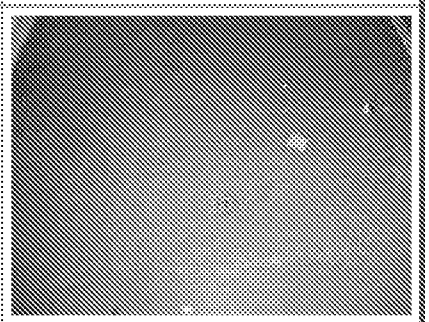

Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O1	0	005/ kitchen	Subfloor	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O1	0	006/ bedroom	Subfloor	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O1	0	007/ bedroom	Subfloor	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

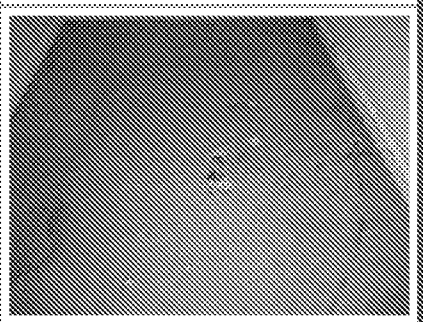
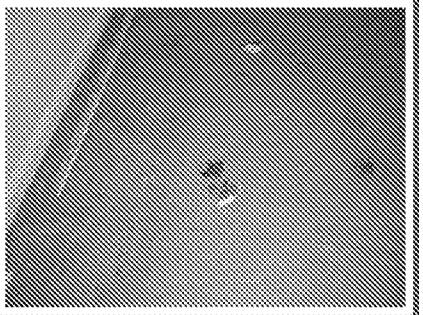
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O1	0	008/ bedroom	Subfloor	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O1	0	009/ bedroom	Subfloor	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O1	0	010/ bedroom	Subfloor	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

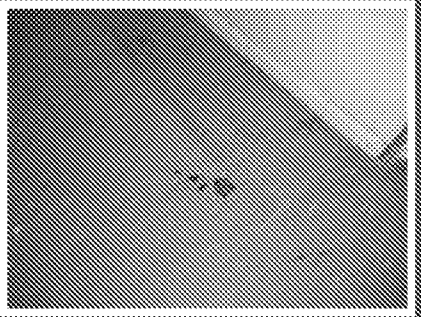
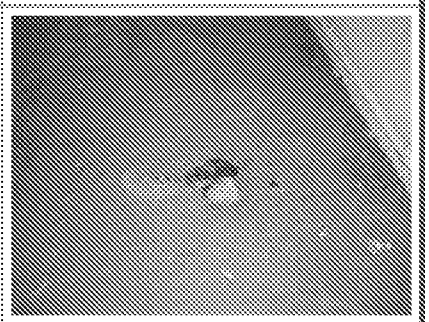

Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O1	0	011/ bedroom	Subfloor	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O1	0	012/ bedroom	Subfloor	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O1	0	013/ bedroom	Subfloor	472686-48	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

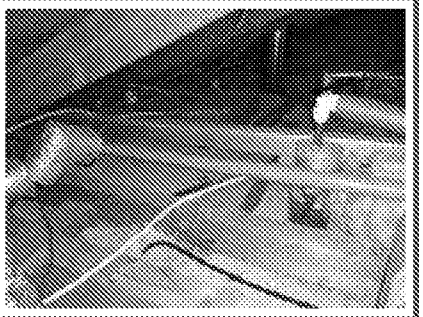
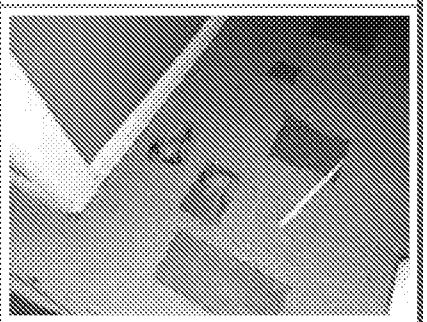
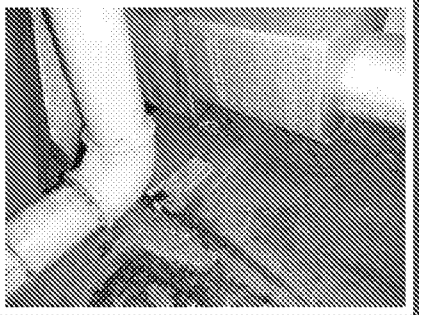
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O1	1	001/loft space	Cement floor to boiler room below	472686-58	Asbestos-containing cement	Chrysotile	4	4 Sqm.	R3	Remove	
Accommodation Hut O2	0	001/ corridor	Subfloor	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	21 Sqm.	R3	Remove	
Accommodation Hut O2	0	002/plant room	Floor covering on duct cover	472686-70	Asbestos-containing floor tile with bitumen adhesive	Chrysotile	3	0.5 Sqm.	R3	Remove	

table continued from previous page...

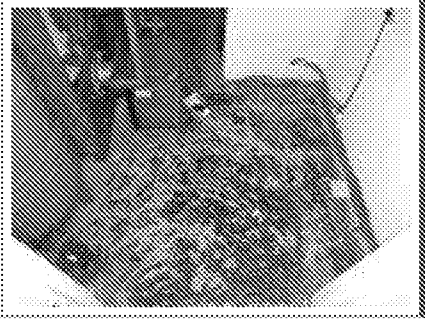
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O2	0	002/plant room	Walls	472686-67	Asbestos-containing cement panels with textured coating	Chrysotile	4	10 Sqm.	R3	Remove	
Accommodation Hut O2	0	002/plant room	Ceiling	472686-66	Asbestos-containing cement panels with textured coating	Chrysotile	4	4 Sqm.	R3	Remove	
Accommodation Hut O2	0	002/plant room	Floor covering	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	4 Sqm.	R3	Remove	

table continued from previous page...

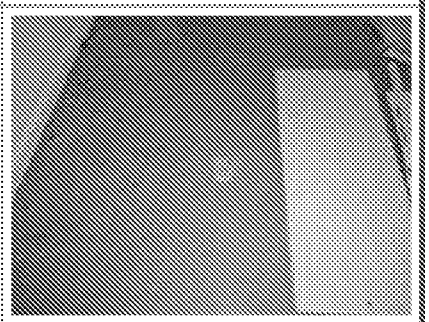
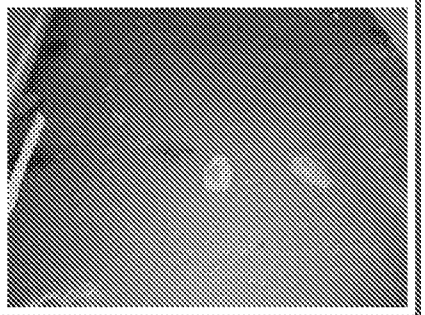
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O2	0	005/ kitchen	Subfloor	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O2	0	006/ bedroom	Subfloor	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O2	0	007/ bedroom	Subfloor	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

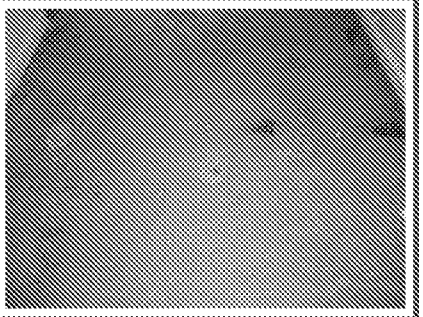
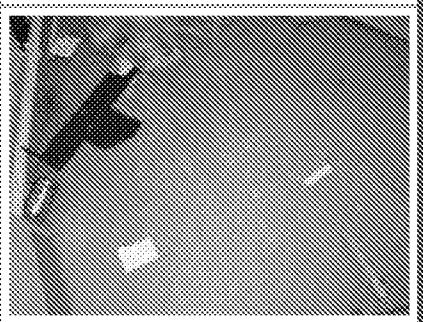
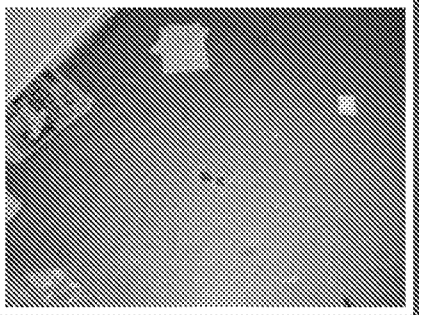
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O2	0	008/ bedroom	Subfloor	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O2	0	009/ bedroom	Subfloor	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O2	0	010/ bedroom	Subfloor	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

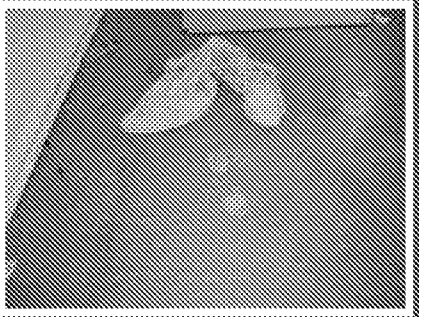
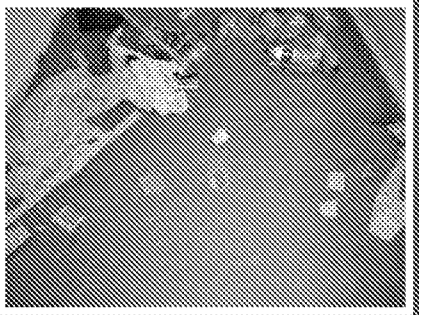
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O2	0	011/ bedroom	Subfloor	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O2	0	012/ bedroom	Subfloor	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut O2	0	013/ bedroom	Subfloor	472686-64	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

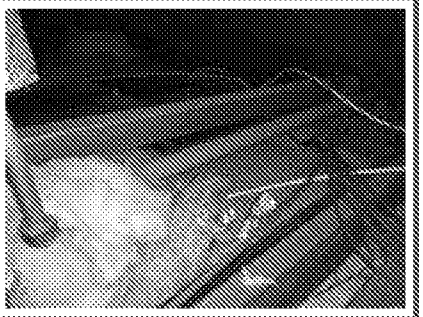
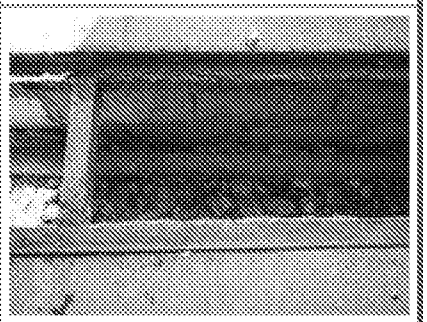
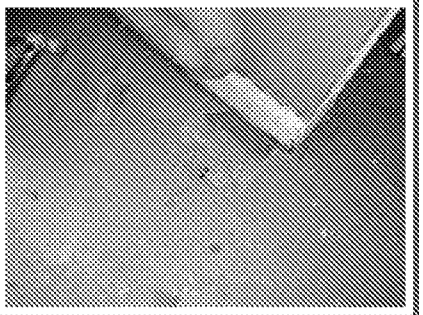
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut O2	1	001/loft space	Cement floor to boiler room below	472686-73	Asbestos-containing cement	Chrysotile	4	4 Sqm.	R3	Remove	
Accommodation Hut P1	0	001/ corridor	Floor tiles debris in floor ducts	472686-25	Asbestos-containing floor tile with bitumen adhesive	Chrysotile	8	0.1 Sqm.	R2	Remove	
Accommodation Hut P1	0	001/ corridor	Subfloor	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	21 Sqm.	R3	Remove	

table continued from previous page...

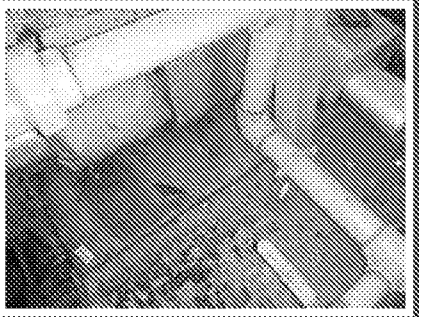
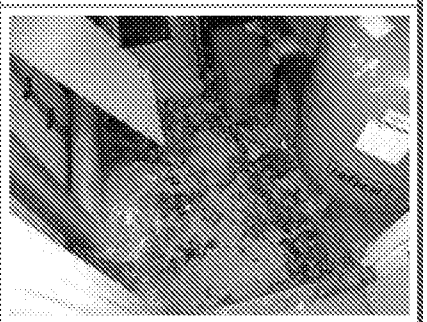
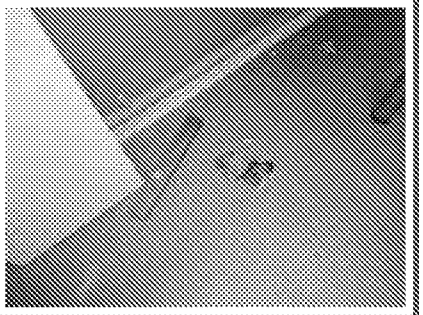
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut P1	0	002/plant room	Floor covering on duct cover	472686-28	Asbestos-containing floor tile with bitumen adhesive	Chrysotile	3	0.5 Sqm.	R3	Remove	
Accommodation Hut P1	0	002/plant room	Floor covering	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	4 Sqm.	R3	Remove	
Accommodation Hut P1	0	005/ kitchen	Subfloor	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

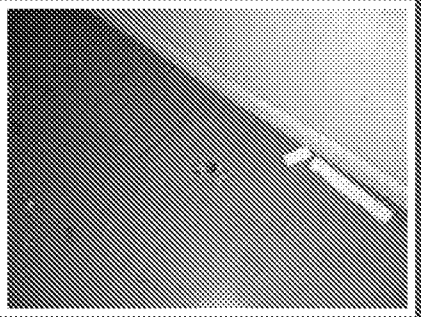
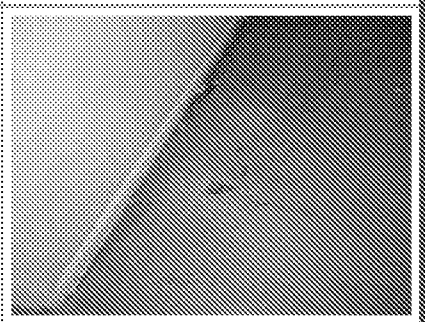
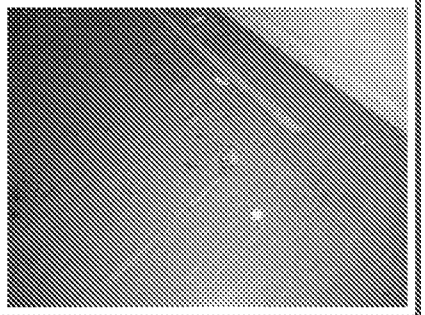
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut P1	0	006/ bedroom	Subfloor	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P1	0	007/ bedroom	Subfloor	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P1	0	008/ bedroom	Subfloor	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

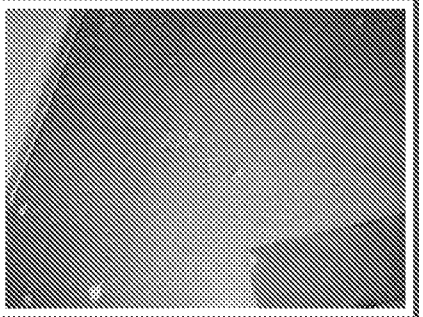
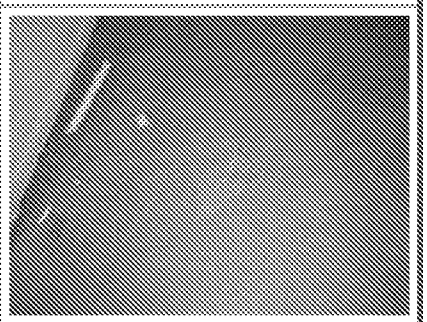
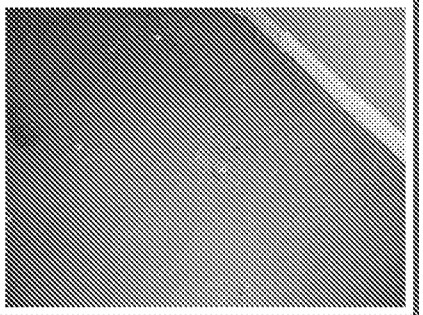
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut P1	0	009/ bedroom	Subfloor	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P1	0	010/ bedroom	Subfloor	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P1	0	011/ bedroom	Subfloor	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

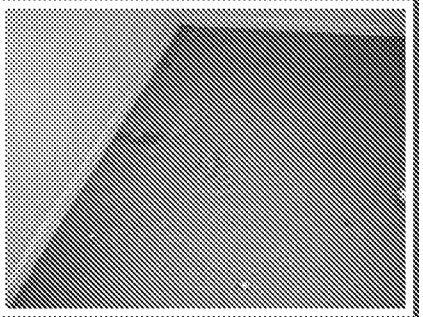
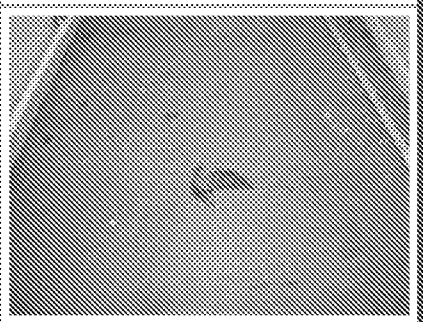
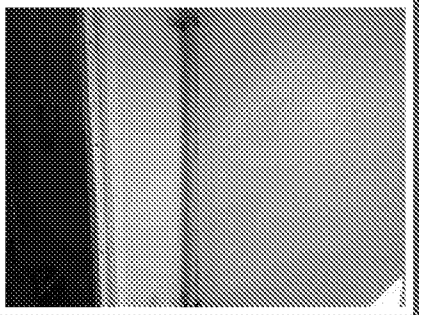
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut P1	0	012/ bedroom	Subfloor	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P1	0	013/ bedroom	Subfloor	472686-24	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P1	9	999/ externals	Wall panels with textured coating in porch	472686-34	Asbestos-containing insulating board	Chrysotile	5	6 Sqm.	R2	Remove	

table continued from previous page...

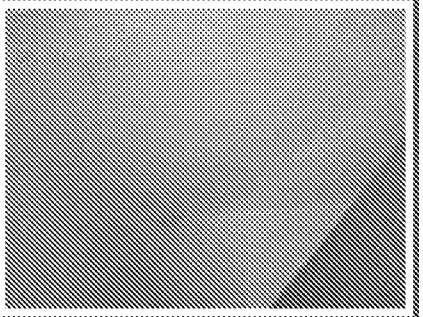
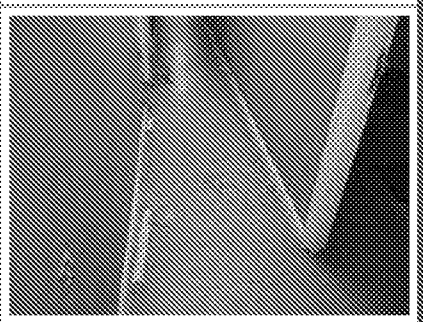
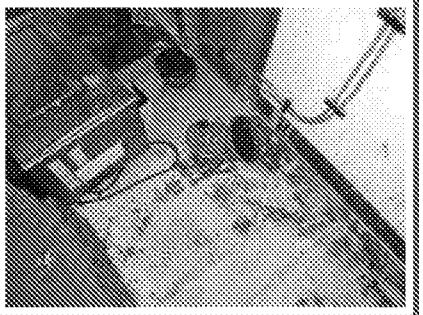
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut P1	9	999/ externals	Ceiling panels with textured coating in porch	472686-33	Asbestos-containing insulating board	Chrysotile	5	2 Sqm.	R3	Remove	
Accommodation Hut P2	0	001/ corridor	Subfloor	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	21 Sqm.	R3	Remove	
Accommodation Hut P2	0	002/plant room	Floor covering	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	4 Sqm.	R3	Remove	

table continued from previous page...

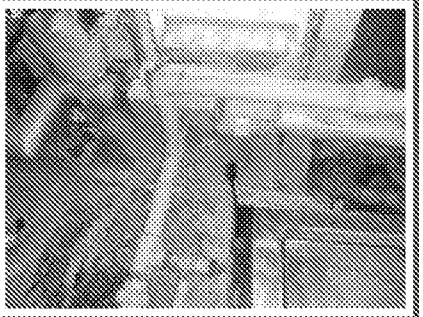
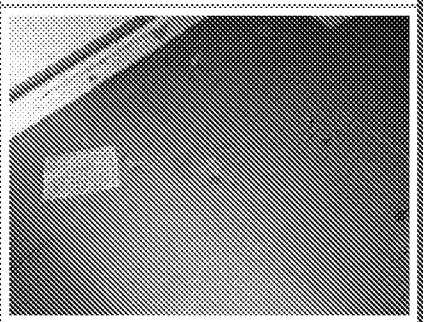
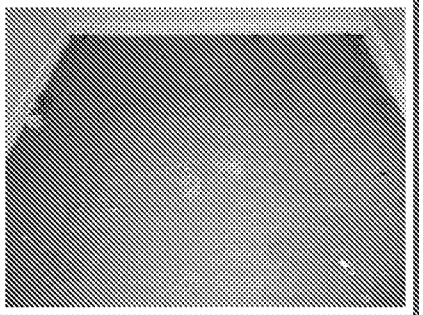
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut P2	0	002/plant room	Floor covering on duct cover	472686-40	Asbestos-containing floor tile with bitumen adhesive	Chrysotile	3	0.5 Sqm.	R3	Remove	
Accommodation Hut P2	0	005/ kitchen	Subfloor	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P2	0	006/ bedroom	Subfloor	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...

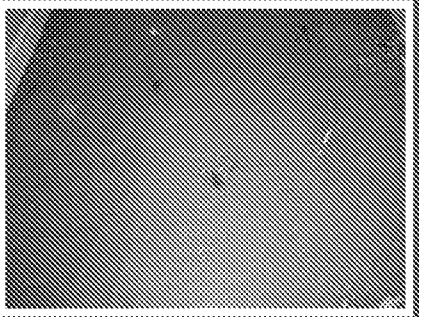

Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut P2	0	007/ bedroom	Subfloor	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P2	0	008/ bedroom	Subfloor	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P2	0	009/ bedroom	Subfloor	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...


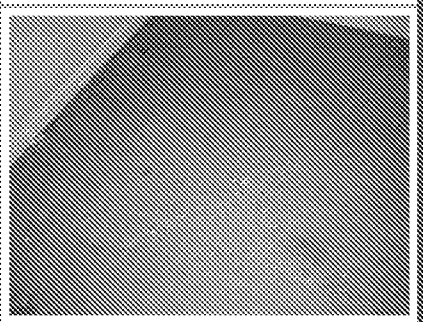
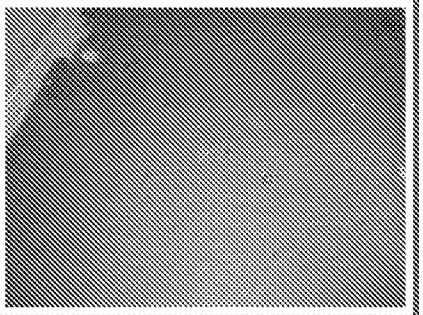
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut P2	0	010/ bedroom	Subfloor	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P2	0	011/ bedroom	Subfloor	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P2	0	012/ bedroom	Subfloor	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	

table continued from previous page...


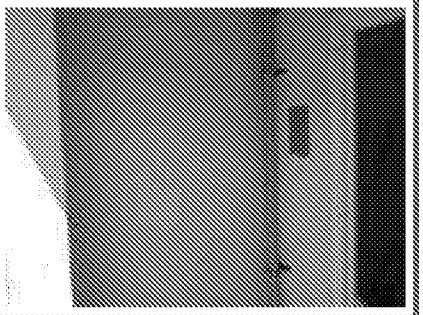
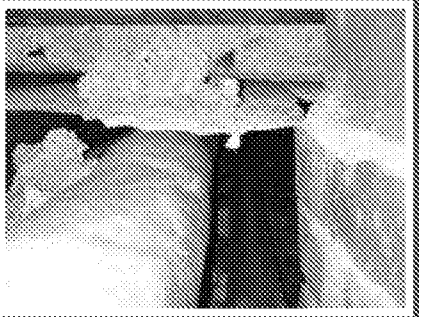
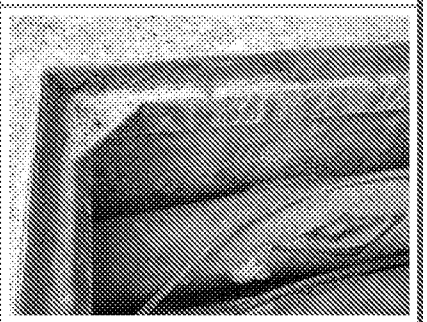
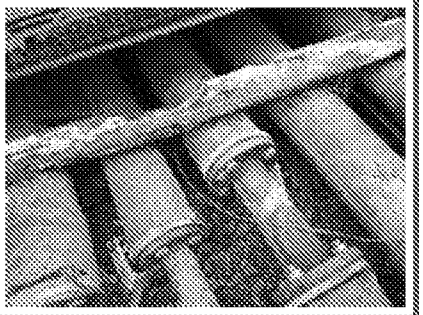
Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
Accommodation Hut P2	0	013/ bedroom	Subfloor	472686-37	Asbestos-containing bitumen adhesive	Chrysotile	3	6 Sqm.	R3	Remove	
Accommodation Hut P2	9	999/ externals	Ceiling panels with textured coating in porch	472686-44	Asbestos-containing insulating board	Chrysotile	5	2 Sqm.	R3	Remove	
Accommodation Hut P2	9	999/ externals	Wall panels with textured coating in porch	472686-45	Asbestos-containing insulating board	Chrysotile	5	6 Sqm.	R2	Remove	


table continued from previous page...

Building	Level	Location	Item / Product Examined	Sample No.	Material Description	Fibre Type	Material Score	Extent	Risk Level Assessment	Initial Control Recommendation	Photograph
external ducts for blocks P, G, H, O, I	9	999/ externals ducts	Shuttering through out the ducts	472686-131	Asbestos-containing cement	Chrysotile	4	200 Sqm.	R3	Remove	
external ducts for blocks P, G, H, O, I	9	999/ externals ducts	Cement debris in ducts	472686-134	Asbestos-containing cement	Chrysotile	8	1 Sqm.	R2	Remove	
external ducts for blocks P, G, H, O, I	9	999/ externals ducts	Pipework flange gasket through out the ducts	472686-135	Asbestos-containing gasket	Chrysotile	7	200 + - No.	R2	Remove	

Areas Excluded & Not Fully Accessed During Survey

Asbestos should be presumed to be present within Locations and Items not accessed until a further assessment can be performed.

Additional surveyor comments.

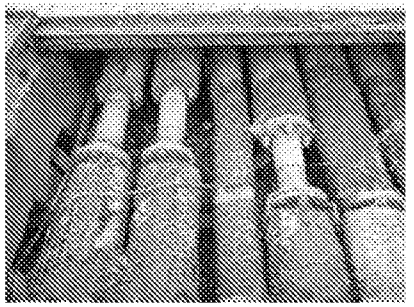Building	Level	Location	Item / Product Examined	Accessibility	Surveyor Additional Comments At Time Of Survey	Photograph
external ducts for blocks P, G, H, O, I	9	999/externals ducts	***Entire Location***	Limited Access	reasons of health and safety	
				Due to services and depth of duct		

Survey Inspection Detail, Sample Test Report and Risk Level Assessment Report

Asbestos should be presumed to be present within Locations and Items not accessed until a further assessment can be performed. Additional surveyor comments.

Building: Accommodation Hut G1 **Level: 0** **Location: 001/corridor**

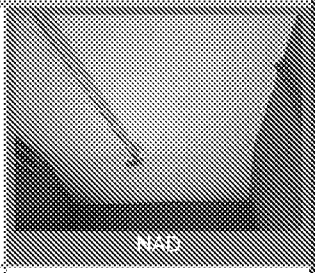
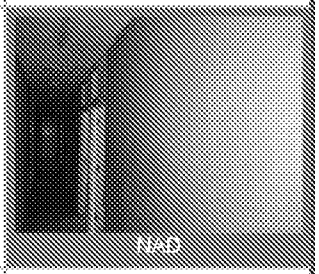
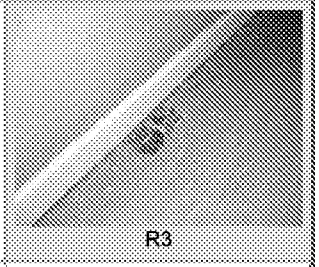
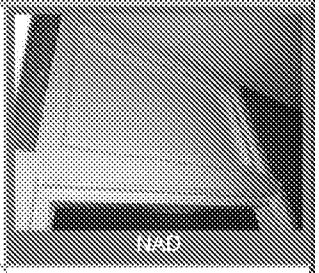
Item/Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Sample	472686-1								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Sample	472686-2								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Sample	472686-3	24 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 001/corridor**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Door header panels	Insulating board	Sample	472686-4								
Packers to door frames	Wood, card and hardboard										
Duct covers	Wood										

Building: Accommodation Hut G1 **Level: 0** **Location: 002/bedroom**

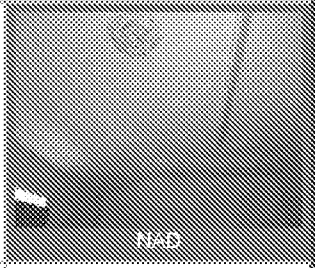
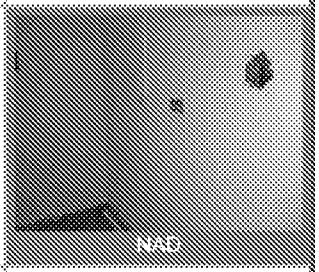


Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 002/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-3	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre	Sample	472686-6								 NAD
Lining within cavity to external walls	Bituminous product	Sample	472686-5								 NAD
Door header panel	Wood										

Building: Accommodation Hut G1 **Level: 0** **Location: 003/bedroom**

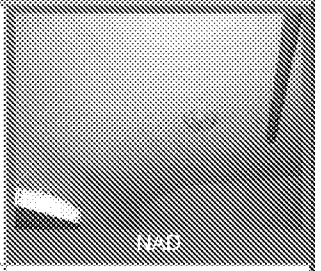
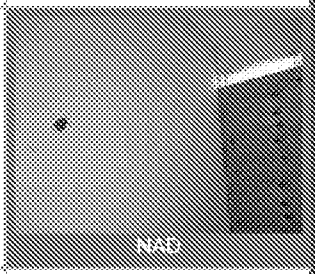

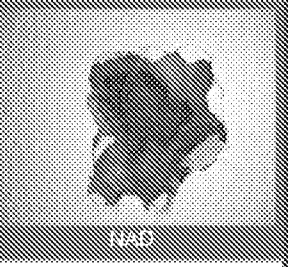
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Found	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-3	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 003/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 NAD
Door header panel	Wood										

Building: Accommodation Hut G1 **Level: 0** **Location: 004/bedroom**

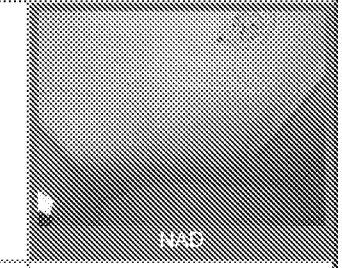
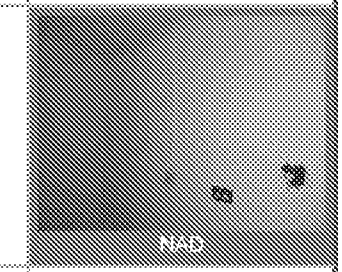

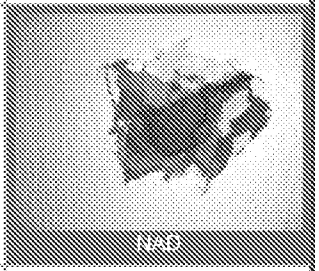
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 004/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-3	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 N/A
Door header panel	Wood										

Building: Accommodation Hut G1 **Level: 0** **Location: 005/bedroom**

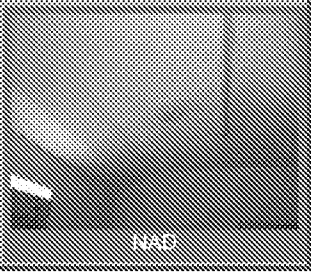
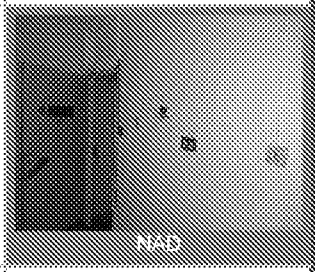

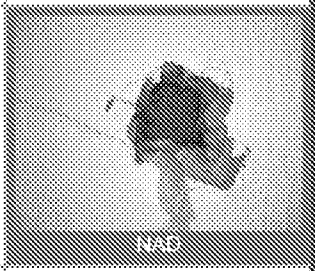
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 N/A

table continued from previous page...

Building: Accommodation Hut G1 Level: 0 Location: 005/bedroom

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-3	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 NAD
Door header panel	Wood										

Building: Accommodation Hut G1 **Level: 0** **Location: 006/bedroom**

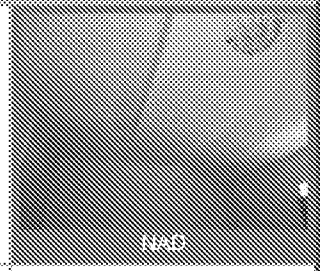
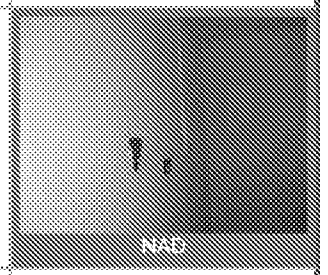
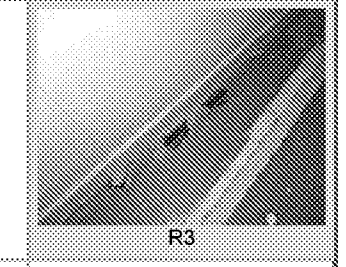
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Found	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-3	6 Sqm.	1	1	0	Chrysotile	3	2	
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 006/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 NAD
Door header panel	Wood										

Building: Accommodation Hut G1 **Level: 0** **Location: 007/bedroom**

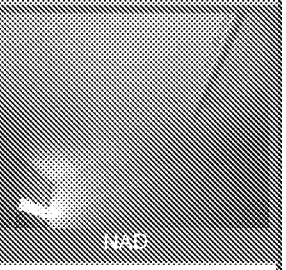
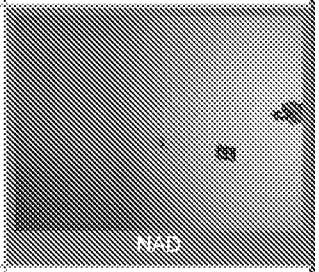

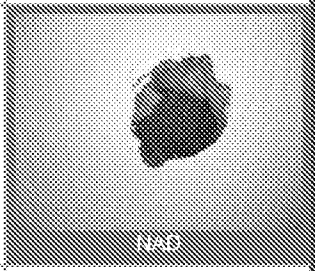
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 007/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-3	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 N/A
Door header panel	Wood										

Building: Accommodation Hut G1 **Level: 0** **Location: 008/bedroom**

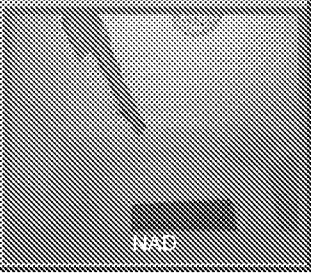
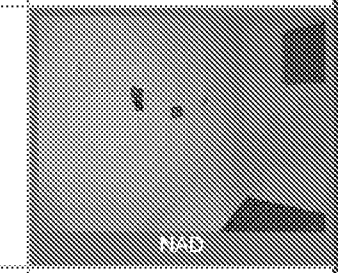

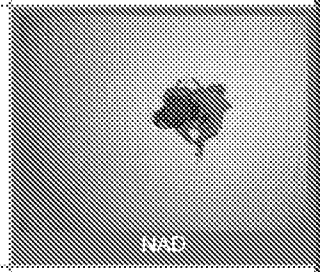
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 N/A

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 008/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-3	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 NAD
Door header panel	Wood										

Building: Accommodation Hut G1 **Level: 0** **Location: 009/bedroom**


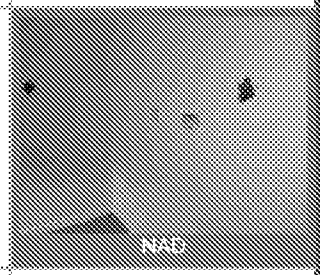

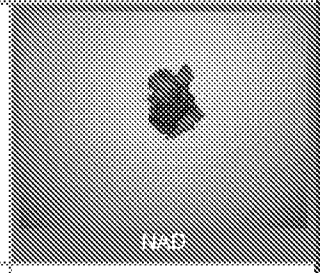
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Found	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-3	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 009/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 NAD
Door header panel	Wood										

Building: Accommodation Hut G1 **Level: 0** **Location: 010/bedroom**

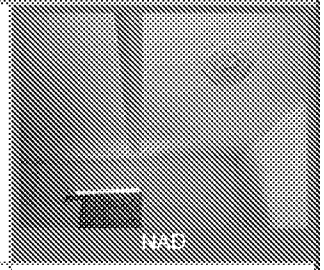
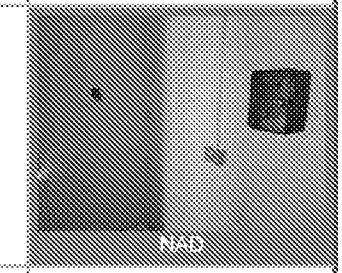
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								 NAD
Floor covering	Modern linoleum										
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 010/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 NAD

Building: Accommodation Hut G1 **Level: 0** **Location: 011/faith room**


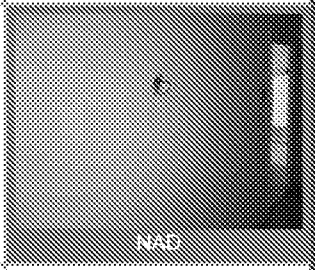
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								 NAD
Floor covering	Modern linoleum										
Floor	Concrete										
Door and frame	Wood										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 011/faith room**


Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 N/D

Building: Accommodation Hut G1 **Level: 0** **Location: 012/bathroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 N/D
Walls	Wood and plastic										
Floor	Concrete										
Floor covering	Modern linoleum										
Window frames	PVC and wood										
Door and frame	Wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Toilet cisterns	Ceramics										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 012/bathroom**

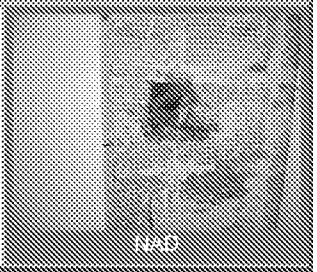Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 NAD

Building: Accommodation Hut G1 **Level: 0** **Location: 013/kitchen**

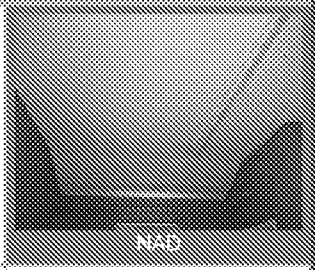
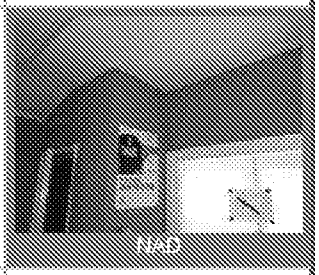

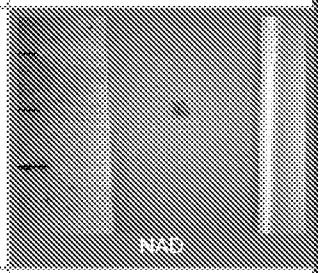
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-2								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 013/kitchen**




Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-3	8 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Window frames	PVC and wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 NAD
Door and frame	Wood										
Water heater	Modern										
Sink pad	Modern										

Building: Accommodation Hut G1 **Level: 0** **Location: 014/electrical cupboard**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard										
Walls	Hardboard										
Floor	Concrete										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 014/electrical cupboard**




Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 N/AD
Door and frame	Wood										
Electrics	Modern										
Pipework insulation in floor duct	Insulation	Sample	472686-7								 N/AD

Building: Accommodation Hut G1 **Level: 0** **Location: 015/boiler room**


Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-1								 N/AD

table continued from previous page...


Building: Accommodation Hut G1 **Level: 0** **Location: 015/boiler room**

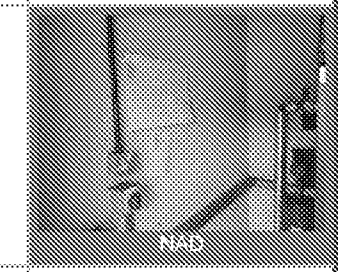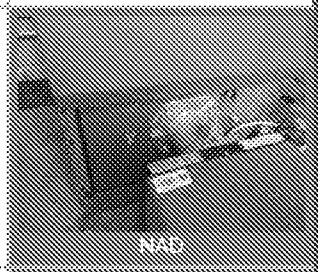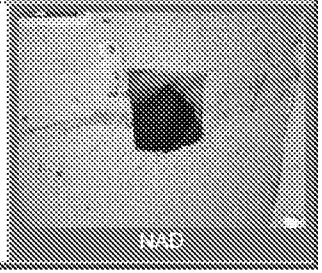Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friability Score	Material Condition	Surface Treatment	Asbestos %	Material Score	Accessibility Score	Risk Level Assessment
Walls	Plasterboard and hardboard										
Walls	Textured coating	Cross Reference	472686-2								 NAD
Door and frame	Wood and metal										
Boiler	Modern										
Pipework	Metal										
Pipe insulation	Metal clad man made mineral fibre										
Floor	Concrete										
Electrics	Modern										
Gasket to boiler	Gasket	Sample	472686-9								 NAD
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-5								 NAD

Building: Accommodation Hut G1 **Level: 1** **Location: 001/loft space**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipe insulation	Man made mineral fibre										
Insulation	Man made mineral fibre										
Slaters felt	Asbestos-containing bituminous product	Sample	472686-8	100 Sqm.	1	1	0	Chrysotile	3	2	 R3

Building: Accommodation Hut G1 **Level: 1** **Location: 002/loft space**


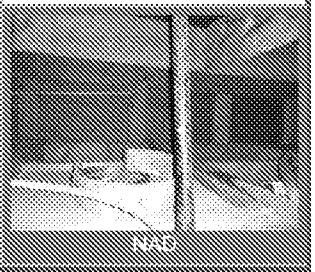
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipe insulation	Man made mineral fibre										
Slaters felt	Lining to external walls	Cross Reference	472686-5								 NAD

Building: Accommodation Hut G1 **Level: 9** **Location: 999/externals**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Roof tiles	Metal										

table continued from previous page...

Building: Accommodation Hut G1 **Level: 0** **Location: 999/externals**

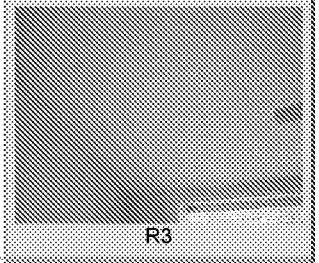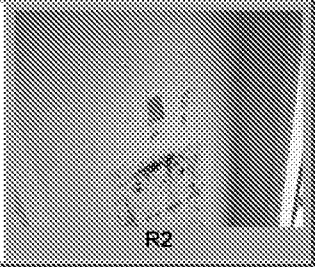Item (Product Examined)	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Facia	Wood and plastic										
Walls	Plastic										
Rainwater goods	Plastic										
Ceiling panels with textured coating in porch	Asbestos-containing insulating board	Sample	472686-10	2 Sqm.	2	1	1	Amosite, Chrysotile	6	2	 R3
Wall panels with textured coating in porch	Asbestos-containing insulating board	Sample	472686-11	6 Sqm.	2	1	1	Amosite, Chrysotile	6	3	 R2

Building: Accommodation Hut G2 **Level: 0** **Location: 001/corridor**

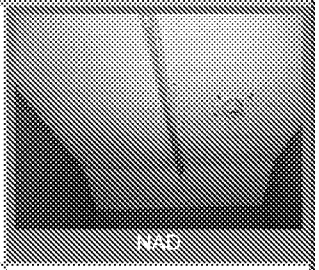
Item (Product Examined)	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Sample	472686-12								 NAD
Walls	Hardboard										

table continued from previous page...

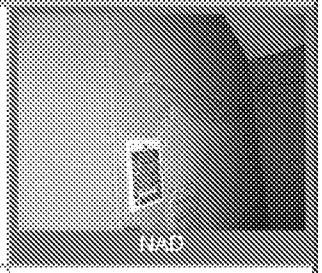
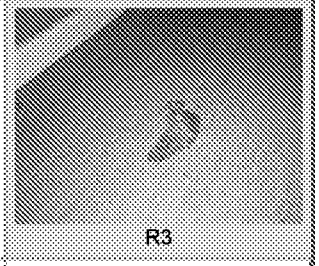
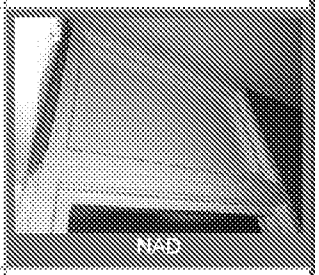
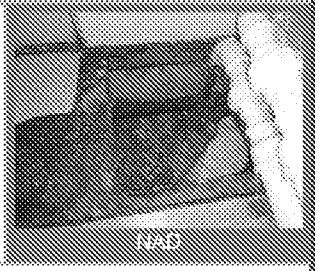
Building: Accommodation Hut G2				Level: 0		Location: 001/corridor					
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Sample	472686-13								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Sample	472686-14	21 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Door header panels	Insulating board	Sample	472686-16								 NAD
Packers to door frames	Wood, card and hardboard										
Duct covers	Wood										

table continued from previous page...

Building: Accommodation Hut G2 **Level: 0** **Location: 001/corridor**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Floor tiles debris in floor ducts	Floor tile with bitumen adhesive	Sample	472686-15								 N/D
		Present in both ducts									
Insulation in floor ducts	Man made mineral fibre										

Building: Accommodation Hut G2 **Level: 0** **Location: 002/plant room**

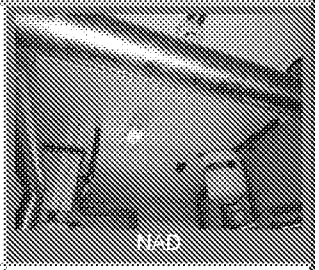
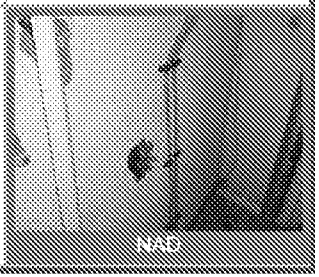
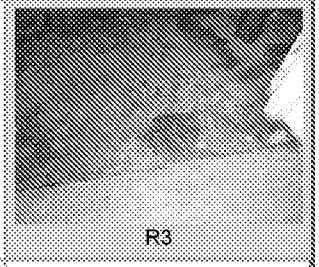
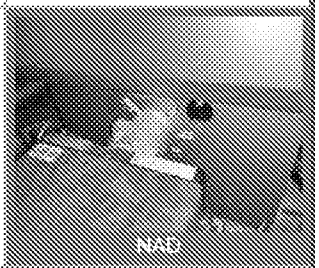

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								 N/D
Walls	Hardboard and plasterboard										
Wall covering	Textured coating	Cross Reference	472686-13								 N/D



table continued from previous page...

Building: Accommodation Hut G2				Level: 0	Location: 002/plant room						
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Floor covering	Asbestos-containing bitumen adhesive	Cross Reference	472686-14	4 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Insulation in floor ducts	Man made mineral fibre										
Pipework	Metal										
Pipework insulation	Metal and man made mineral fibre										
Electrics	Modern										
Boiler	Modern										
Gasket to boiler	Gasket	Sample	472686-17								 NAD
Panels around vents	Insulating board	Sample	472686-18								 NAD

Building: Accommodation Hut G2 **Level: 0** **Location: 003/cupboard**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friability	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Wood										
Walls	Wood and hardboard										
Floor covering	Modern linoleum										
Floor	Concrete and ceramic										
Door and frame	Wood										

Building: Accommodation Hut G2 **Level: 0** **Location: 004/bathroom**

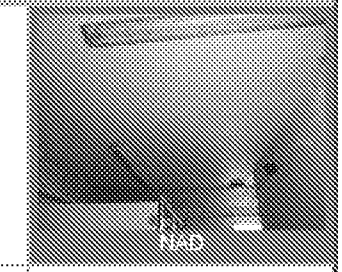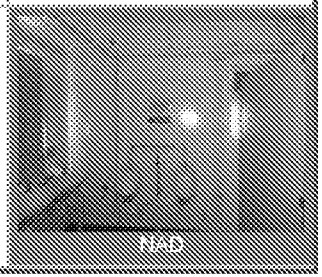Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friability	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								
Walls	Wood and plastic										
Floor covering	Modern linoleum										
Floor	Concrete and ceramic										
Door and frame	Wood										
Window frames	PVC and wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Toilet cisterns	Ceramics										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-19								

Building: Accommodation Hut G2 **Level: 0** **Location: 005/kitchen**

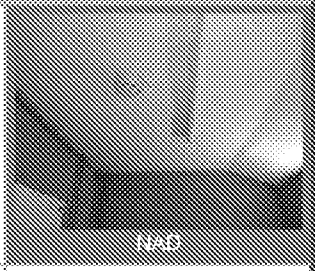
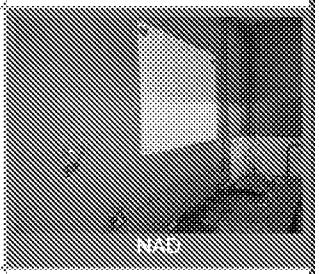
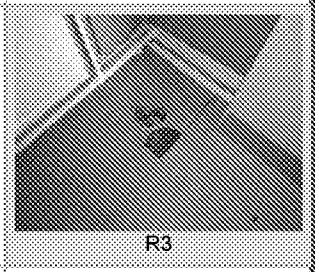
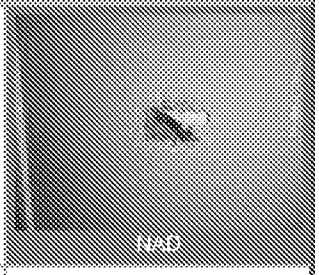

Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-13								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-14	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut G2 **Level: 0** **Location: 005/kitchen**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos ID	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Sample	472686-19								
Sink pad	Modern										
Water heater	Modern										

Building: Accommodation Hut G2 **Level: 0** **Location: 006/bedroom**




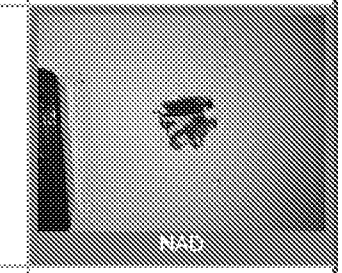
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos ID	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut G2 **Level: 0** **Location: 006/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-13								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-14	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-19								 NAD
Door header panel	Wood										

Building: Accommodation Hut G2 **Level: 0** **Location: 007/bedroom**

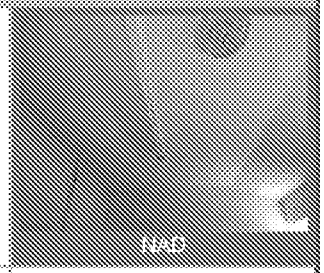
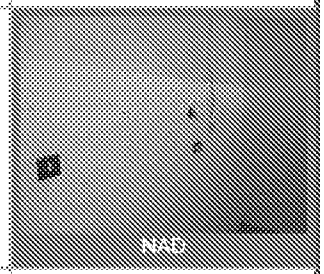

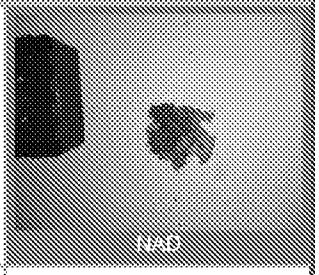
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-13								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-14	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut G2 **Level: 0** **Location: 007/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-19								 NAD
Door header panel	Wood										

Building: Accommodation Hut G2 **Level: 0** **Location: 008/bedroom**

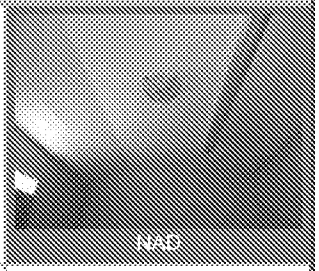
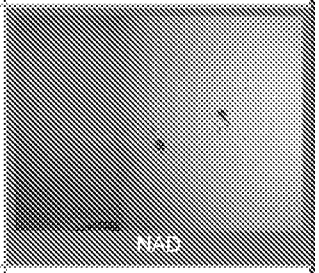
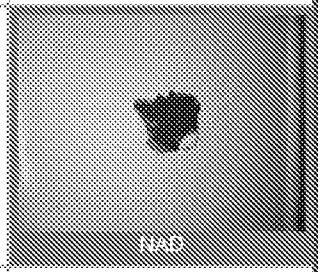
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-13								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut G2 **Level: 0** **Location: 008/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-14	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-19								 N/A
Door header panel	Wood										

Building: Accommodation Hut G2 **Level: 0** **Location: 009/bedroom**

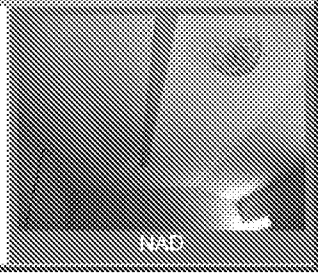
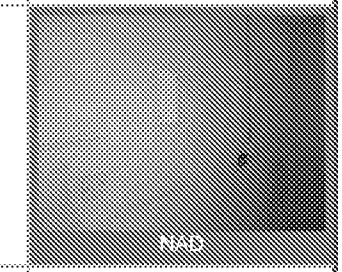

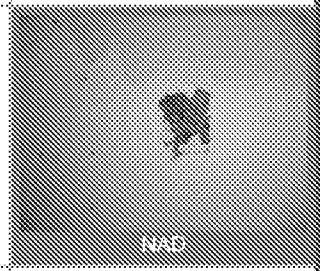
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								 N/A

table continued from previous page...

Building: Accommodation Hut G2				Level: 0		Location: 009/bedroom					
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-13								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-14	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-19								 NAD
Door header panel	Wood										

Building: Accommodation Hut G2 **Level: 0** **Location: 010/bedroom**

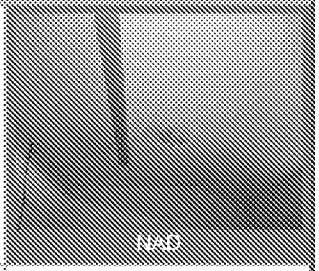
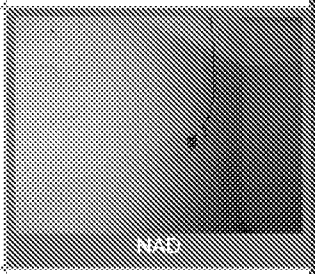

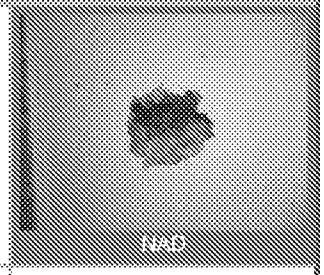
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-13								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-14	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut G2 **Level: 0** **Location: 010/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-19								 NAD
Door header panel	Wood										

Building: Accommodation Hut G2 **Level: 0** **Location: 011/bedroom**

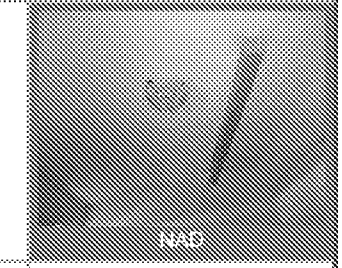
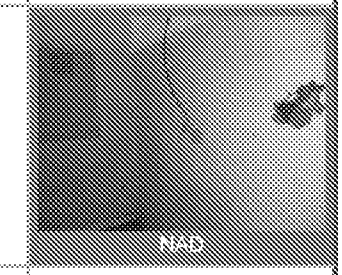

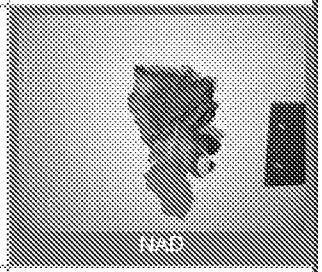
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-13								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut G2 **Level: 0** **Location: 011/bedroom**

Item / Position Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-14	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-19								 N/A
Door header panel	Wood										

Building: Accommodation Hut G2 **Level: 0** **Location: 012/bedroom**




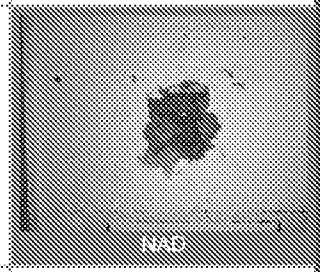
Item / Position Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								 N/A

table continued from previous page...

Building: Accommodation Hut G2				Level: 0			Location: 012/bedroom				
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-13								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-14	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-19								 NAD
Door header panel	Wood										

Building: Accommodation Hut G2 **Level: 0** **Location: 013/bedroom**

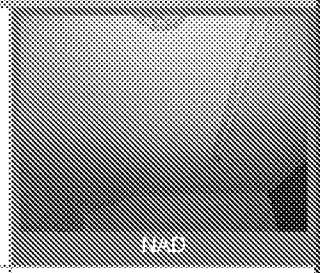


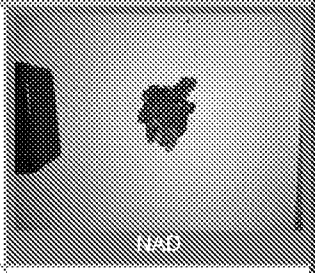
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-12								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-13								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-14	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut G2 **Level: 0** **Location: 013/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-19								
Door header panel	Wood										

Building: Accommodation Hut G2 **Level: 1** **Location: 001/loft space**



Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipe insulation	Man made mineral fibre										
Insulation	Man made mineral fibre										

Building: Accommodation Hut G2 **Level: 9** **Location: 999/externals**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof tiles	Metal										
Facia	Wood and plastic										
Walls	Plastic										
Rainwater goods	Plastic										

table continued from previous page...

Building: Accommodation Hut G2 **Level: 0** **Location: 999/externals**

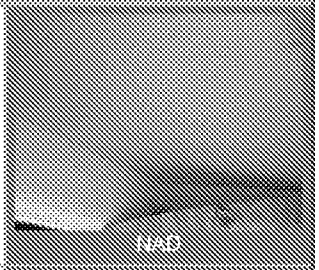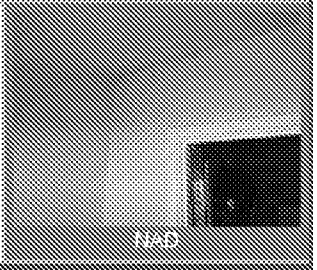Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling panels with textured coating in porch	Textured coating	Sample	472686-20								 NAD
Wall panels with textured coating in porch	Textured coating	Sample	472686-21								 NAD

Building: Accommodation Hut H1 **Level: 0** **Location: 001/corridor**

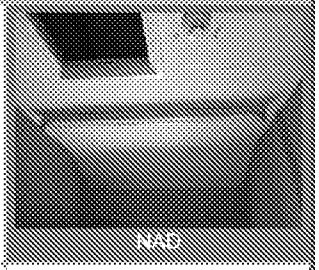
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Sample	472686-77								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 001/corridor**



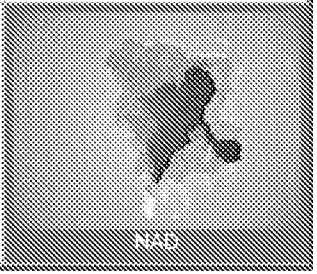
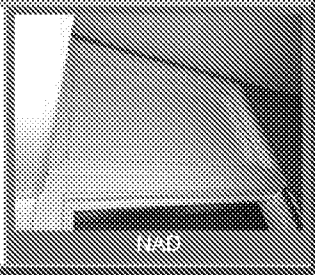
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Sample	472686-78								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Sample	472686-79	21 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Duct covers	Wood										
Insulation in floor ducts	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Sample	472686-80								 NAD

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 001/corridor**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Header panels	Insulating board	Sample	472686-81								 NAD

Building: Accommodation Hut H1 **Level: 0** **Location: 002/plant room**

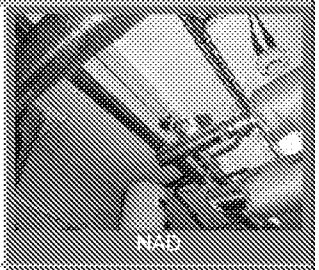
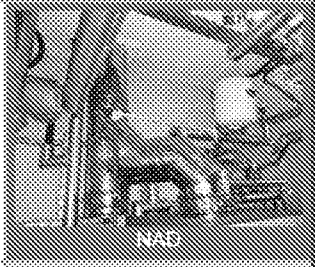

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard panels with textured coating	Cross Reference	472686-77								 NAD
Walls	Hardboard panels with textured coating	Cross Reference	472686-78								 NAD
Floor covering	Asbestos-containing bitumen adhesive	Cross Reference	472686-79	4 Sqm.	1	1	0	Chrysotile	3	3	 R3

table continued from previous page...

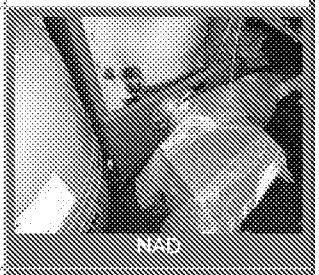
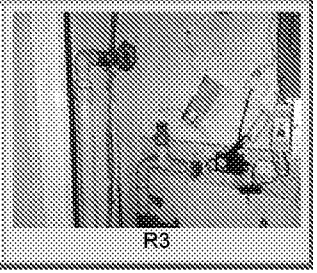


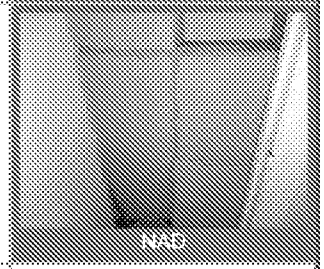
Building: Accommodation Hut H1				Level: 0		Location: 002/plant room					
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Floor	Concrete										
Door and frame	Wood										
Insulation in floor duct	Man made mineral fibre										
Pipework	Metal										
Pipework insulation	Metal and man made mineral fibre										
Electrics	Modern										
Boiler	Modern										
Gasket to boiler	Gasket	Sample	472686-82								 NAD
Panels around vents	Insulating board	Sample	472686-83								 NAD
Lining panels to walls in electrical area	Asbestos-containing cement	Sample	472686-84	4 Sqm.	1	1	1	Chrysotile	4	3	 R3



table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 002/plant room**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								 NAD

Building: Accommodation Hut H1 **Level: 0** **Location: 003/cupboard**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard panels with textured coating	Cross Reference	472686-77								 NAD
Walls	Hardboard panels with textured coating	Cross Reference	472686-78								 NAD
Floor	Concrete										
Door and frame	Wood										

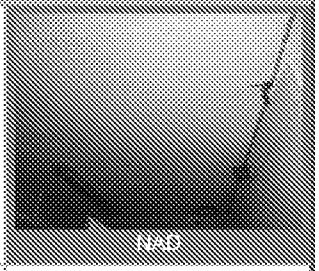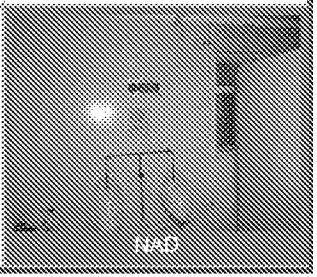Building: Accommodation Hut H1				Level: 0		Location: 004/bathroom					
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								
Walls	Wood and plastic										
Floor covering	Modern linoleum										
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Toilet cisterns	Ceramics										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								

Building: Accommodation Hut H1 **Level: 0** **Location: 005/kitchen**

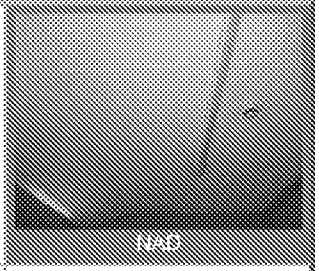
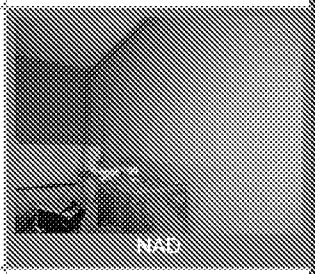
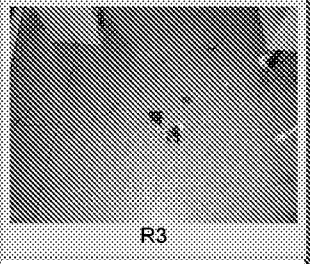
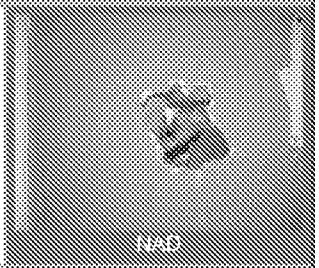
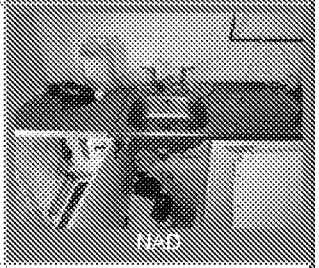
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-78								
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-79	6 Sqm.	1	1	0	Chrysotile	3	2	
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 005/kitchen**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								
Sink pad	Bituminous product	Sample	472686-85								
Water heater	Modern										

Building: Accommodation Hut H1 **Level: 0** **Location: 006/bedroom**

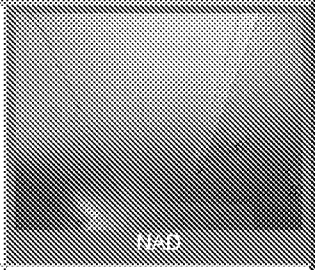
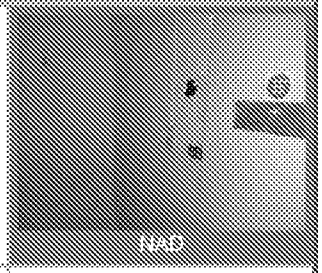

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 006/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-78								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-79	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								 NAD


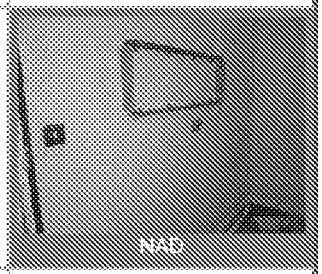
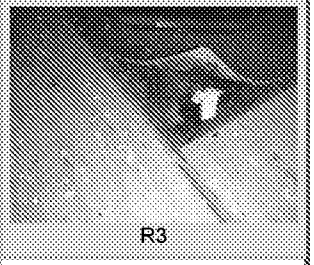
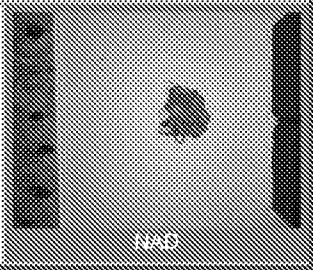
Building: Accommodation Hut H1				Level: 0		Location: 007/bedroom					
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-78								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-79	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 007/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								 NAD

Building: Accommodation Hut H1 **Level: 0** **Location: 008/bedroom**


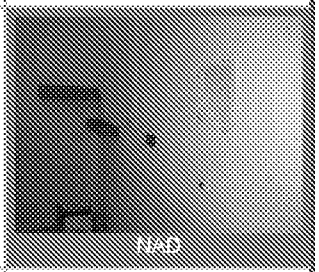


Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-78								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut H1 Level: 0 Location: 008/bedroom

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-79	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								 NAD

Building: Accommodation Hut H1 Level: 0 Location: 009/bedroom


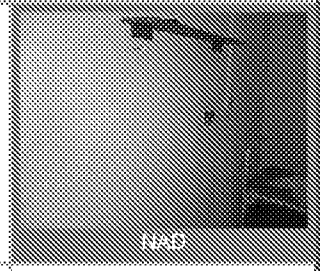

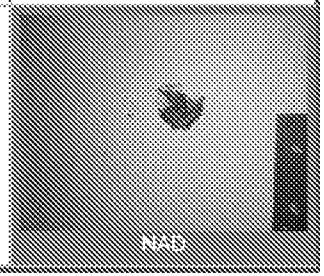
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 009/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friability Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-78								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-79	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								 NAD

Building: Accommodation Hut H1 **Level: 0** **Location: 010/bedroom**

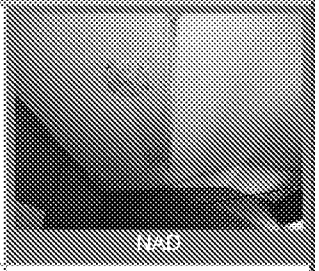
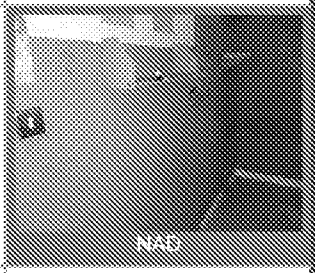
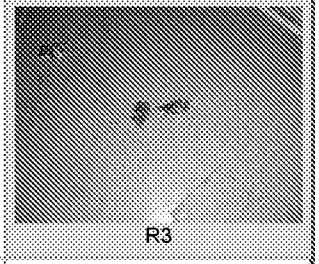

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Found	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-78								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-79	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 010/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								 NAD

Building: Accommodation Hut H1 **Level: 0** **Location: 011/bedroom**

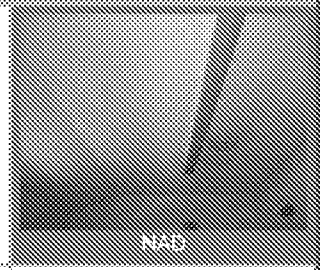
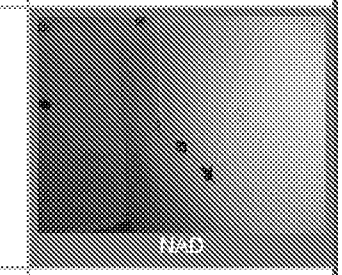

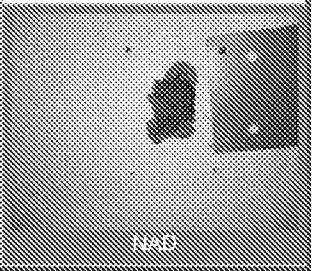
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-78								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 011/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-79	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								 NAD

Building: Accommodation Hut H1 **Level: 0** **Location: 012/bedroom**




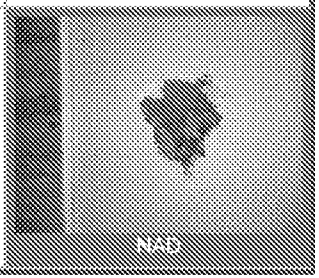
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 012/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-78								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-79	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								 NAD

Building: Accommodation Hut H1 **Level: 0** **Location: 013/bedroom**


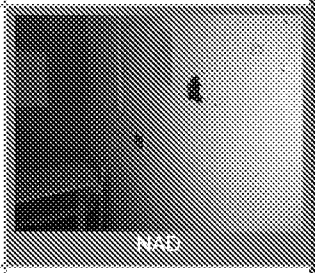


Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-78								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-79	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 013/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-80								 N/D

Building: Accommodation Hut H1 **Level: 1** **Location: 001/loft space**



Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipework insulation	Man made mineral fibre and foam										
Insulation	Man made mineral fibre										
Slaters felt	Asbestos-containing bituminous product	Sample	472686-86	100 Sqm.	1	1	0	Chrysotile	3	2	 R3
		Viable above timber									

Building: Accommodation Hut H1 **Level: 9** **Location: 999/externals**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof tiles	Metal										
Facia	Wood and plastic										
Walls	Plastic										

table continued from previous page...

Building: Accommodation Hut H1 **Level: 0** **Location: 999/externals**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Rainwater goods	Plastic										
Hardboard panels to ceiling with textured coating in porch	Textured coating	Sample	472686-87								 NAD
Hardboard panels to walls with textured coating in porch	Textured coating	Sample	472686-88								 NAD

Building: Accommodation Hut H2 **Level: 0** **Location: 001/corridor**

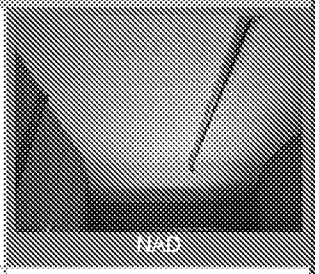


Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Sample	472686-89								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 001/corridor**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Sample	472686-90								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Sample	472686-91	21 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Duct covers	Wood										
Insulation in floor ducts	Man made mineral fibre										

Building: Accommodation Hut H2 **Level: 0** **Location: 002/plant room**


Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Asbestos-containing cement panels with textured coating	Sample	472686-92	4 Sqm.	1	1	1	Chrysotile	4	2	 R3

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 002/plant room**






Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Walls	Asbestos-containing cement panels with textured coating	Sample	472686-93	10 Sqm.	1	1	1	Chrysotile	4	2	 R3
Floor covering	Asbestos-containing bitumen adhesive	Cross Reference	472686-91	4 Sqm.	1	1	0	Chrysotile	3	3	 R3
Floor	Concrete										
Door and frame	Wood										
Insulation in floor duct	Man made mineral fibre										
Pipework	Metal										
Pipework insulation	Metal and man made mineral fibre										
Electrics	Modern										
Boiler	Modern										
Gasket to boiler	Gasket	Sample	472686-94								 NAD

table continued from previous page...



Building: Accommodation Hut H2 **Level: 0** **Location: 002/plant room**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Panels around vents	Insulating board	Sample	472686-95								 NAD
Floor covering on duct cover and in electrical area	Asbestos-containing floor tile with bitumen adhesive	Sample	472686-96	0.5 Sqm.	1	1	0	Chrysotile	3	3	 R3
Walls	Plasterboard and hardboard										

Building: Accommodation Hut H2 **Level: 0** **Location: 003/cupboard**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard										
Walls	Wood and hardboard										
Floor covering	Modern linoleum										
Floor	Concrete										
Door and frame	Wood										

Building: Accommodation Hut H2 **Level: 0** **Location: 004/bathroom**

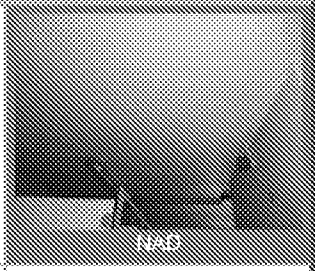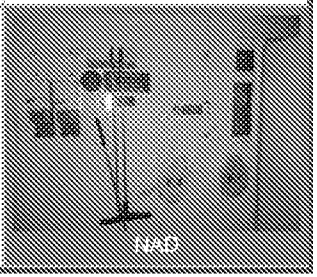Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friability	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-77								
Walls	Wood and plastic										
Floor covering	Ceramics and modern linoleum										
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Toilet cisterns	Ceramics										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-97								

Building: Accommodation Hut H2 **Level: 0** **Location: 005/kitchen**

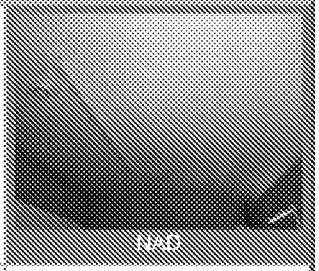
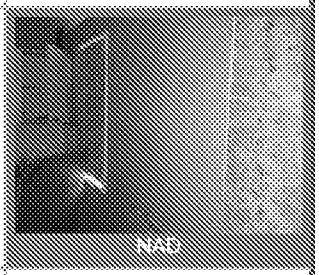

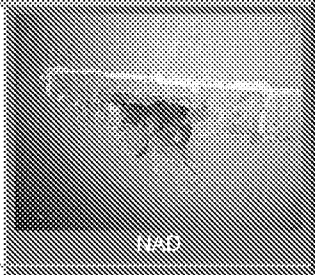
Item / Finish / Element	Additional Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-89								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-90								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-91	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 005/kitchen**

Item / Position Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Sample	472686-97								 NAD
Sink pad	Bituminous product	Sample	472686-98								 NAD

Building: Accommodation Hut H2 **Level: 0** **Location: 006/bedroom**

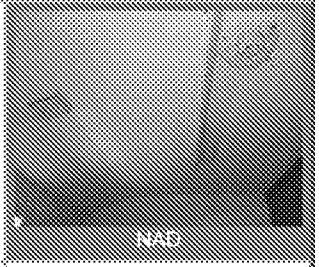
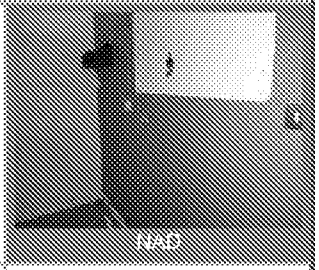

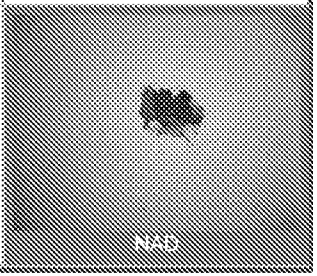
Item / Position Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-89								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 006/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-90								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-91	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-97								 NAD

Building: Accommodation Hut H2 **Level: 0** **Location: 007/bedroom**


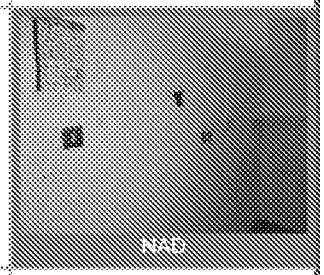

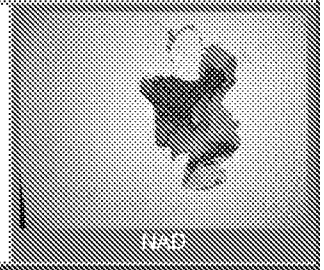
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Found	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-89								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-90								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-91	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 007/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-97								 NAD

Building: Accommodation Hut H2 **Level: 0** **Location: 008/bedroom**

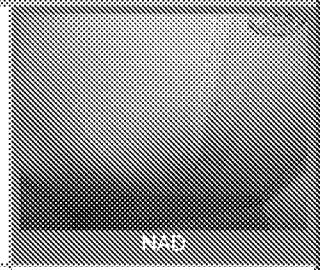
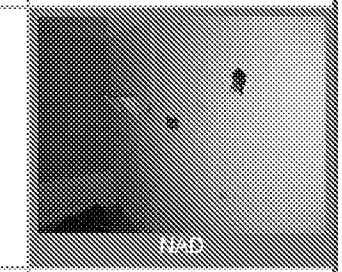

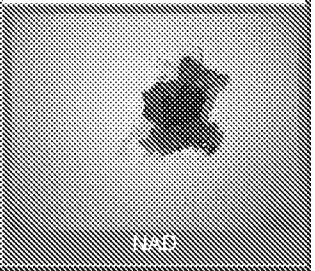
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-89								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-90								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 008/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-91	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-97								 NAD

Building: Accommodation Hut H2 **Level: 0** **Location: 009/bedroom**

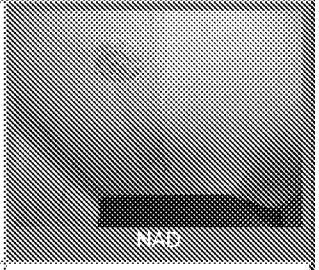
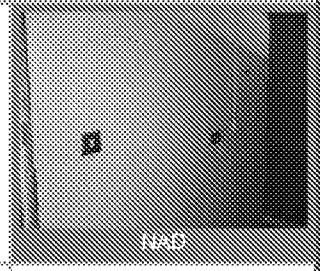
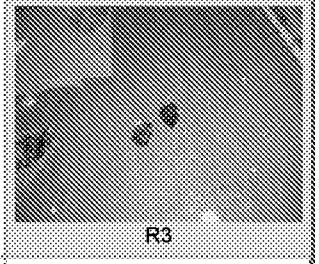
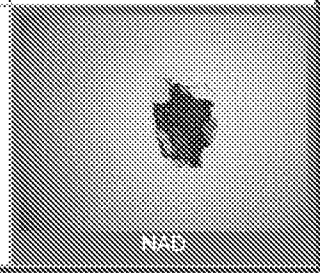
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-89								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 009/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-90								
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-91	6 Sqm.	1	1	0	Chrysotile	3	2	
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-97								

Building: Accommodation Hut H2 **Level: 0** **Location: 010/bedroom**


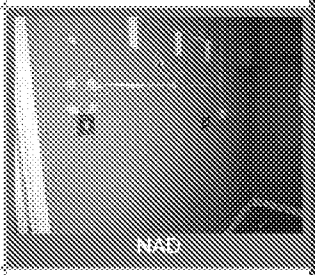
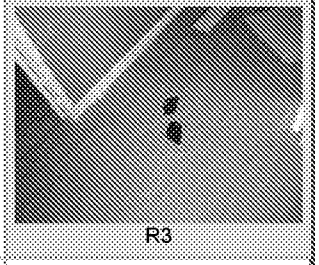

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-89								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-90								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-91	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 010/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-97								

Building: Accommodation Hut H2 **Level: 0** **Location: 011/bedroom**

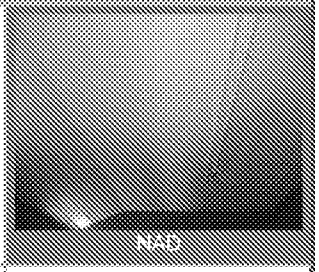


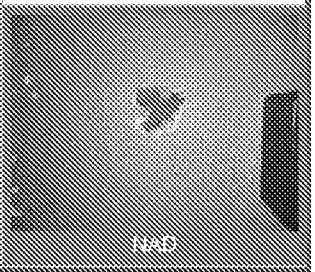
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-89								
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-90								
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 011/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-91	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-97								 N4B

Building: Accommodation Hut H2 **Level: 0** **Location: 012/bedroom**


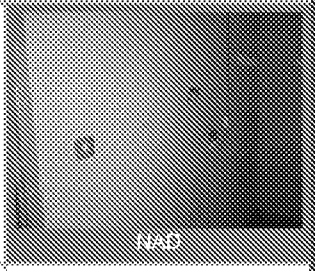

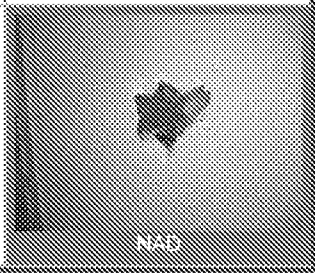
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-89								 N4B
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 012/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friability Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-90								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-91	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-97								 NAD

Building: Accommodation Hut H2 **Level: 0** **Location: 013/bedroom**




Item / Product / Component	Additional Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Found	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-89								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-90								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-91	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 013/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-97								 H&D

Building: Accommodation Hut H2 **Level: 1** **Location: 001/loft space**



Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Cement floor to boiler room below	Asbestos-containing cement	Sample	472686-99	4 Sqm.	1	1	1	Chrysotile	4	2	 R3
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipework insulation	Man made mineral fibre										
Insulation	Man made mineral fibre										

Building: Accommodation Hut H2 **Level: 9** **Location: 999/externals**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof tiles	Metal										
Facia	Wood and plastic										
Walls	Plastic										
Rainwater goods	Plastic										

table continued from previous page...

Building: Accommodation Hut H2 **Level: 0** **Location: 999/externals**

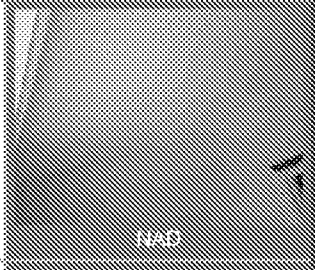Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Hardboard panels to ceiling with textured coating in porch	Textured coating	Sample	472686-100								 NAD
Hardboard panels to walls with textured coating in porch	Textured coating	Sample	472686-101								 NAD

Building: Accommodation Hut H **Level: 0** **Location: 001/corridor**

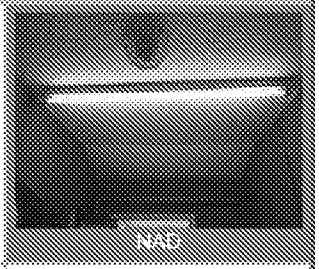
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Sample	472686-102								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 001/corridor**

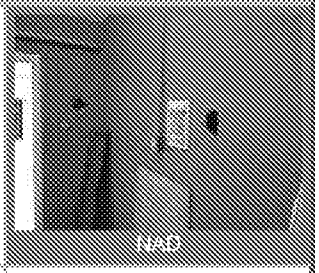

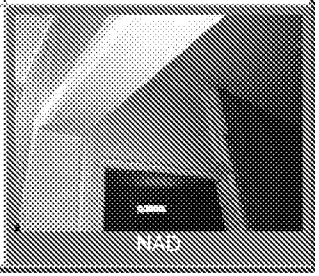



Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Sample	472686-103								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Sample	472686-104	21 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Duct covers	Wood										
Insulation in floor ducts	Man made mineral fibre										
Header panels	Insulating board	Sample	472686-105								 NAD

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 001/corridor**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Sample	472686-106	0.5 Sqm.	1	1	0	Chrysotile	3	3	 R3
		On both duct covers									
Cement debris in duct	Asbestos-containing cement	Sample	472686-107	0.1 Sqm.	1	3	3	Chrysotile	8	2	 R2
		In duct by front door only									
Felt debris in floor duct	Bituminous product	Sample	472686-108								 N/D
		In duct by front door only									

Building: Accommodation Hut I1 **Level: 0** **Location: 002/plant room**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Plasterboard										
Walls	Plasterboard										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 002/plant room**



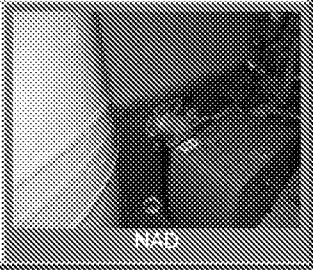
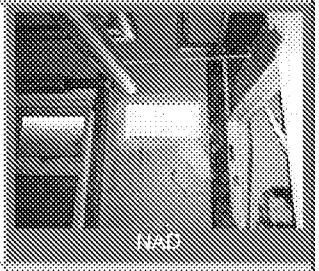

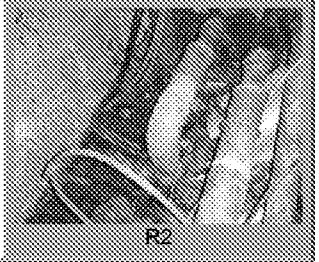
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Floor covering	Asbestos-containing floor tile with bitumen adhesive	Sample	472686-109	4 Sqm.	1	1	0	Chrysotile	3	3	 R3
Floor	Concrete										
Door and frame	Wood										
Insulation in floor duct	Man made mineral fibre										
Pipework	Metal										
Pipework insulation	Metal and man made mineral fibre										
Electrics	Modern										
Boiler	Modern										
Gasket to boiler	Gasket	Sample	472686-110								 NAD

table continued from previous page...




Building: Accommodation Hut I1 **Level: 0** **Location: 002/plant room**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Panels around vents	Insulating board	Sample	472686-111								 N/D
Lining panels to walls in electrical area	Asbestos-containing cement	Sample	472686-112	4 Sqm.	1	1	1	Chrysotile	4	3	 R3
Lining within cavity to external walls	Modern										
Cement debris in floor duct	Asbestos-containing cement	Cross Reference	472686-107	0.1 Sqm.	1	3	3	Chrysotile	8	2	 R2

Building: Accommodation Hut I1 **Level: 0** **Location: 003/cupboard**

Item / Product Examined	Material prescription	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard										
Walls	Hardboard										
Floor covering	Modern linoleum										
Floor	Concrete										
Door and frame	Wood										

Building: Accommodation Hut I1 **Level: 0** **Location: 004/bathroom**

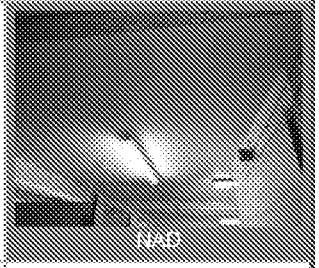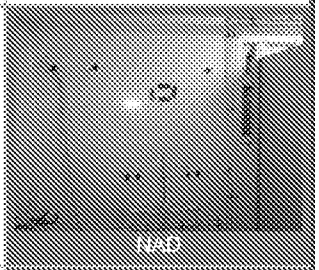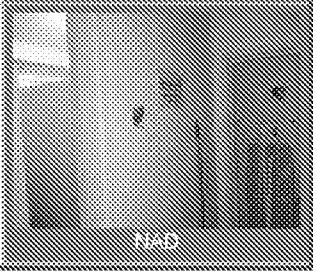Item / Product / Element	Material Description	Sampling Strategy	Sample No	Colour	Product Score	Material Condition	Surface Treatment	Friability	Damage Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-102								
Walls	Wood and plastic										
Floor covering	Ceramics and modern linoleum										
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Toilet cisterns	Ceramics										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-113								
Walls	Hardboard panels with textured coating	Cross Reference	472686-103								

Building: Accommodation Hut H1 **Level: 0** **Location: 005/kitchen**

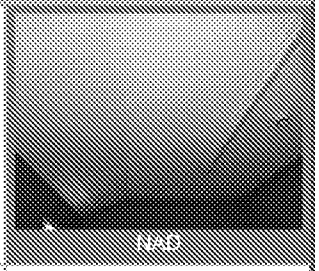
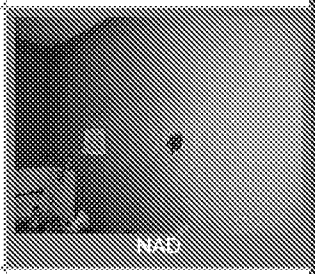

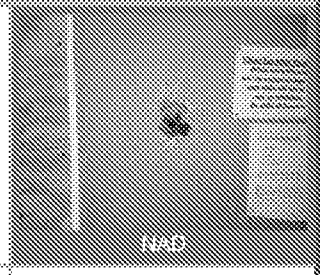
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Quantities	Surface Treatment	Friability	Release of Fibres	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-102								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-103								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-104	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 005/kitchen**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Sample	472686-113								
Water heater	Modern										
Sink pad	Modern										

Building: Accommodation Hut I1 **Level: 0** **Location: 006/bedroom**

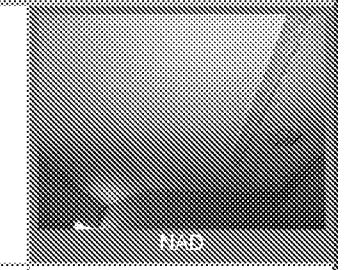
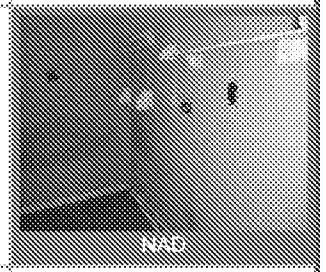
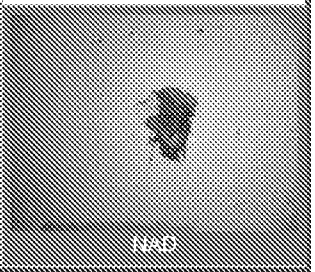
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-102								
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-103								
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 006/bedroom**




Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-104	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-113								 N4B

Building: Accommodation Hut I1 **Level: 0** **Location: 007/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-102								N4B
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 007/bedroom**

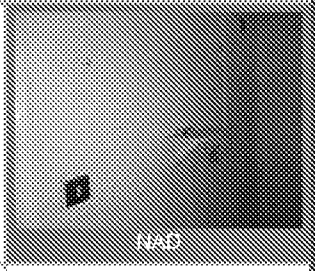Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-103								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-104	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-113								 NAD

Building: Accommodation Hut H **Level: 0** **Location: 008/bedroom**

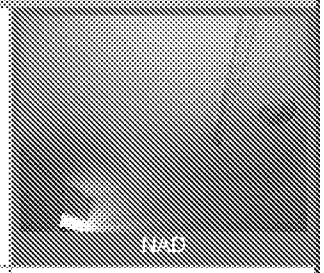
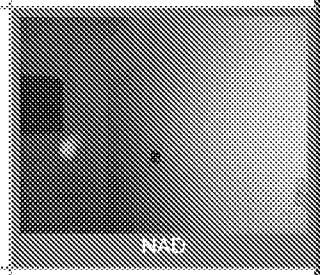


Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Quantities	Surface Treatment	Friability	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-102								
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-103								
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-104	6 Sqm.	1	1	0	Chrysotile	3	2	
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 008/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-113								 NAD

Building: Accommodation Hut I1 **Level: 0** **Location: 009/bedroom**

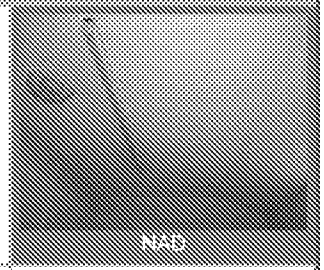
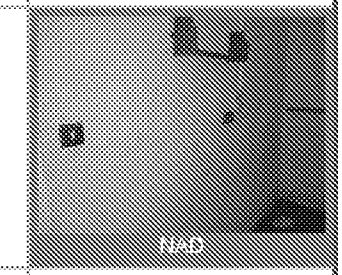

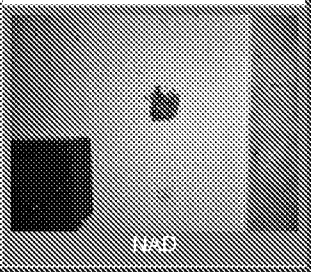
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-102								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-103								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 009/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-104	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-113								 NAD

Building: Accommodation Hut I1 **Level: 0** **Location: 010/bedroom**

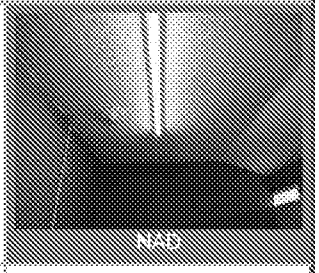
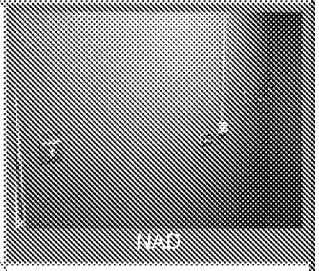

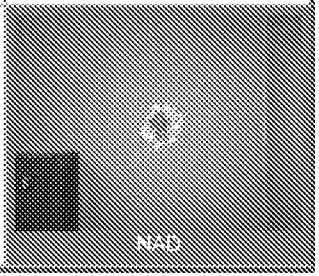
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-102								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 010/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-103								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-104	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-113								 NAD

Building: Accommodation Hut H1 **Level: 0** **Location: 011/bedroom**

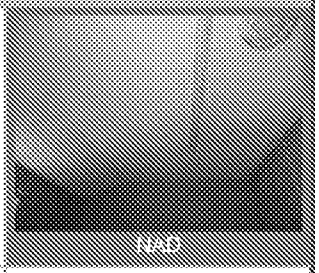
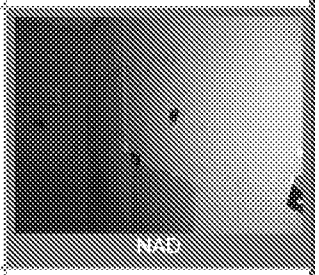

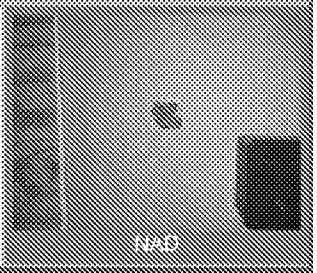
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friability	Debris Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-102								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-103								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-104	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 011/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-113								 NAD

Building: Accommodation Hut I1 **Level: 0** **Location: 012/bedroom**

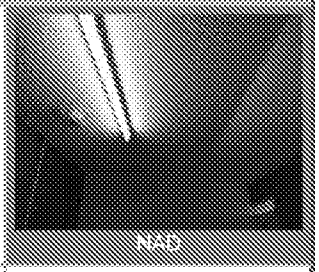
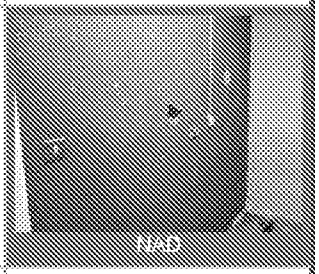

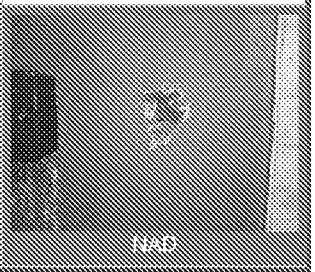
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-102								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-103								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 012/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-104	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-113								 NAD

Building: Accommodation Hut I1 **Level: 0** **Location: 013/bedroom**

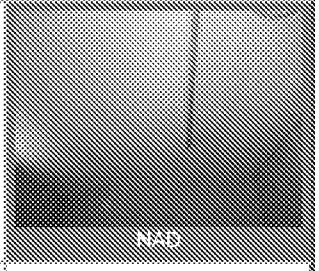
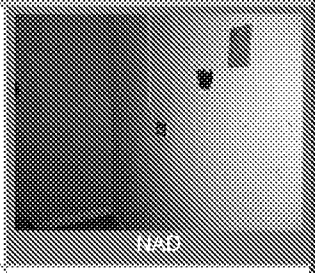

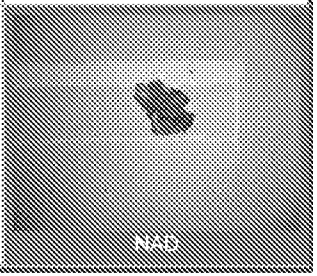
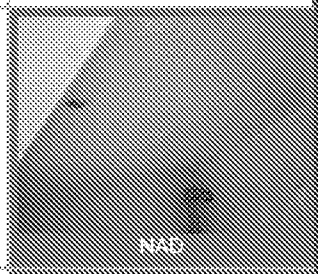
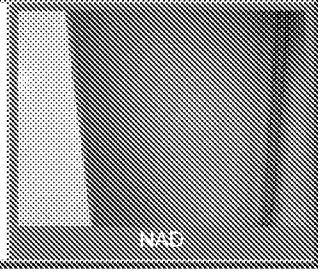
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-102								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut I1 **Level: 0** **Location: 013/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-103								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-104	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-113								 NAD

Building: Accommodation Hut I1					Level: 1				Location: 001/loft space		
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipework insulation	Man made mineral fibre and foam										
Insulation	Man made mineral fibre										

Building: Accommodation Hut I1					Level: 9				Location: 999/externals		
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof tiles	Metal										
Facia	Wood and plastic										
Walls	Plastic										
Rainwater goods	Plastic										
Hardboard panels to ceiling with textured coating in porch	Textured coating	Sample	472686-114								
Hardboard panels to walls with textured coating in porch	Textured coating	Sample	472686-115								

Building: Accommodation Hut I2 **Level: 0** **Location: 001/corridor**

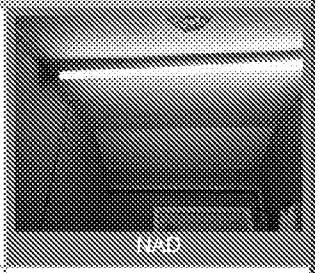
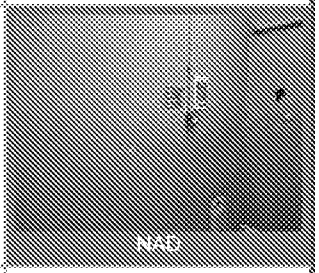
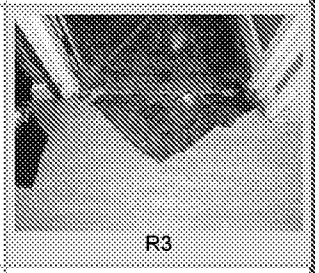
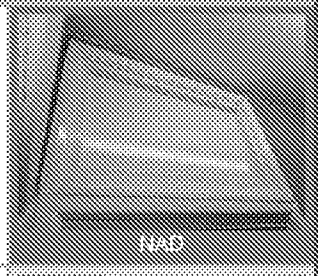
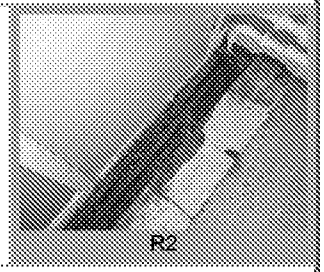
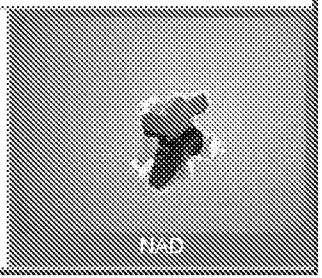
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Quantities	Surface Treatment	Friability	Release of Fibres	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Sample	472686-116								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Sample	472686-117								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Sample	472686-118	21 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Duct covers	Wood										
Insulation in floor ducts	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 001/corridor**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Header panels	Insulating board	Sample	472686-119								 N4D
Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Sample	472686-120	0.5 Sqm.	1	1	0	Chrysotile	3	3	 R3
		On both duct covers									
Cement debris in duct	Asbestos-containing cement	Sample	472686-121	0.1 Sqm.	1	1	3	Chrysotile	6	3	 R2
		In duct by front door only									
Lining within cavity to external wall	Bituminous product	Cross Reference	472686-126								 N4D

Building: Accommodation Hut I2 **Level: 0** **Location: 002/plant room**







Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Asbestos-containing cement with textured coating	Sample	472686-122	4 Sqm.	1	1	1	Chrysotile	4	2	 R3
Walls	Asbestos-containing cement with textured coating	Sample	472686-123	14 Sqm.	1	1	1	Chrysotile	4	3	 R3
Floor covering	Asbestos-containing bitumen adhesive	Cross Reference	472686-118	4 Sqm.	1	1	0	Chrysotile	3	3	 R3
Floor	Concrete										
Door and frame	Wood										
Insulation in floor duct	Man made mineral fibre										
Pipework	Metal										
Pipework insulation	Metal and man made mineral fibre										
Electrics	Modern										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 002/plant room**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Boiler	Modern										
Gasket to boiler	Gasket	Sample	472686-124								 N/AD
Panels around vents	Insulating board	Sample	472686-125								 N/AD
Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Cross Reference	472686-120	0.3 Sqm.	1	1	0	Chrysotile	3	3	 R3

Building: Accommodation Hut I2 **Level: 0** **Location: 003/cupboard**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 003/cupboard**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Walls	Hardboard										
Floor covering	Modern linoleum										
Floor	Concrete										
Door and frame	Wood										

Building: Accommodation Hut I2 **Level: 0** **Location: 004/bathroom**

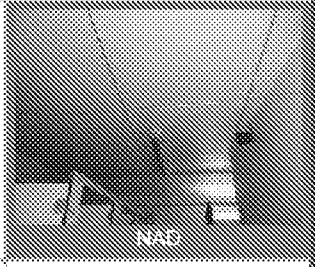


Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-116								 NAD
Walls	Wood and plastic										
Floor covering	Ceramics and modern linoleum										
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Toilet cisterns	Ceramics										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-126								 NAD

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 004/bathroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Walls	Hardboard panels with textured coating	Cross Reference	472686-117								 NAD

Building: Accommodation Hut I2 **Level: 0** **Location: 005/kitchen**

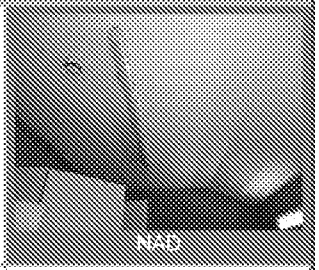
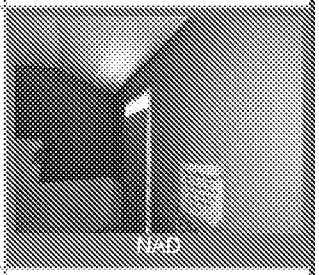

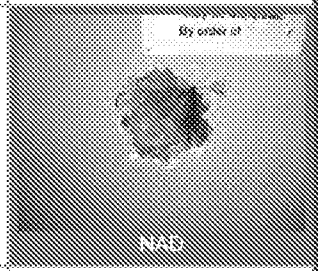
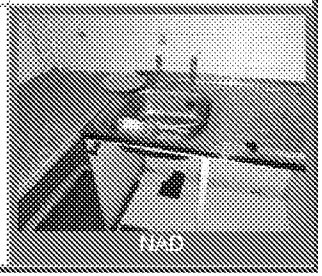
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-116								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-117								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 005/kitchen**

Item / Position Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-118	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Sample	472686-126								 N/D
Water heater	Modern										
Sink pad	Modern	Sample	472686-127								 N/D

Building: Accommodation Hut I2 **Level: 0** **Location: 006/bedroom**


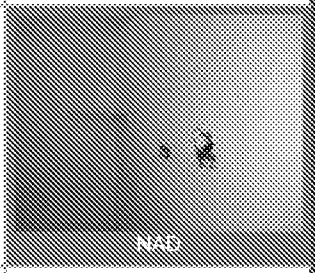

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friability	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-116								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-117								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-118	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 006/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-126								 NAD

Building: Accommodation Hut I2 **Level: 0** **Location: 007/bedroom**


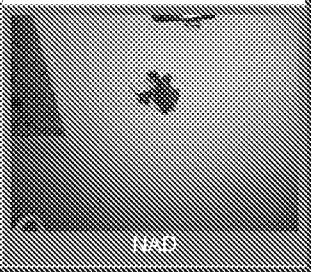
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-116								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-117								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 007/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-118	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-126								 NAD

Building: Accommodation Hut I2 **Level: 0** **Location: 008/bedroom**


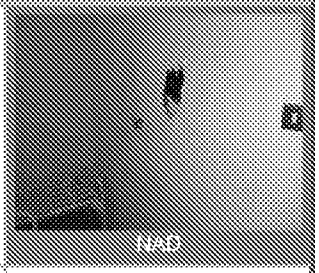

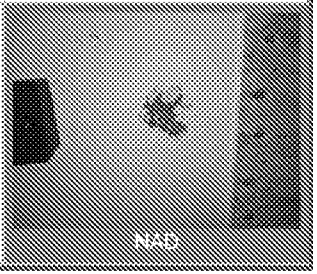
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-116								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 008/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-117								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-118	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-126								 NAD

Building: Accommodation Hut I2 **Level: 0** **Location: 009/bedroom**

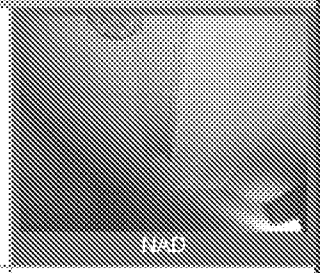
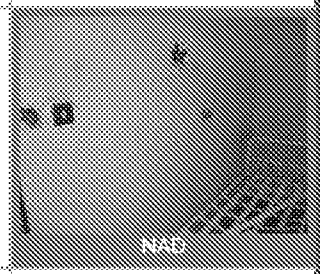

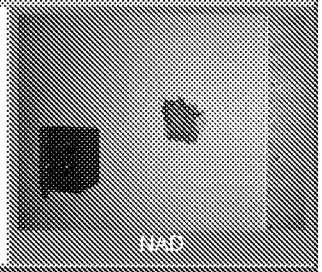
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friability	Debris Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-116								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-117								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-118	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 009/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-126								 NAD

Building: Accommodation Hut I2 **Level: 0** **Location: 010/bedroom**

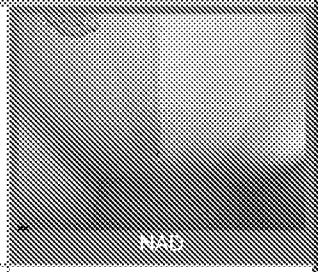
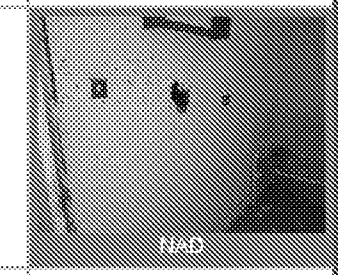


Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-116								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-117								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 010/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-118	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-126								 NAD

Building: Accommodation Hut I2 **Level: 0** **Location: 011/bedroom**

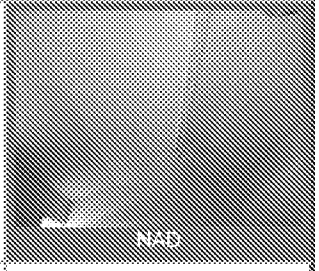
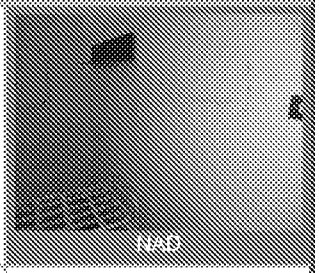

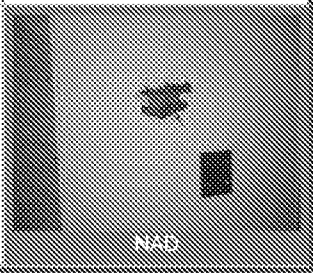
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-116								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 011/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-117								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-118	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-126								 NAD

Building: Accommodation Hut I2 **Level: 0** **Location: 012/bedroom**


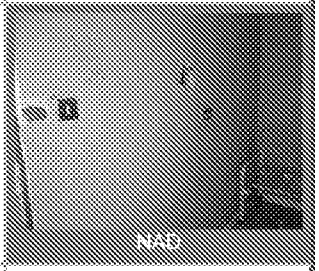
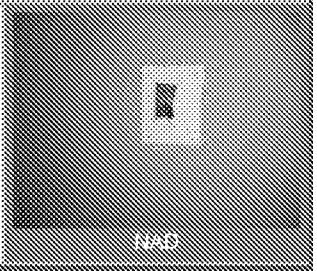
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Quantities	Surface Treatment	Friability	Release of Fibres	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-116								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-117								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-118	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 012/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-126								 NAD

Building: Accommodation Hut I2 **Level: 0** **Location: 013/bedroom**

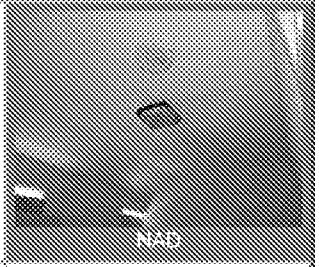
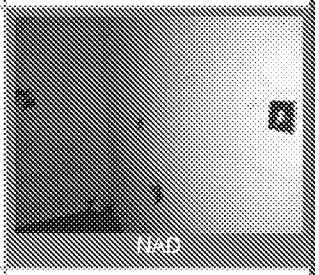


Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-116								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-117								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 0** **Location: 013/bedroom**


Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-118	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-126								 R4B

Building: Accommodation Hut I2 **Level: 1** **Location: 001/loft space**



Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipework insulation	Man made mineral fibre and foam										
Insulation	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut I2 **Level: 1** **Location: 001/loft space**

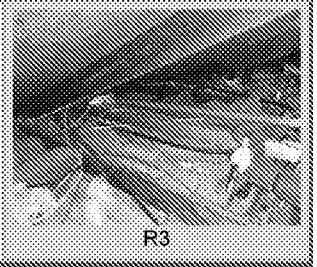Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Cement panels to ceiling below	Asbestos-containing cement	Sample	472686-128	4 Sqm.	1	1	1	Chrysotile	4	2	 R3

Building: Accommodation Hut I2 **Level: 9** **Location: 999/externals**

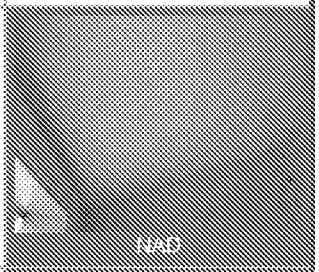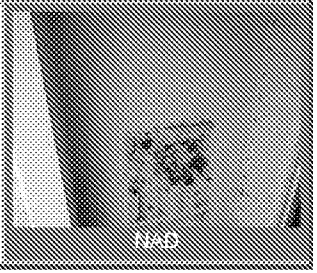Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre ID	Material Score	Accessibility Score	Risk Level Assessment
Roof tiles	Metal										
Facia	Wood and plastic										
Walls	Plastic										
Rainwater goods	Plastic										
Hardboard panels to ceiling with textured coating in porch	Textured coating	Sample	472686-129								 NAD
Hardboard panels to walls with textured coating in porch	Textured coating	Sample	472686-130								 NAD

Building: Accommodation Hut O1 **Level: 0** **Location: 001/corridor**

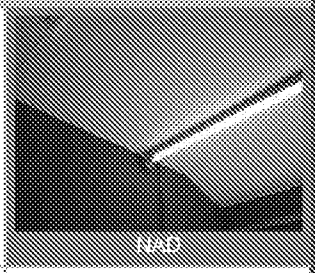
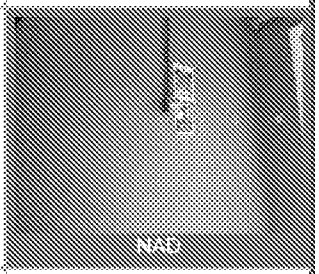
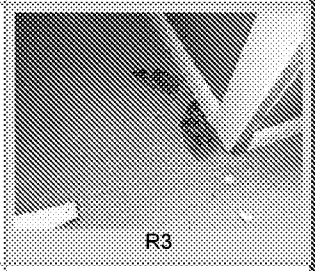
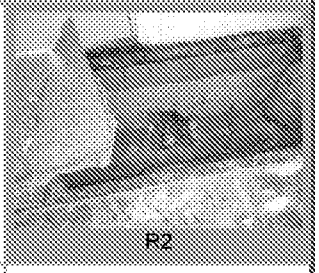
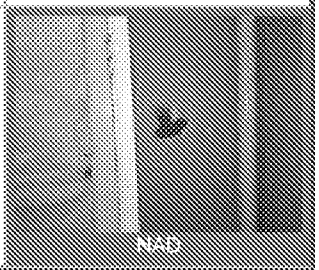
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Sample	472686-46								
Walls	Hardboard										
Wall covering	Textured coating	Sample	472686-47								
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Sample	472686-48	21 Sqm.	1	1	0	Chrysotile	3	2	
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Duct covers	Wood										

table continued from previous page...

Building: Accommodation Hut O1 **Level: 0** **Location: 001/corridor**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Felt debris in floor ducts	Asbestos-containing bituminous product	Sample	472686-50	0.1 Sqm.	1	3	3	Chrysotile	8	2	 P2
Insulation in floor ducts	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Sample	472686-49								 NAD

Building: Accommodation Hut O1 **Level: 0** **Location: 002/plant room**


Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Cement lining to walls & ceiling	Asbestos-containing cement panels with textured coating	Sample	472686-51	4 Sqm.	1	1	1	Chrysotile	4	2	 R3

table continued from previous page...

Building: Accommodation Hut O1 **Level: 0** **Location: 002/plant room**




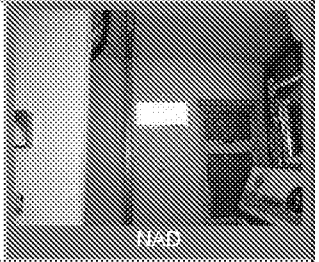

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Floor tiles & adhesive	Asbestos-containing cement panels with textured coating	Sample	472686-52	10 Sqm.	1	1	1	Chrysotile	4	2	 R3
Floor covering	Asbestos-containing bitumen adhesive	Cross Reference	472686-48	4 Sqm.	1	1	0	Chrysotile	3	3	 R3
Floor	Concrete										
Door and frame	Wood										
Insulation in floor duct	Man made mineral fibre										
Pipework	Metal										
Pipework insulation	Metal and man made mineral fibre										
Electrics	Modern										
Boiler	Modern										

table continued from previous page...




Building: Accommodation Hut O1 **Level: 0** **Location: 002/plant room**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Gasket to boiler	Gasket	Sample	472686-53								 N/AD
Panels around vents	Insulating board	Sample	472686-54								 N/AD
Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Sample	472686-55	0.5 Sqm.	1	1	0	Chrysotile	3	3	 R3
Walls	Plasterboard and hardboard										

Building: Accommodation Hut O1 **Level: 0** **Location: 003/cupboard**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Wood										
Walls	Wood and hardboard										
Floor covering	Modern screed										
Floor	Concrete										
Door and frame	Wood										

Building: Accommodation Hut O1 **Level: 0** **Location: 004/bathroom**

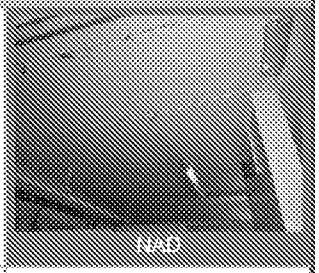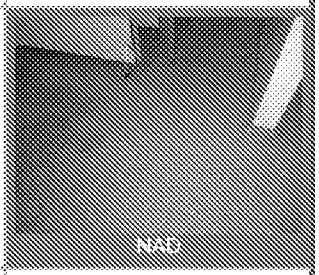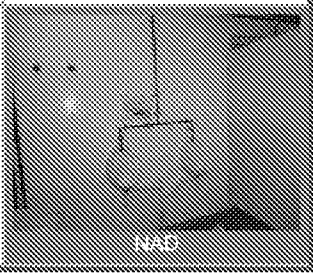Item / Finish / Element	Material Description	Sampling Strategy	Sample No	Extent	Product Type	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-46								 NAD
Walls	Wood and plastic										
Floor covering	Screed	Sample	472686-56								 NAD
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Toilet cisterns	Ceramics										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-49								 NAD

Building: Accommodation Hut O1 **Level: 0** **Location: 005/kitchen**

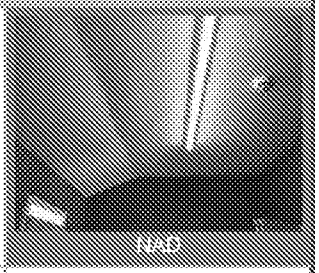
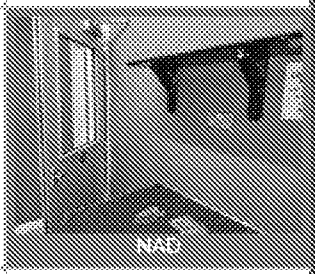
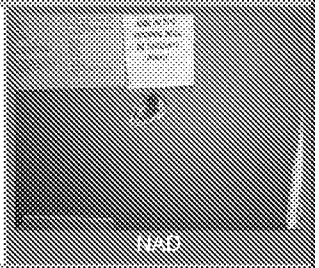
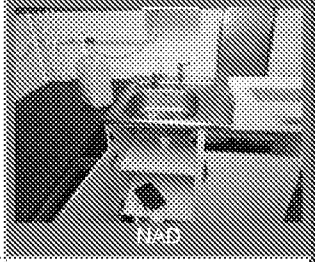
Item / Product / Element	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-46								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-47								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-48	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut O1 **Level: 0** **Location: 005/kitchen**




Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-49								 N/AD
Sink pad	Bituminous product	Sample	472686-57								 N/AD
Water heater	Modern										

Building: Accommodation Hut O1 **Level: 0** **Location: 006/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-46								N/AD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut O1 Level: 0 Location: 006/bedroom

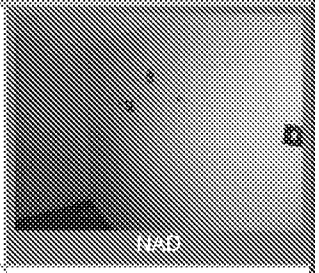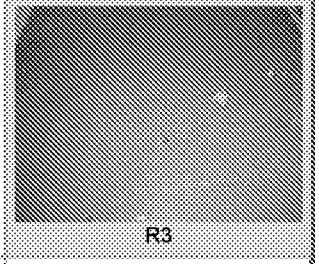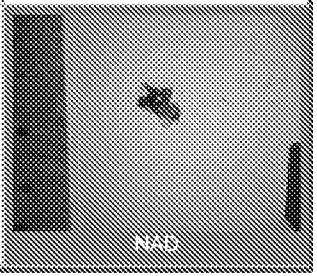Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-47								
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-48	6 Sqm.	1	1	0	Chrysotile	3	2	
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-49								

Building: Accommodation Hut O1 **Level: 0** **Location: 007/bedroom**


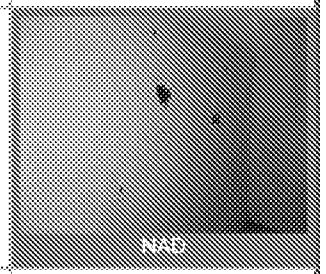

Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Found	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-46								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-47								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-48	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut O1 **Level: 0** **Location: 007/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-49								

Building: Accommodation Hut O1 **Level: 0** **Location: 008/bedroom**

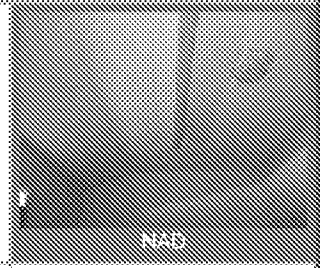
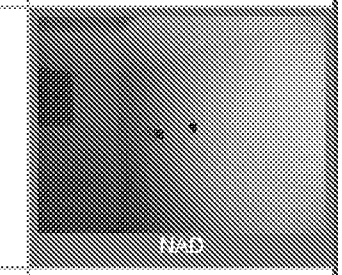

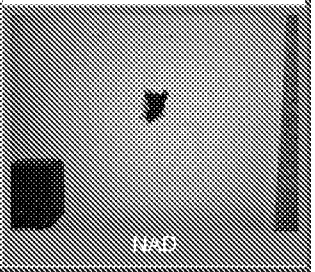
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-46								
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-47								
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut O1 **Level: 0** **Location: 008/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-48	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-49								 N/A

Building: Accommodation Hut O1 **Level: 0** **Location: 009/bedroom**


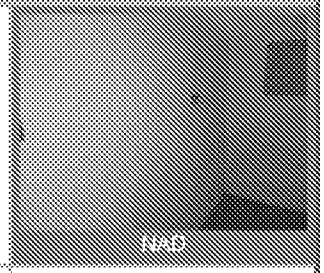

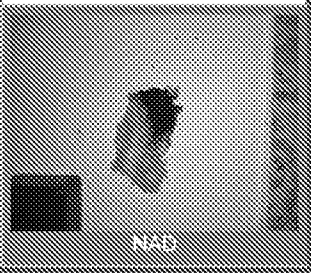
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-46								 N/A
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut O1 Level: 0 Location: 009/bedroom

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-47								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-48	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-49								 NAD

Building: Accommodation Hut O1 **Level: 0** **Location: 010/bedroom**


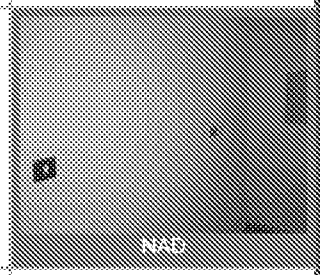


Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-46								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-47								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-48	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut O1 **Level: 0** **Location: 010/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-49								 NAD

Building: Accommodation Hut O1 **Level: 0** **Location: 011/bedroom**

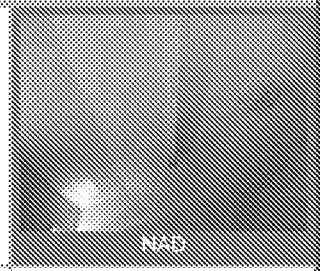
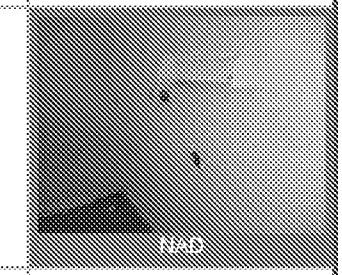

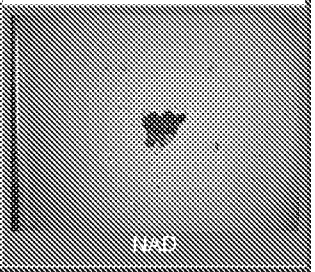
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-46								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-47								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut O1 **Level: 0** **Location: 011/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-48	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-49								 N/A

Building: Accommodation Hut O1 **Level: 0** **Location: 012/bedroom**


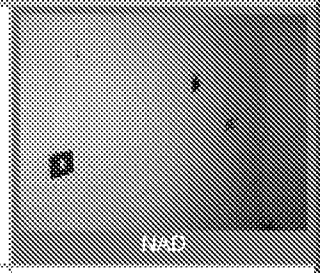


Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-46								 N/A
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut O1 **Level: 0** **Location: 012/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-47								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-48	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-49								 NAD

Building: Accommodation Hut O1 **Level: 0** **Location: 013/bedroom**


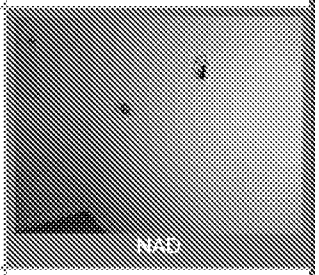

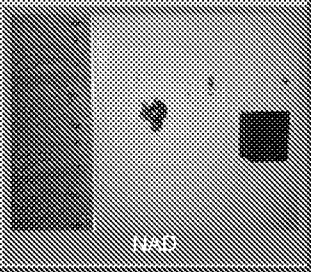
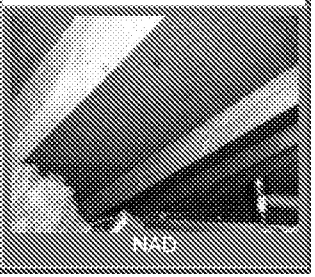
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-46								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-47								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-48	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...



Building: Accommodation Hut O1 **Level: 0** **Location: 013/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-49								 N4D

Building: Accommodation Hut O1 **Level: 1** **Location: 001/loft space**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Cement floor to boiler room below	Asbestos-containing cement	Sample	472686-58	4 Sqm.	1	1	1	Chrysotile	4	2	 R3
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipework insulation	Man made mineral fibre										
Insulation	Man made mineral fibre										
Slaters felt	Bituminous product	Sample	472686-59								 N4D

Building: Accommodation Hut O1 **Level: 9** **Location: 999/externals**

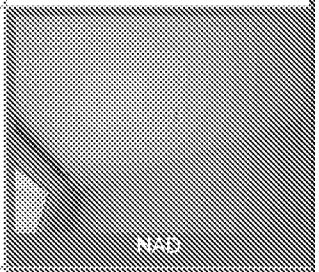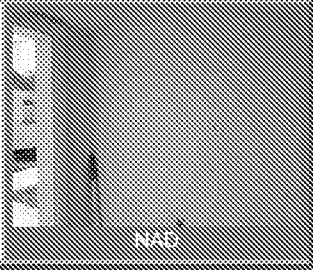Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Roof tiles	Metal										
Facia	Wood and plastic										
Walls	Plastic										
Rainwater goods	Plastic										
Hardboard panels to ceiling with textured coating in porch	Textured coating	Sample	472686-60								 NAD
Hardboard panels to walls with textured coating in porch	Textured coating	Sample	472686-61								 NAD

Building: Accommodation Hut O2 **Level: 0** **Location: 001/corridor**

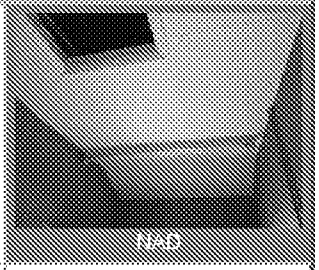
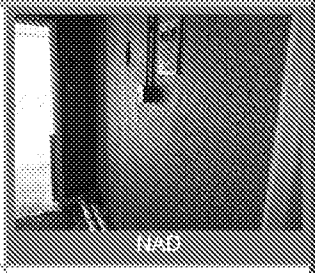
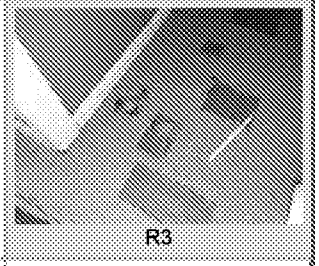
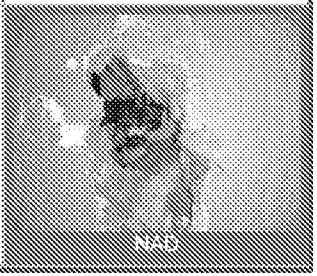
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Sample	472686-62								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut O2 **Level: 0** **Location: 001/corridor**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Sample	472686-63								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Sample	472686-64	21 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Duct covers	Wood										
Insulation in floor ducts	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Sample	472686-65								 NAD

Building: Accommodation Hut O2 **Level: 0** **Location: 002/plant room**






Item / Sample Examined	Additional Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Asbestos-containing cement panels with textured coating	Sample	472686-66	4 Sqm.	1	1	1	Chrysotile	4	2	 R3
Walls	Asbestos-containing cement panels with textured coating	Sample	472686-67	10 Sqm.	1	1	1	Chrysotile	4	2	 R3
Floor covering	Asbestos-containing bitumen adhesive	Cross Reference	472686-64	4 Sqm.	1	1	0	Chrysotile	3	3	 R3
Floor	Concrete										
Door and frame	Wood										
Insulation in floor duct	Man made mineral fibre										
Pipework	Metal										
Pipework insulation	Metal and man made mineral fibre										
Electrics	Modern										
Boiler	Modern										

table continued from previous page...




Building: Accommodation Hut O2 **Level: 0** **Location: 002/plant room**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Gasket to boiler	Gasket	Sample	472686-68								 NAD
Panels around vents	Insulating board	Sample	472686-69								 NAD
Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Sample	472686-70	0.5 Sqm.	1	1	0	Chrysotile	3	3	 R3
Walls	Plasterboard and hardboard										

Building: Accommodation Hut O2 **Level: 0** **Location: 003/cupboard**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Wood										
Walls	Wood and hardboard										
Floor covering	Modern screed										
Floor	Concrete										
Door and frame	Wood										

Building: Accommodation Hut O2 **Level: 0** **Location: 004/bathroom**

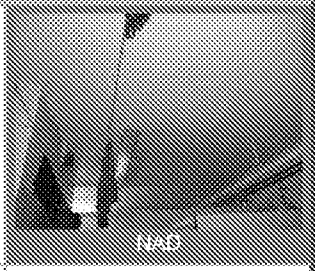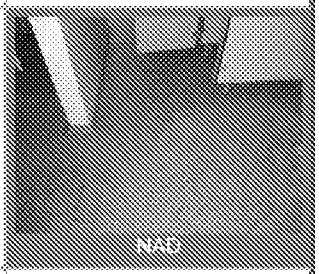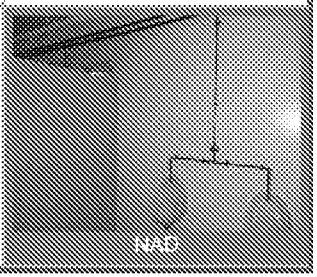Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-62								 NAD
Walls	Wood and plastic										
Floor covering	Screed	Sample	472686-71								 NAD
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Toilet cisterns	Ceramics										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-65								 NAD

Building: Accommodation Hut O2 **Level: 0** **Location: 005/kitchen**

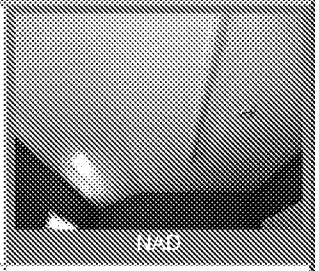
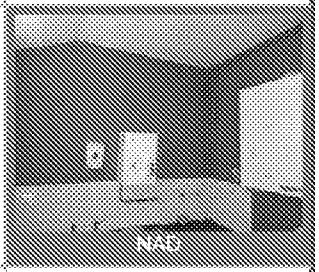
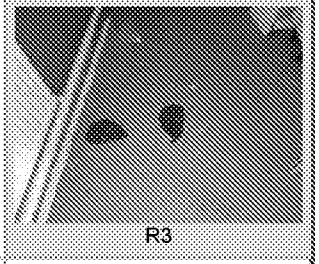
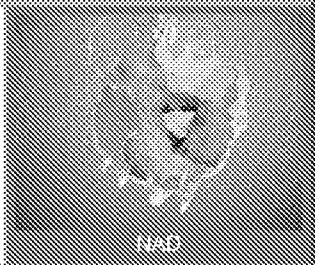
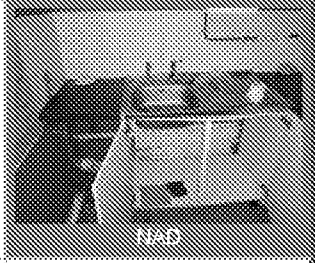
Item / Finish / Element	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-62								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-63								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-64	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut O2 **Level: 0** **Location: 005/kitchen**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-65								 NAD
Sink pad	Bituminous product	Sample	472686-72								 NAD
Water heater	Modern										

Building: Accommodation Hut O2 **Level: 0** **Location: 006/bedroom**

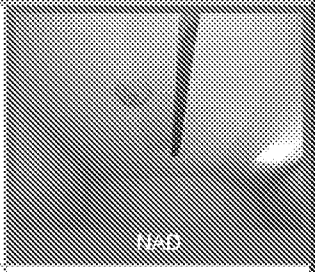
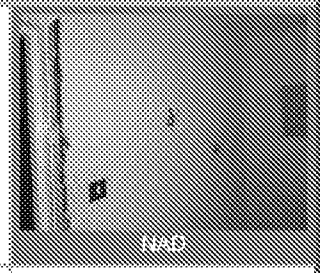

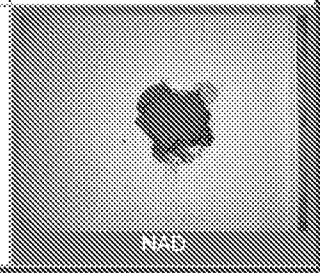
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-62								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut O2 **Level: 0** **Location: 006/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-63								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-64	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-65								 NAD

Building: Accommodation Hut O2 **Level: 0** **Location: 007/bedroom**

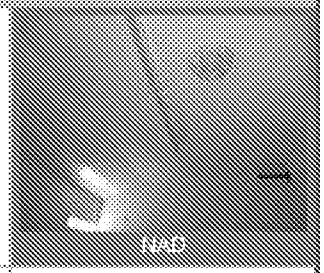


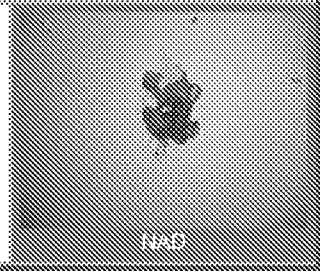
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Found	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-62								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-63								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-64	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut O2 **Level: 0** **Location: 007/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-65								 NAD

Building: Accommodation Hut O2 **Level: 0** **Location: 008/bedroom**


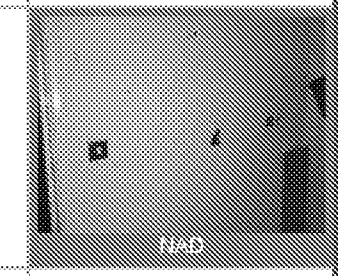


Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-62								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-63								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut O2 **Level: 0** **Location: 008/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-64	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-65								 N4B

Building: Accommodation Hut O2 **Level: 0** **Location: 009/bedroom**

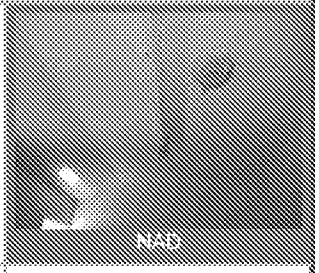
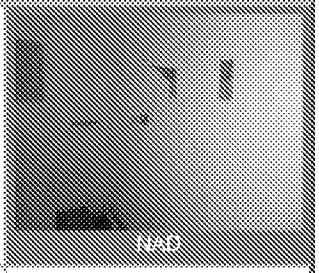

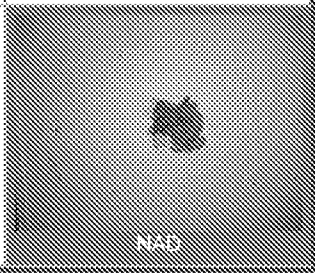
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-62								 N4B
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut O2 **Level: 0** **Location: 009/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-63								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-64	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-65								 NAD

Building: Accommodation Hut O2 **Level: 0** **Location: 010/bedroom**

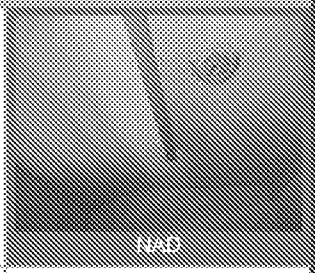

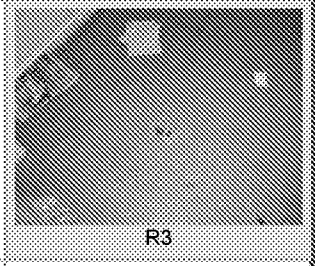
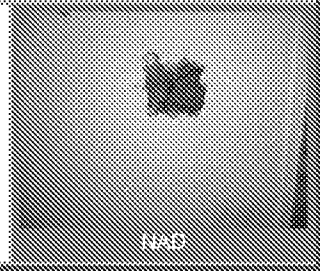
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friability	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-62								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-63								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-64	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut O2 **Level: 0** **Location: 010/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-65								 NAD

Building: Accommodation Hut O2 **Level: 0** **Location: 011/bedroom**

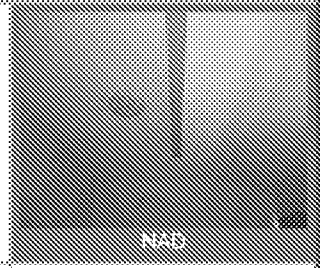
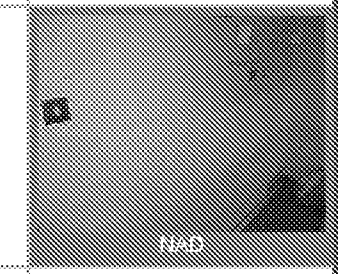

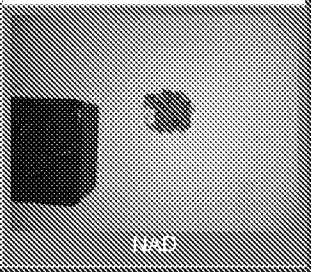
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-62								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-63								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut O2 **Level: 0** **Location: 011/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-64	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-65								 NAD

Building: Accommodation Hut O2 **Level: 0** **Location: 012/bedroom**


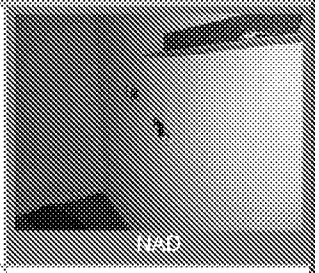

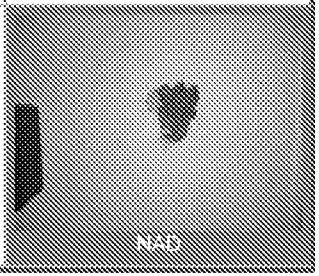
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-62								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut O2 **Level: 0** **Location: 012/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-63								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-64	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-65								 NAD

Building: Accommodation Hut O2 **Level: 0** **Location: 013/bedroom**

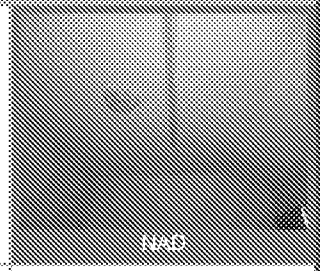
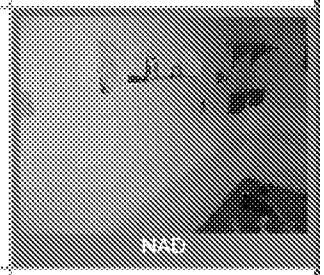

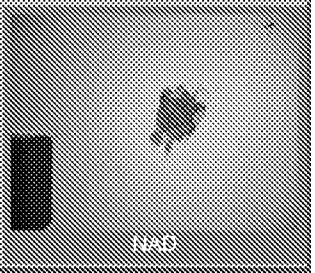
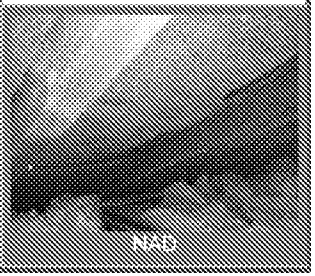
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-62								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-63								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-64	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...


Building: Accommodation Hut O2 **Level: 0** **Location: 013/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-65								 N4D

Building: Accommodation Hut O2 **Level: 1** **Location: 001/loft space**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Cement floor to boiler room below	Asbestos-containing cement	Sample	472686-73	4 Sqm.	1	1	1	Chrysotile	4	2	 R3
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipework insulation	Man made mineral fibre										
Insulation	Man made mineral fibre										
Slaters felt	Bituminous product	Sample	472686-74								 N4D

Building: Accommodation Hut O2 **Level: 9** **Location: 999/externals**

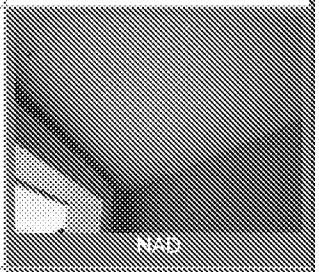Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof tiles	Metal										
Facia	Wood and plastic										
Walls	Plastic										
Rainwater goods	Plastic										
Hardboard panels to ceiling with textured coating in porch	Textured coating	Sample	472686-75								 NAD
Hardboard panels to walls with textured coating in porch	Textured coating	Sample	472686-76								 NAD

Building: Accommodation Hut P1 **Level: 0** **Location: 001/corridor**

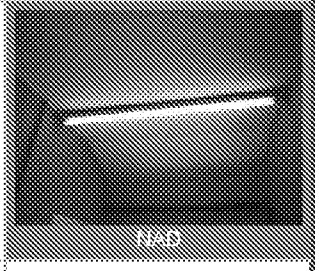
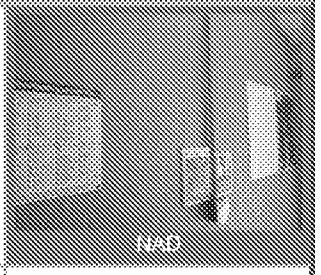

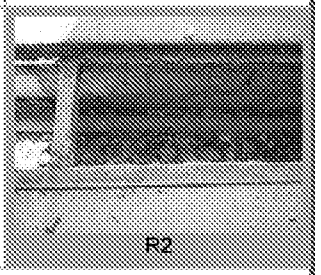
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Sample	472686-22								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 001/corridor**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Sample	472686-23								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Sample	472686-24	21 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Duct covers	Wood										
Floor tiles debris in floor ducts	Asbestos-containing floor tile with bitumen adhesive	Sample	472686-25	0.1 Sqm.	1	3	3	Chrysotile	8	2	 P2
		Present in both ducts									
Insulation in floor ducts	Man made mineral fibre										

Building: Accommodation Hut P1 **Level: 0** **Location: 002/plant room**

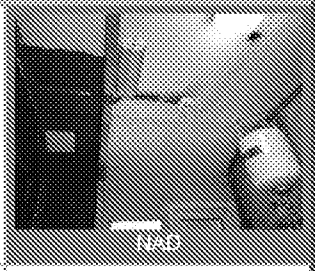
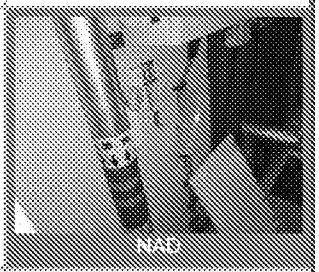
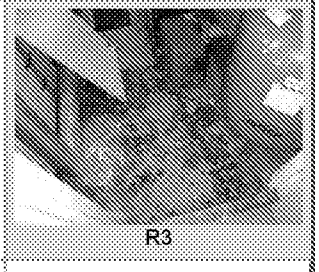
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								 TP&D
Walls	Hardboard and plasterboard										
Wall covering	Textured coating	Cross Reference	472686-23								 N&D
Floor covering	Asbestos-containing bitumen adhesive	Cross Reference	472686-24	4 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Insulation in floor ducts	Man made mineral fibre										
Pipework	Metal										
Pipework insulation	Metal and man made mineral fibre										
Electrics	Modern										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 002/plant room**





Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Boiler	Modern										
Gasket to boiler	Gasket	Sample	472686-26								 NAD
Panels around vents	Insulating board	Sample	472686-27								 NAD
Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Sample	472686-28	0.5 Sqm.	1	1	0	Chrysotile	3	3	 R3

table continued from previous page...



Building: Accommodation Hut P1 **Level: 0** **Location: 002/plant room**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Blanking panel debris in duct	Insulating board	Sample	472686-29								 NAD
Blanking panel	Insulating board	Sample	472686-30								 NAD

Building: Accommodation Hut P1 **Level: 0** **Location: 003/cupboard**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Wood										
Walls	Wood and hardboard										
Floor covering	Ceramics										
Floor	Concrete										
Door and frame	Wood										

Building: Accommodation Hut P1 **Level: 0** **Location: 004/bathroom**

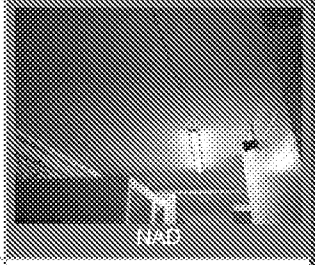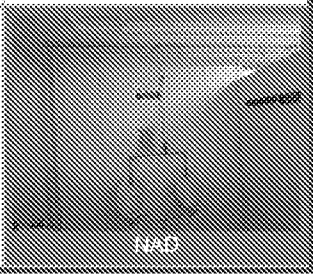Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								
Walls	Wood and plastic										
Floor covering	Ceramics										
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Toilet cisterns	Ceramics										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-31								

Building: Accommodation Hut P1 **Level: 0** **Location: 005/kitchen**

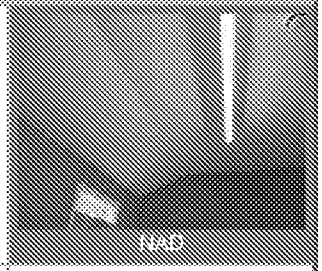
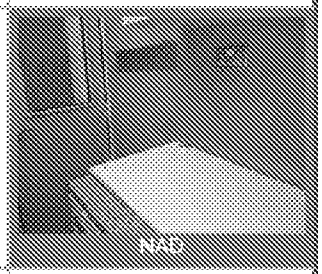
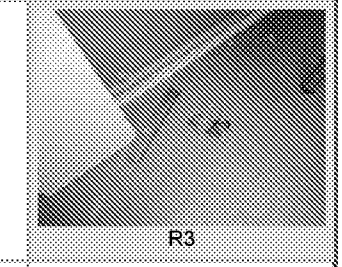
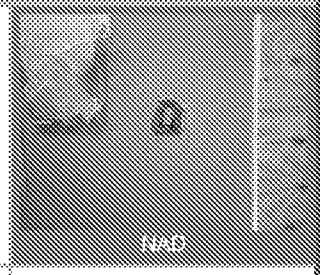

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-23								
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-24	6 Sqm.	1	1	0	Chrysotile	3	2	
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 005/kitchen**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable (y/n)	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Sample	472686-31								
Sink pad	Modern										
Water heater	Modern										

Building: Accommodation Hut P1 **Level: 0** **Location: 006/bedroom**


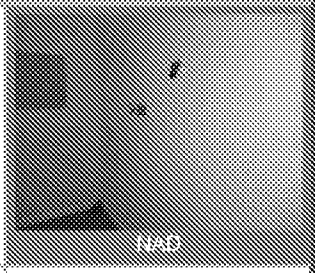

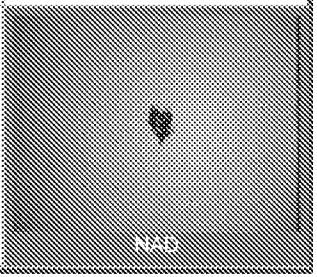
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable (y/n)	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 006/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friability Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-23								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-24	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-31								 NAD

Building: Accommodation Hut P1 **Level: 0** **Location: 007/bedroom**

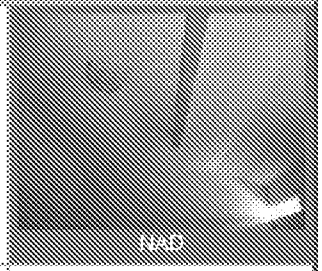
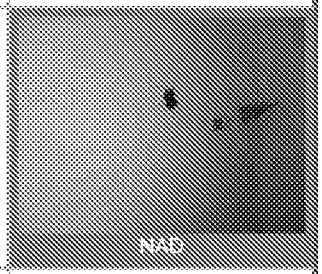
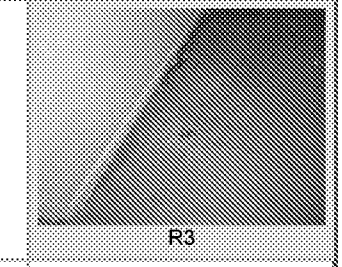

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-23								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-24	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 007/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-31								 NAD

Building: Accommodation Hut P1 **Level: 0** **Location: 008/bedroom**

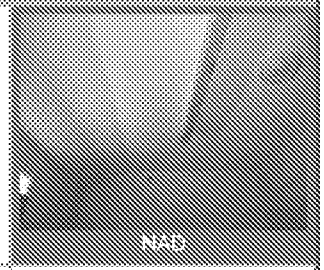
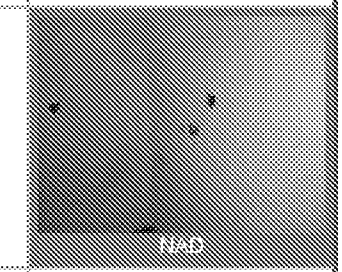


Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-23								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 008/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-24	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-31								 N4D

Building: Accommodation Hut P1 **Level: 0** **Location: 009/bedroom**

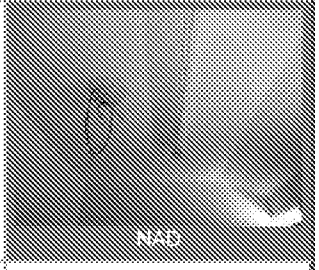
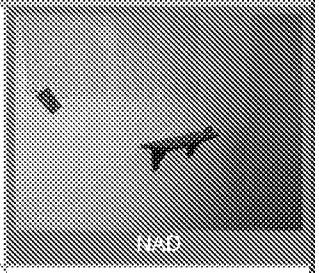

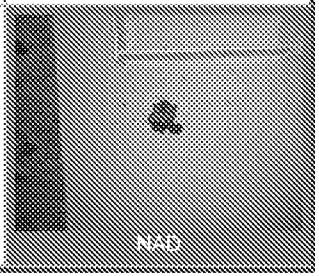
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								 N4D
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 009/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-23								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-24	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-31								 NAD

Building: Accommodation Hut P1 **Level: 0** **Location: 010/bedroom**

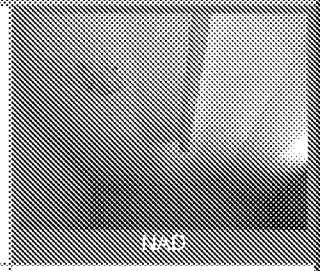
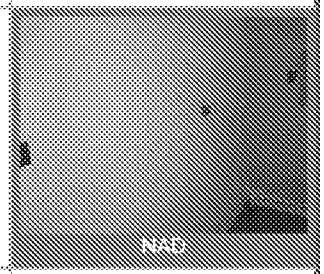

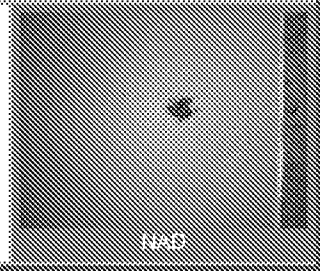
Item / Product / Component	Additional Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-23								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-24	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 010/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-31								 NAD

Building: Accommodation Hut P1 **Level: 0** **Location: 011/bedroom**


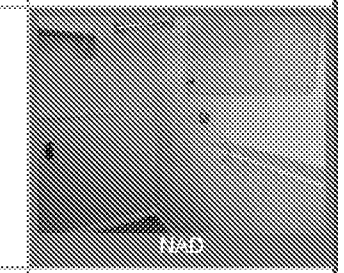

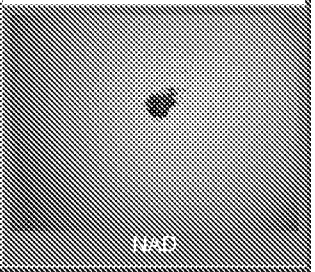
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-23								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 011/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-24	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-31								 N/AS

Building: Accommodation Hut P1 **Level: 0** **Location: 012/bedroom**

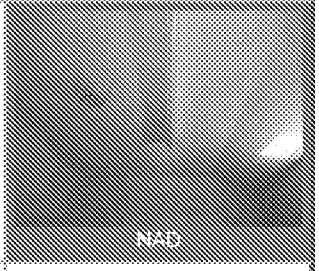
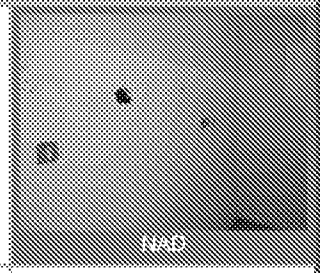

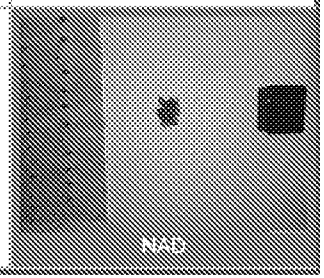
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								 N/AS
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 012/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-23								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-24	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-31								 NAD

Building: Accommodation Hut P1 **Level: 0** **Location: 013/bedroom**

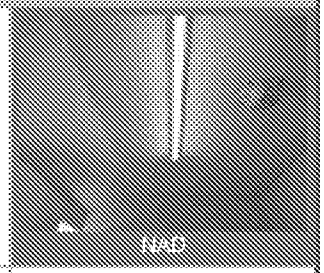

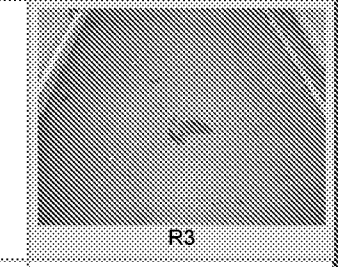

Item / Product / Component	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-22								
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-23								
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-24	6 Sqm.	1	1	0	Chrysotile	3	2	
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 013/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-31								 NAD

Building: Accommodation Hut P1 **Level: 1** **Location: 001/loft space**



Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipe insulation	Man made mineral fibre										
Insulation	Man made mineral fibre										
Slaters felt	Bituminous product	Sample	472686-32								 NAD

Building: Accommodation Hut P1 **Level: 9** **Location: 999/externals**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof tiles	Metal										
Facia	Wood and plastic										
Walls	Plastic										
Rainwater goods	Plastic										

table continued from previous page...

Building: Accommodation Hut P1 **Level: 0** **Location: 999/externals**

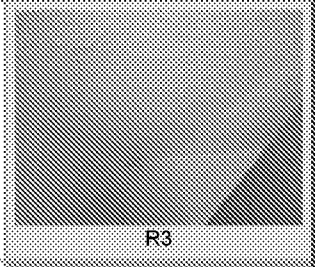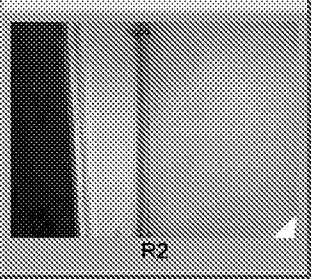Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling panels with textured coating in porch	Asbestos-containing insulating board	Sample	472686-33	2 Sqm.	2	1	1	Chrysotile	5	2	
Wall panels with textured coating in porch	Asbestos-containing insulating board	Sample	472686-34	6 Sqm.	2	1	1	Chrysotile	5	3	

Building: Accommodation Hut P2 **Level: 0** **Location: 001/corridor**

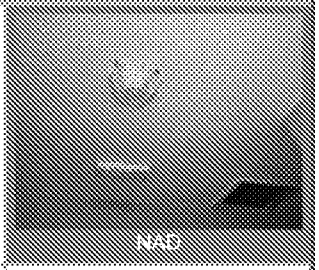
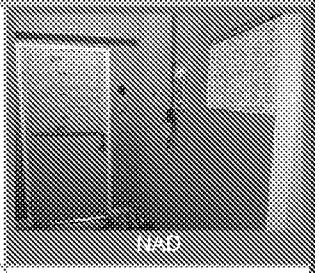

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Sample	472686-35								
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut P2 Level: 0 Location: 001/corridor

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Sample	472686-36								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Sample	472686-37	21 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Duct covers	Wood										

Building: Accommodation Hut P2 Level: 0 Location: 002/plant room

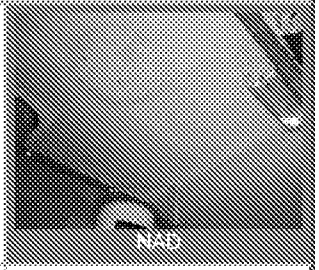
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								 NAD
Walls	Hardboard and plasterboard										

table continued from previous page...

Building: Accommodation Hut P2 **Level: 0** **Location: 002/plant room**




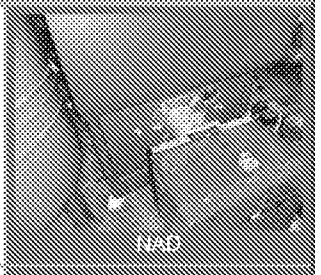
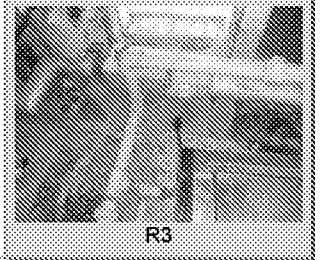
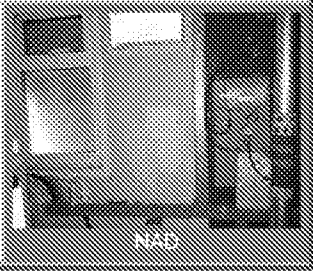
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-36								 NAD
Floor covering	Asbestos-containing bitumen adhesive	Cross Reference	472686-37	4 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Insulation in floor ducts	Man made mineral fibre										
Pipework	Metal										
Pipework insulation	Metal and man made mineral fibre										
Electrics	Modern										
Boiler	Modern										

table continued from previous page...



Building: Accommodation Hut P2 **Level: 0** **Location: 002/plant room**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos	Material Score	Accessibility Score	Risk Level Assessment
Gasket to boiler	Gasket	Sample	472686-38								
Panels around vents	Insulating board	Sample	472686-39								
Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Sample	472686-40	0.5 Sqm.	1	1	0	Chrysotile	3	3	
Blanking panel	Insulating board	Sample	472686-41								

Building: Accommodation Hut P2 **Level: 0** **Location: 003/cupboard**

Item / Product / Element	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friability	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Wood										
Walls	Wood and hardboard										
Floor	Concrete										
Door and frame	Wood										

Building: Accommodation Hut P2 **Level: 0** **Location: 004/bathroom**

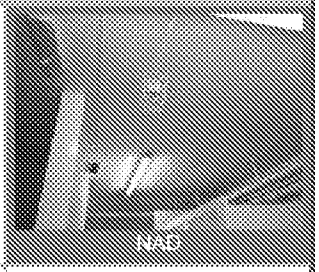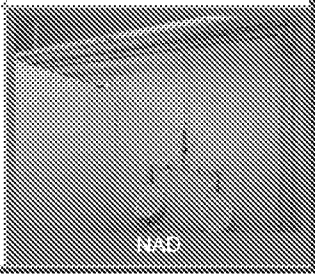Item / Product / Element	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friability	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								
Walls	Wood and plastic										
Floor covering	Ceramics										
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Toilet cisterns	Ceramics										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-42								

Building: Accommodation Hut P2 **Level: 0** **Location: 005/kitchen**

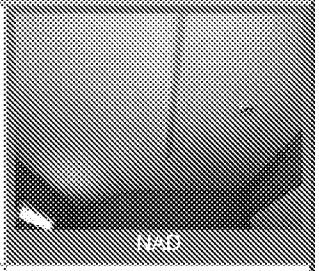
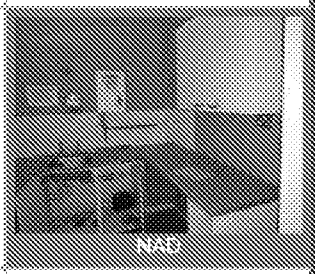
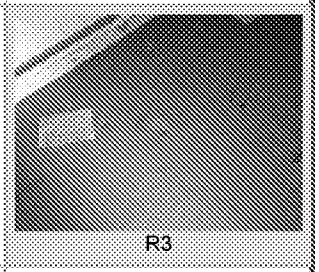
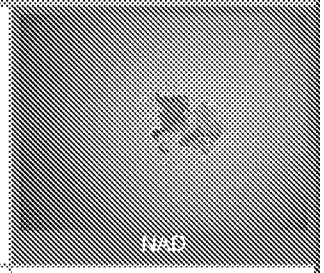
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-36								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-37	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frames	Wood										
Packers to door frames	Wood, card and hardboard										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut P2 **Level: 0** **Location: 005/kitchen**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Sample	472686-42								 NAD
Sink pad	Modern										
Water heater	Modern										

Building: Accommodation Hut P2 **Level: 0** **Location: 006/bedroom**

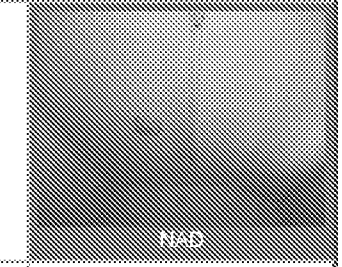
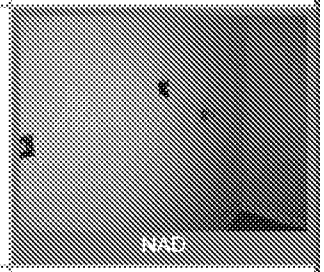

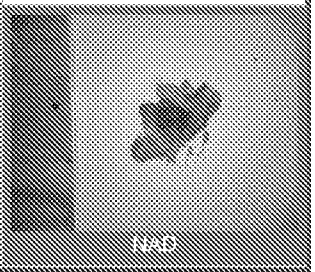
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-36								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut P2 **Level: 0** **Location: 006/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-37	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-42								 NAD

Building: Accommodation Hut P2 **Level: 0** **Location: 007/bedroom**




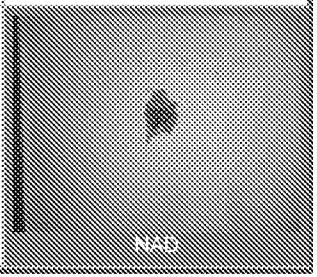
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut P2				Level: 0		Location: 007/bedroom					
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-36								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-37	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-42								 NAD

Building: Accommodation Hut P2 Level: 0 Location: 008/bedroom

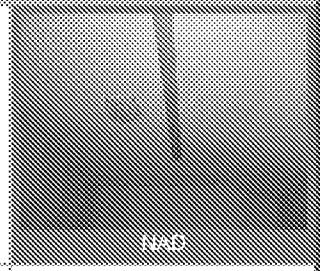
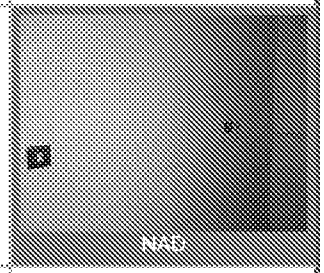
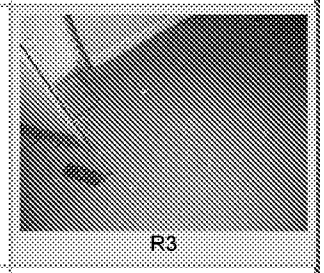
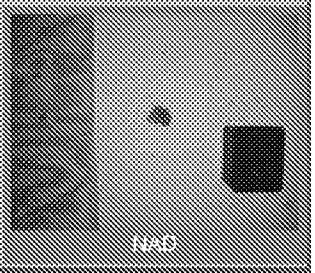
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-36								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-37	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut P2 **Level: 0** **Location: 008/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-42								 NAD

Building: Accommodation Hut P2 **Level: 0** **Location: 009/bedroom**

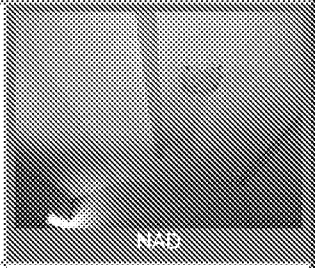
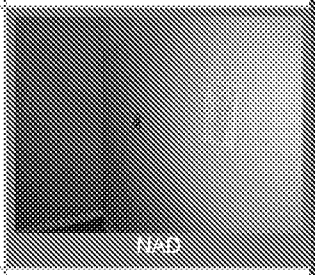

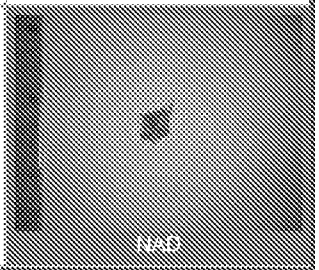
Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-36								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut P2 **Level: 0** **Location: 009/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-37	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-42								 NAD

Building: Accommodation Hut P2 **Level: 0** **Location: 010/bedroom**

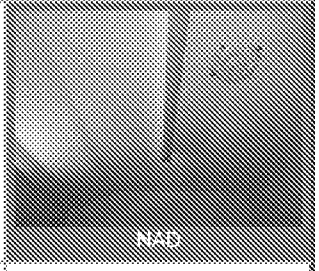
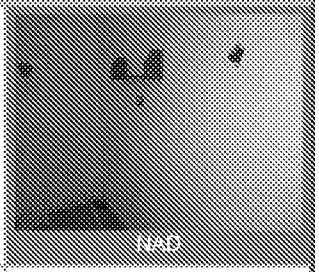

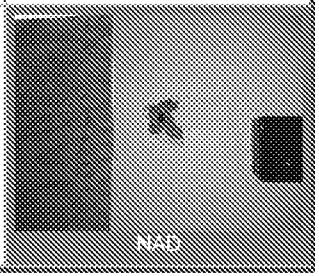
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								 NAD
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut P2 **Level: 0** **Location: 010/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-36								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-37	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-42								 NAD

Building: Accommodation Hut P2 **Level: 0** **Location: 011/bedroom**

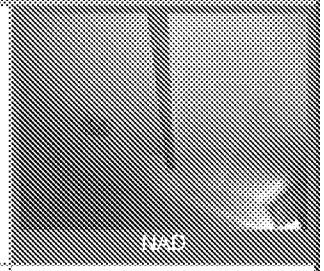
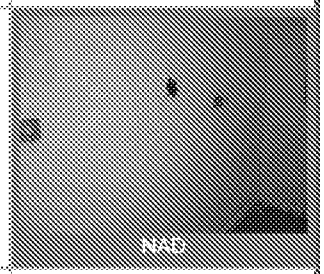

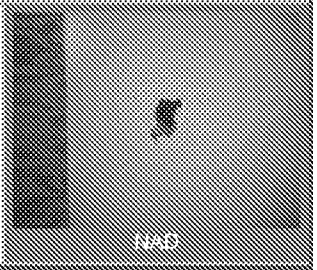
Item / Product Examined	Additional Description	Sampling Strategy	Sample No	Extent	Friable Score	Material Condition	Surface Treatment	Material	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-36								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-37	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										

table continued from previous page...

Building: Accommodation Hut P2 **Level: 0** **Location: 011/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-42								 NAD

Building: Accommodation Hut P2 **Level: 0** **Location: 012/bedroom**

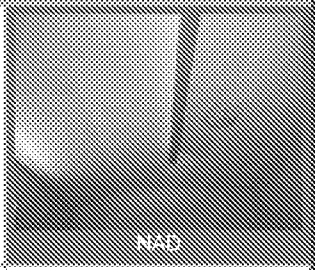
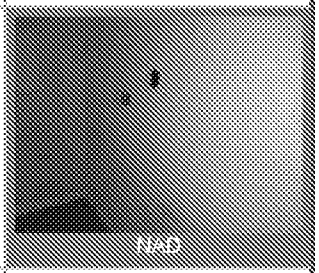


Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								 NAD
Walls	Hardboard										
Wall covering	Textured coating	Cross Reference	472686-36								 NAD
Floor covering	Modern linoleum										

table continued from previous page...

Building: Accommodation Hut P2 **Level: 0** **Location: 012/bedroom**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-37	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-42								 N4B

Building: Accommodation Hut P2 **Level: 0** **Location: 013/bedroom**





Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Ceiling	Hardboard with textured coating	Cross Reference	472686-35								 N4B
Walls	Hardboard										

table continued from previous page...

Building: Accommodation Hut P2 Level: 0 Location: 013/bedroom

Item / Product Examined	Material Description	Sampling Strategy	Sample No	Extent	Friability Score	Material Condition	Surface Treatment	Asbestos Type	Material Score	Accessibility Score	Risk Level Assessment
Wall covering	Textured coating	Cross Reference	472686-36								 NAD
Floor covering	Modern linoleum										
Subfloor	Asbestos-containing bitumen adhesive	Cross Reference	472686-37	6 Sqm.	1	1	0	Chrysotile	3	2	 R3
Floor	Concrete										
Door and frame	Wood										
Window frames	PVC and wood										
Radiator and pipework	Metal										
Insulation within cavity walls	Man made mineral fibre										
Lining within cavity to external walls	Bituminous product	Cross Reference	472686-42								 NAD

Building: Accommodation Hut P2 **Level: 1** **Location: 001/loft space**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof	Wood										
Joists and beams	Wood										
Pipework	Metal										
Pipe insulation	Man made mineral fibre										
Insulation	Man made mineral fibre										
Slaters felt	Bituminous product	Sample	472686-43								 N/D

Building: Accommodation Hut P2 **Level: 9** **Location: 999/externals**



Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Friable	Material Score	Accessibility Score	Risk Level Assessment
Roof tiles	Metal										
Facia	Wood and plastic										
Walls	Plastic										
Rainwater goods	Plastic										
Ceiling panels with textured coating in porch	Asbestos-containing insulating board	Sample	472686-44	2 Sqm.	2	1	1	Chrysotile	5	2	 R3

table continued from previous page...

Building: Accommodation Hut P2 **Level: 9** **Location: 999/externals**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Wall panels with textured coating in porch	Asbestos-containing insulating board	Sample	472686-45	6 Sqm.	2	1	1	Chrysotile	5	3	 P2

Building: external ducts for blocks P, G, H, O, I **Level: 9** **Location: 999/externals ducts**

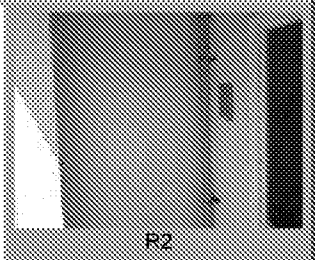

Limited Access: reasons of health and safety Due to services and depth of duct


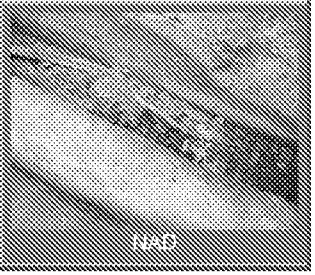
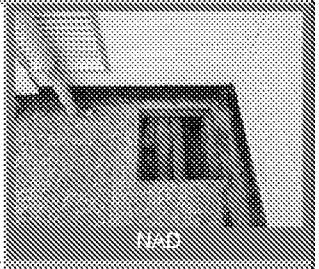
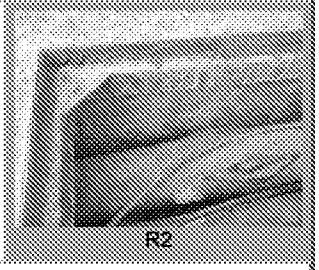
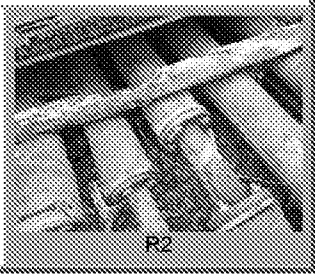
Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Product Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Shuttering through out the ducts	Asbestos-containing cement	Sample	472686-131	200 Sqm.	1	1	1	Chrysotile	4	2	 R3
Panel debris between P1 and P2	Insulating board	Sample	472686-132								 NAD

table continued from previous page...

Building: external ducts for blocks P, G, H, O, I **Level: 9** **Location: 999/externals ducts**

Item / Product Examined	Material Description	Sampling Strategy	Sample No.	Extent	Friable Score	Material Condition	Surface Treatment	Fibre Id.	Material Score	Accessibility Score	Risk Level Assessment
Pipework insulation through out all ducts	Insulation	Sample	472686-133								
Cement debris in ducts	Asbestos-containing cement	Sample	472686-134	1 Sqm.	1	3	3	Chrysotile	8	2	
		Presumed to be through out all ducts									
Pipework flange gasket through out the ducts	Asbestos-containing gasket	Sample	472686-135	200 + - No.	2	2	2	Chrysotile	7	2	

Annotated Plans and Other Additional Documents

The following documents accompany this report and should be regarded as an integral part of this report.

They can be downloaded from https://web.lucion.co.uk/reports/472686/attachments.

- Method Statement [https://web.lucion.co.uk/print/method_statements/472686?s=0d95aca851a2910794a0f49decfb0f55]
- Risk Assessment [https://web.lucion.co.uk/print/risk_assessment/472686?s=50352838bf9b4282a58aff3bcf395f1a]
- A4-Plan_472686_HMP-Ford.pdf

Additional Advice and Information

As the reader of this report you are recommended to make sure that it meets with your requirements. Publication HSG 264 Asbestos: The survey guide suggests the following:

- Check your report against our quotation or your tender
- Check for any caveats or disclaimers you are unsure of
- Check that the survey is as you requested
- Check you understand the included plans
- Check that we have accessed all the areas and rooms you wanted us to

Lucion Environmental Ltd
Registered in England + Wales 6495874
VAT Registration Number 208156326

Asbestos Fibre Identification Material Test Certificate

Job Ref No: **472686**, Account Ref No: **21795**, Contract Ref No: **66629**

This certificate is for the attention of	**Terence Coston** **Gov Facility Services Limited (GFSL)** Accero 3, Concourse Way Sheaf Street Sheffield S1 2BJ United Kingdom
Site Address	HMP Ford, Ford Road, Arundel, West Sussex, BN18 0BX
Sampled Buildings	Accommodation Hut G1, Accommodation Hut G2, Accommodation Hut H1, Accommodation Hut H2, Accommodation Hut I1, Accommodation Hut I2, Accommodation Hut O1, Accommodation Hut O2, Accommodation Hut P1, Accommodation Hut P2, external ducts for blocks P, G, H, O, I
Analyst(s)	Sarah Bell, Michaela White, Mark Davison, Kelly Harrison, Jennifer Hardy, Jennifer Gibson, Jarek Galik, Jake Scott
[redacted]	
Approved signatory	Joel Walker
[redacted]	
Approval date	Monday, 21st June, 2021
Report Rendered on	Mon 21 Jun 2021 @ 15:16:09

Analysis method - In-house method TOP01.03 in accordance with HSG 248 - Asbestos: The Analysts' Guide For Sampling, Analysis and Clearance Procedures H.S.E. 2005.

Lucion bear no responsibility for sample collection or sample description related information provided by the client.

Where Lucion Environmental Ltd has not undertaken sampling; any prior sampling activity is beyond the company's responsibility. Where Lucion Environmental Ltd has sampled the test material, this has been done in accordance with in-house method TOP01.02. Any opinions and interpretations expressed herein are outside the scope of UKAS accreditation.

The results quoted in this report relate to:

1. Samples analysed in accordance with methods described above
2. Samples analysed and not necessarily to the material from which the samples were taken
3. The time during which sampling took place and to the conditions prevailing during that time

The samples referred to in this report will be retained for 6 months unless requested otherwise.

Total Samples	No Asbestos Detected	Asbestos-Containing Samples	Presumed Asbestos Items
135	88	47	0

Head Office
7 Halifax Court, Dunston,
Gateshead, NE11 9JT
E: *enquiries@lucionservices.com*
T: *0345 5040 303*

UKAS TESTING
2569

ARUN DISTRICT COUNCIL P/26/21/DEM

Fibre Identification Analysis Results

Sample No.	Analysis Date	Building	Level	Location	Item / Product Examined	Material Description	Analyst Comments	Fibre Identification
472686-1	2021-06-16	Accommodation Hut G1	0	001/ corridor	Ceiling	Hardboard with textured coating		NAD
472686-2	2021-06-16	Accommodation Hut G1	0	001/ corridor	Wall covering	Textured coating		NAD
472686-3	2021-06-16	Accommodation Hut G1	0	001/ corridor	Subfloor	Asbestos-containing bitumen adhesive		Chrysotile
472686-4	2021-06-16	Accommodation Hut G1	0	001/ corridor	Door header panels	Insulating board		NAD
472686-5	2021-06-16	Accommodation Hut G1	0	002/ bedroom	Lining within cavity to external walls	Bituminous product		NAD
472686-6	2021-06-16	Accommodation Hut G1	0	002/ bedroom	Insulation within cavity walls	Man made mineral fibre		NAD
472686-7	2021-06-16	Accommodation Hut G1	0	014/ electrical cupboard	Pipework insulation in floor duct	Insulation		NAD
472686-8	2021-06-16	Accommodation Hut G1	1	001/loft space	Slaters felt	Asbestos-containing bituminous product		Chrysotile
472686-9	2021-06-16	Accommodation Hut G1	0	015/ boiler room	Gasket to boiler	Gasket		NAD
472686-10	2021-06-16	Accommodation Hut G1	9	999/ externals	Ceiling panels with textured coating in porch	Asbestos-containing insulating board		Amosite, Chrysotile
472686-11	2021-06-16	Accommodation Hut G1	9	999/ externals	Wall panels with textured coating in porch	Asbestos-containing insulating board		Amosite, Chrysotile
472686-12	2021-06-16	Accommodation Hut G2	0	001/ corridor	Ceiling	Hardboard with textured coating		NAD
472686-13	2021-06-16	Accommodation Hut G2	0	001/ corridor	Wall covering	Textured coating		NAD
472686-14	2021-06-16	Accommodation Hut G2	0	001/ corridor	Subfloor	Asbestos-containing bitumen adhesive		Chrysotile
472686-15	2021-06-16	Accommodation Hut G2	0	001/ corridor	Floor tiles debris in floor ducts	Floor tile with bitumen adhesive		NAD
472686-16	2021-06-16	Accommodation Hut G2	0	001/ corridor	Door header panels	Insulating board		NAD
472686-17	2021-06-16	Accommodation Hut G2	0	002/plant room	Gasket to boiler	Gasket		NAD
472686-18	2021-06-16	Accommodation Hut G2	0	002/plant room	Panels around vents	Insulating board		NAD
472686-19	2021-06-16	Accommodation Hut G2	0	005/ kitchen	Lining within cavity to external walls	Bituminous product		NAD
472686-20	2021-06-16	Accommodation Hut G2	9	999/ externals	Ceiling panels with textured coating in porch	Textured coating		NAD
472686-21	2021-06-16	Accommodation Hut G2	9	999/ externals	Wall panels with textured coating in porch	Textured coating		NAD
472686-22	2021-06-16	Accommodation Hut P1	0	001/ corridor	Ceiling	Hardboard with textured coating		NAD

table continued from previous page...

Sample No	Analysis Date	Building	Level	Location	Item / Product Examined	Material Description	Analyst Comments	Fibre Identification
472686-23	2021-06-16	Accommodation Hut P1	0	001/ corridor	Wall covering	Textured coating		NAD
472686-24	2021-06-16	Accommodation Hut P1	0	001/ corridor	Subfloor	Asbestos-containing bitumen adhesive		Chrysotile
472686-25	2021-06-16	Accommodation Hut P1	0	001/ corridor	Floor tiles debris in floor ducts	Asbestos-containing floor tile with bitumen adhesive	positive in both elements	Chrysotile
472686-26	2021-06-16	Accommodation Hut P1	0	002/plant room	Gasket to boiler	Gasket		NAD
472686-27	2021-06-16	Accommodation Hut P1	0	002/plant room	Panels around vents	Insulating board		NAD
472686-28	2021-06-16	Accommodation Hut P1	0	002/plant room	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	positive in both elements	Chrysotile
472686-29	2021-06-16	Accommodation Hut P1	0	002/plant room	Blanking panel debris in duct	Insulating board		NAD
472686-30	2021-06-16	Accommodation Hut P1	0	002/plant room	Blanking panel	Insulating board		NAD
472686-31	2021-06-16	Accommodation Hut P1	0	005/ kitchen	Lining within cavity to external walls	Bituminous product		NAD
472686-32	2021-06-15	Accommodation Hut P1	1	001/loft space	Slaters felt	Bituminous product		NAD
472686-33	2021-06-15	Accommodation Hut P1	9	999/ externals	Ceiling panels with textured coating in porch	Asbestos-containing insulating board		Chrysotile
472686-34	2021-06-15	Accommodation Hut P1	9	999/ externals	Wall panels with textured coating in porch	Asbestos-containing insulating board		Chrysotile
472686-35	2021-06-15	Accommodation Hut P2	0	001/ corridor	Ceiling	Hardboard with textured coating		NAD
472686-36	2021-06-15	Accommodation Hut P2	0	001/ corridor	Wall covering	Textured coating		NAD
472686-37	2021-06-15	Accommodation Hut P2	0	001/ corridor	Subfloor	Asbestos-containing bitumen adhesive		Chrysotile
472686-38	2021-06-15	Accommodation Hut P2	0	002/plant room	Gasket to boiler	Gasket		NAD
472686-39	2021-06-15	Accommodation Hut P2	0	002/plant room	Panels around vents	Insulating board		NAD
472686-40	2021-06-15	Accommodation Hut P2	0	002/plant room	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Both tile and bitumen positive	Chrysotile
472686-41	2021-06-15	Accommodation Hut P2	0	002/plant room	Blanking panel	Insulating board		NAD
472686-42	2021-06-15	Accommodation Hut P2	0	005/ kitchen	Lining within cavity to external walls	Bituminous product		NAD
472686-43	2021-06-15	Accommodation Hut P2	1	001/loft space	Slaters felt	Bituminous product		NAD
472686-44	2021-06-15	Accommodation Hut P2	9	999/ externals	Ceiling panels with textured coating in porch	Asbestos-containing insulating board		Chrysotile

table continued from previous page...

Sample No	Analysis Date	Building	Level	Location	Item / Product Examined	Material Description	Analyst Comments	Fibre Identification
472686-45	2021-06-15	Accommodation Hut P2	9	999/ externals	Wall panels with textured coating in porch	Asbestos-containing insulating board		Chrysotile
472686-46	2021-06-15	Accommodation Hut O1	0	001/ corridor	Ceiling	Hardboard with textured coating		NAD
472686-47	2021-06-15	Accommodation Hut O1	0	001/ corridor	Wall covering	Textured coating		NAD
472686-48	2021-06-15	Accommodation Hut O1	0	001/ corridor	Subfloor	Asbestos-containing bitumen adhesive		Chrysotile
472686-49	2021-06-15	Accommodation Hut O1	0	001/ corridor	Lining within cavity to external walls	Bituminous product		NAD
472686-50	2021-06-15	Accommodation Hut O1	0	001/ corridor	Felt debris in floor ducts	Asbestos-containing bituminous product		Chrysotile
472686-51	2021-06-15	Accommodation Hut O1	0	002/plant room	Cement lining to walls & ceiling	Asbestos-containing cement panels with textured coating		Chrysotile
472686-52	2021-06-15	Accommodation Hut O1	0	002/plant room	Floor tiles & adhesive	Asbestos-containing cement panels with textured coating		Chrysotile
472686-53	2021-06-15	Accommodation Hut O1	0	002/plant room	Gasket to boiler	Gasket		NAD
472686-54	2021-06-15	Accommodation Hut O1	0	002/plant room	Panels around vents	Insulating board		NAD
472686-55	2021-06-15	Accommodation Hut O1	0	002/plant room	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Both tile and bitumen positive	Chrysotile
472686-56	2021-06-15	Accommodation Hut O1	0	004/ bathroom	Floor covering	Screed		NAD
472686-57	2021-06-15	Accommodation Hut O1	0	005/ kitchen	Sink pad	Bituminous product		NAD
472686-58	2021-06-15	Accommodation Hut O1	1	001/loft space	Cement floor to boiler room below	Asbestos-containing cement		Chrysotile
472686-59	2021-06-15	Accommodation Hut O1	1	001/loft space	Slaters felt	Bituminous product		NAD
472686-60	2021-06-15	Accommodation Hut O1	9	999/ externals	Hardboard panels to ceiling with textured coating in porch	Textured coating		NAD
472686-61	2021-06-15	Accommodation Hut O1	9	999/ externals	Hardboard panels to walls with textured coating in porch	Textured coating		NAD
472686-62	2021-06-17	Accommodation Hut O2	0	001/ corridor	Ceiling	Hardboard with textured coating		NAD
472686-63	2021-06-17	Accommodation Hut O2	0	001/ corridor	Wall covering	Textured coating		NAD
472686-64	2021-06-17	Accommodation Hut O2	0	001/ corridor	Subfloor	Asbestos-containing bitumen adhesive		Chrysotile
472686-65	2021-06-17	Accommodation Hut O2	0	001/ corridor	Lining within cavity to external walls	Bituminous product		NAD

table continued from previous page...

Sample No	Analysis Date	Building	Level	Location	Item / Product Examined	Material Description	Analyst Comments	Fibre Identification
472686-66	2021-06-17	Accommodation Hut O2	0	002/plant room	Ceiling	Asbestos-containing cement panels with textured coating		Chrysotile
472686-67	2021-06-17	Accommodation Hut O2	0	002/plant room	Walls	Asbestos-containing cement panels with textured coating		Chrysotile
472686-68	2021-06-17	Accommodation Hut O2	0	002/plant room	Gasket to boiler	Gasket		NAD
472686-69	2021-06-17	Accommodation Hut O2	0	002/plant room	Panels around vents	Insulating board		NAD
472686-70	2021-06-17	Accommodation Hut O2	0	002/plant room	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive		Chrysotile
472686-71	2021-06-17	Accommodation Hut O2	0	004/ bathroom	Floor covering	Screed		NAD
472686-72	2021-06-17	Accommodation Hut O2	0	005/ kitchen	Sink pad	Bituminous product		NAD
472686-73	2021-06-17	Accommodation Hut O2	1	001/loft space	Cement floor to boiler room below	Asbestos-containing cement		Chrysotile
472686-74	2021-06-17	Accommodation Hut O2	1	001/loft space	Slaters felt	Bituminous product		NAD
472686-75	2021-06-17	Accommodation Hut O2	9	999/ externals	Hardboard panels to ceiling with textured coating in porch	Textured coating		NAD
472686-76	2021-06-17	Accommodation Hut O2	9	999/ externals	Hardboard panels to walls with textured coating in porch	Textured coating		NAD
472686-77	2021-06-17	Accommodation Hut H1	0	001/ corridor	Ceiling	Hardboard with textured coating		NAD
472686-78	2021-06-17	Accommodation Hut H1	0	001/ corridor	Wall covering	Textured coating		NAD
472686-79	2021-06-17	Accommodation Hut H1	0	001/ corridor	Subfloor	Asbestos-containing bitumen adhesive		Chrysotile
472686-80	2021-06-17	Accommodation Hut H1	0	001/ corridor	Lining within cavity to external walls	Bituminous product		NAD
472686-81	2021-06-17	Accommodation Hut H1	0	001/ corridor	Header panels	Insulating board		NAD
472686-82	2021-06-17	Accommodation Hut H1	0	002/plant room	Gasket to boiler	Gasket		NAD
472686-83	2021-06-17	Accommodation Hut H1	0	002/plant room	Panels around vents	Insulating board		NAD
472686-84	2021-06-17	Accommodation Hut H1	0	002/plant room	Lining panels to walls in electrical area	Asbestos-containing cement		Chrysotile
472686-85	2021-06-17	Accommodation Hut H1	0	005/ kitchen	Sink pad	Bituminous product		NAD
472686-86	2021-06-17	Accommodation Hut H1	1	001/loft space	Slaters felt	Asbestos-containing bituminous product		Chrysotile

table continued from previous page...

Sample No	Analysis Date	Building	Level	Location	Item / Product Examined	Material Description	Analyst Comments	Fibre Identification
472686-87	2021-06-17	Accommodation Hut H1	9	999/ externals	Hardboard panels to ceiling with textured coating in porch	Textured coating		NAD
472686-88	2021-06-17	Accommodation Hut H1	9	999/ externals	Hardboard panels to walls with textured coating in porch	Textured coating		NAD
472686-89	2021-06-17	Accommodation Hut H2	0	001/ corridor	Ceiling	Hardboard with textured coating		NAD
472686-90	2021-06-17	Accommodation Hut H2	0	001/ corridor	Wall covering	Textured coating		NAD
472686-91	2021-06-17	Accommodation Hut H2	0	001/ corridor	Subfloor	Asbestos-containing bitumen adhesive		Chrysotile
472686-92	2021-06-17	Accommodation Hut H2	0	002/plant room	Ceiling	Asbestos-containing cement panels with textured coating		Chrysotile
472686-93	2021-06-17	Accommodation Hut H2	0	002/plant room	Walls	Asbestos-containing cement panels with textured coating		Chrysotile
472686-94	2021-06-17	Accommodation Hut H2	0	002/plant room	Gasket to boiler	Gasket		NAD
472686-95	2021-06-17	Accommodation Hut H2	0	002/plant room	Panels around vents	Insulating board		NAD
472686-96	2021-06-17	Accommodation Hut H2	0	002/plant room	Floor covering on duct cover and in electrical area	Asbestos-containing floor tile with bitumen adhesive		Chrysotile
472686-97	2021-06-17	Accommodation Hut H2	0	005/ kitchen	Lining within cavity to external walls	Bituminous product		NAD
472686-98	2021-06-17	Accommodation Hut H2	0	005/ kitchen	Sink pad	Bituminous product		NAD
472686-99	2021-06-17	Accommodation Hut H2	1	001/loft space	Cement floor to boiler room below	Asbestos-containing cement		Chrysotile
472686-100	2021-06-17	Accommodation Hut H2	9	999/ externals	Hardboard panels to ceiling with textured coating in porch	Textured coating		NAD
472686-101	2021-06-17	Accommodation Hut H2	9	999/ externals	Hardboard panels to walls with textured coating in porch	Textured coating		NAD
472686-102	2021-06-17	Accommodation Hut I1	0	001/ corridor	Ceiling	Hardboard with textured coating		NAD
472686-103	2021-06-17	Accommodation Hut I1	0	001/ corridor	Wall covering	Textured coating		NAD
472686-104	2021-06-17	Accommodation Hut I1	0	001/ corridor	Subfloor	Asbestos-containing bitumen adhesive		Chrysotile
472686-105	2021-06-17	Accommodation Hut I1	0	001/ corridor	Header panels	Insulating board		NAD
472686-106	2021-06-17	Accommodation Hut I1	0	001/ corridor	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Tile positive - Bitumen positive	Chrysotile


table continued from previous page...

Sample No	Analysis Date	Building	Level	Location	Item / Product Examined	Material Description	Analyst Comments	Fibre Identification
472686-107	2021-06-17	Accommodation Hut I1	0	001/ corridor	Cement debris in duct	Asbestos-containing cement		Chrysotile
472686-108	2021-06-17	Accommodation Hut I1	0	001/ corridor	Felt debris in floor duct	Bituminous product		NAD
472686-109	2021-06-17	Accommodation Hut I1	0	002/plant room	Floor covering	Asbestos-containing floor tile with bitumen adhesive	Tile positive - Bitumen positive	Chrysotile
472686-110	2021-06-17	Accommodation Hut I1	0	002/plant room	Gasket to boiler	Gasket		NAD
472686-111	2021-06-17	Accommodation Hut I1	0	002/plant room	Panels around vents	Insulating board		NAD
472686-112	2021-06-17	Accommodation Hut I1	0	002/plant room	Lining panels to walls in electrical area	Asbestos-containing cement		Chrysotile
472686-113	2021-06-17	Accommodation Hut I1	0	005/ kitchen	Lining within cavity to external walls	Bituminous product		NAD
472686-114	2021-06-17	Accommodation Hut I1	9	999/ externals	Hardboard panels to ceiling with textured coating in porch	Textured coating		NAD
472686-115	2021-06-17	Accommodation Hut I1	9	999/ externals	Hardboard panels to walls with textured coating in porch	Textured coating		NAD
472686-116	2021-06-17	Accommodation Hut I2	0	001/ corridor	Ceiling	Hardboard with textured coating		NAD
472686-117	2021-06-17	Accommodation Hut I2	0	001/ corridor	Wall covering	Textured coating		NAD
472686-118	2021-06-17	Accommodation Hut I2	0	001/ corridor	Subfloor	Asbestos-containing bitumen adhesive		Chrysotile
472686-119	2021-06-17	Accommodation Hut I2	0	001/ corridor	Header panels	Insulating board		NAD
472686-120	2021-06-17	Accommodation Hut I2	0	001/ corridor	Floor covering on duct cover	Asbestos-containing floor tile with bitumen adhesive	Chrysotile identified in tile and bitumen adhesive, Tile positive - Bitumen positive	Chrysotile
472686-121	2021-06-17	Accommodation Hut I2	0	001/ corridor	Cement debris in duct	Asbestos-containing cement		Chrysotile
472686-122	2021-06-17	Accommodation Hut I2	0	002/plant room	Ceiling	Asbestos-containing cement with textured coating		Chrysotile
472686-123	2021-06-17	Accommodation Hut I2	0	002/plant room	Walls	Asbestos-containing cement with textured coating		Chrysotile
472686-124	2021-06-17	Accommodation Hut I2	0	002/plant room	Gasket to boiler	Gasket		NAD
472686-125	2021-06-17	Accommodation Hut I2	0	002/plant room	Panels around vents	Insulating board		NAD
472686-126	2021-06-17	Accommodation Hut I2	0	005/ kitchen	Lining within cavity to external walls	Bituminous product		NAD
472686-127	2021-06-17	Accommodation Hut I2	0	005/ kitchen	Sink pad	Modern		NAD


table continued from previous page...

Sample No	Analysis Date	Building	Level	Location	Item / Product Examined	Material Description	Analyst Comments	Fibre Identification
472686-128	2021-06-17	Accommodation Hut I2	1	001/loft space	Cement panels to ceiling below	Asbestos-containing cement		Chrysotile
472686-129	2021-06-17	Accommodation Hut I2	9	999/ externals	Hardboard panels to ceiling with textured coating in porch	Textured coating		NAD
472686-130	2021-06-17	Accommodation Hut I2	9	999/ externals	Hardboard panels to walls with textured coating in porch	Textured coating		NAD
472686-131	2021-06-17	external ducts for blocks P, G, H, O, I	9	999/ externals ducts	Shuttering through out the ducts	Asbestos-containing cement		Chrysotile
472686-132	2021-06-17	external ducts for blocks P, G, H, O, I	9	999/ externals ducts	Panel debris between P1 and P2	Insulating board		NAD
472686-133	2021-06-17	external ducts for blocks P, G, H, O, I	9	999/ externals ducts	Pipework insulation through out all ducts	Insulation		NAD
472686-134	2021-06-17	external ducts for blocks P, G, H, O, I	9	999/ externals ducts	Cement debris in ducts	Asbestos-containing cement		Chrysotile
472686-135	2021-06-17	external ducts for blocks P, G, H, O, I	9	999/ externals ducts	Pipework flange gasket through out the ducts	Asbestos-containing gasket		Chrysotile


Annotated Plans A4-Plan_472686_HMP-Ford.pdf

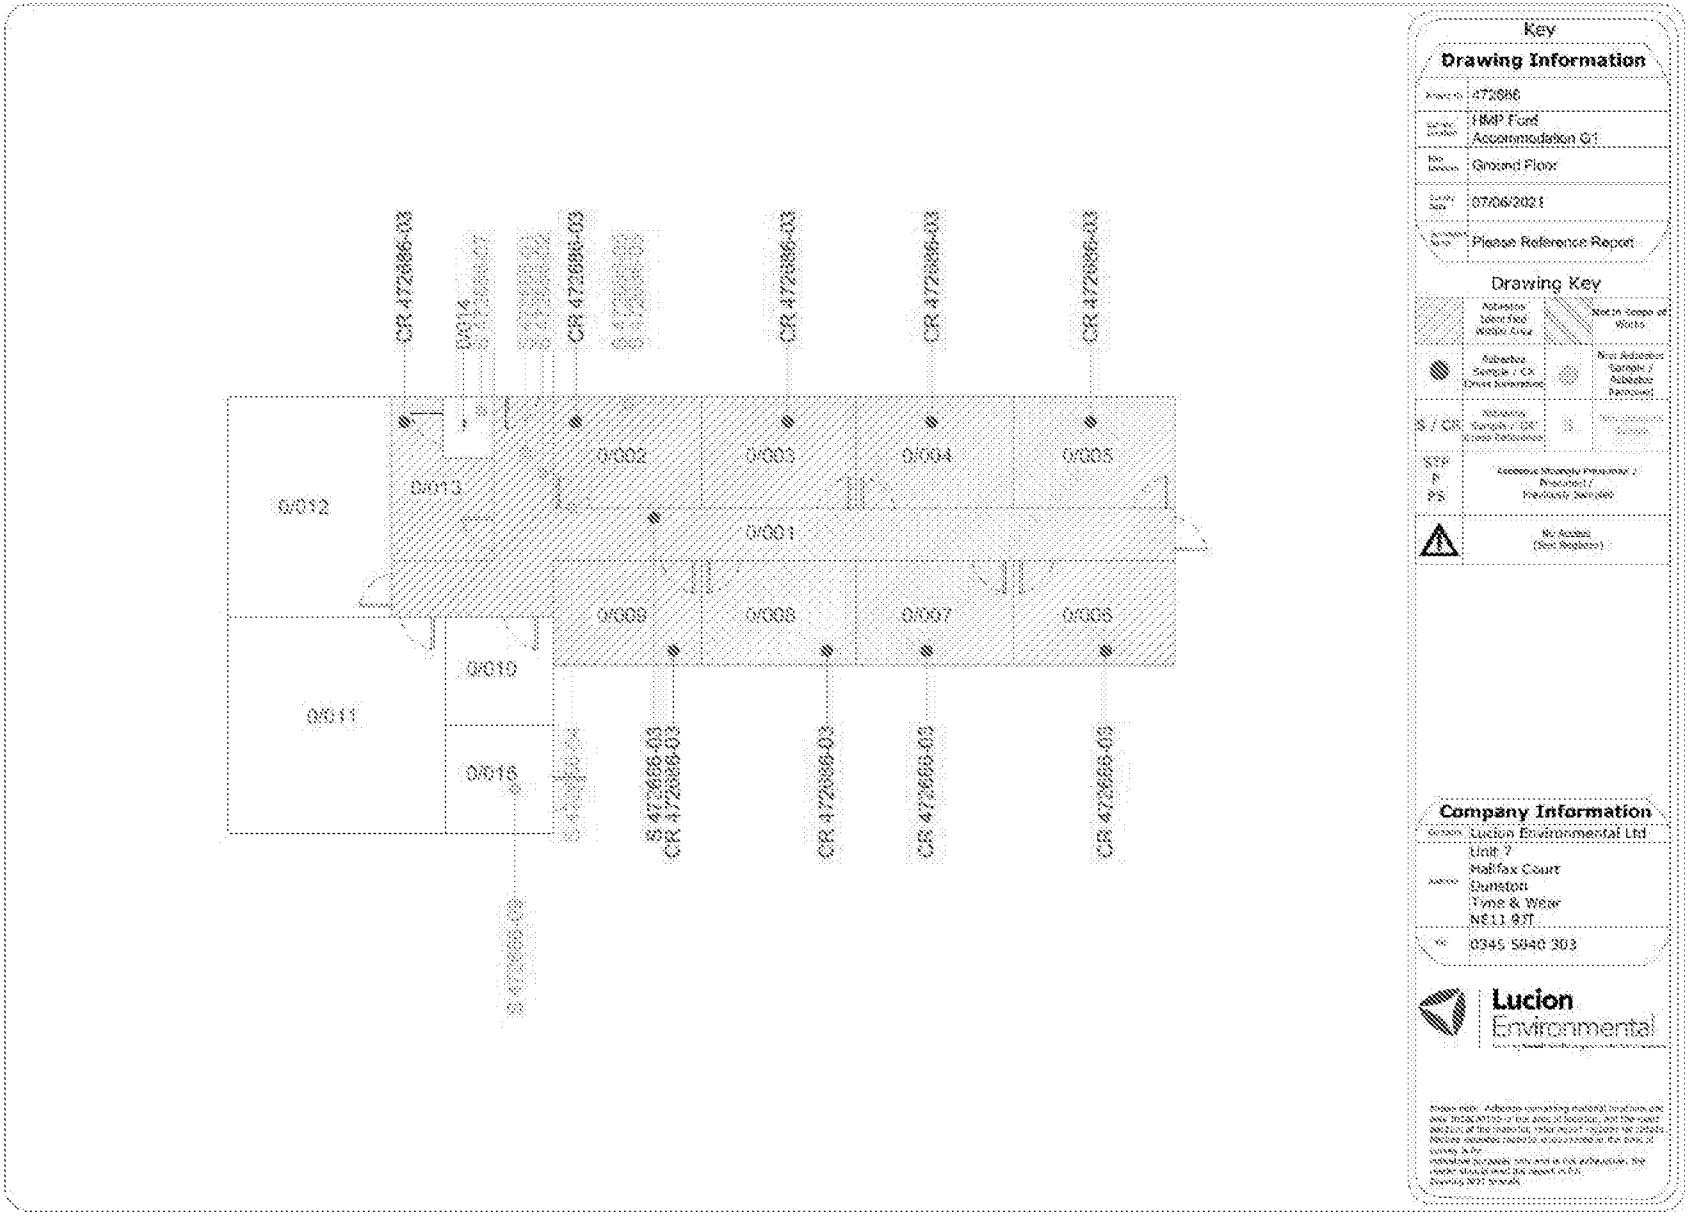


A4-Plan_472686_HMP-Ford.pdf

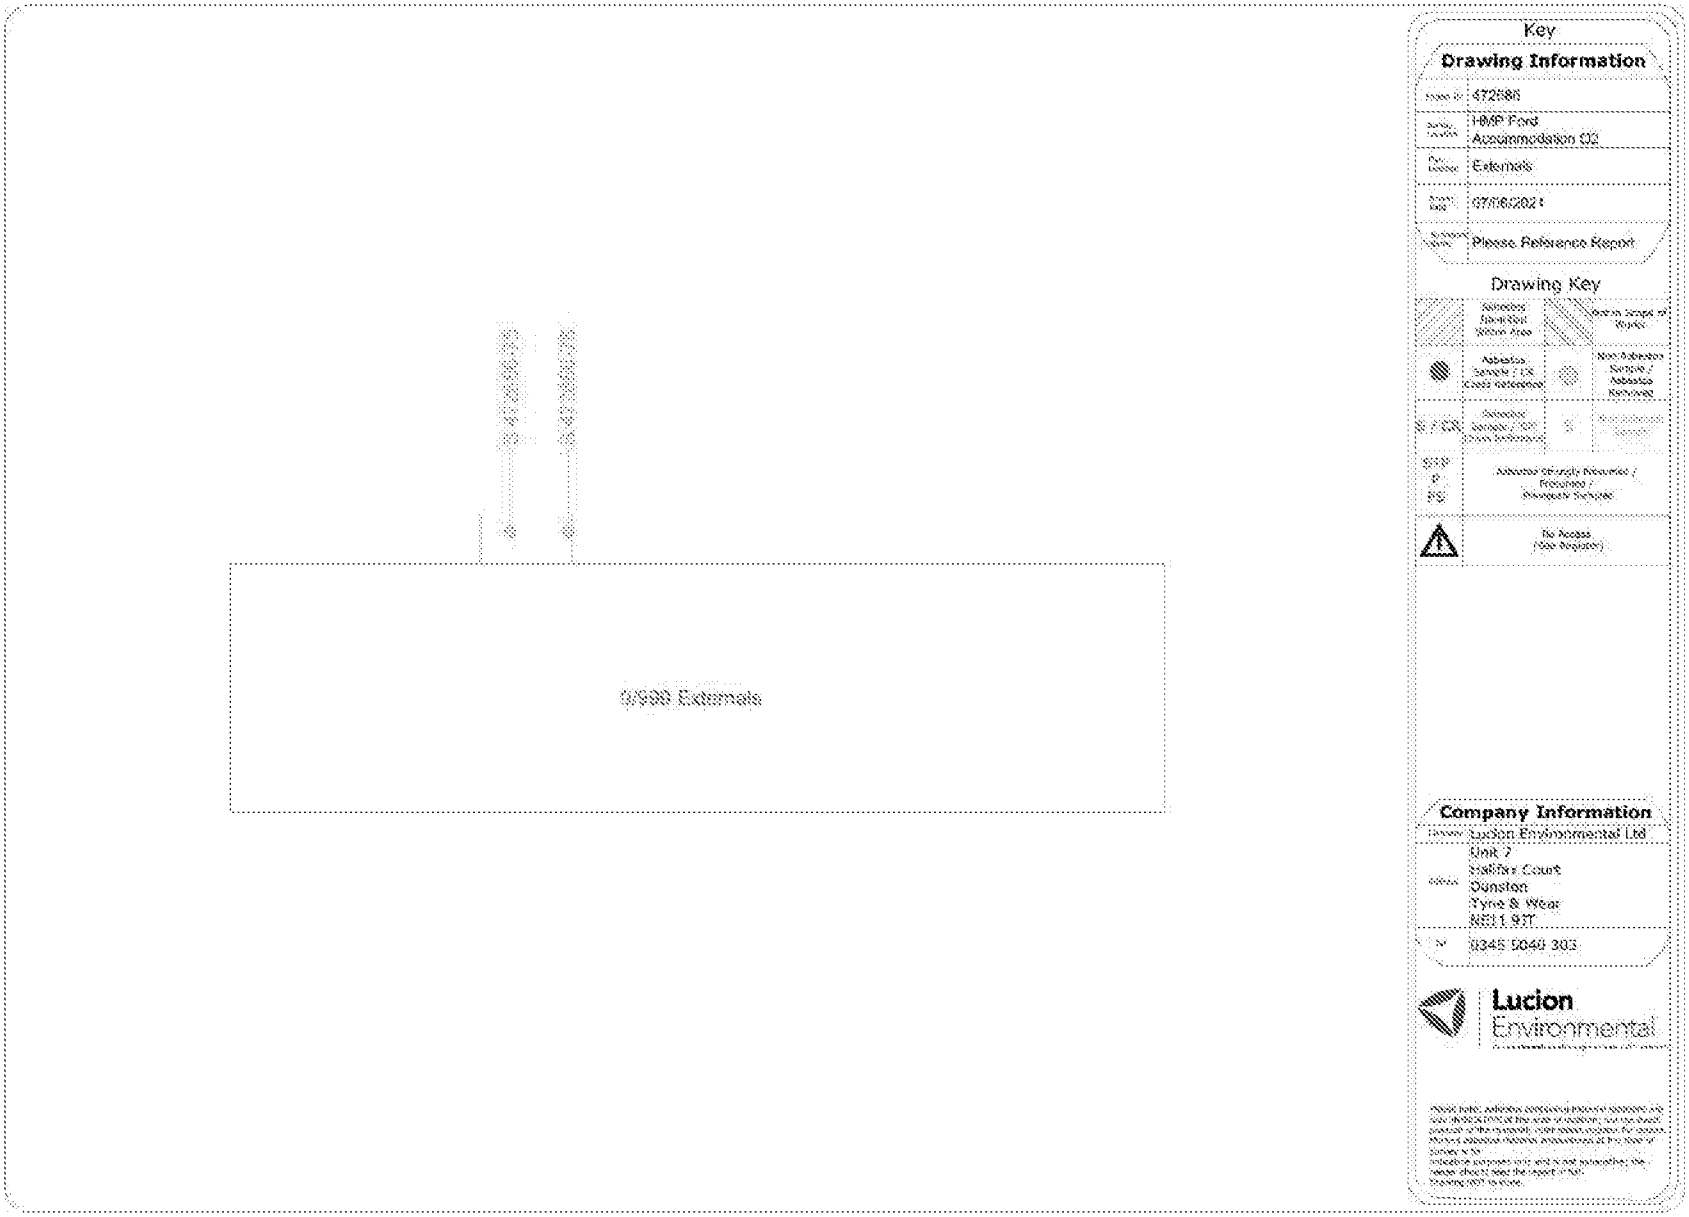


A4-Plan_472686_HMP-Ford.pdf

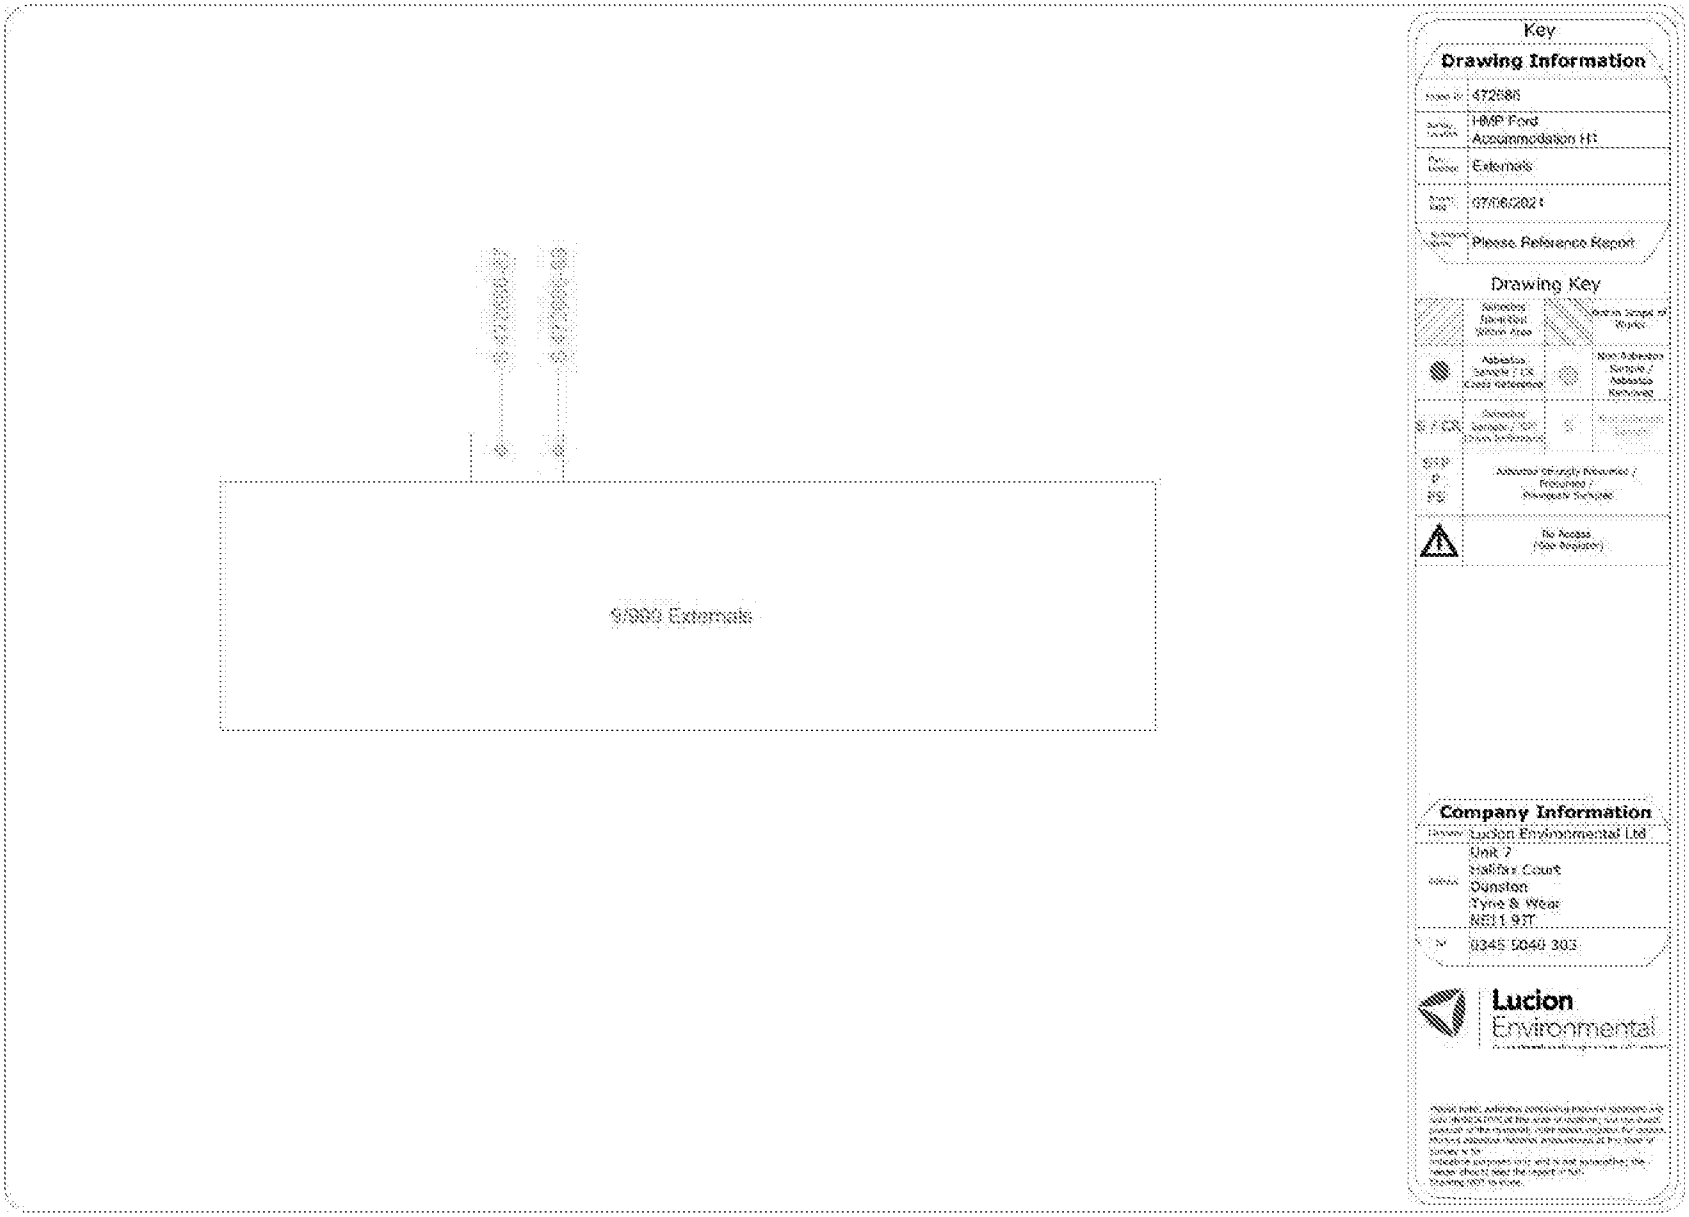


A4-Plan_472686_HMP-Ford.pdf

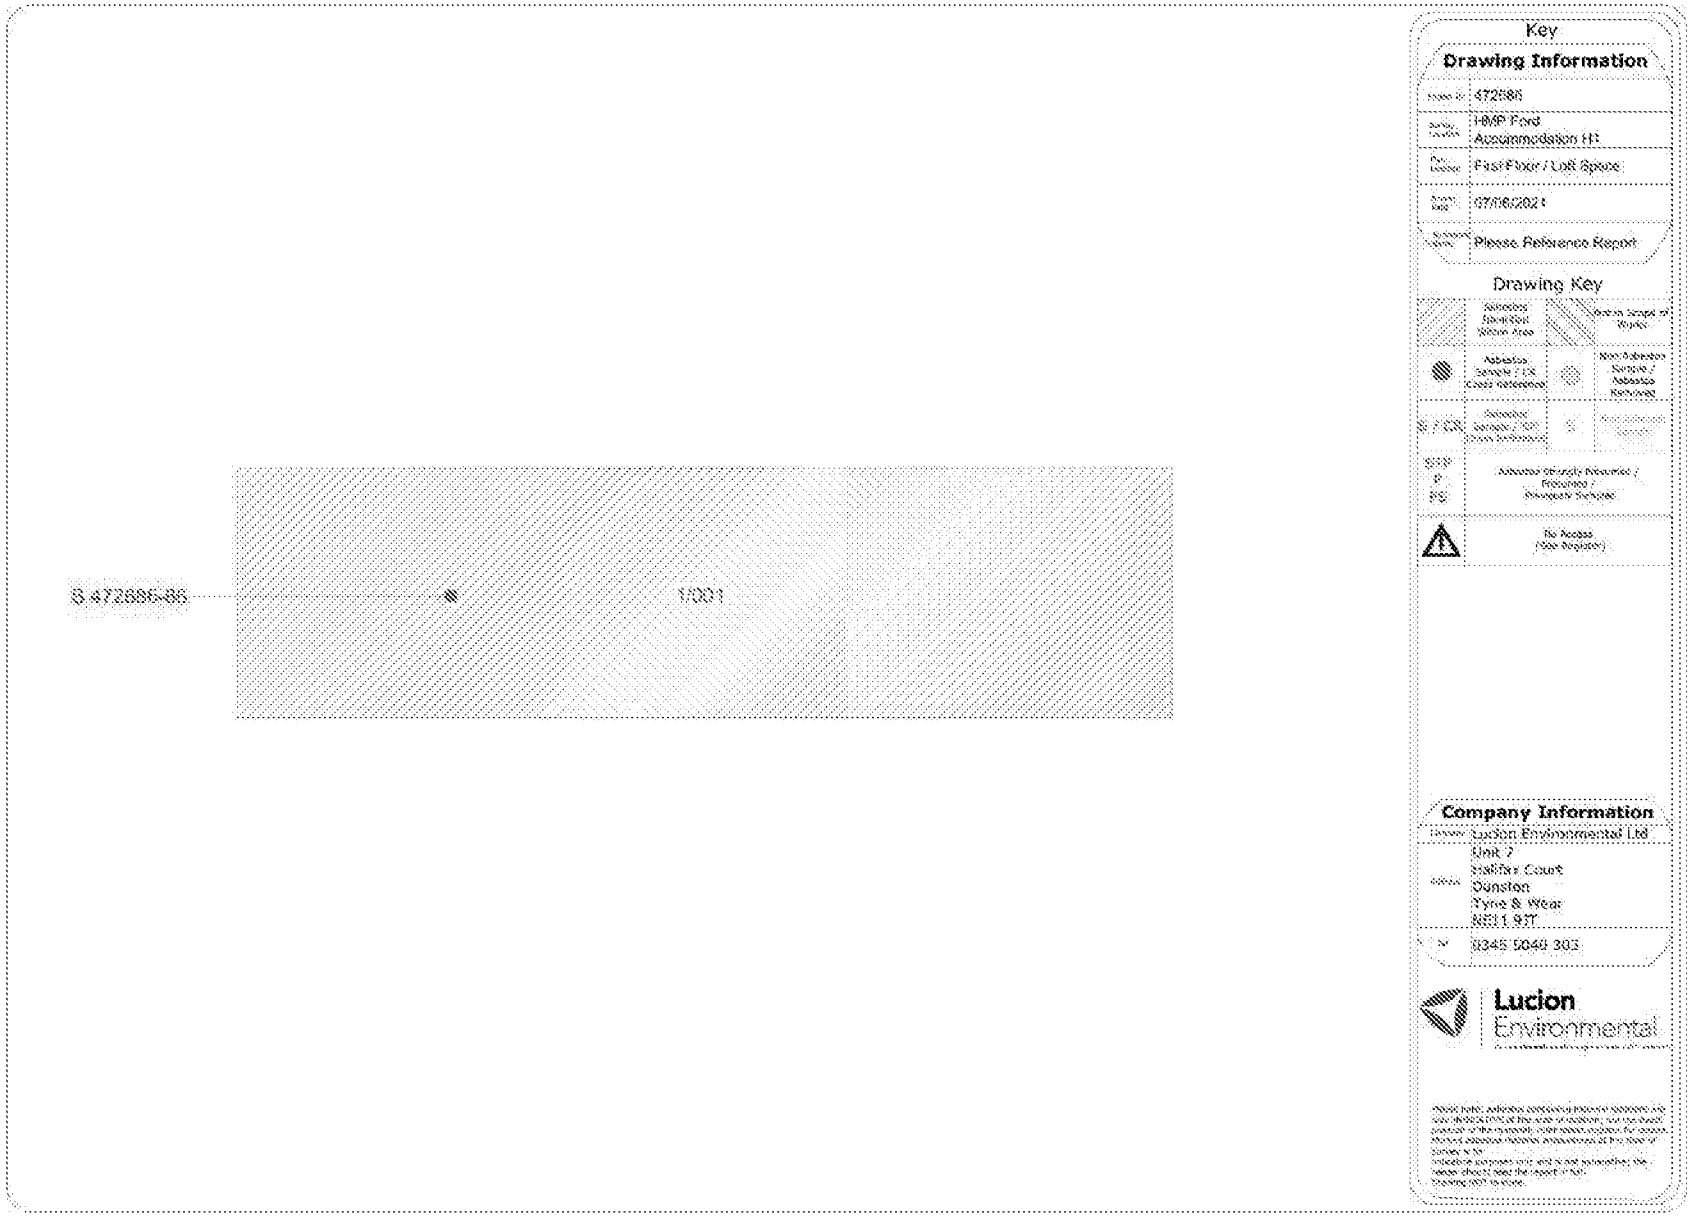


A4-Plan_472686_HMP-Ford.pdf

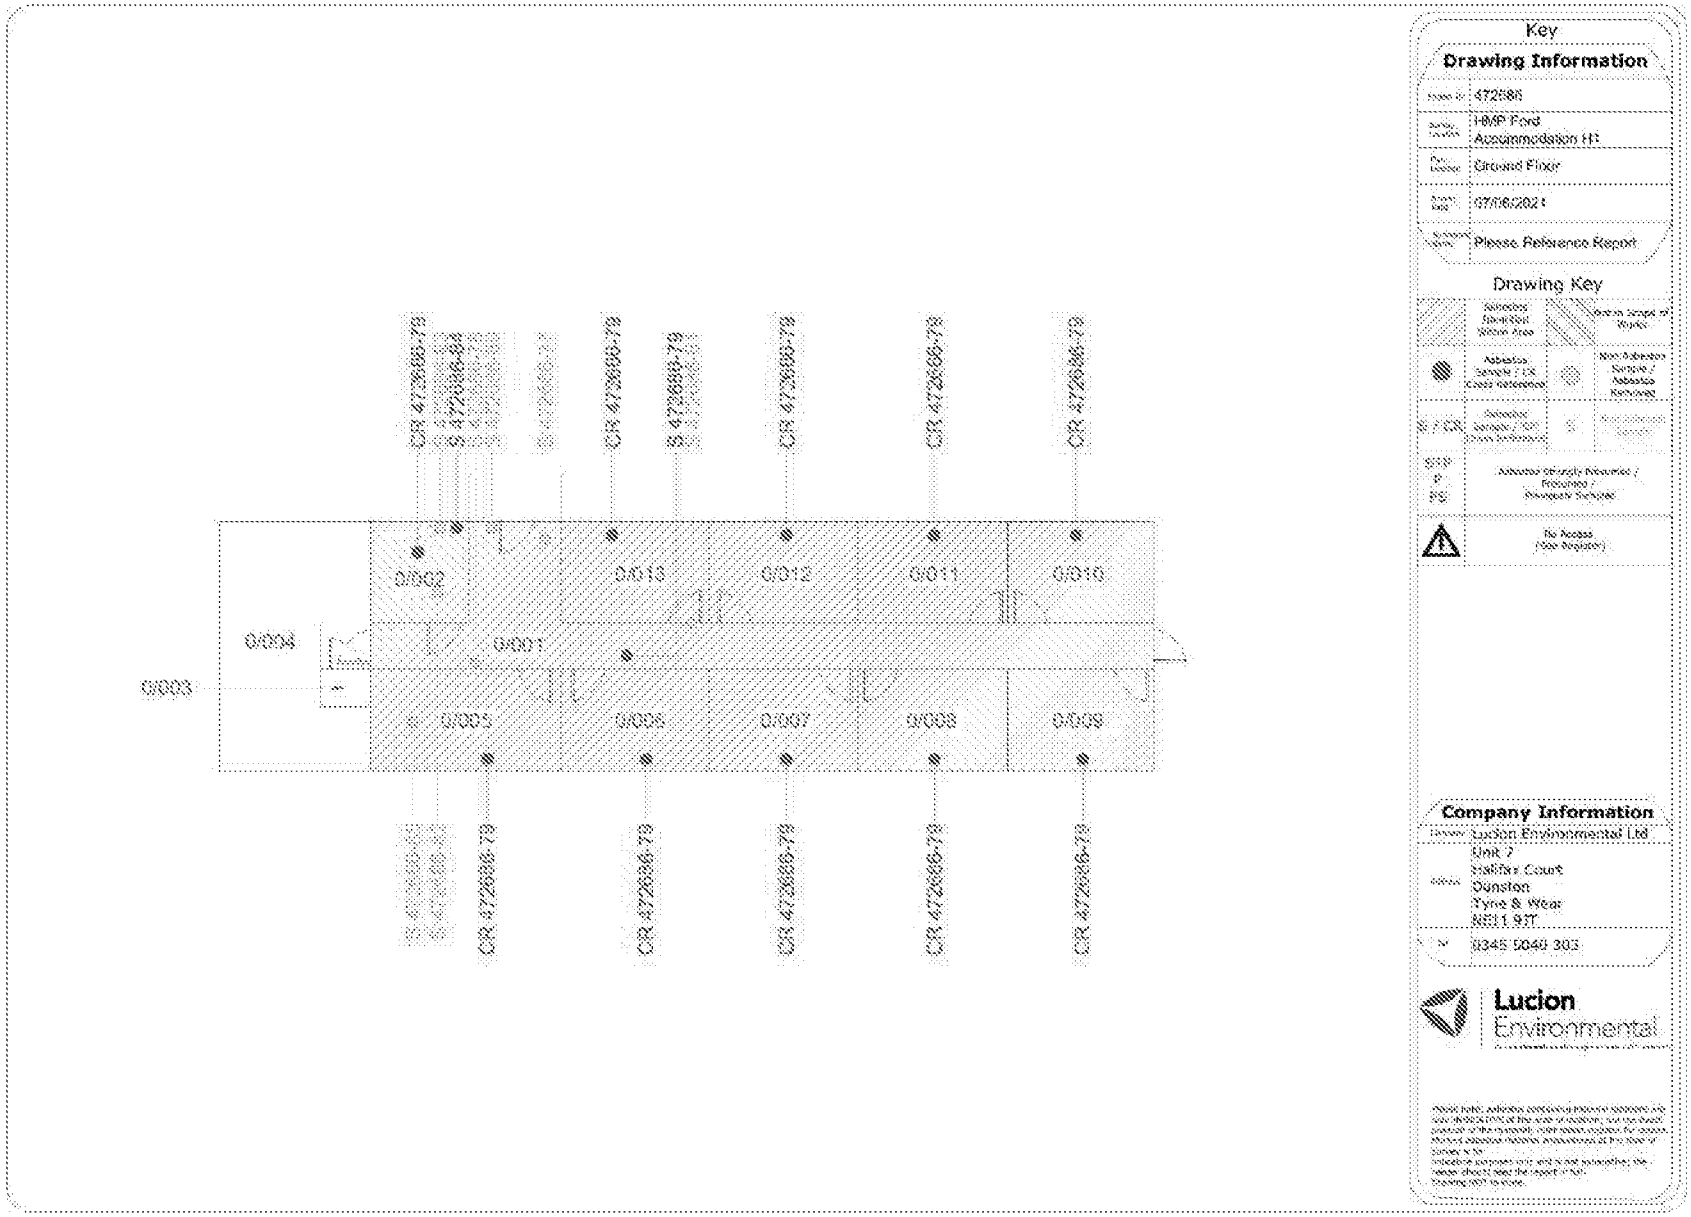


A4-Plan_472686_HMP-Ford.pdf

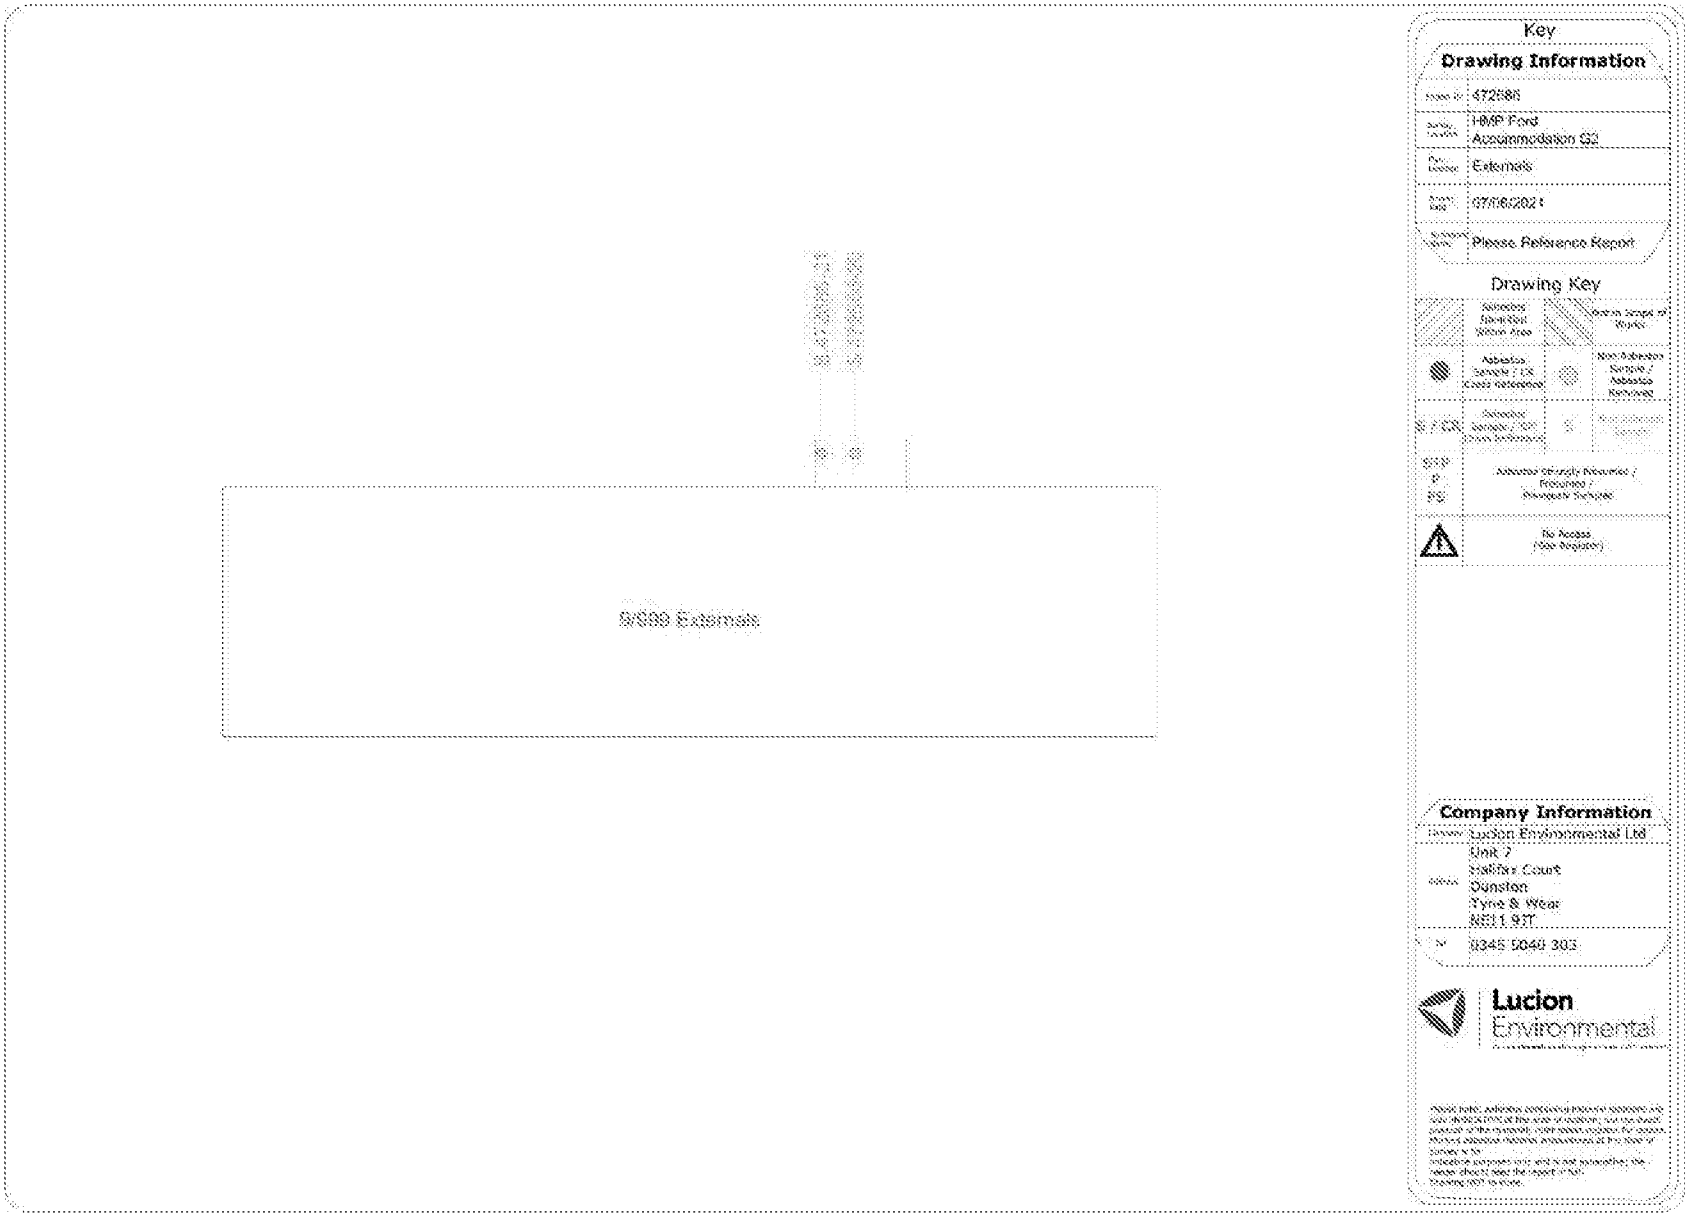


A4-Plan_472686_HMP-Ford.pdf

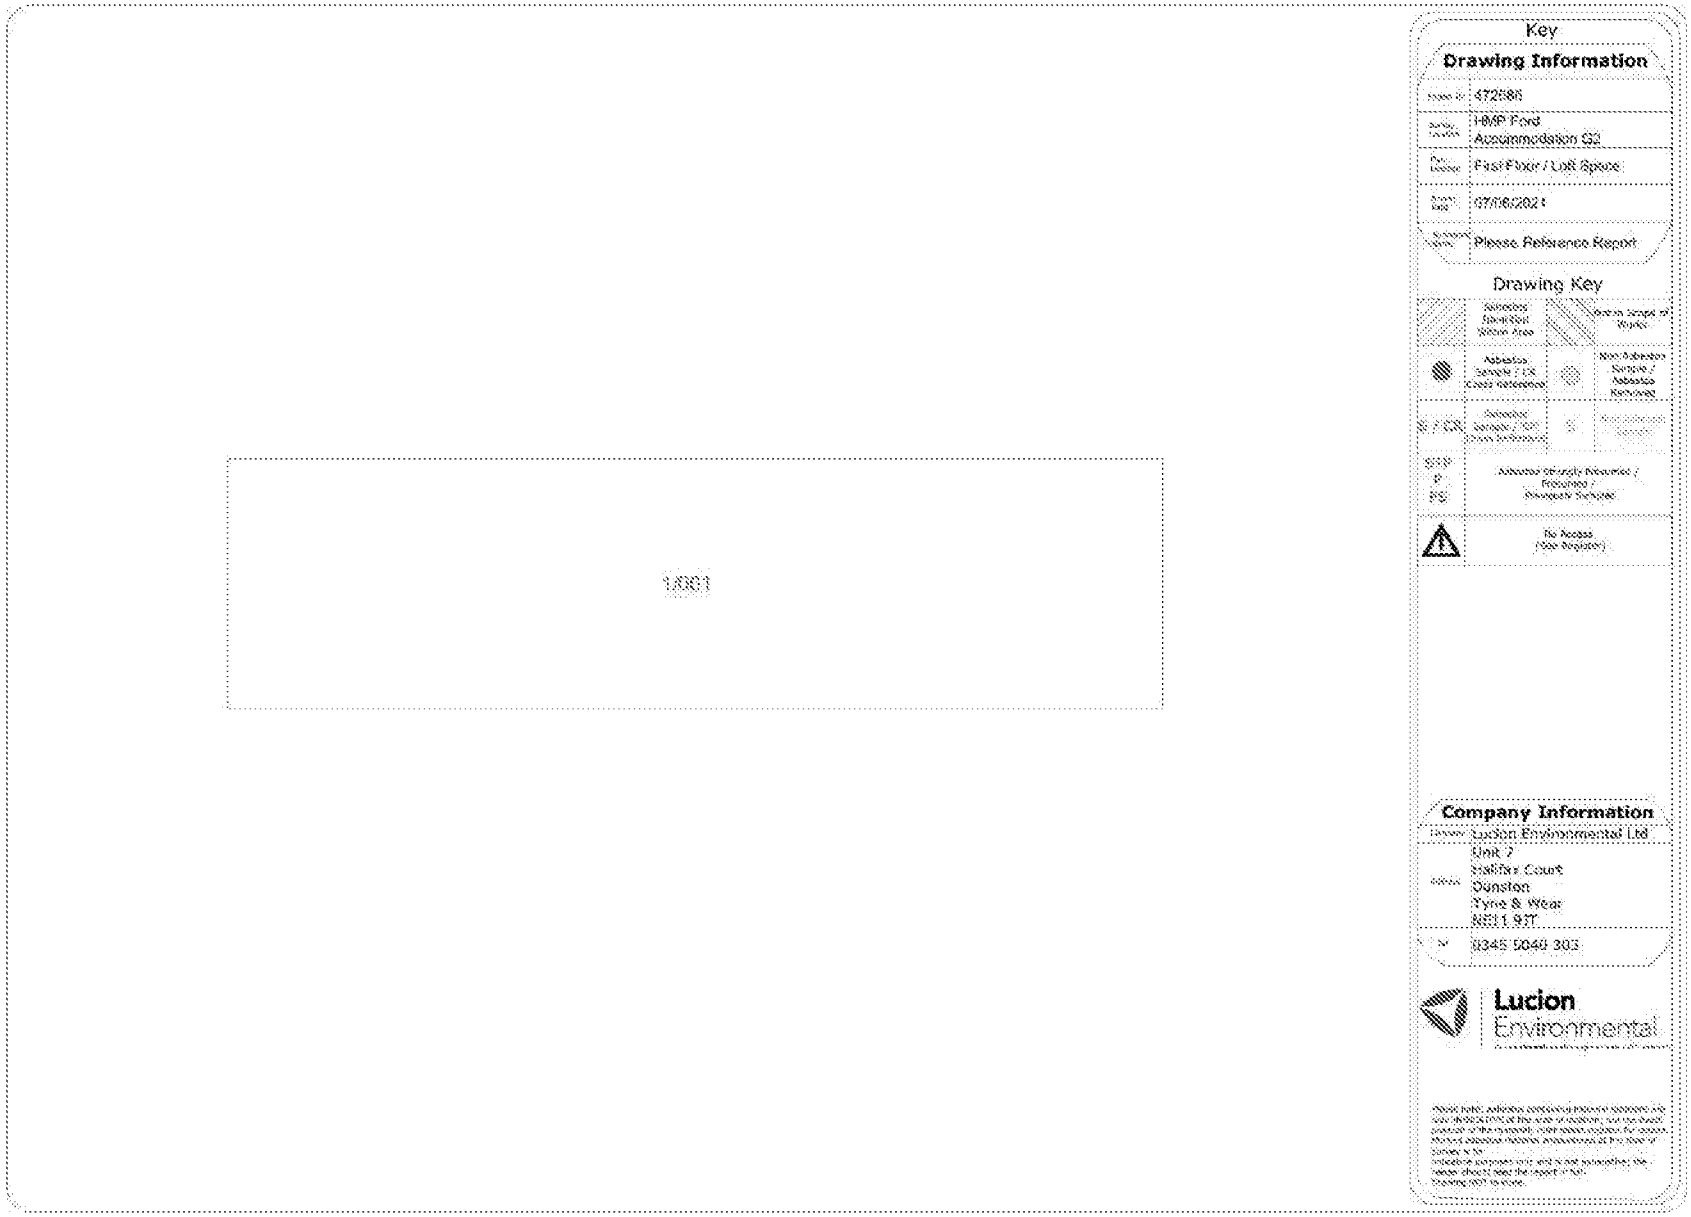


A4-Plan_472686_HMP-Ford.pdf

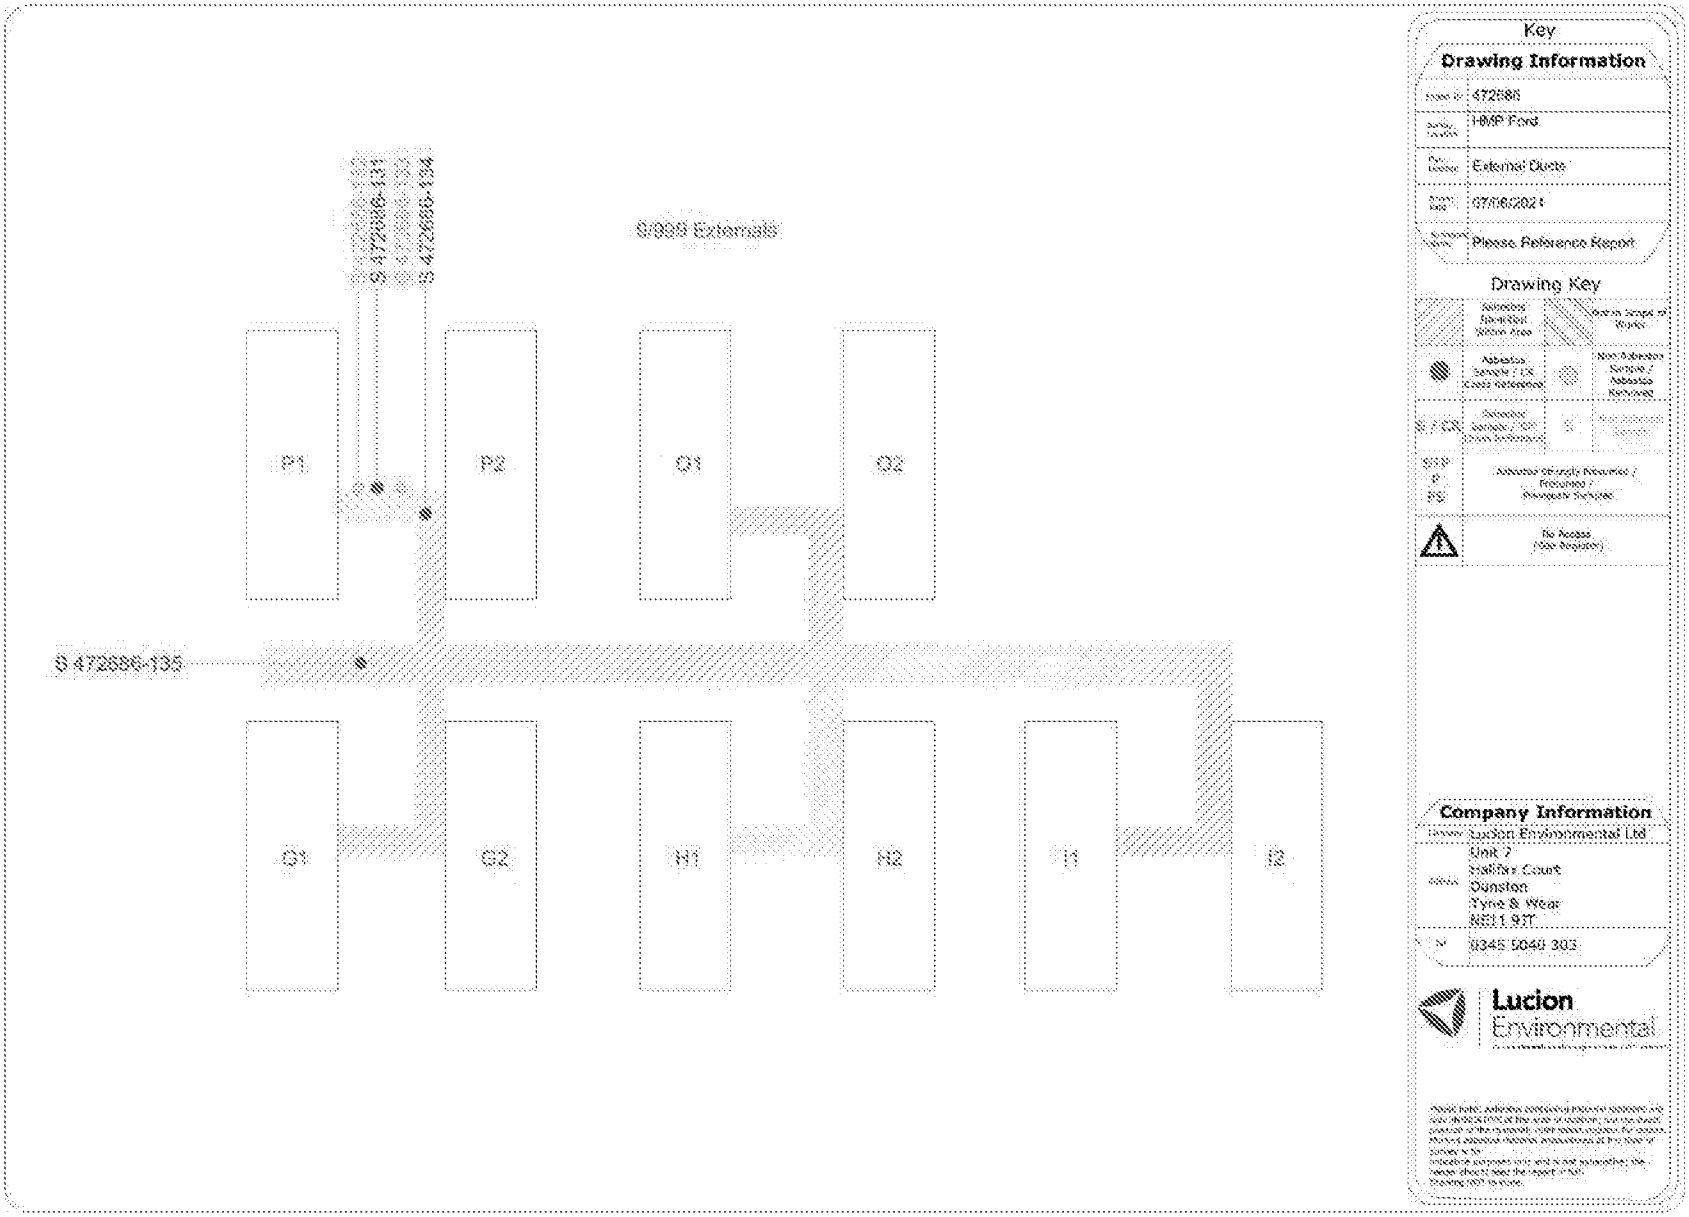


A4-Plan_472686_HMP-Ford.pdf

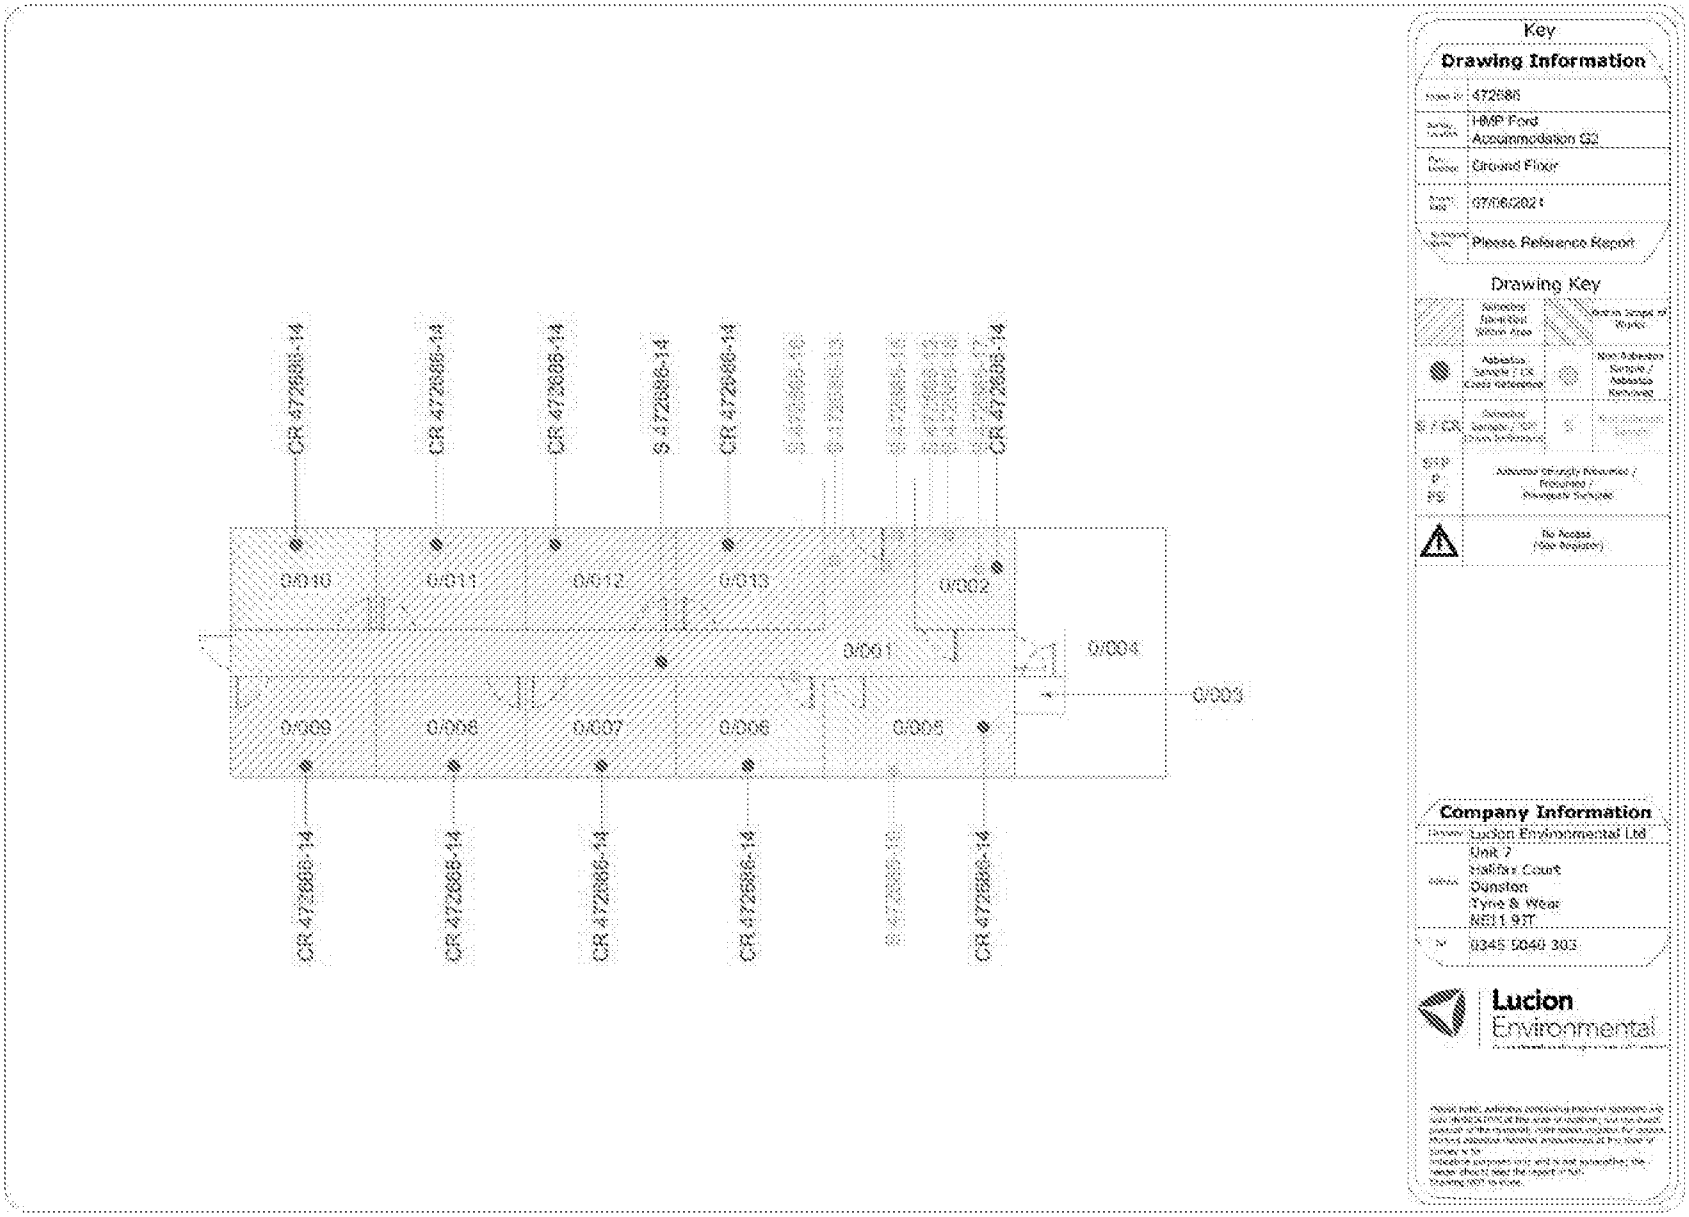


A4-Plan_472686_HMP-Ford.pdf

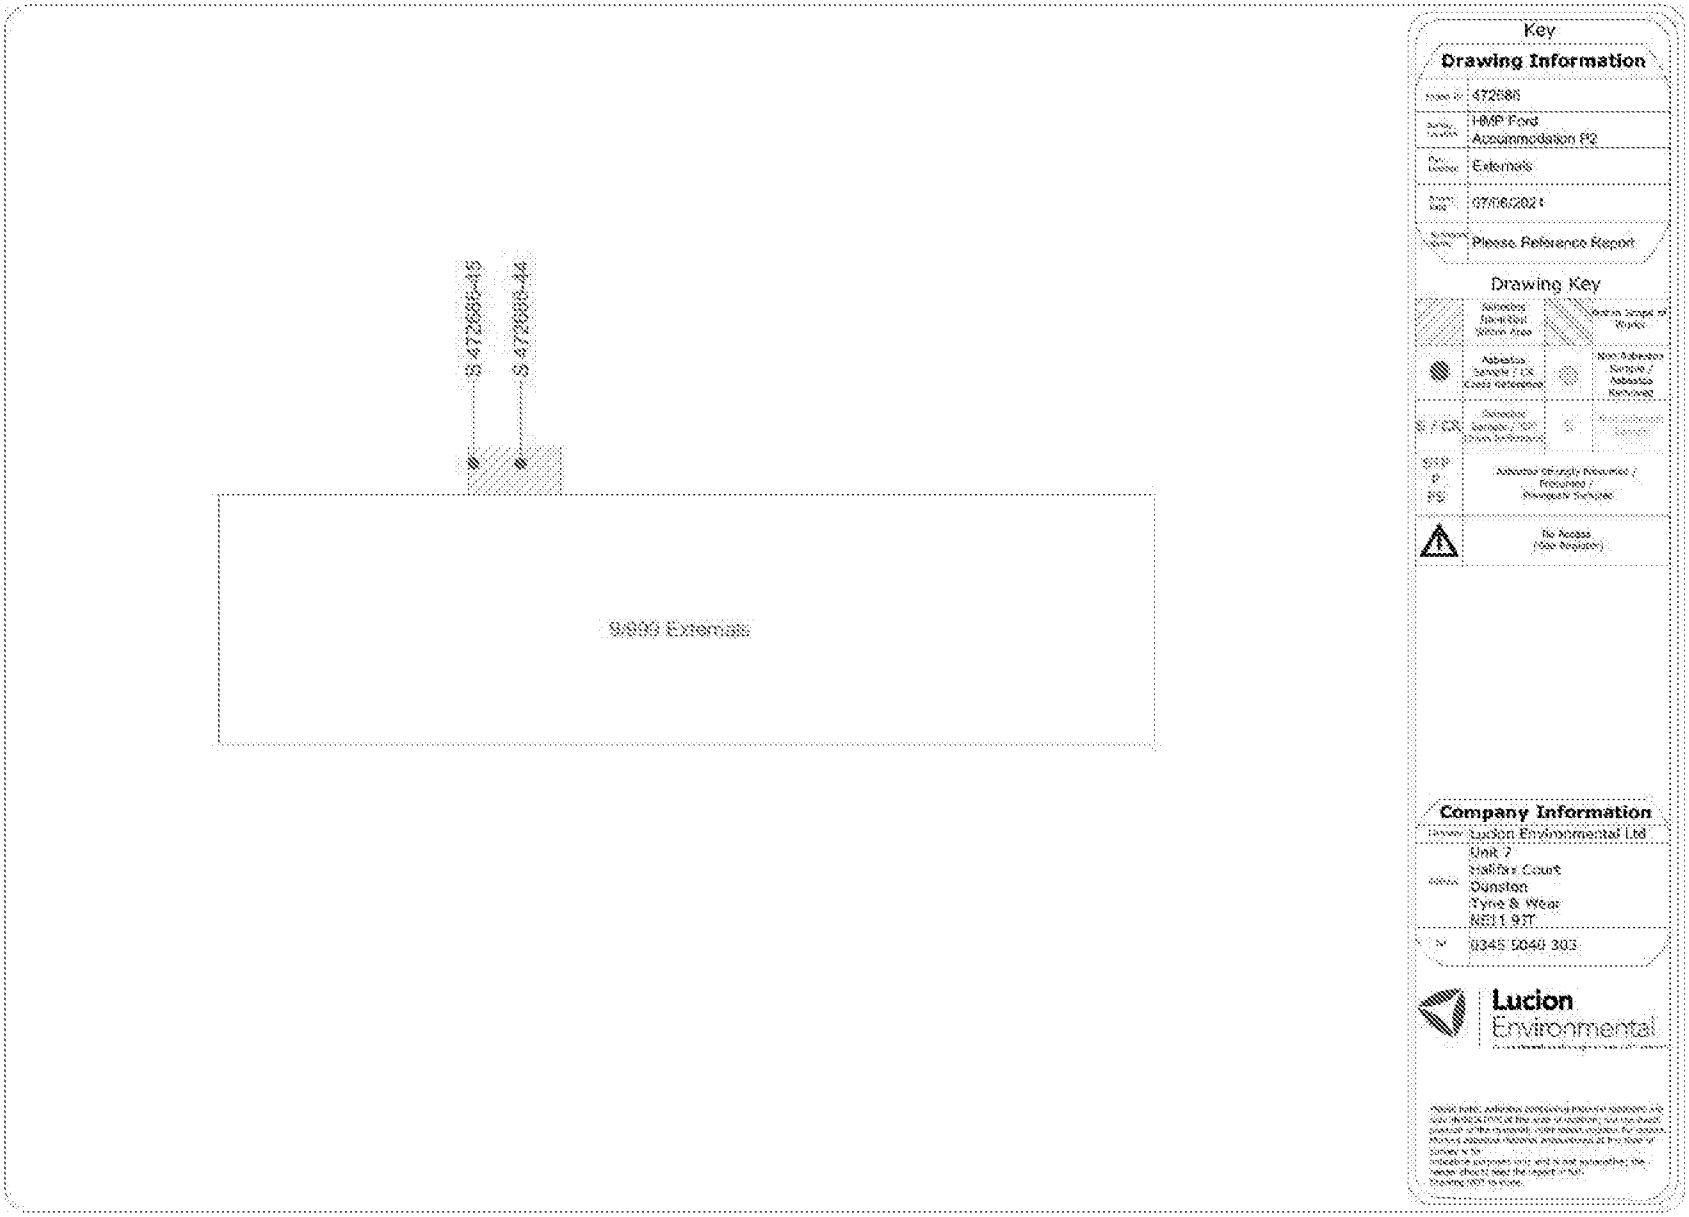


A4-Plan_472686_HMP-Ford.pdf

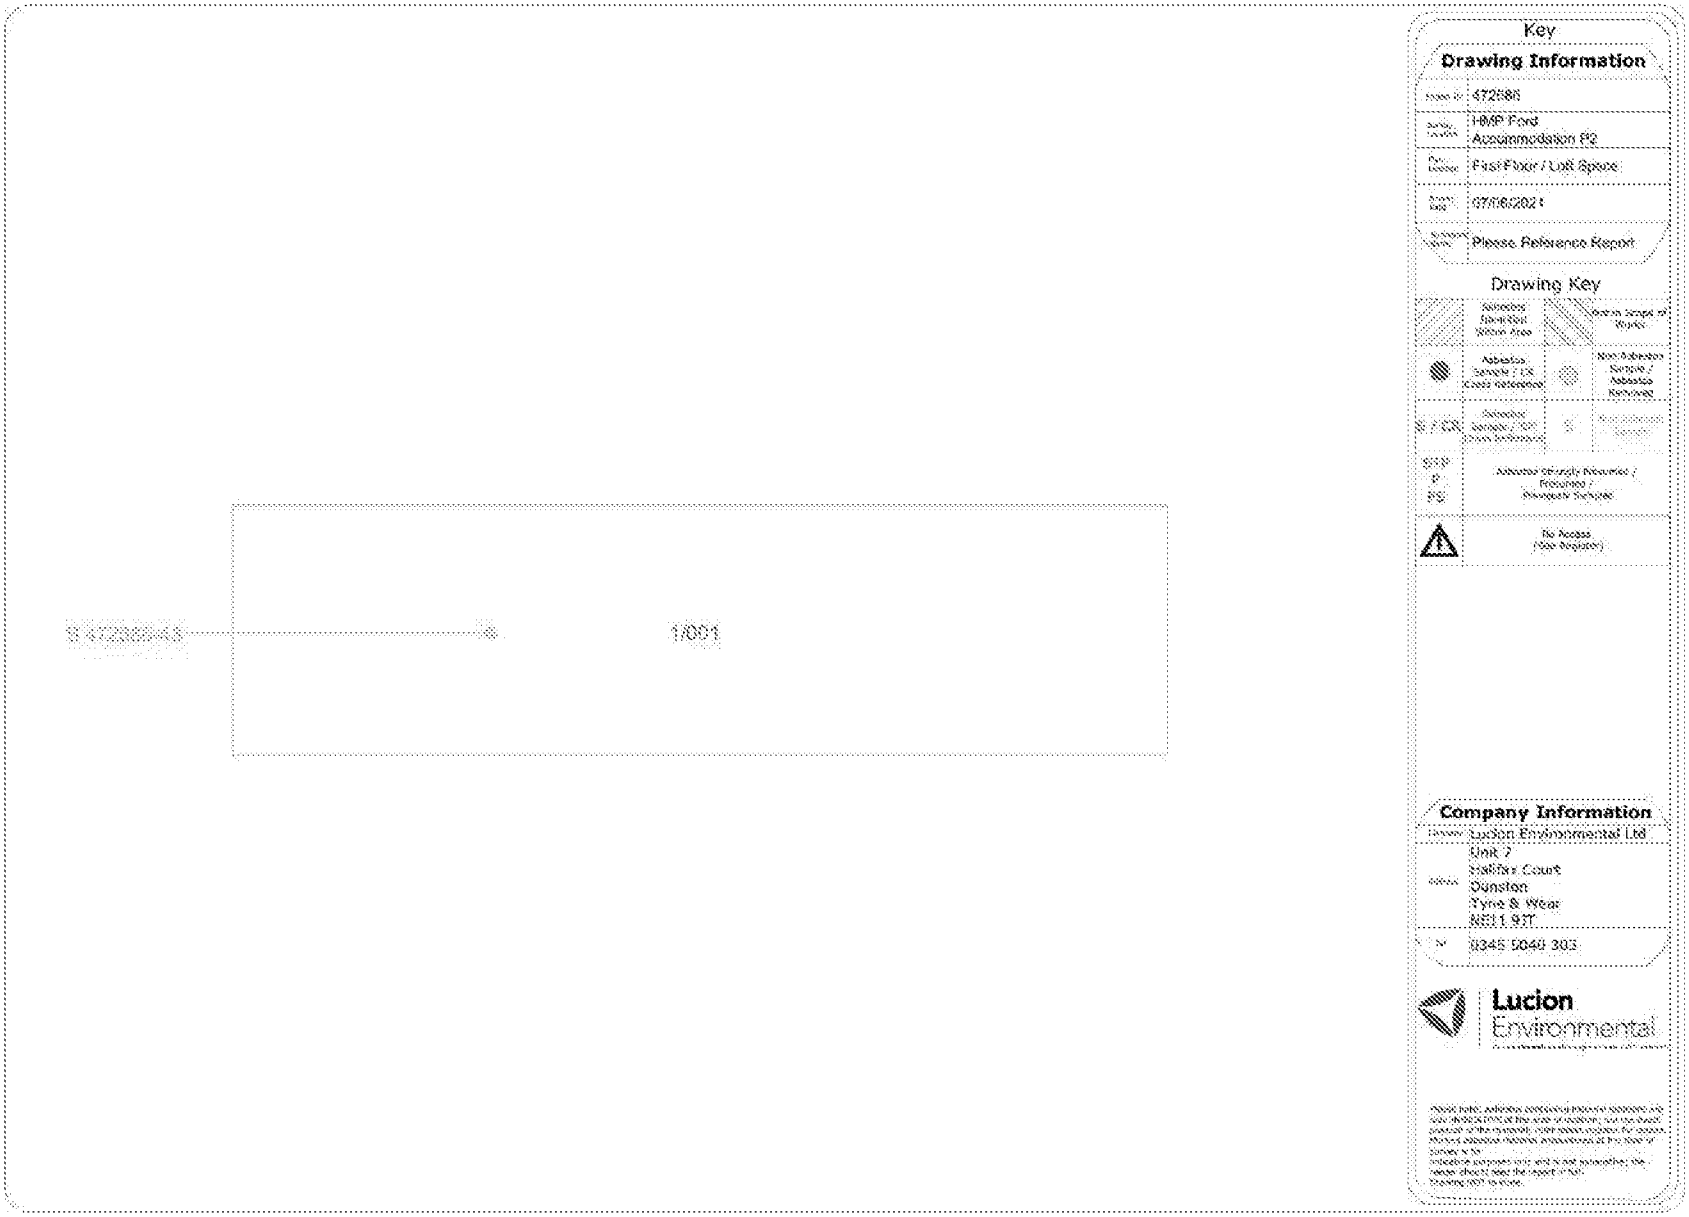


A4-Plan_472686_HMP-Ford.pdf

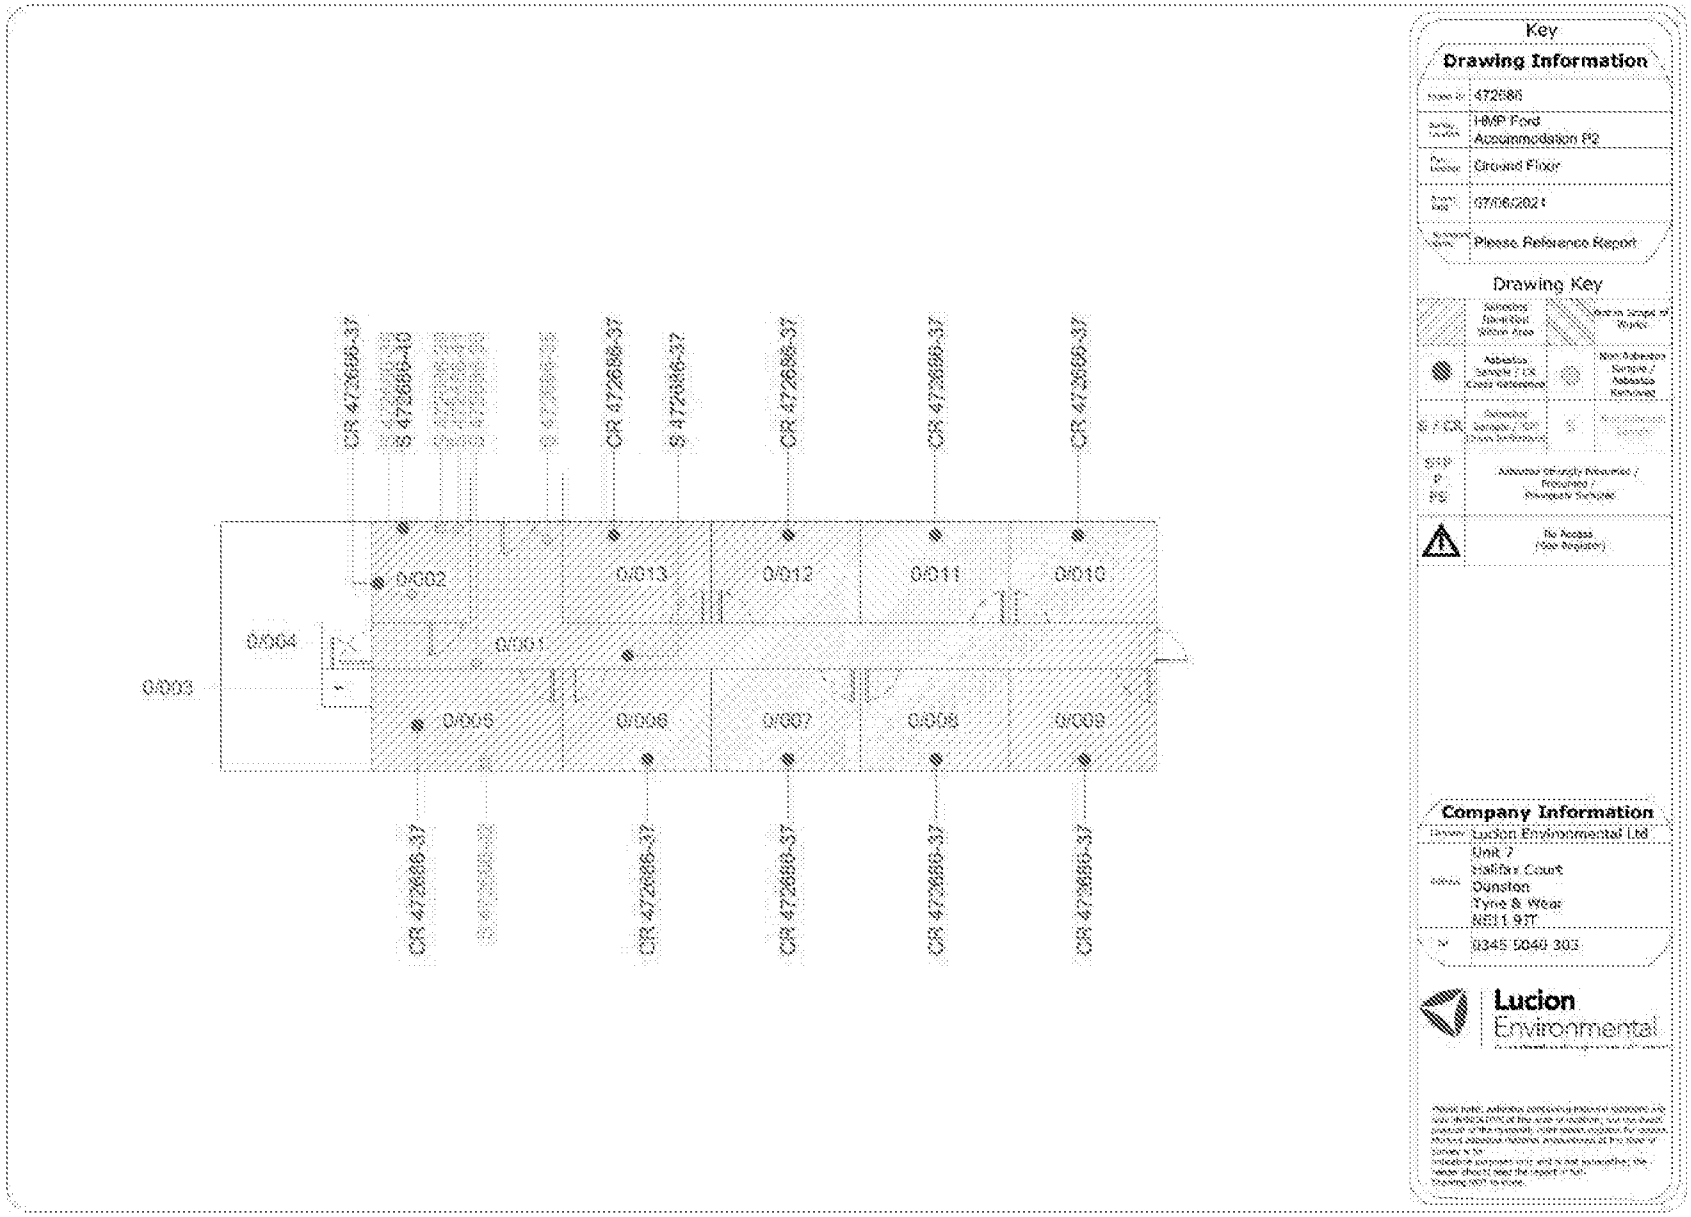


A4-Plan_472686_HMP-Ford.pdf

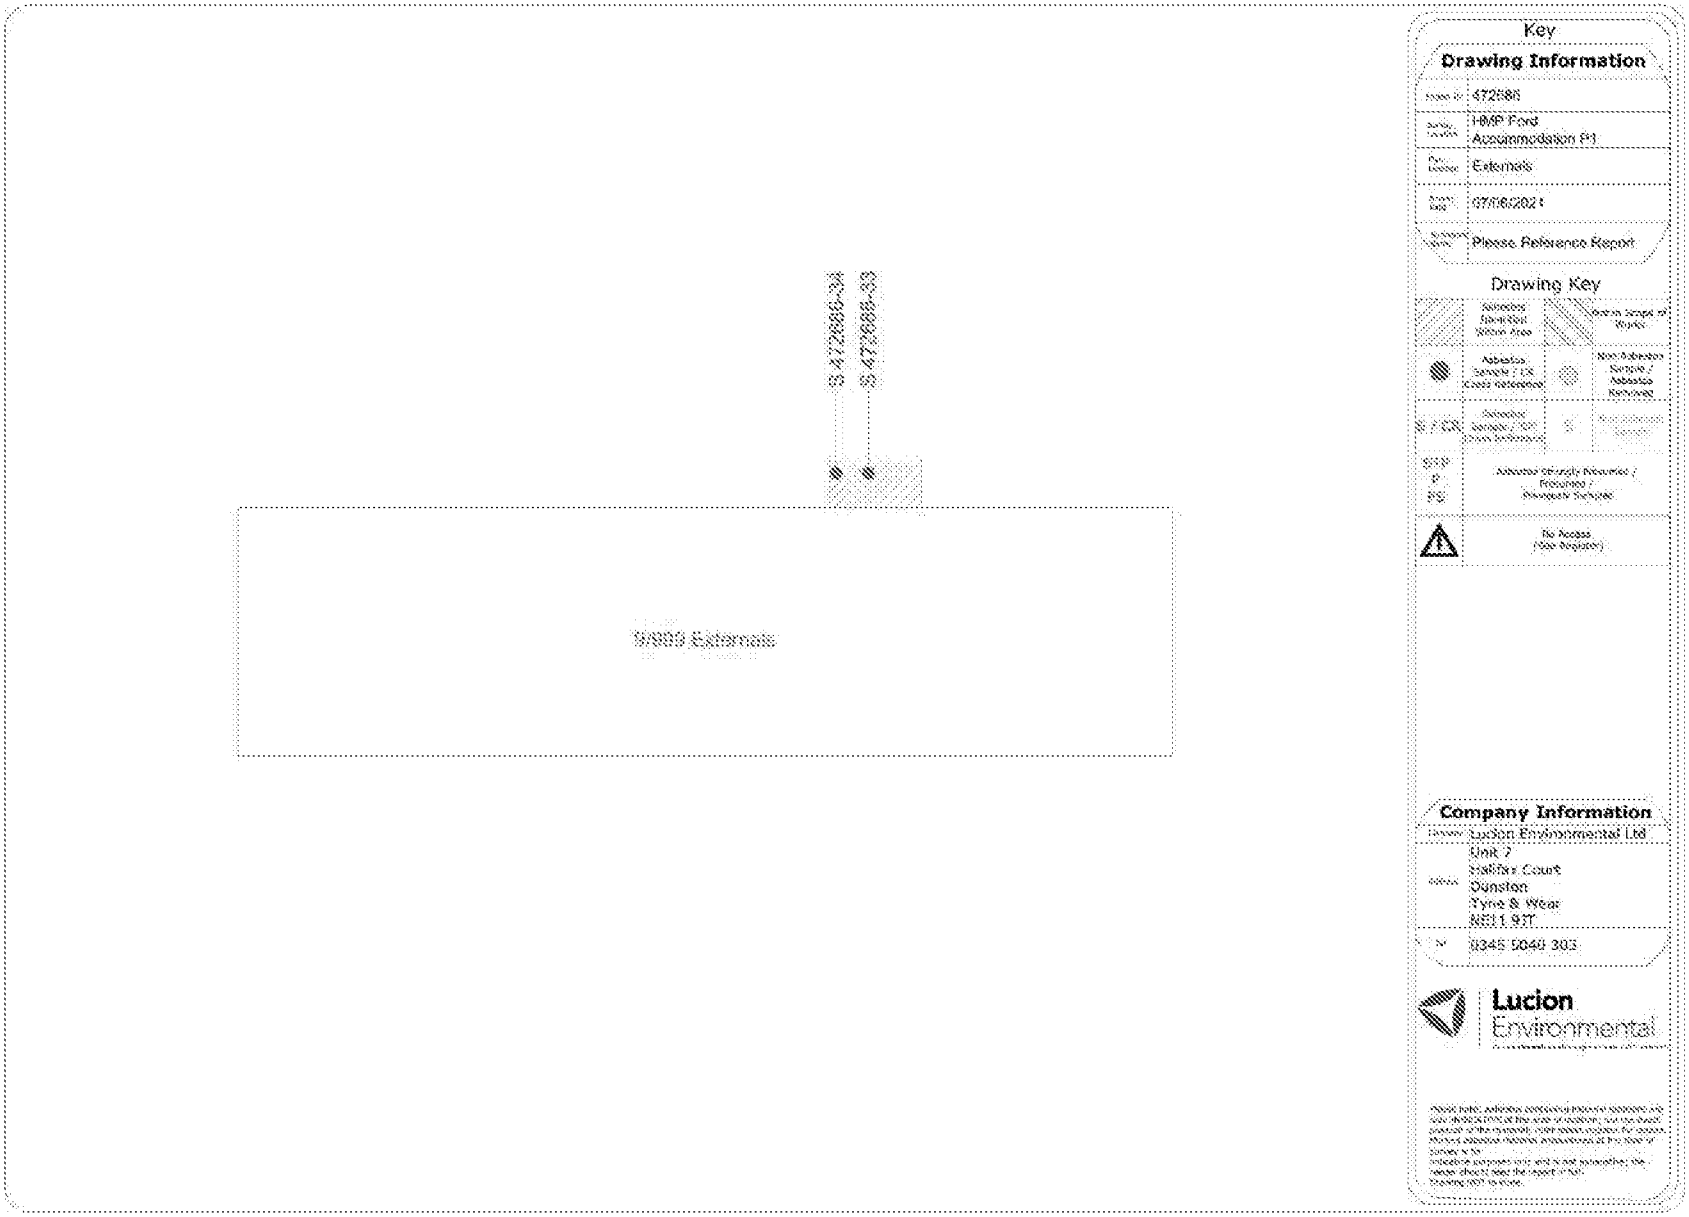

A4-Plan_472686_HMP-Ford.pdf

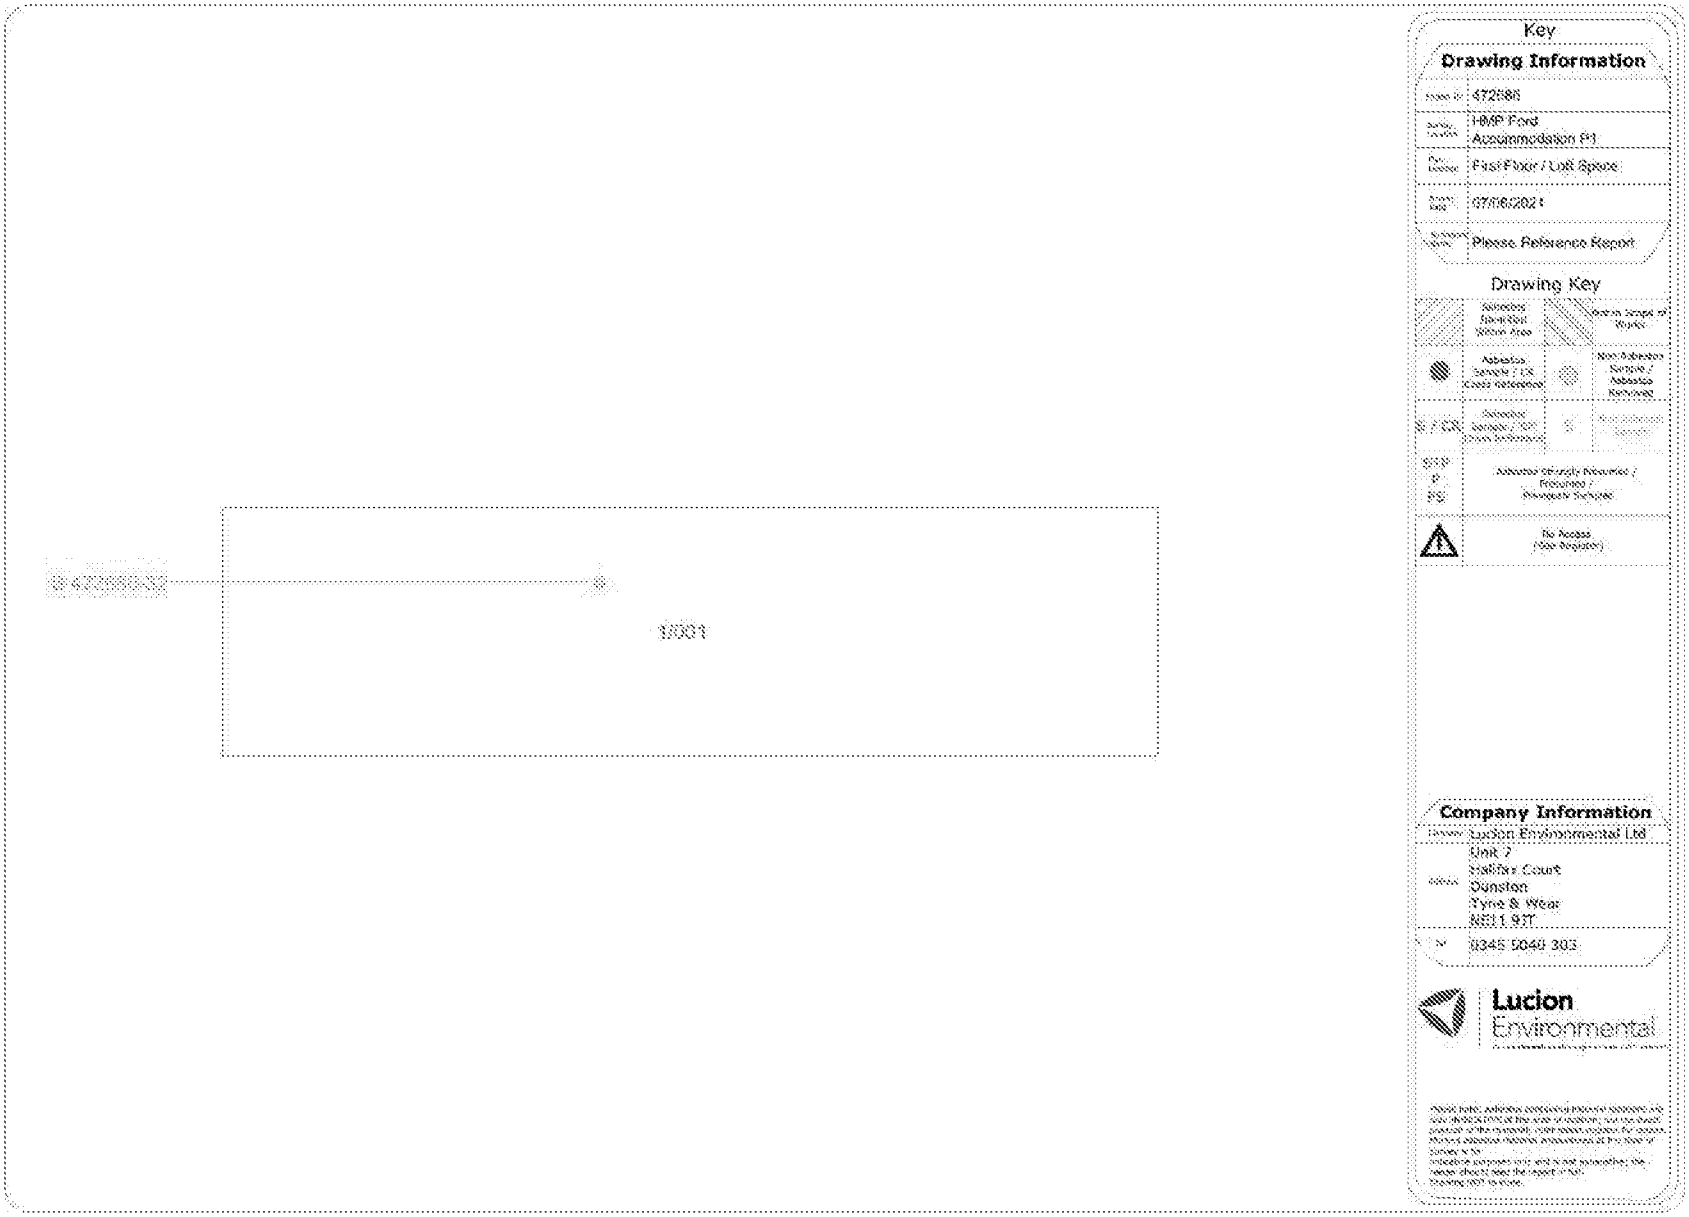


A4-Plan_472686_HMP-Ford.pdf

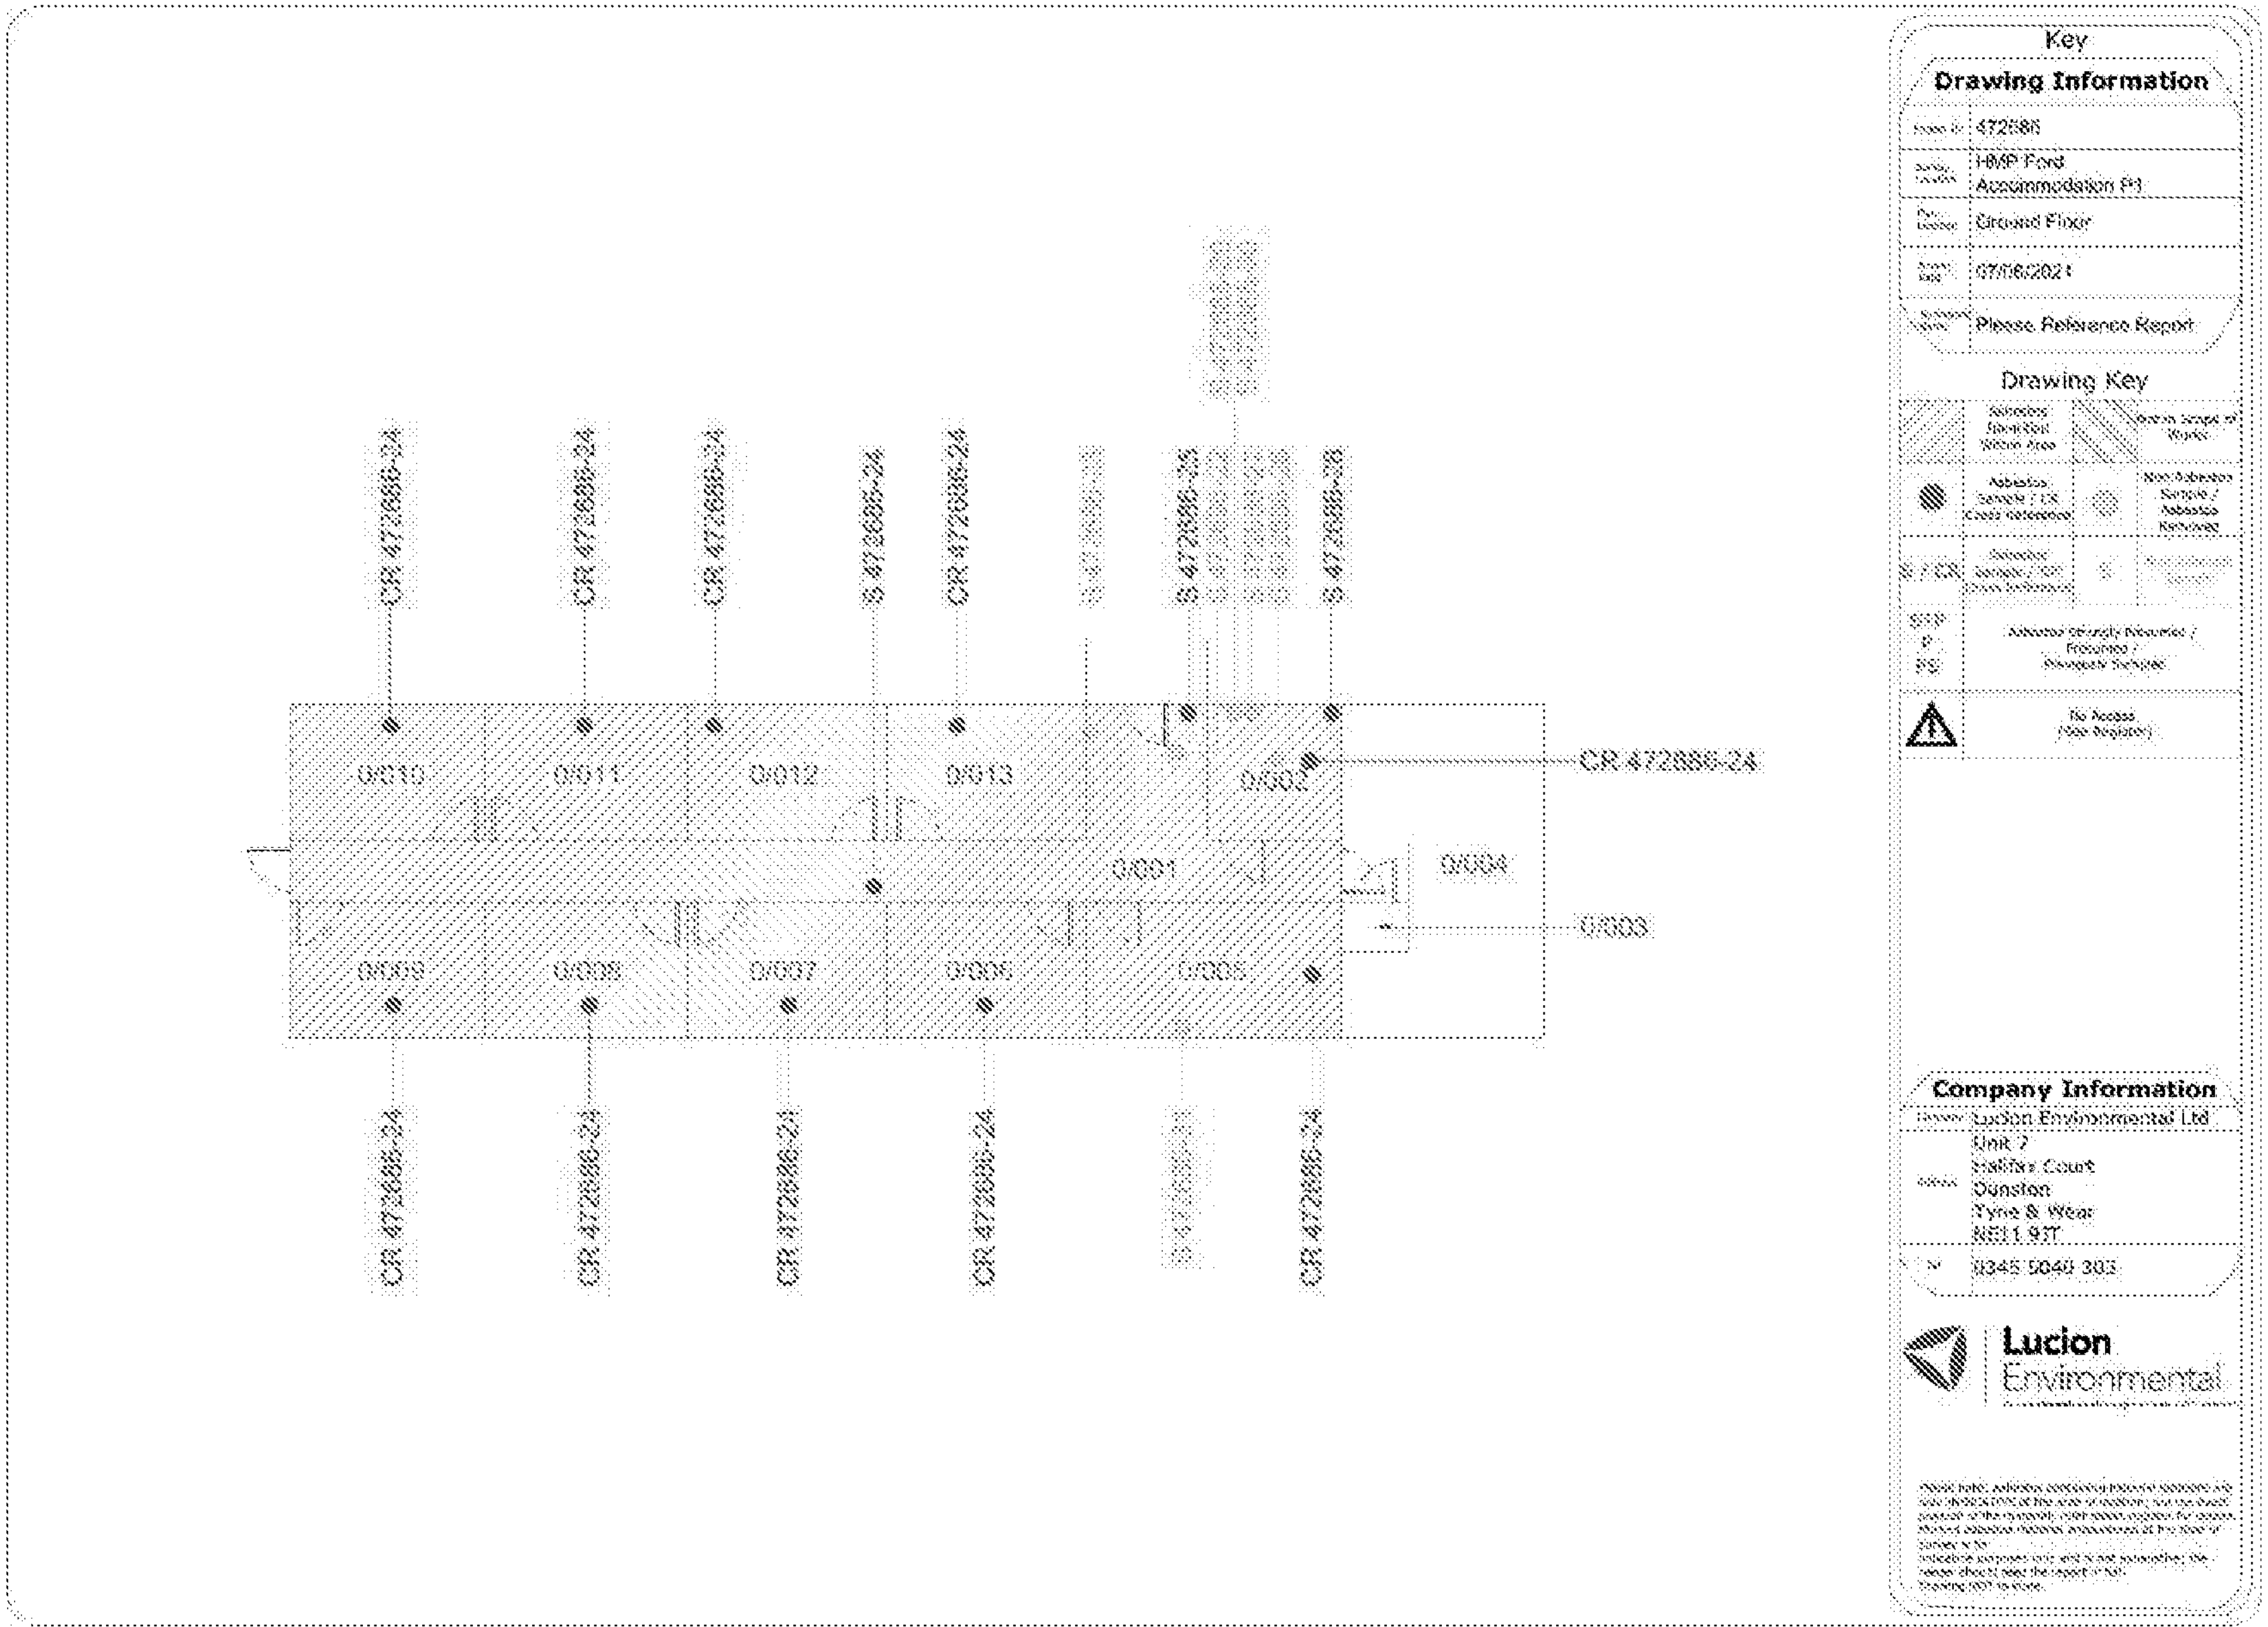


ARUN DISTRICT COUNCIL F/26/21/DEM


A4-Plan_472686_HMP-Ford.pdf

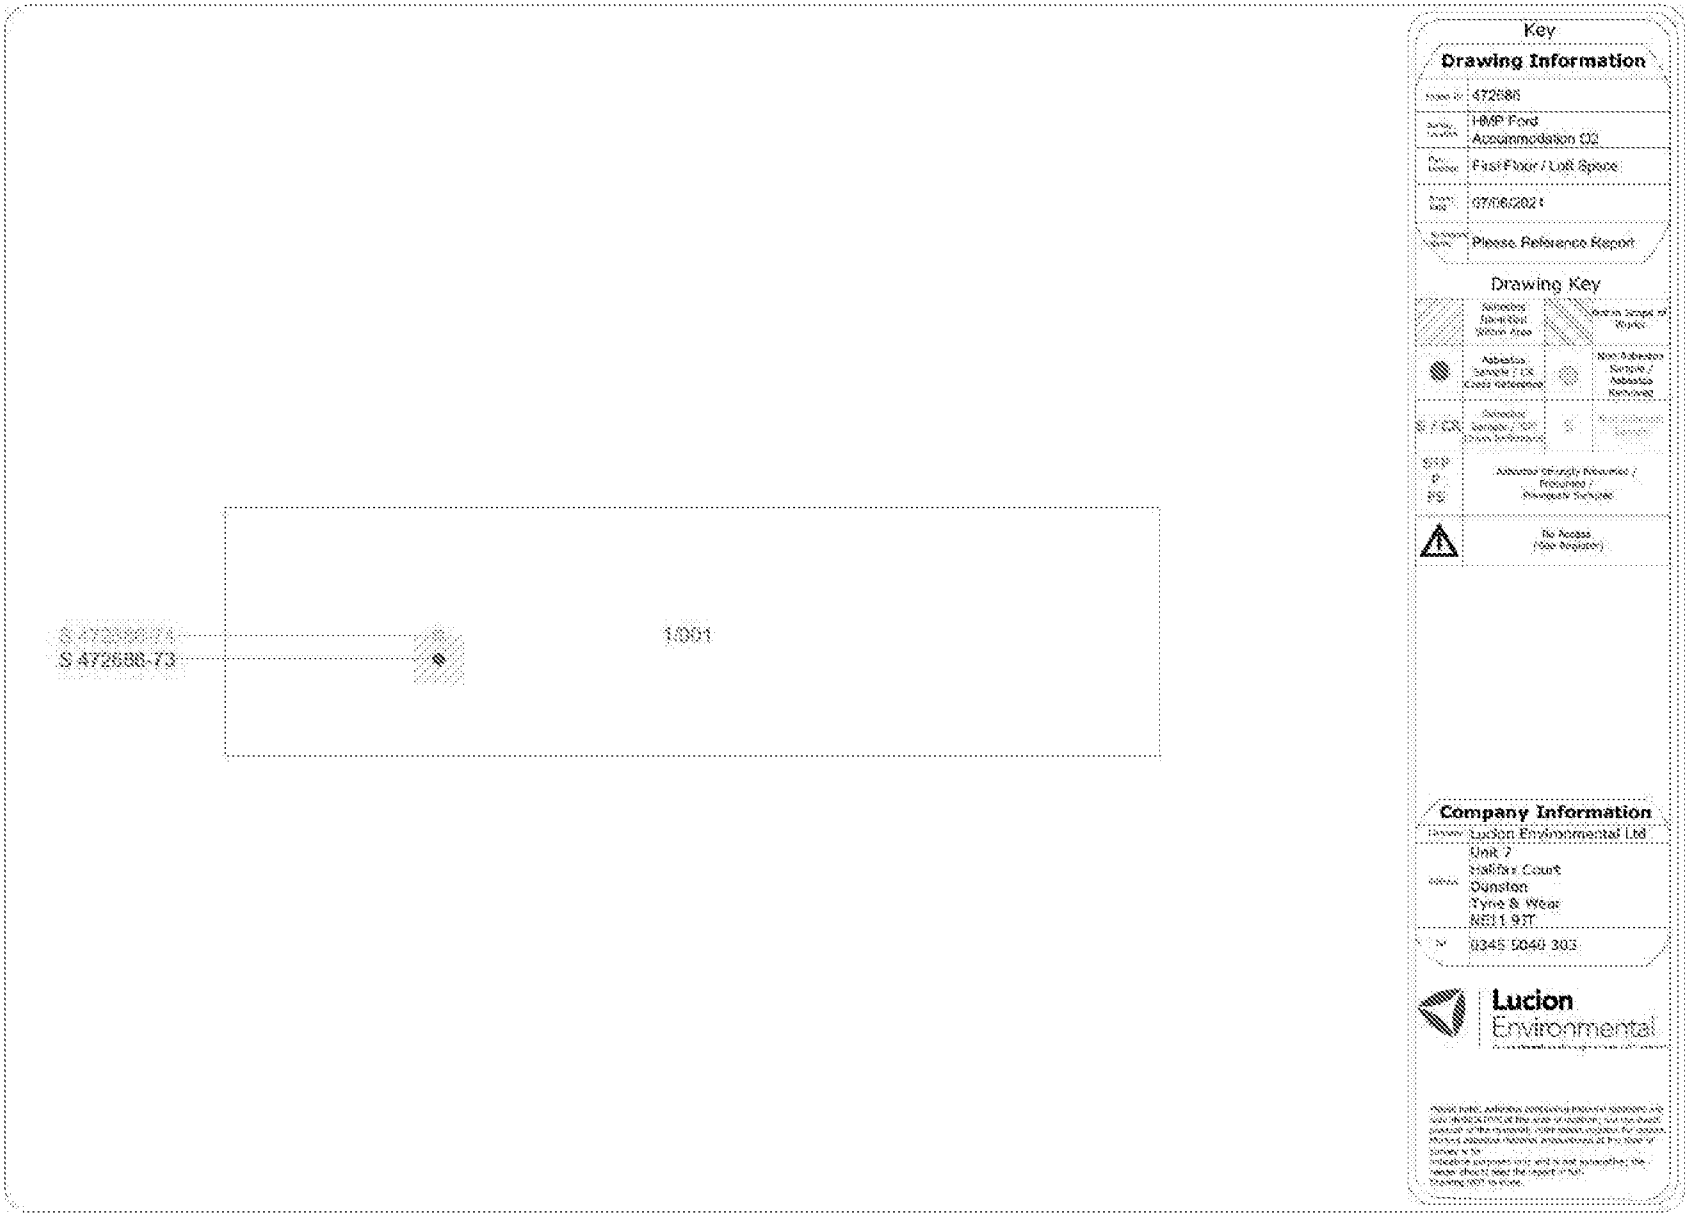


A4-Plan_472686_HMP-Ford.pdf

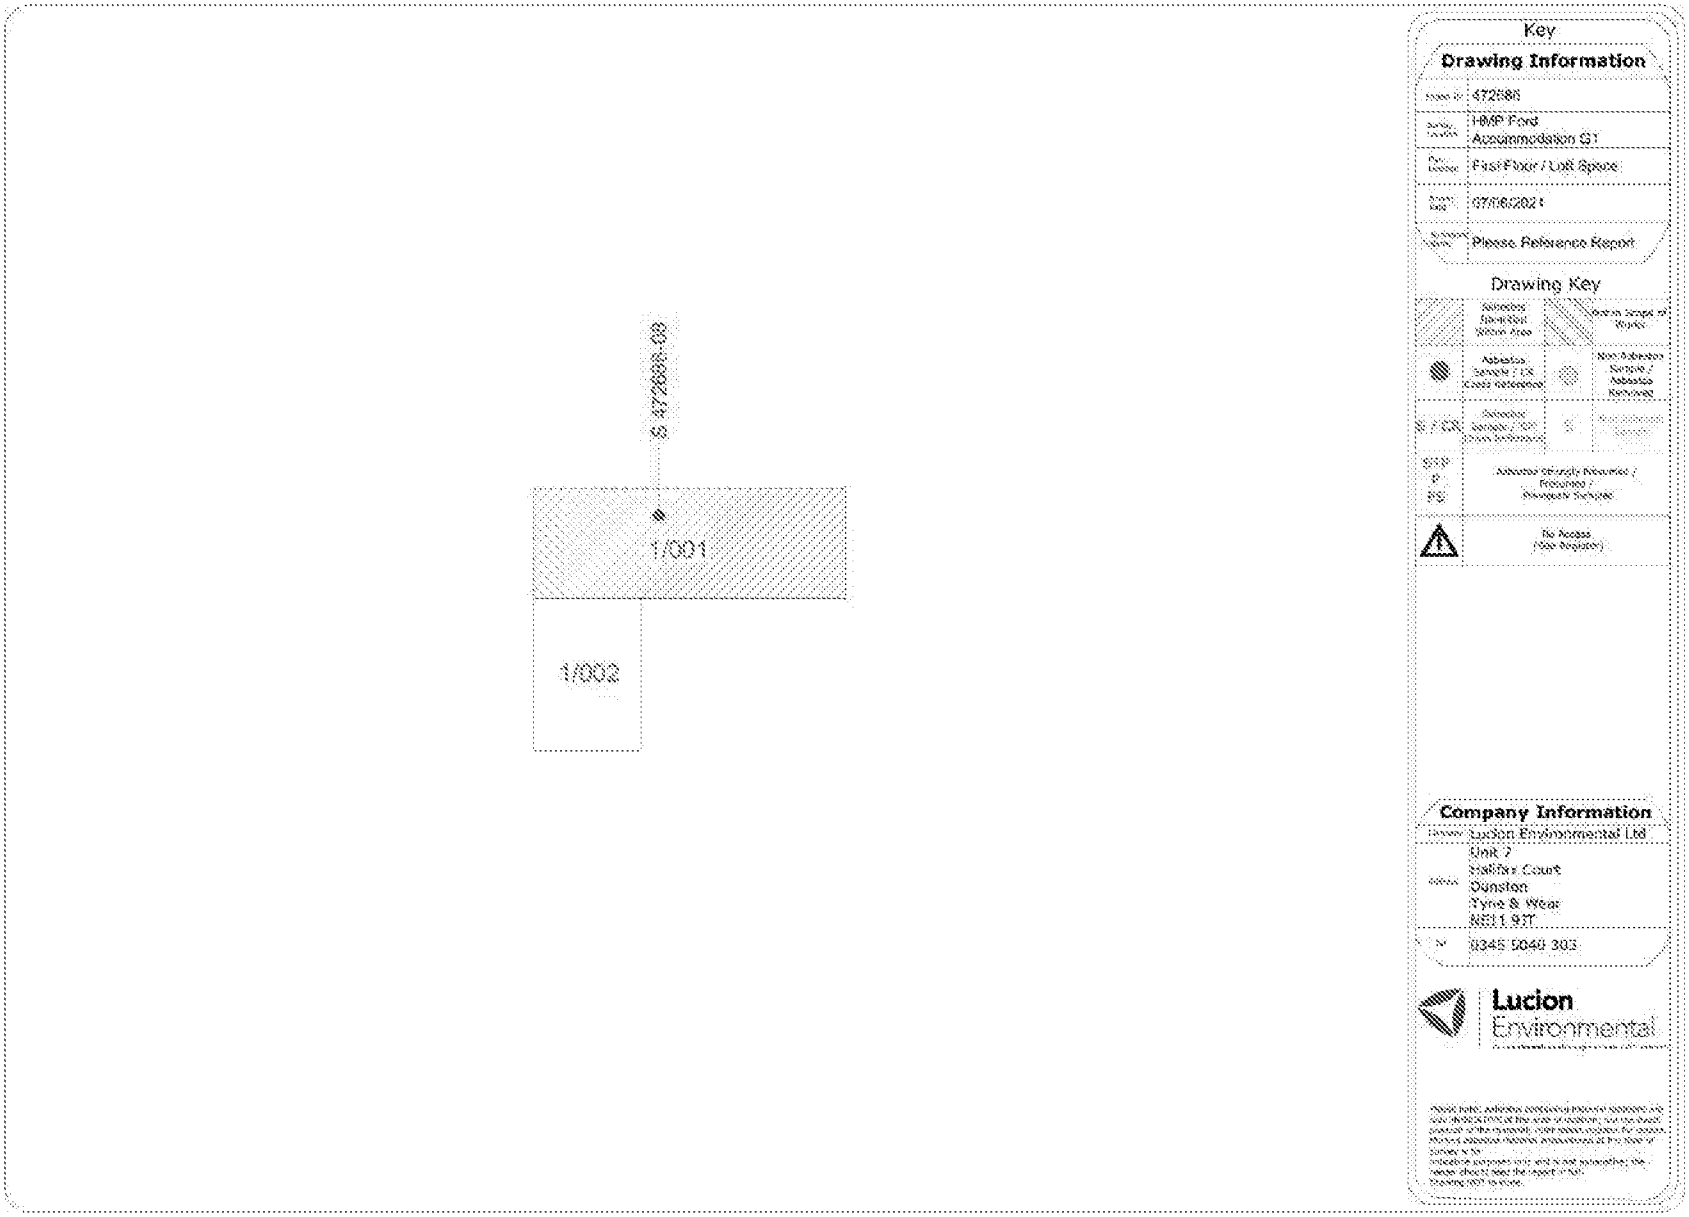


A4-Plan_472686_HMP-Ford.pdf

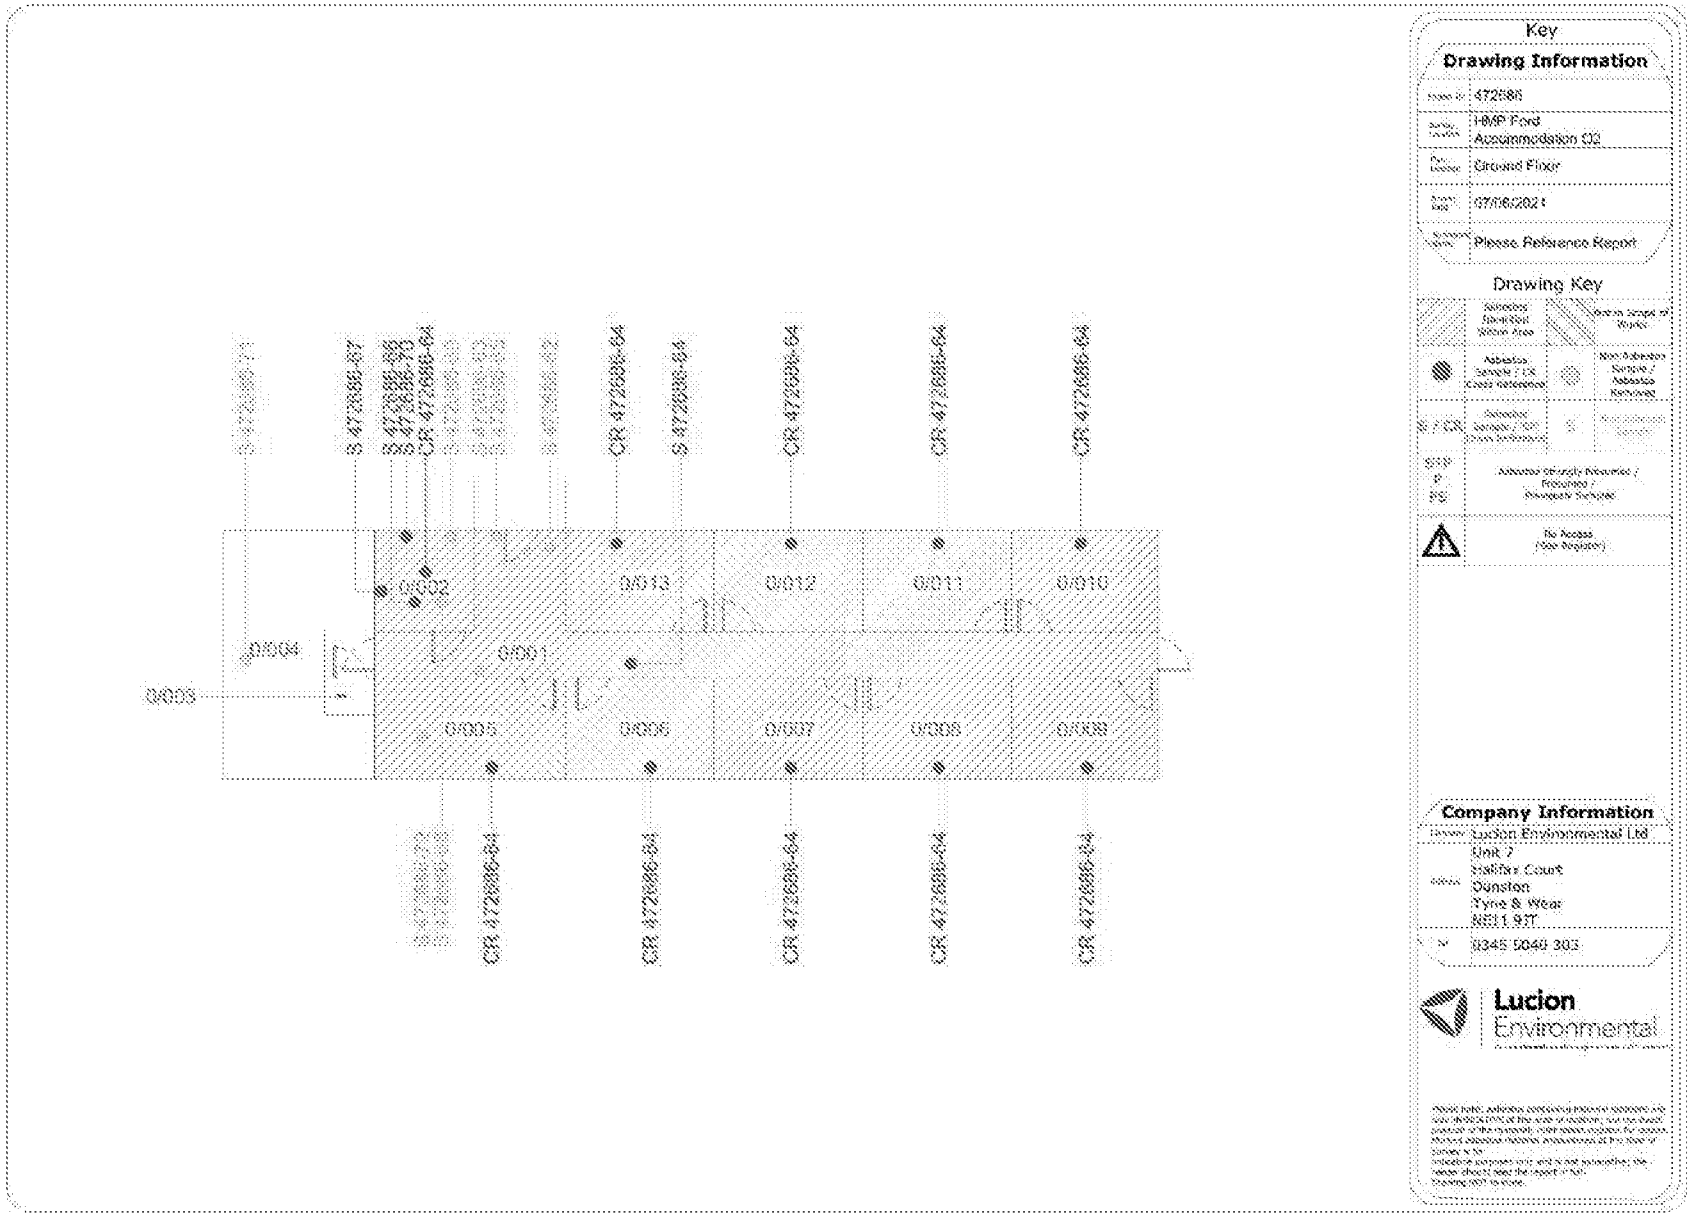


A4-Plan_472686_HMP-Ford.pdf

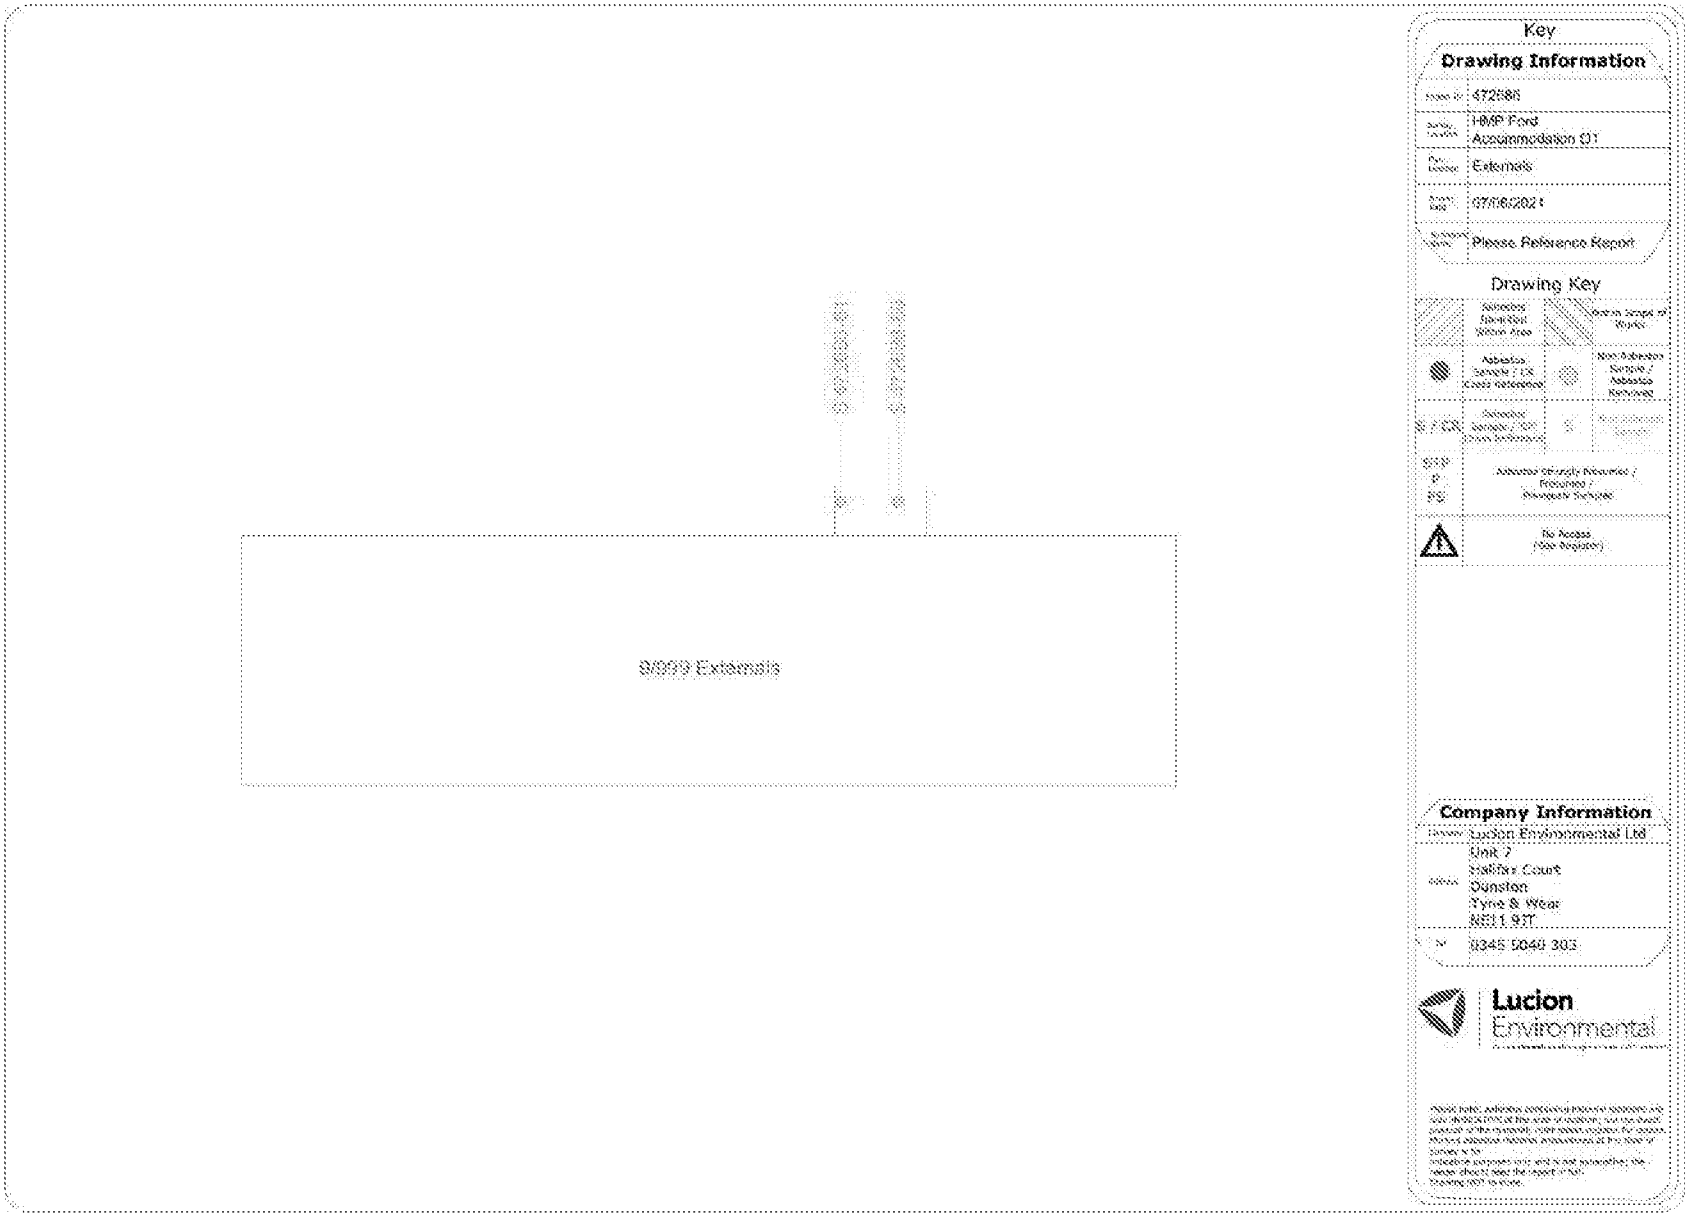


A4-Plan_472686_HMP-Ford.pdf

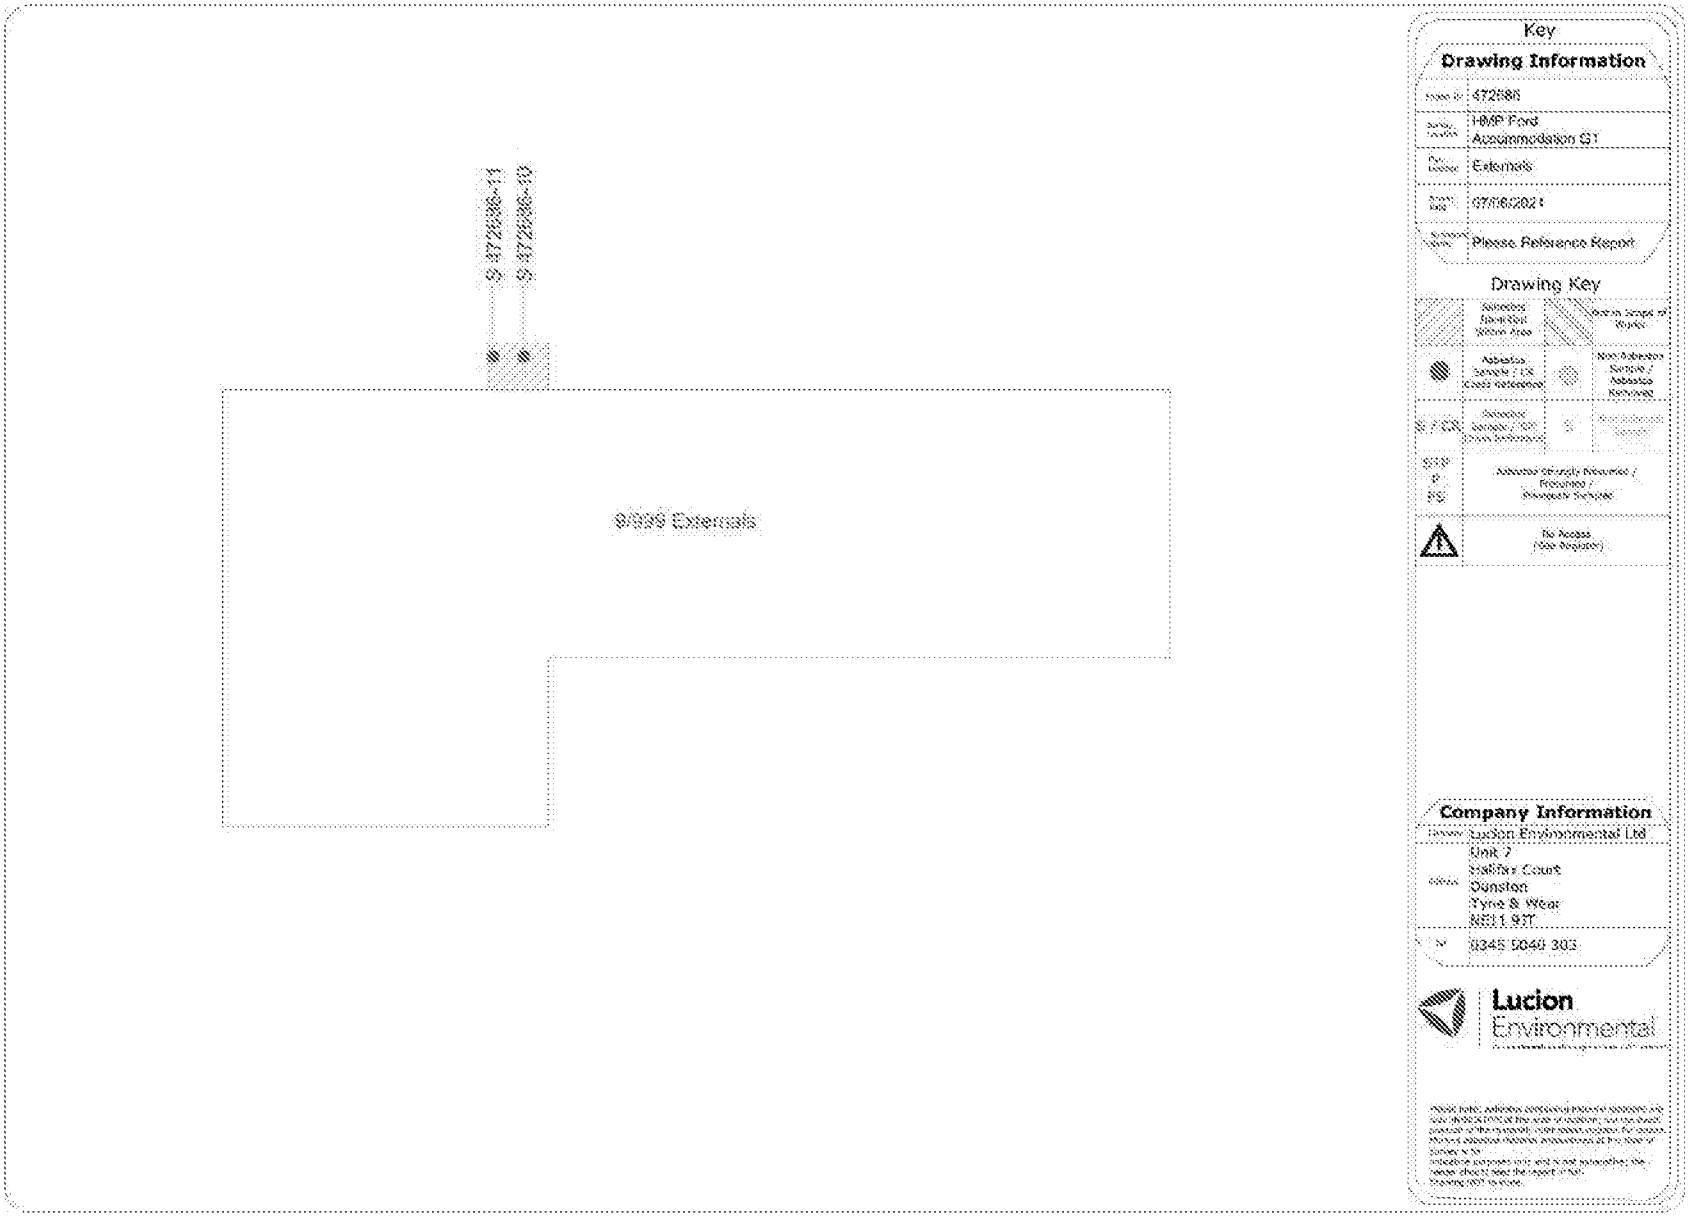


A4-Plan_472686_HMP-Ford.pdf

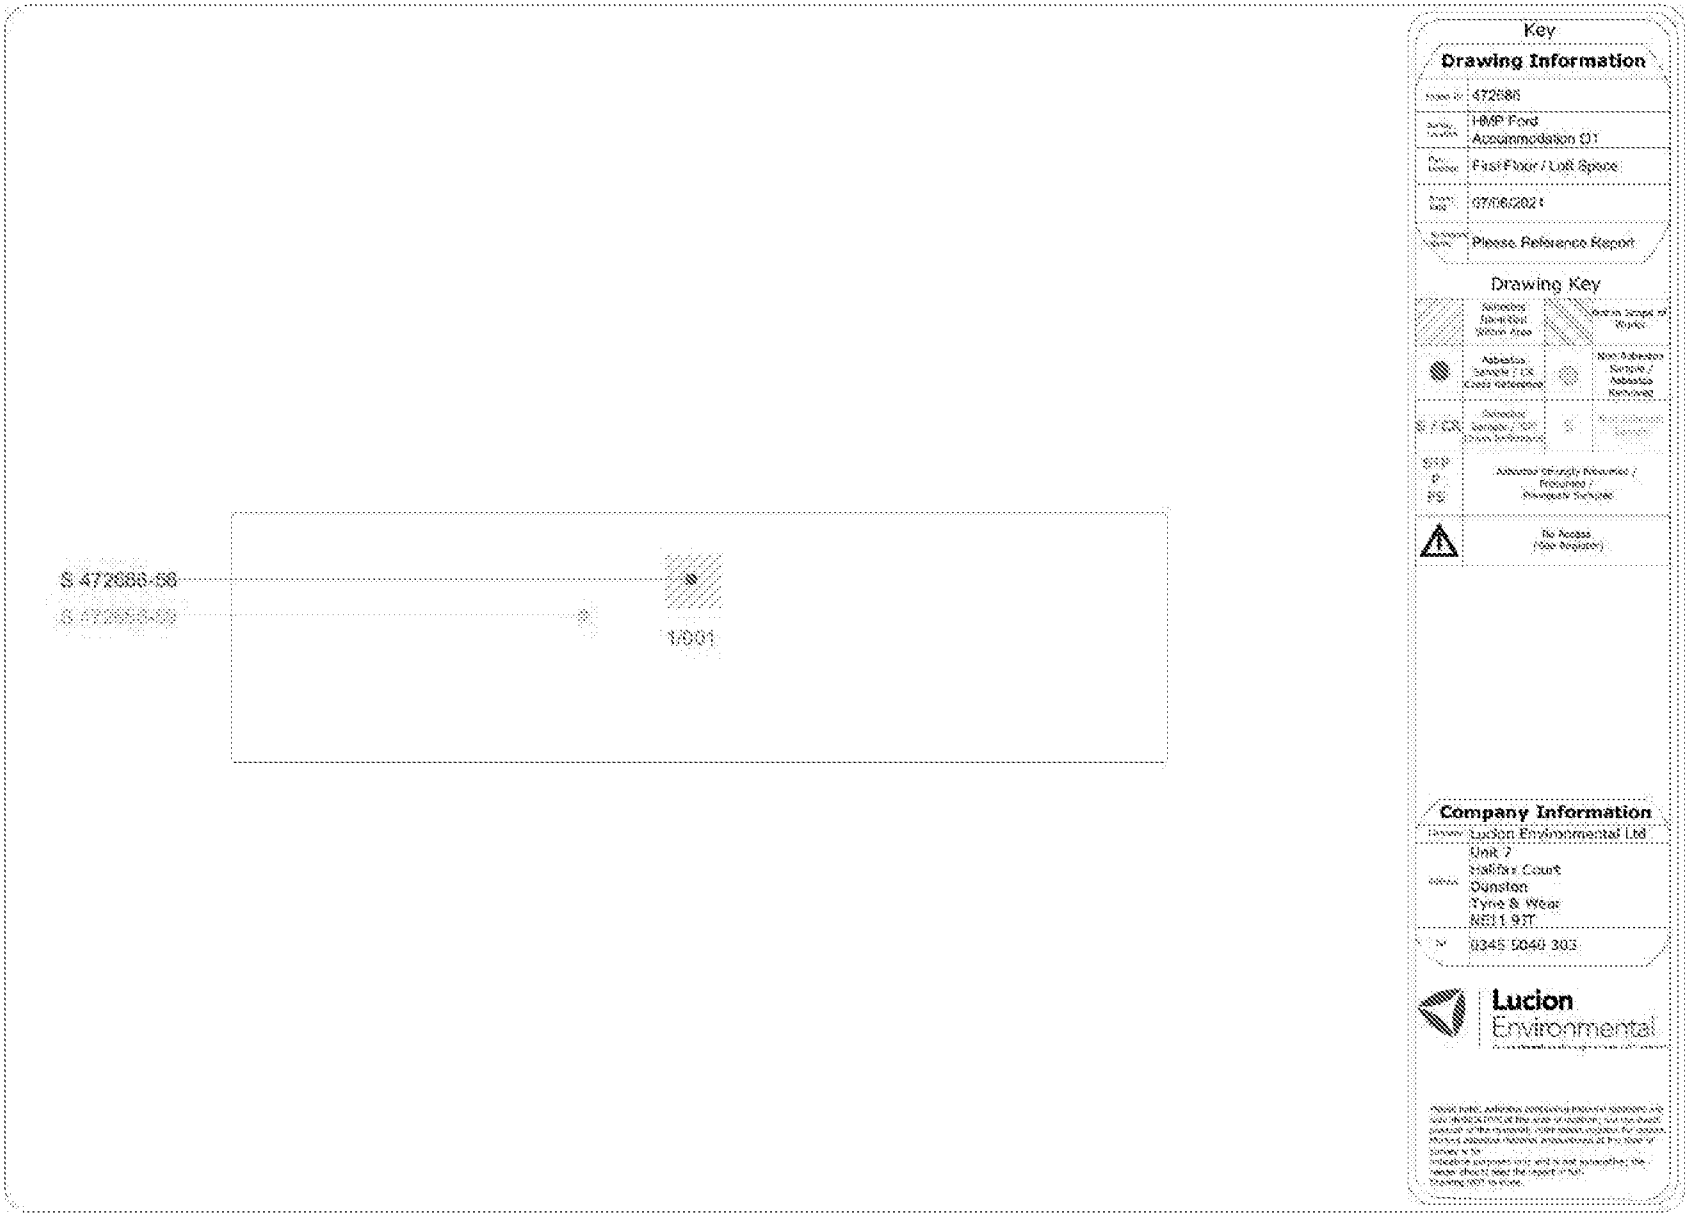


A4-Plan_472686_HMP-Ford.pdf

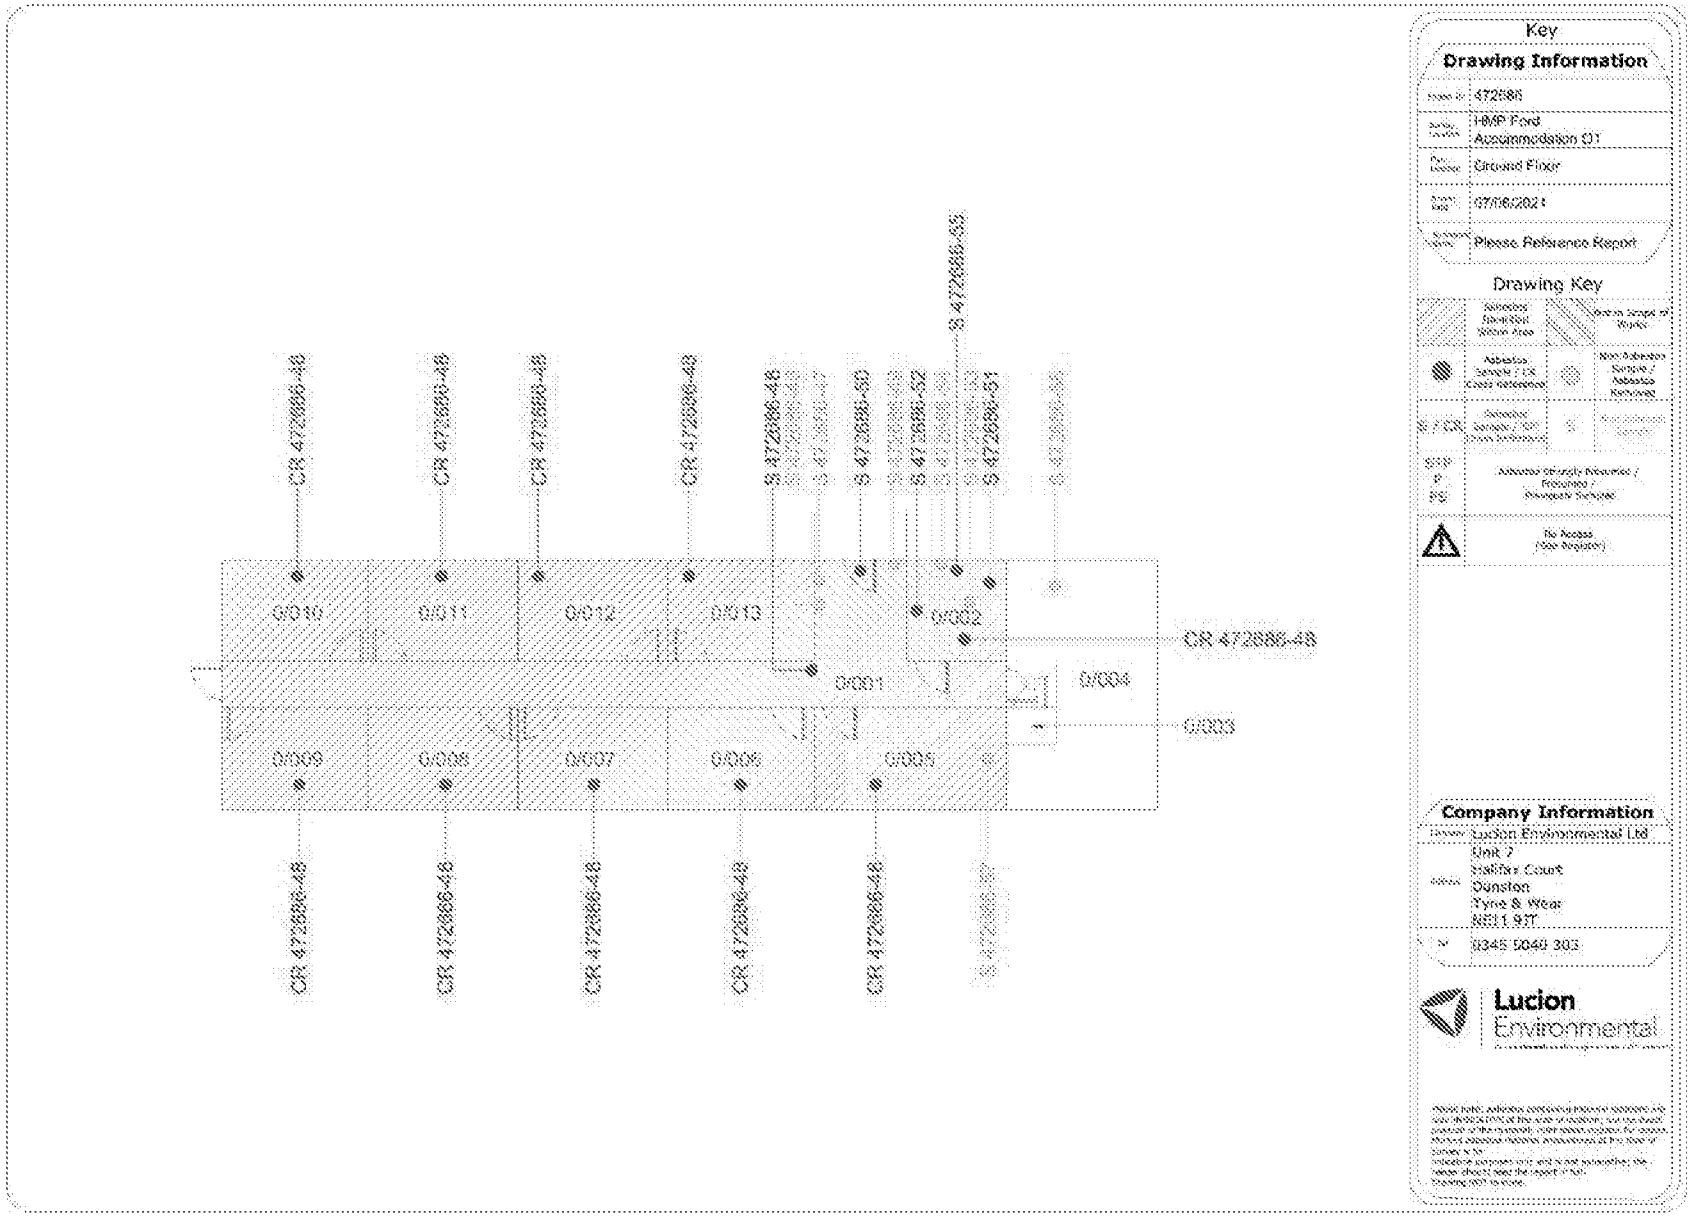


A4-Plan_472686_HMP-Ford.pdf

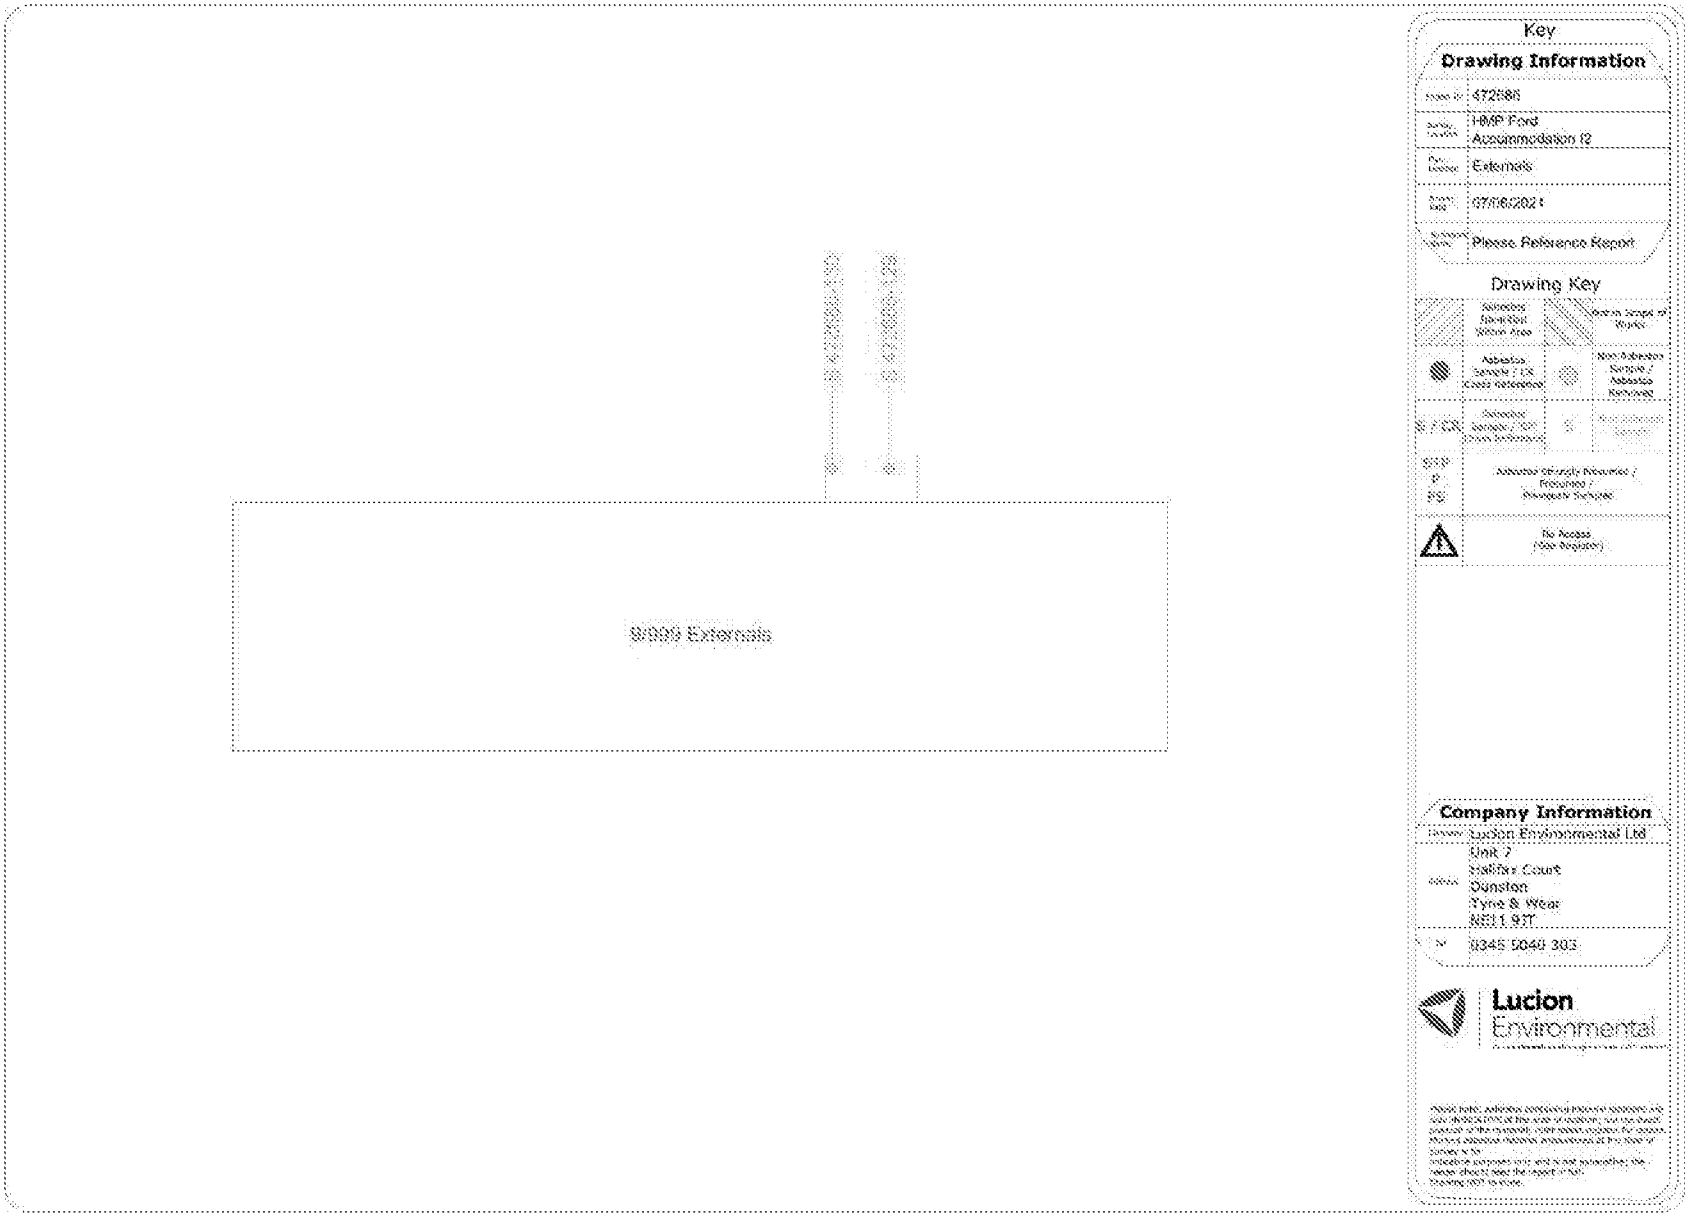


A4-Plan_472686_HMP-Ford.pdf

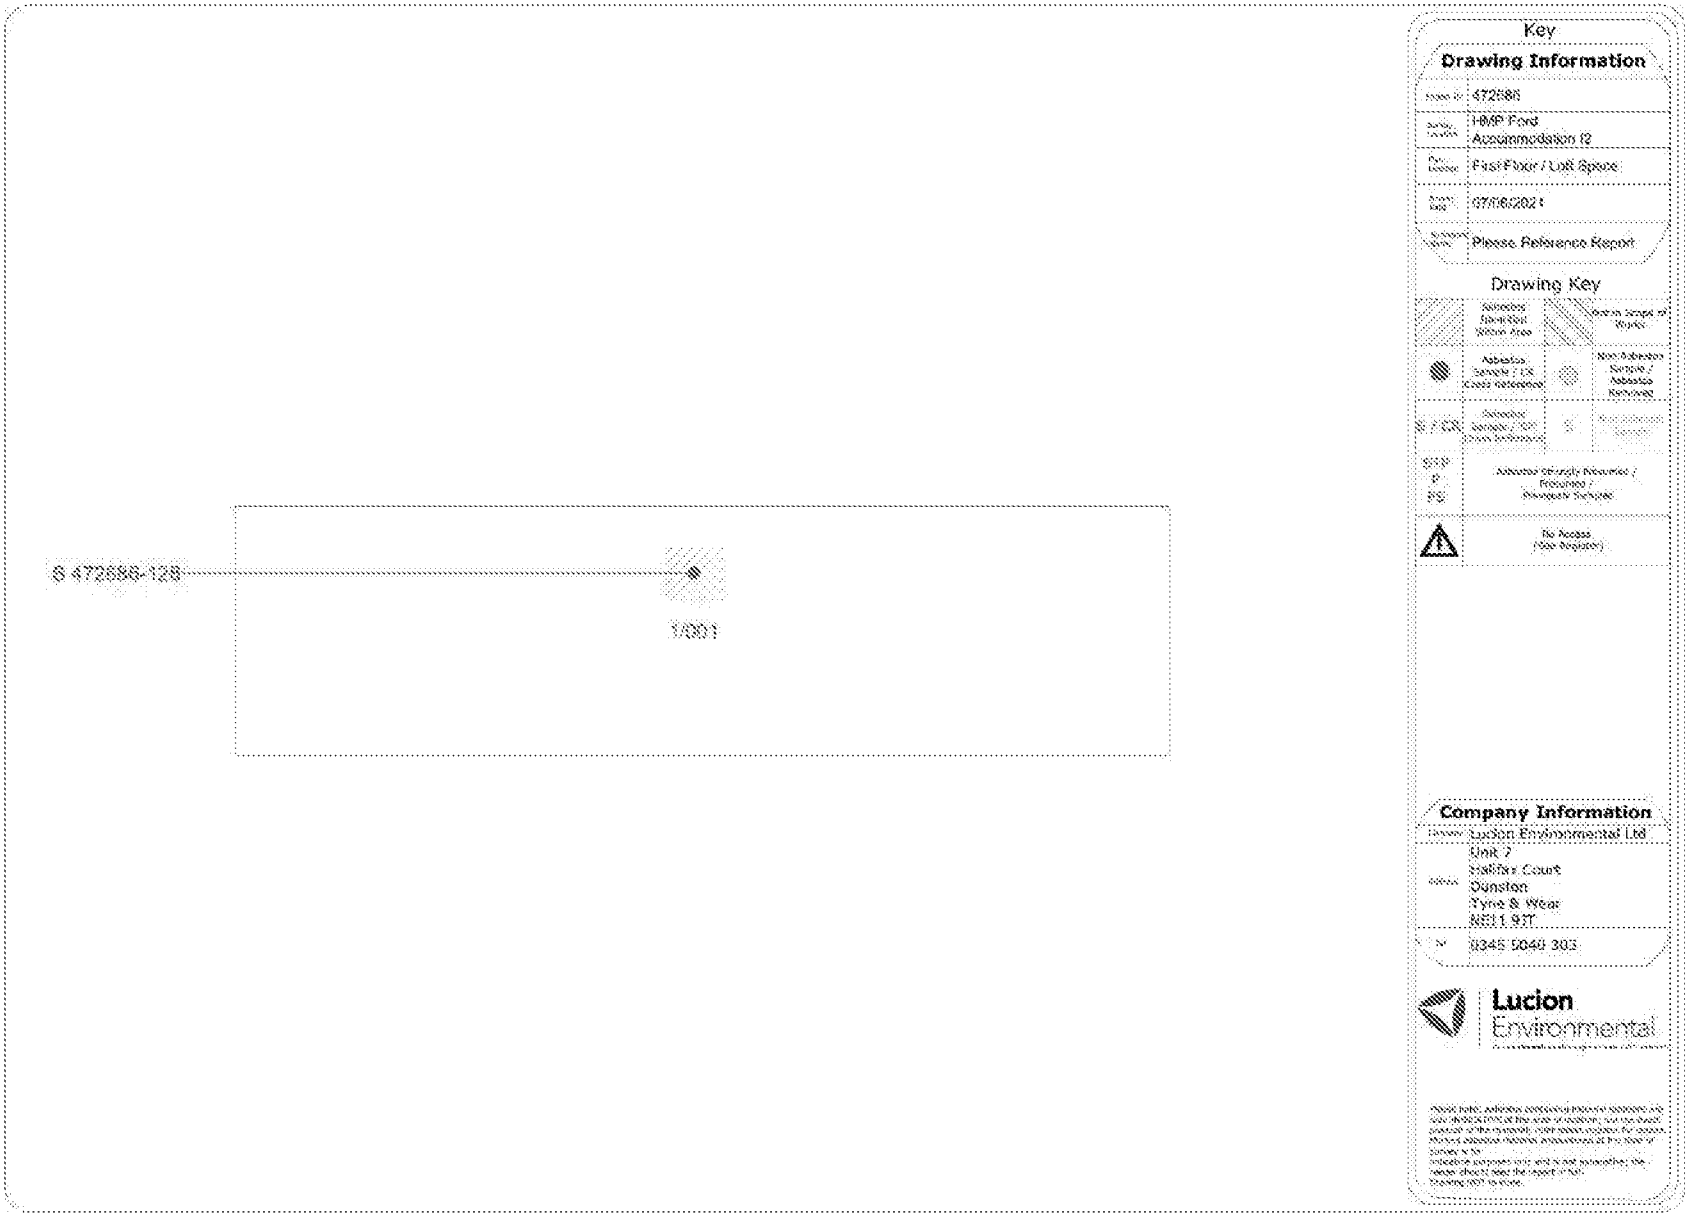


A4-Plan_472686_HMP-Ford.pdf

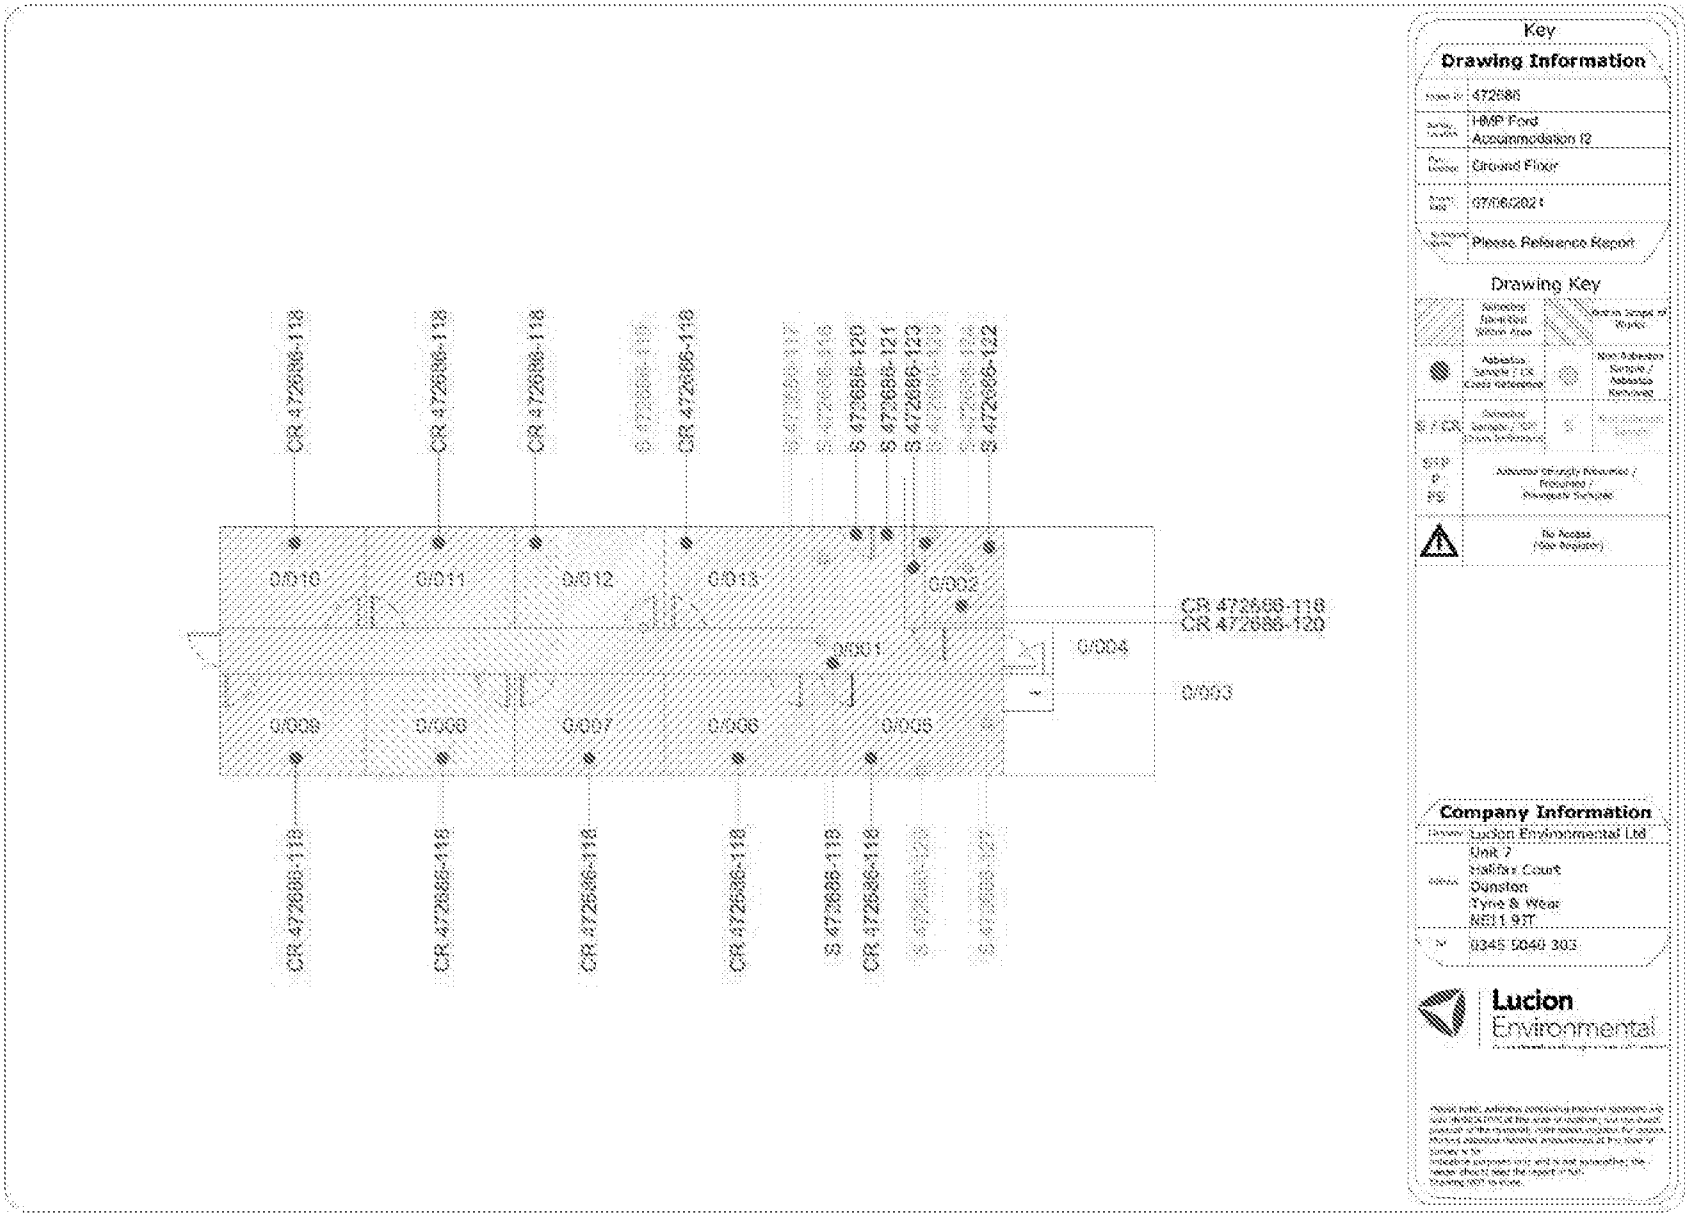


A4-Plan_472686_HMP-Ford.pdf

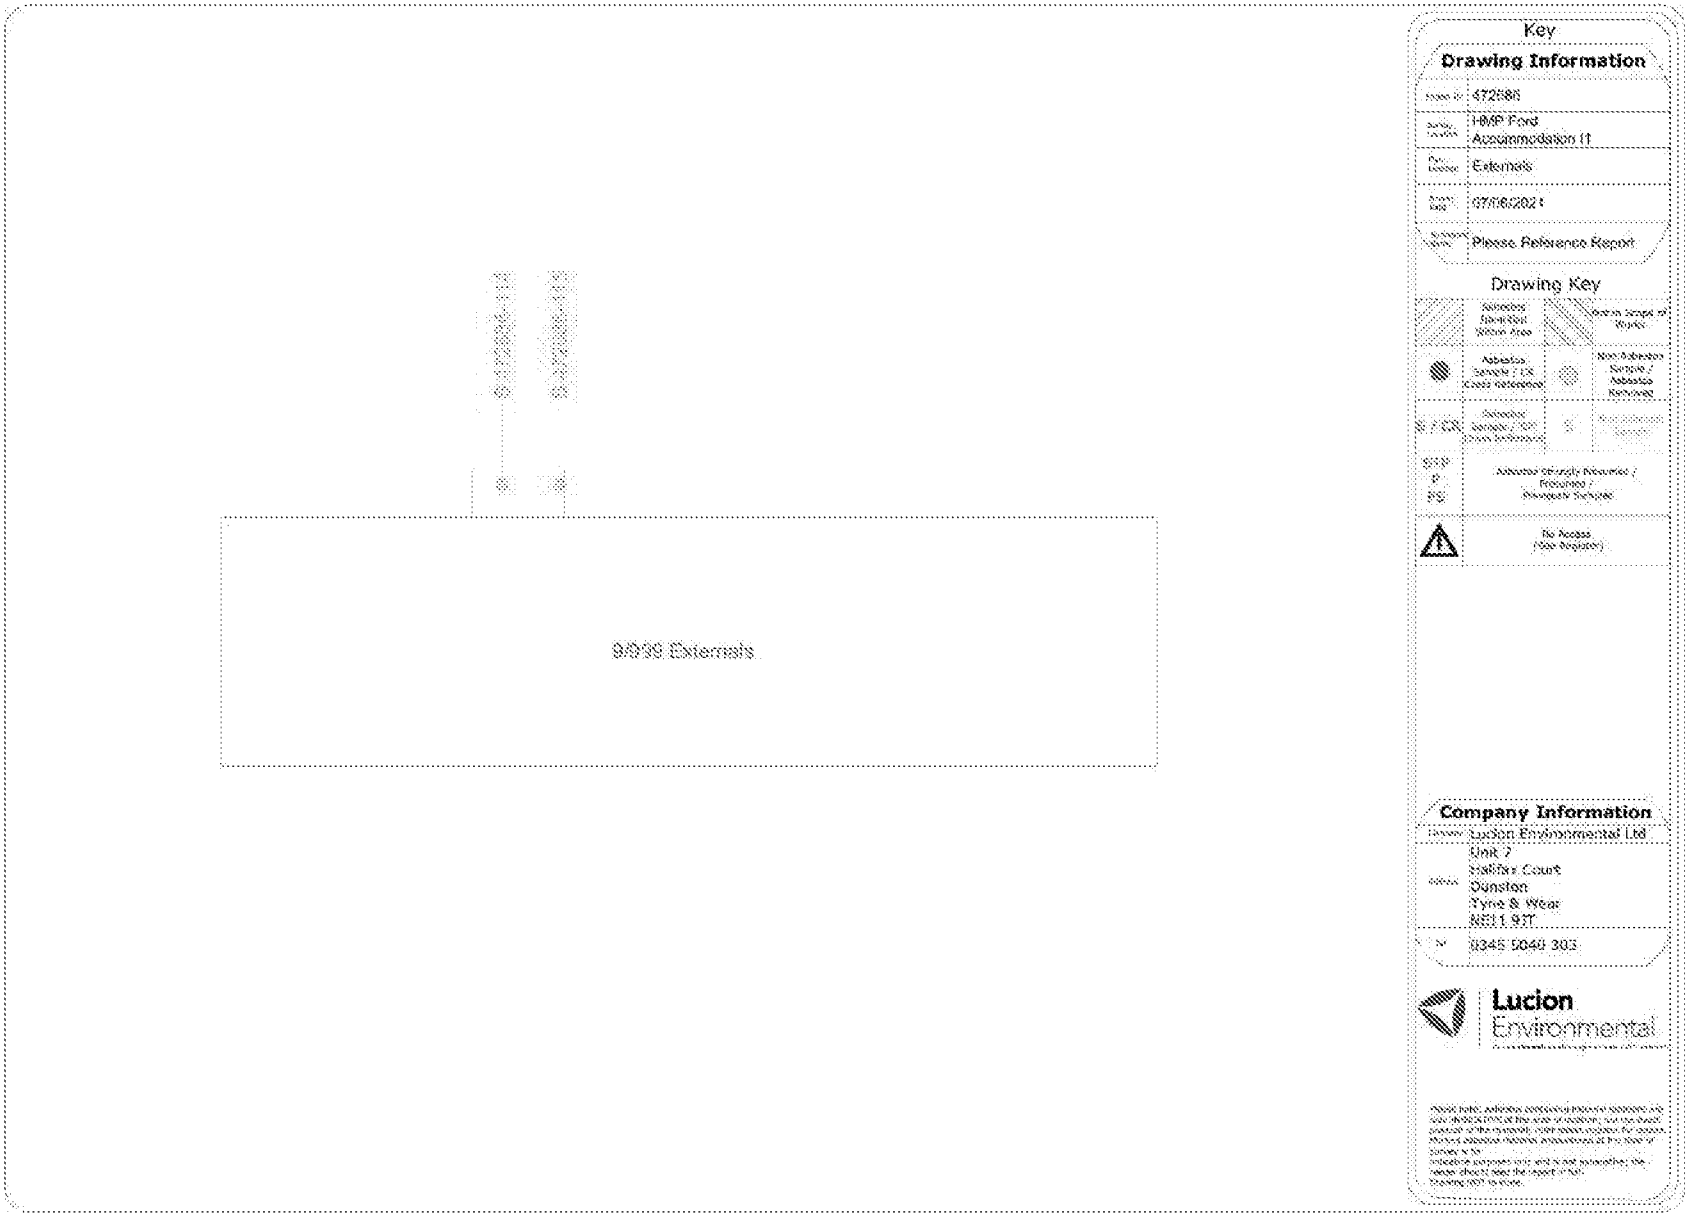


A4-Plan_472686_HMP-Ford.pdf

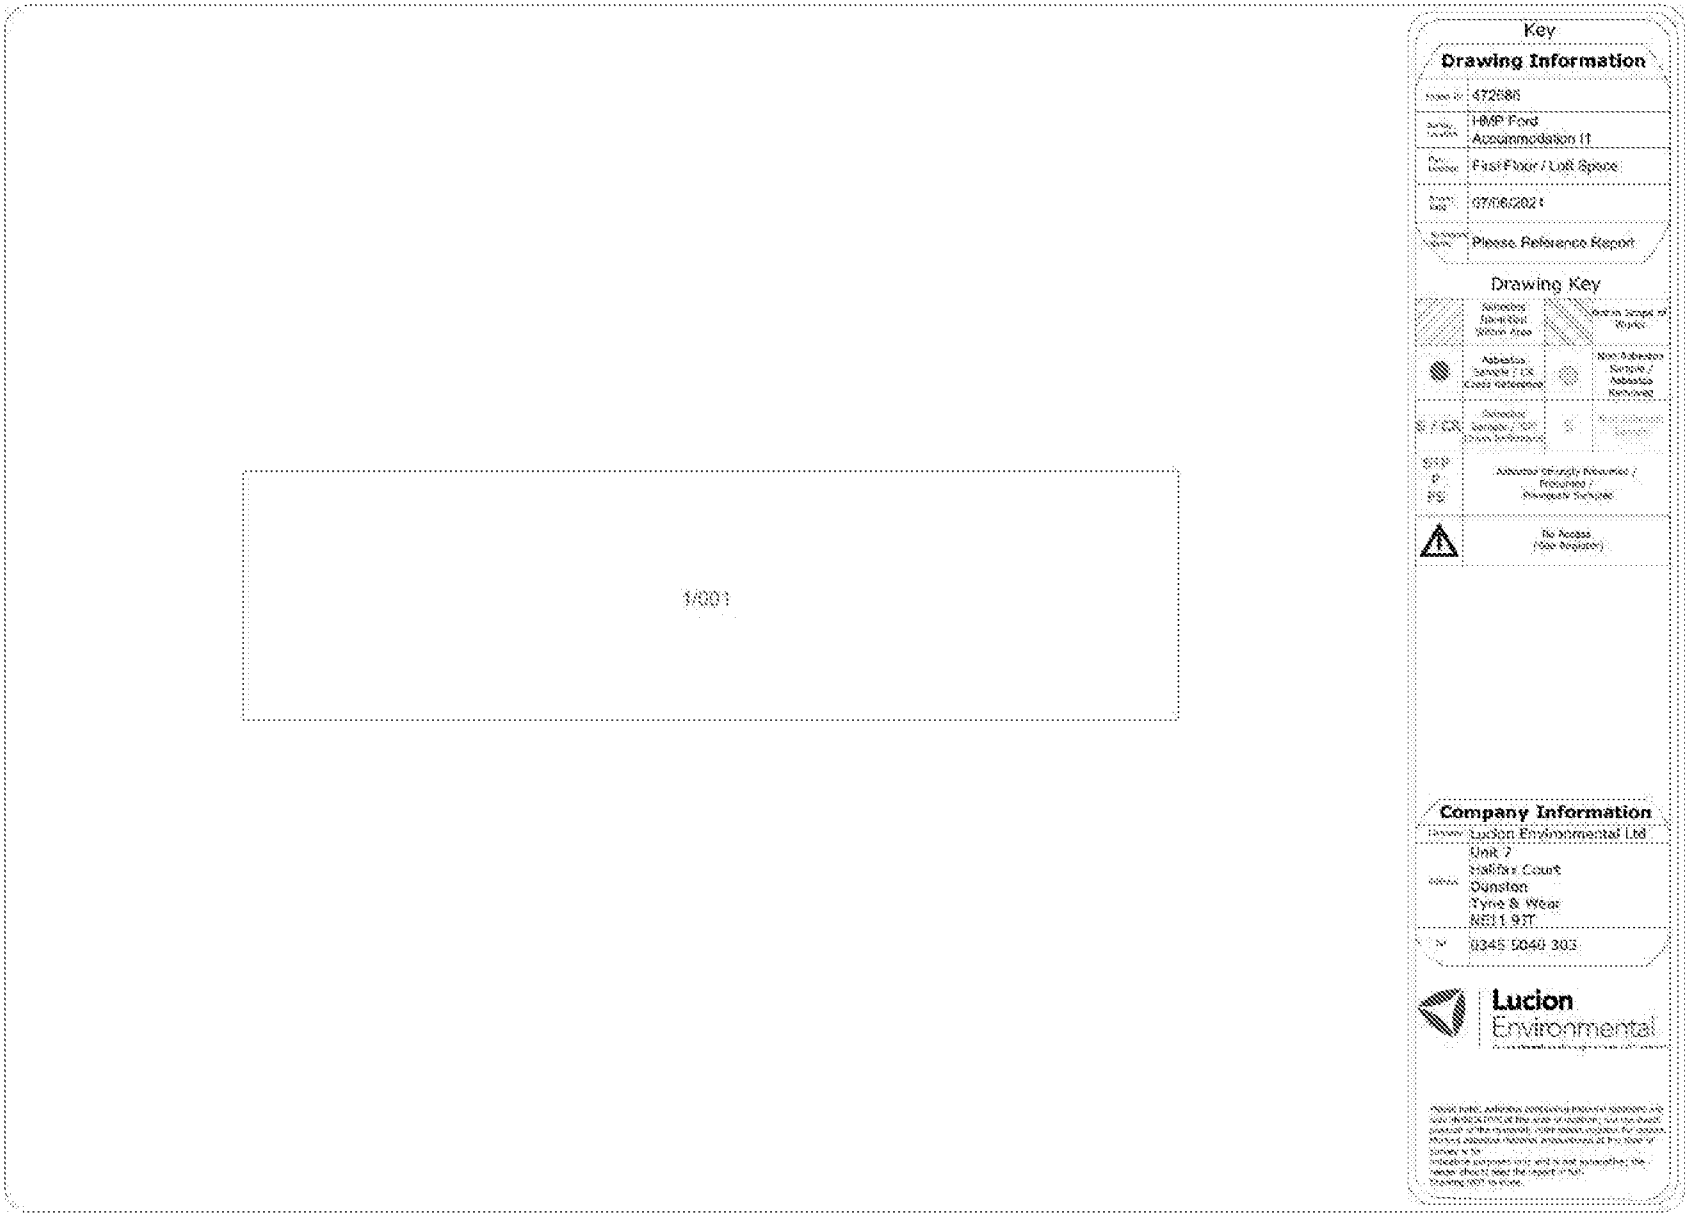


A4-Plan_472686_HMP-Ford.pdf

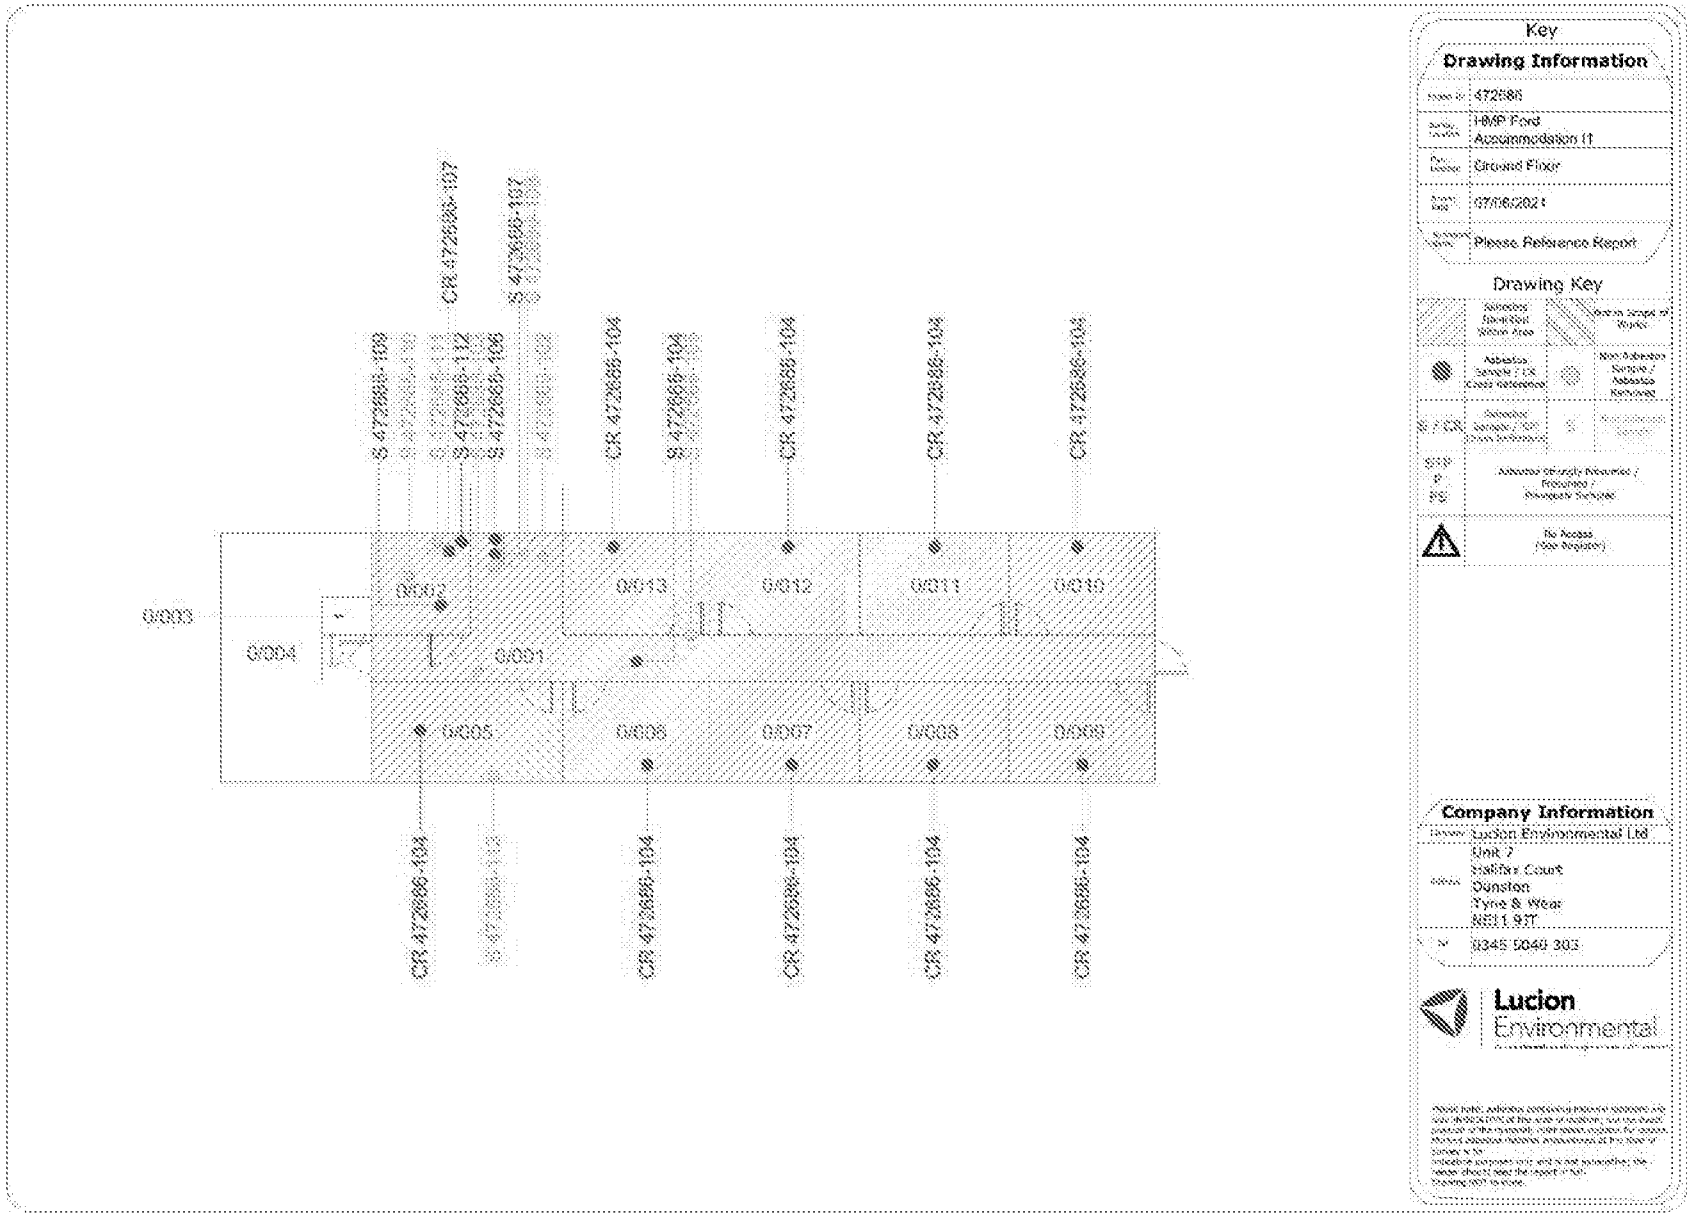

A4-Plan_472686_HMP-Ford.pdf

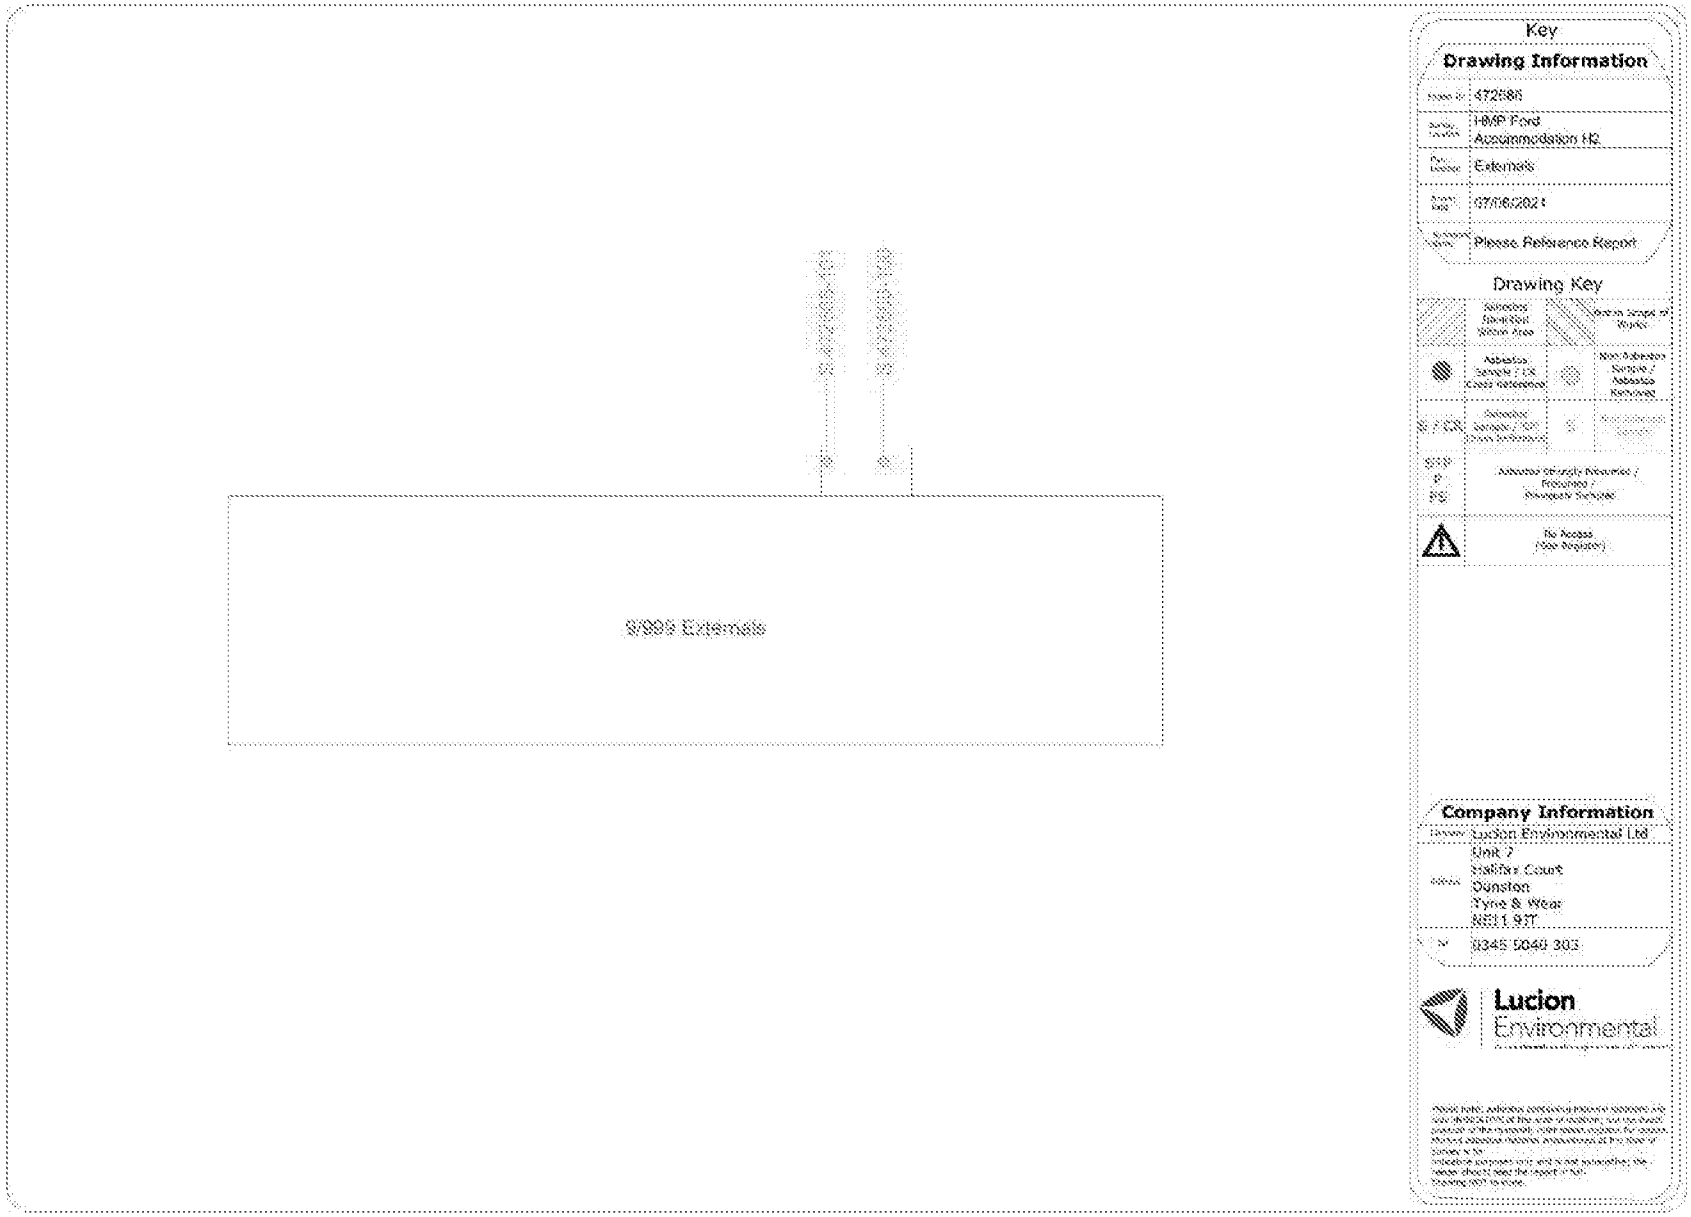

A4-Plan_472686_HMP-Ford.pdf

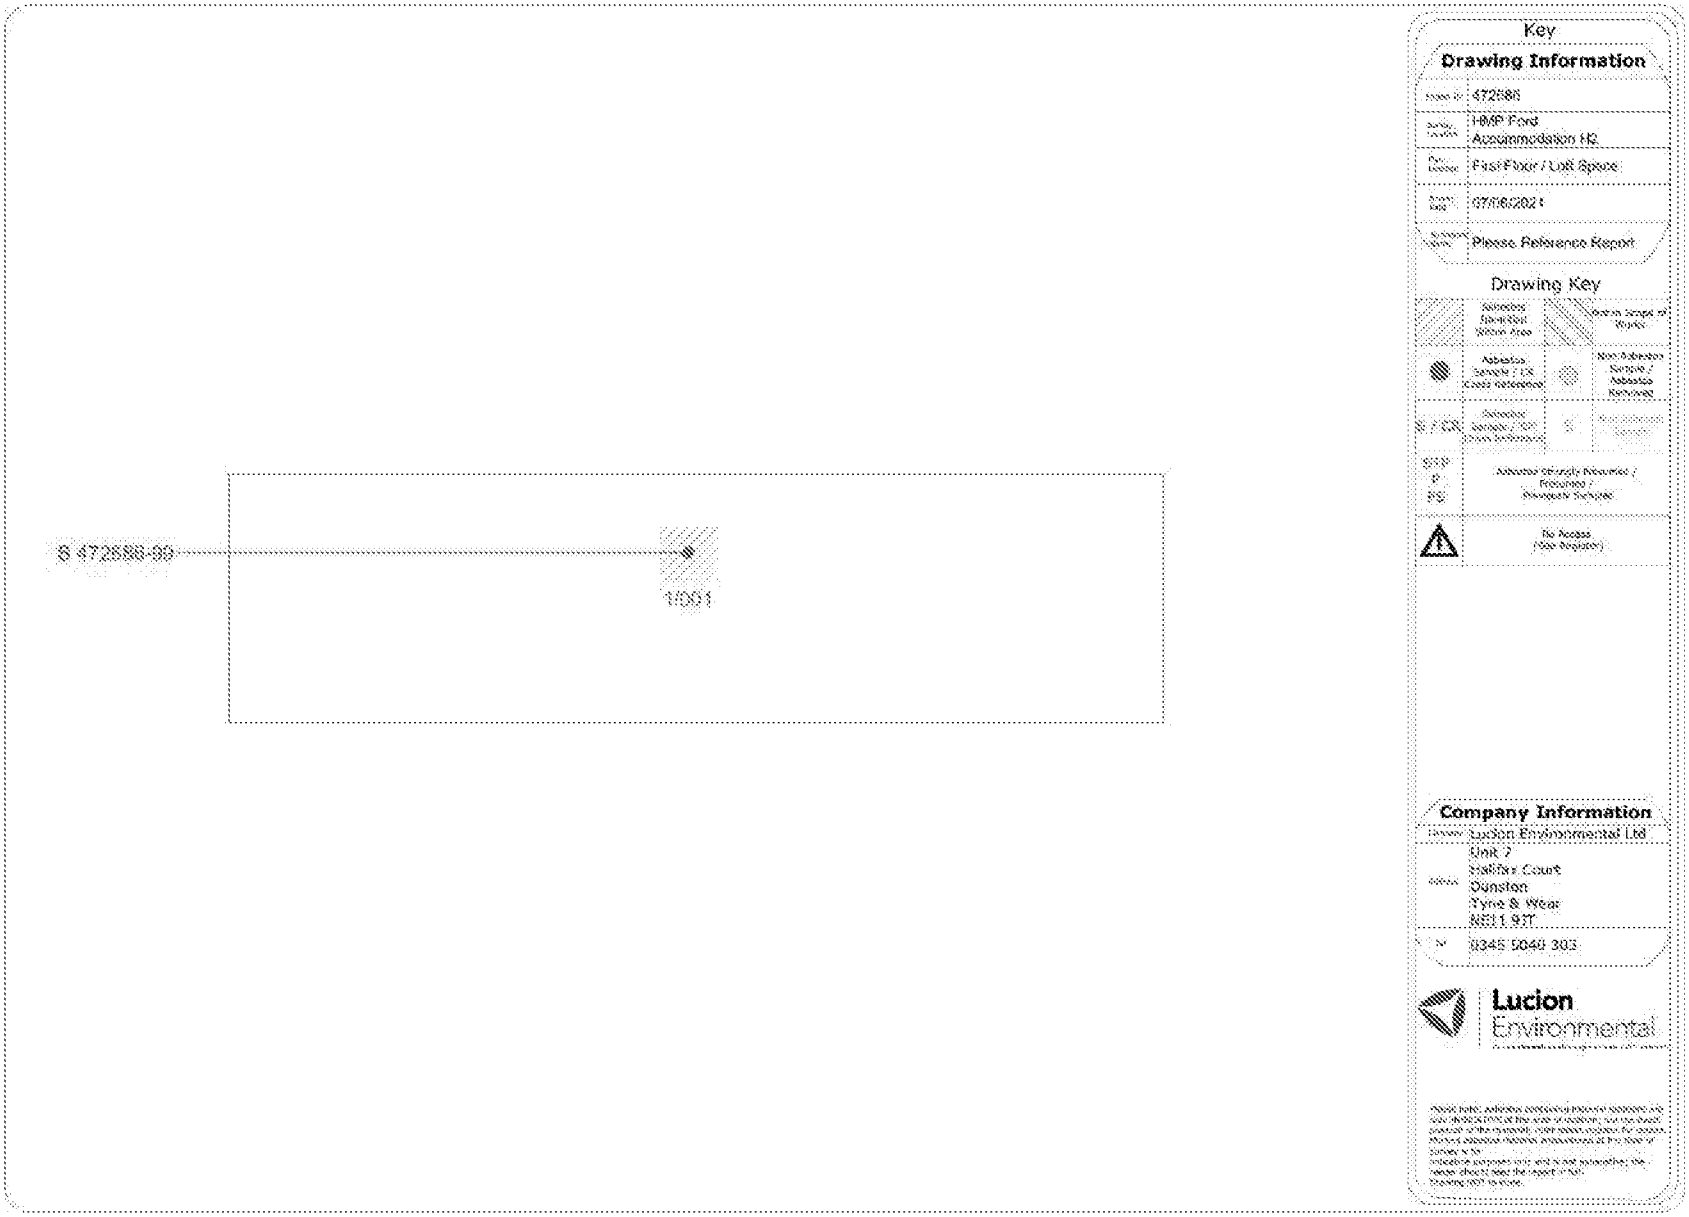

A4-Plan_472686_HMP-Ford.pdf

